NEW CASTLE COUNTY
VO-TECH SCHOOL DISTRICT

PAUL M. HODGSON
VOCATIONAL TECHNICAL HIGH SCHOOL

2575 Glasgow Avenue, Newark, DE 19702

PROJECT MANUAL

BSA+A PROJECT #22.011

Contract No. NCC2401D

Volume I
Divisions 00 through 01

BID PACKAGE D – BUILDING ENVELOPE AND FIT OUT
ISSUE FOR BID – ADDENDUM #1

December 28, 2023

ABHA | BSA+A

PROJECT MANUAL

NEW CASTLE COUNTY VO-TECH SCHOOL DISTRICT

PAUL M. HODGSON VOCATIONAL-TECHNICAL HIGH SCHOOL

Contract No. NCC2401D

OWNER
New Castle County Vo-Tech School District
1417 Newport Rd
Wilmington, DE 19804
(302) 995.8000
fax (302) 995.1579

ARCHITECT
ABHA|BSA+A, LLC
1621 North Lincoln St.
Wilmington, DE 19801
(302) 658.6426
(302) 658.9300
Fax (302) 658.8431

CONSTRUCTION MANAGER
EDiS Company
110 South Poplar St., Suite 400
Wilmington, DE 19801
(302) 421.2973

CIVIL ENGINEER
Landmark Science & Engineering
200 Continental Dr., Suite 400
Newark, DE 19713
(302) 323.9377

STRUCTURAL ENGINEER
DCI Engineers
2 Mill Road, Suite 100
Wilmington, DE 19806
(302) 252.9200
Fax (302) 252.9201

MECHANICAL/ELECTRICAL/ PLUMBING ENGINEER
Gipe Associates, Inc.
8719 Brooks Drive
Easton, MD 21601
(410) 822.8688

FOOD SERVICE CONSULTANT
Corsi Associates, LLC
300 Smith St.
Farmingdale, NY 11735
(610) 888.1955

THEATER CONSULTANT
Stages Consultants, LLC
300 Raritan Ave 2nd Floor
Highland Park, NJ 08904
(732) 333.8003

ACOUSTICAL CONSULTANT
Acentech
620 W. Germantown Pike, Suite 210
Plymouth Meeting, PA 19462
(215) 245.8244

SECURITY/TECHNOLOGY CONSULTANT
Educational Systems Planning
2448 Holly Avenue, Suite 302
Annapolis, MD 21401
(410) 573.9148

ISSUE FOR BID
December 28, 2023

SECTION 00 01 07
SEALS PAGE

DESIGN PROFESSIONALS OF RECORD

Architect
ABHA|BSA+A, LLC
1621 North Lincoln St.
Wilmington, DE 19801
(302) 658.6426
(302) 658.9300

Civil Engineer
Landmark Science & Engineering
200 Continental Dr., Suite 400
Newark, DE 19713
(302) 323.9377

Structural Engineer
DCI Engineers
2 Mill Road, Suite 100
Wilmington, DE 19806
302-252-9200

MEP-FP Engineer
Gipe Associates
8719 Brooks Drive
Easton, MD 21601
(410) 822-8688

END OF SECTION

000110 - TABLE OF CONTENTS

The following previously issued Bid Package documentation is included by reference:
BPB Sitework and Utilities dated 25 May 23
BPB Addendum #1 dated 1 Aug 23
BPB Addendum #2 dated 7 Aug 23
BPB Addendum #3 dated 10 Aug 23
BPC Foundations and Structures 31 Aug 23
BPC Addendum #1 dated 29 Sept 23
BPC Addendum #2 dated 11 Oct 23
BPC Addendum #3 dated 12 Oct 23
BPC Addendum #4 dated 20 oct 23
BPC Addendum #5 dated 23 Oct 23

VOLUME 1

Division 00 - Procurement and Contract Requirements

000110	Table of Contents
000115	List of Drawings
001116	Invitation to Bid
002113	Instructions to Bidders
003132	Geotechnical Data
004100	Bid Forms and Attachments: • Subcontractor List • Non-Collusion Statement • Consent of Surety • Affidavit of Employee Drug Testing Program • Affidavit of Contractor Qualifications • DBS Subcontractor List
004313	Bid Bond
005200	Agreement Forms: • AIA Document A132-2019 Standard Form of Agreement Between Owner and Contractor • AIA Document A132-2019 Exhibit A - Insurance and Bonds
005413	Supplement to Agreement Between Owner and Contractor A132-2019
005414	Supplement to A132-2019 – Exhibit A - Insurance and Bonds
006113	Performance and Payment Bond Forms
006216	Certificate of Insurance
007200	General Conditions AIA Document A232 - 2019
007300	Supplementary General Conditions A232-2019
007343	Wage Rate Requirements
008113	General Requirements • Quarterly DBE Report
008114	Drug Testing Program and Forms
008115	Affidavit of Craft Training Compliance

Division 01 - General Requirements

011100 Summary of Work - Work Covered by Contract Documents
012100 Allowances
- Allowance Authorization Form

012200 Unit Prices
012300 Alternates
012600 Change Order Procedures
- Change Order Detail Form
- Labor Detail Form

012613 Contractor Compensation
012900 Payment Procedures
013113 Project Coordination Meetings
013119 Preinstallation Meetings
013125 Web-Based Project Management System
013216 Construction Progress Schedule
013219 Submittals Register
013226 Contractor Daily Reports
- Contractor's Daily Report Form

013300 Submittal Procedures
013500 Contractor Employee Background Check
013523 Safety Program
- Competent/Qualified Person Designation Log
- Certificate of Training Documents
- Job Hazard/Risk Analysis

013700 BIM Project Executive Plan
014000 Quality Requirements
014500 Quality Control
015113 Temporary Electricity
015123 Temporary Heating, Cooling and Ventilating
015200 Construction Facilities & Temporary Controls
016200 Material and Equipment
017123 Field Engineering
017329 Cutting and Patching
017419 Construction Waste Management
017700 Contract Closeout
017900 Demonstration and Training
019113 General Commissioning Requirements
019114 Plumbing Commissioning Requirements
019115 HVAC Commissioning Requirements
019116 Electrical Systems Commissioning Requirements

VOLUME 2
Division 03 – Concrete
03 30 00 Cast in Place Concrete

Division 04 – Masonry
04 20 00 Unit Masonry

04 72 00 Cast Stone Masonry

Division 05 – Metals
05 12 00 Structural Steel
05 21 00 Steel Joist Framing
05 31 00 Steel Deck
05 40 00 Cold-Formed Metal Framing
05 50 00 Metal Fabrications
05 51 00 Metal Stairs
05 51 33 Metal Ladders
05 52 13 Pipe and Tube Railings
05 58 00 Architectural Metal Column Covers
05 73 00 Decorative Metal Railings

Division 06 – Wood and Plastic
06 10 00 Rough Carpentry
06 20 00 Finish Carpentry
06 20 23 Interior Finish Carpentry

Division 07 – Thermal and Moisture Protection
07 05 53 Fire and Smoke Assembly Identification
07 13 00 Sheet Waterproofing
07 20 00 Thermal Insulation
07 21 29 Sprayed Acoustical Insulation
07 25 00 Weather Barriers
07 26 16 Under-Slab Vapor Barriers
07 26 40 Spray Polyurethane Foam Insulating Air Barrier
07 42 13.13 Metal Wall and Roof Panels
07 42 13.23 Metal Composite Material Wall Panels
07 53 00 Elastomeric Membrane Roofing
07 62 00 Sheet Metal Flashing and Trim
07 71 00 Roof Specialties
07 71 23 Manufactured Gutters and Downspouts
07 72 00 Roof Accessories
07 81 00 Applied Fireproofing
07 84 00 Fire Stopping
07 84 13 Fire Protection, HVAC & Plumbing Penetration Firestopping
07 91 00 Preformed Joint Sealants
07 92 00 Joint Sealants

Division 08 - Openings
08 11 13 Hollow Metal Doors and Frames
08 14 16 Flush Wood Floors
08 16 13 Integrated Door Openings Assemblies
08 31 00 Access Doors and Panels
08 33 23 Overhead Coiling Doors

08 43 13 Aluminum Framed Storefronts
08 43 33 Folding Glass Storefront
08 44 13 Glazed Aluminum Curtain Walls
08 45 23 Translucent Wall Assemblies
08 71 00 Door Hardware
08 71 06 Door Hardware Schedule
08 80 00 Glazing
08 87 23 Safety and Security Films
08 91 00 Louvers

Division 09 – Finishes
09 05 61 Common Work Results for Flooring Preparation
09 21 16 Gypsum Board Assemblies
09 30 00 Tiling
09 51 00 Acoustical Ceilings
09 54 00 Specialty Ceiling Systems
09 64 29 Wood Strip Flooring
09 65 00 Resilient Flooring
09 65 66 Resilient Athletic Flooring
09 66 16 Precast Cement Terrazzo Treads and Landings
09 66 23 Resin Matrix Terrazzo Flooring
09 67 00 Fluid Applied Flooring
09 68 13 Tile Carpeting
09 68 16 Sheet Carpeting
09 69 33 Low-Profile Fixed Height Access Flooring
09 84 00 Acoustic Room Components
09 91 13 Exterior Painting
09 91 23 Interior Painting

Division 10 – Specialties
10 11 01 Visual Display Boards and Display Cases
10 21 13.19 Plastic Toilet Compartments
10 21 23 Cubicle Curtains and Track
10 22 39 Vertically Retractable Walls
10 26 00 Wall Protection
10 28 00 Toilet Accessories
10 44 00 Fire Protection Specialties
10 51 00 Metal Lockers
10 73 16.13 Metal Canopies

Division 11 - Equipment
11 40 00 Foodservice Equipment
11 61 33 Rigging Systems and Draperies
11 61 63 Loose Performance Lighting Fixtures
11 66 25 Gymnasium Equipment
11 66 53 Gymnasium Dividers

Division 12 – Furnishings
12 24 13 Window Treatment – Roller Shades
12 34 00 Manufactured Plastic Laminate Casework
12 36 00 Countertops, Backsplashes, and Window Stools
12 61 13 Fixed Audience Seating
12 66 13 Telescoping Bleachers
12 66 23 Telescoping Chair Platforms
12 93 00 Site Furnishings

Division 13 – Special Construction
Not Used

Division 14 – Conveying Equipment
14 20 13 Hydraulic Holeless Passenger Elevator

VOLUME 3
Division 21 – Fire Protection
21 05 00 Common Work Results for Fire Protection
21 05 05 Fire Suppression System Piping, Fitting and Valves
21 10 00 Water Based Fire Suppression System – Fire Pump

Division 22 – Plumbing
22 05 00 Common Work Results for Plumbing
22 05 05 Plumbing Piping, Fitting and Valves
22 07 01 Plumbing Insulation
22 40 00 Plumbing Fixtures
22 40 05 Plumbing Equipment
22 61 13 Compressed-Air Piping for Dental Systems
22 61 19 Compressed Air Equipment for Dental Systems
22 62 13 Vacuum Piping for Dental Systems
22 62 19 Vacuum Equipment for Dental Systems

VOLUME 4
Division 23 – HVAC
23 05 00 Common Work Results for HVAC
23 05 05 HVAC Piping, Fittings and Valves
23 05 48 Vibration Controls for HVAC, Plumbing and Fire Protection Equipment
23 05 93 Testing, Adjusting and Balancing for HVAC and Plumbing
23 06 00 Heating, Ventilating and Air Conditioning Equipment
23 07 01 HVAC Insulation
23 07 10 Dust Collection System
23 09 00 Instrumentation and Controls of HVAC and Plumbing Systems
23 09 23 Airflow Monitoring Stations
23 33 00 HVAC Air Distribution
23 82 20 Carbon Monoxide Exhaust System

23 82 21 Welding Fume Exhaust System
23 82 22 Packaged Kitchen Hood Ventilation Control System
23 83 12 Electrical Heating Cables

VOLUME 5
Division 26 – Electrical
26 05 00 Common Work Results for Electrical
26 05 13 Medium-Voltage Cables
26 05 19 Low-Voltage Electrical Power Conductors and Cabling
26 05 26 Grounding and Bonding for Electrical Systems
26 05 29 Hangers and Supports for Electrical Systems
26 05 33 Raceways and Boxes for Electrical Systems
26 05 43 Underground Ductbanks
26 05 53 Identification for Electrical Systems
26 05 73 Short Circuit Analysis, Coordination Study, and Arc Flash Hazard Analysis
26 09 23 Lighting Control Devices
26 09 43 Network Lighting Controls
26 09 61 Performance Lighting Systems
26 09 63 Performance Lighting Systems Installation
26 09 73 Audio Video Systems Installation
26 11 20 Utility Incoming Service Provisions
26 22 00 Low-Voltage Transformers
26 24 13 Switchboards
26 24 16 Panelboards
26 25 50 Manual Transfer Switch/Generator Docking Station
26 27 16 Commercial Pedestals
26 27 26 Wiring Devices
26 28 13 Fuses
26 28 16 Enclosed Switches and Circuit Breakers
26 29 13 Enclosed Controllers
26 32 13 Engine Generators
26 36 00 Transfer Switches
26 41 13 Lightening Protection System
26 43 13 Surge Protection Devices
26 51 00 Interior Lighting
26 56 00 Exterior Lighting
26 60 10 Rigging Systems Electrical Work

VOLUME 6
Division 27 – Communications
27 05 00 Telecommunications Pathways and Spaces
27 10 00 Structured Cabling
27 20 00 Network Equipment
27 40 00 Classroom and Conference Room AV Equipment
27 41 00 Specialized AV Systems
27 41 17 Audio Video Systems

27 50 00 Public Address and Clock

Division 28 – Electronic Safety and Security
28 05 01 Security Pathways and Spaces
28 10 00 Intrusion Detection System
28 11 00 Access Control System
28 20 00 Video Surveillance System
28 31 12 Public Safety – First Responder Radio Amplification System
28 46 21 Addressable Fire Alarm Systems

DIVISION 31 EARTHWORK
31 23 00 Excavation & Backfill for Pipelines and Structure

DIVISION 32 SITE IMPROVEMENT
32 13 13 Concrete Paving
32 18 00 Synthetic Turf Shock Pad
32 18 13 Synthetic Turf Carpet
32 31 19 Decorative Metal Fences and Gates

END OF SECTION

SECTION 000115 - LIST OF DRAWINGS

All previously issued Bid Packages and Addendum are to be included by reference.

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
General				
G001	Cover Sheet – Volume 1	D	12/28/23	
G002	Drawing List	D	12/28/23	
G003	Code Review	D	12/28/23	
G004	Code Review Plan First Floor	D	12/28/23	
G005	Code Review Plan Second Floor	D	12/28/23	
G007	School Safety Review – Overall Plans	D	12/28/23	
G008	Dema – Main Office Security Plan, Elevations, and Details	D	12/28/23	
G009	Keyplans	D	12/28/23	
G010	Exterior Wall Mockup	D	12/28/23	
Structural				
S001	Cover Sheet	D	12/28/23	
S002	General Notes	D	12/28/23	
S003	General Notes and Special Inspections	D	12/28/23	
S004	Project Schedules	D	12/28/23	
S101	Overall Foundation Plan	D	12/28/23	
S102	Overall Second Floor Framing Plan	D	12/28/23	
S103	Overall Roof Framing Plan	D	12/28/23	
S111	Keyplan 1 - Foundation Plan	D	12/28/23	
S112	Keyplan 2 - Foundation Plan	D	12/28/23	
S113	Keyplan 3 - Foundation Plan	D	12/28/23	
S114	Keyplan 4 - Foundation Plan	D	12/28/23	
S115	Keyplan 5 - Foundation Plan	D	12/28/23	
S116	Keyplan 6 - Foundation Plan	D	12/28/23	
S116A	Keyplan 6 - Alternate Foundation Plan	D	12/28/23	
S117	Keyplan 7 - Foundation Plan	D	12/28/23	
S118	Keyplan 8 - Foundation Plan	D	12/28/23	
S119	Keyplan 9 - Foundation Plan	D	12/28/23	
S120	Keyplan 10 - Foundation Plan	D	12/28/23	
S121	Keyplan 11 - Foundation Plan	D	12/28/23	
S131	Keyplan 1 - Second Floor Framing Plan	D	12/28/23	
S132	Keyplan 2 - Second Floor Low Roof Framing Plan	D	12/28/23	
S133	Keyplan 3 - Second Floor Framing Plan	D	12/28/23	
S134	Keyplan 4 - Second Floor Framing Plan	D	12/28/23	
S135	Keyplan 5 - Second Floor Framing Plan	D	12/28/23	
S136	Keyplan 6 - Second Floor Framing Plan	D	12/28/23	
S136A	Keyplan 6 - Alternate Second Floor Framing Plan	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
S137	Keyplan 7 - Second Floor Framing Plan	D	12/28/23	
S138	Keyplan 8 - Second Floor Framing Plan	D	12/28/23	
S139	Keyplan 9 - Second Floor Framing Plan	D	12/28/23	
S140	Keyplan 10 - Second Floor Framing Plan	D	12/28/23	
S141	Keyplan 11 - Second Floor Framing Plan	D	12/28/23	
S151	Keyplan 1 - Roof Framing Plan	D	12/28/23	
S152	Keyplan 2 - Roof Framing Plan	D	12/28/23	
S154	Keyplan 4 - Roof Framing Plan	D	12/28/23	
S155	Keyplan 5 - Roof Framing Plan	D	12/28/23	
S156	Keyplan 6 - Roof Framing Plan	D	12/28/23	
S156A	Keyplan 6 - Alternate Roof Framing Plan	D	12/28/23	
S157	Keyplan 7 - Roof Framing Plan	D	12/28/23	
S158	Keyplan 8 - Roof Framing Plan	D	12/28/23	
S159	Keyplan 9 - Roof Framing Plan	D	12/28/23	
S160	Keyplan 10 - Roof Framing Plan	D	12/28/23	
S161	Keyplan 11 - Roof Framing Plan	D	12/28/23	
S201	Exterior Elevations	D	12/28/23	
S401	Enlarged Plans	D	12/28/23	
S501	Typical Foundation Details	D	12/28/23	
S502	Typical Foundation Details	D	12/28/23	
S503	Typical Foundation Details	D	12/28/23	
S504	Foundation Sections and Details	D	12/28/23	
S505	Foundation Sections and Details	D	12/28/23	
S506	Foundation Sections and Details	D	12/28/23	
S511	Typical Framing Details	D	12/28/23	
S512	Typical Framing Details	D	12/28/23	
S513	Typical Framing Details	D	12/28/23	
S514	Framing Sections and Details	D	12/28/23	
S515	Framing Sections and Details	D	12/28/23	
S516	Framing Sections and Details	D	12/28/23	
S517	Framing Sections and Details	D	12/28/23	
S518	Framing Sections and Details	D	12/28/23	
S519	Framing Sections and Details	D	12/28/23	
S520	Framing Sections and Details	D	12/28/23	
S521	Framing Sections and Details	D	12/28/23	
S522	Framing Sections and Details	D	12/28/23	
S523	Framing Sections and Details	D	12/28/23	
S524	Framing Sections and Details	D	12/28/23	
S601	Live Load Diagrams	D	12/28/23	
S602	Live Load Diagrams	D	12/28/23	
S603	Live Load Diagrams	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
S720	CFMF Details	D	12/28/23	
Architectural				
G001	Cover Sheet - Volume 2	D	12/28/23	
G002	Drawing List	D	12/28/23	
A001	General Notes, Symbols and Abbreviations	D	12/28/23	
A002	Accessible Restroom Details	D	12/28/23	
A003	Exterior Wall Assemblies	D	12/28/23	
A004	Partition Types	D	12/28/23	
A100	Architectural Site Plan	D	12/28/23	
A101	Overall First Floor Plan - Base Bid	D	12/28/23	
A102	Overall Second Floor Plan - Base Bid	D	12/28/23	
A103	Floor Plan - Shops - Mezzanine Level	D	12/28/23	
A104	Overall First Floor Plan – Add Alternate #3	D	12/28/23	
A105	Overall Second Floor Plan – Add Alternate #3	D	12/28/23	
A106	Courtyard Plans	D	12/28/23	
A111	First Floor Plan - Keyplan 1	D	12/28/23	
A112	First Floor Plan - Keyplan 2	D	12/28/23	
A113	First Floor Plan - Keyplan 3	D	12/28/23	
A114	First Floor Plan - Keyplan 4	D	12/28/23	
A115	First Floor Plan - Keyplan 5	D	12/28/23	
A116	First Floor Plan - Keyplan 6	D	12/28/23	
A116A	First Floor Plan - Keyplan 6 – Alternate #3	D	12/28/23	
A117	First Floor Plan - Keyplan 7	D	12/28/23	
A118	First Floor Plan- Keyplan 8	D	12/28/23	
A119	First Floor Plan - Keyplan 9	D	12/28/23	
A120	First Floor Plan - Keyplan 10	D	12/28/23	
A121	First Floor Plan - Keyplan 11	D	12/28/23	
A131	Second Floor Plan - Keyplan 4	D	12/28/23	
A132	Second Floor Plan- Keyplan 5	D	12/28/23	
A133	Second Floor Plan - Keyplan 7	D	12/28/23	
A134	Second Floor Plan - Keyplan 8	D	12/28/23	
A135	Second Floor Plan - Keyplan 9	D	12/28/23	
A136	Second Floor Plan - Keyplan 10	D	12/28/23	
A137	Partial Plans – Mech Equipment Rooms	D	12/28/23	
A138	Overall RCP – First Floor	D	12/28/23	
A139	Overall RCP – First Floor	D	12/28/23	
A140	Overall RCP – Second Floor	D	12/28/23	
A141	First Floor Reflected Ceiling Plan – Keyplan 1	D	12/28/23	
A142	First Floor Reflected Ceiling Plan – Keyplan 2	D	12/28/23	
A143	First Floor Reflected Ceiling Plan - Keyplan 3	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
A144	First Floor Reflected Ceiling Plan - Keyplan 4	D	12/28/23	
A145	First Floor Reflected Ceiling Plan - Keyplan 5	D	12/28/23	
A146	First Floor Reflected Ceiling - Keyplan 6	D	12/28/23	
A146A	First Floor Reflected Ceiling Plan - Keyplan 6a (Add Alt. #3)	D	12/28/23	
A147	First Floor Reflected Ceiling Plan - Keyplan 7	D	12/28/23	
A148	First Floor Reflected Ceiling Plan - Keyplan 8	D	12/28/23	
A149	First Floor Reflected Ceiling Plan - Keyplan 9	D	12/28/23	
A150	First Floor Reflected Ceiling Plan - Keyplan 10	D	12/28/23	
A151	First Floor Reflected Ceiling Floor - Keyplan 11	D	12/28/23	
A152	Mezzanine Level RCP - Shops	D	12/28/23	
A153	Second Floor RCP - Keyplan 4	D	12/28/23	
A154	Second Floor RCP - Keyplan 5	D	12/28/23	
A155	Second Floor RCP - Keyplan 7	D	12/28/23	
A156	Second Floor RCP - Keyplan 8	D	12/28/23	
A157	Second Floor RCP - Keyplan 9	D	12/28/23	
A158	Second Floor RCP - Keyplan 10	D	12/28/23	
A161	Enlarged RCP - Auditorium & MP Rooms	D	12/28/23	
A162	Enlarged RCP - Media Center	D	12/28/23	
A163	Enlarged RCP - Cafeteria	D	12/28/23	
A164	Enlarged RCP - Cafeteria	D	12/28/23	
A165	Enlarged RCP - Miscellaneous	D	12/28/23	
A191	Roof Plan - Overall	D	12/28/23	
A192	Roof Plan - Areas 1 & 2	D	12/28/23	
A193	Roof Plan - Areas 3 & 6	D	12/28/23	
A194	Roof Plan - Areas 6, 8, & 11	D	12/28/23	
A195	Roof Plan - Areas 4, 5, 7, 8, 9, 10	D	12/28/23	
A201	Exterior Building Elevations	D	12/28/23	
A202	Exterior Building Elevations	D	12/28/23	
A203	Exterior Building Elevations	D	12/28/23	
A204	Exterior Building Elevations	D	12/28/23	
A205	Exterior Building Elevations	D	12/28/23	
A206	Exterior Building Elevations	D	12/28/23	
A207	Exterior Building Elevations	D	12/28/23	
A208	Exterior Building Elevations - Alternate #3	D	12/28/23	
A301	Building Sections	D	12/28/23	
A302	Building Sections	D	12/28/23	
A303	Building Sections	D	12/28/23	
A304	Building Sections	D	12/28/23	
A305	Building Sections	D	12/28/23	
A306	Building Sections	D	12/28/23	
A307	Building Sections	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
A308	Building Sections	D	12/28/23	
A311	Wall Sections – Area 1	D	12/28/23	
A312	Wall Sections – Area 1	D	12/28/23	
A313	Wall Sections – Area 1	D	12/28/23	
A314	Wall Sections – Area 2	D	12/28/23	
A315	Wall Sections – Area 2	D	12/28/23	
A316	Wall Sections – Area 2 (Fire Walls)	D	12/28/23	
A317	Wall Sections – Area 2	D	12/28/23	
A318	Wall Sections – Area 3	D	12/28/23	
A319	Wall Sections – Area 3 & 4	D	12/28/23	
A320	Wall Sections– Area 4	D	12/28/23	
A321	Wall Sections – Area 4	D	12/28/23	
A322	Wall Sections – Area 4	D	12/28/23	
A323	Wall Sections – Area 4	D	12/28/23	
A324	Wall Sections – Area 5	D	12/28/23	
A325	Wall Sections – Area 6	D	12/28/23	
A326	Wall Sections – Area 6	D	12/28/23	
A327	Wall Sections – Area 7	D	12/28/23	
A328	Wall Sections – Area 7 & 8	D	12/28/23	
A329	Wall Sections – Area 8	D	12/28/23	
A330	Wall Sections – Area 8 & 9	D	12/28/23	
A331	Wall Sections – Area 9	D	12/28/23	
A332	Wall Sections – Area 9	D	12/28/23	
A333	Wall Sections – Area 9	D	12/28/23	
A334	Wall Sections – Area 10	D	12/28/23	
A335	Wall Sections – Area 11	D	12/28/23	
A401	Enlarged Plans -Toilet Rooms	D	12/28/23	
A402	Enlarged Plans - Toilet Rooms	D	12/28/23	
A403	Restroom Elevations	D	12/28/23	
A404	Restroom Elevations and Locker Types	D	12/28/23	
A405	Enlarged Plan Auditorium	D	12/28/23	
A406	Gymnasium Detailed Plans	D	12/28/23	
A407	Enlarged Plan – Kitchen & Servery	D	12/28/23	
A420	Enlarged Plan - PTMA	D	12/28/23	
A421	Enlarged Plan - Nurse Tech	D	12/28/23	
A422	Enlarged Plan - Technical Drafting	D	12/28/23	
A423	Enlarged Plan - CNAP & Drivers Ed	D	12/28/23	
A424	Enlarged Plan - Electrical Shop	D	12/28/23	
A425	Enlarged Plan - Masonry Shop	D	12/28/23	
A426	Enlarged Plan - Plumbing Shop	D	12/28/23	
A427	Enlarged Plan - Carpentry Shop	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
A428	Enlarged Plan - Cosmetology	D	12/28/23	
A429	Enlarged Plan - Dental Assisting	D	12/28/23	
A430	Enlarged Plan - Industrial Millwright	D	12/28/23	
A431	Enlarged Plan - Auto Body	D	12/28/23	
A432	Enlarged Plan - Auto Tech	D	12/28/23	
A433	Enlarged Plans - Typical Classrooms	D	12/28/23	
A434	Enlarged Plans - Science Classrooms	D	12/28/23	
A435	Enlarged Plans - Administration & Guidance Suites	D	12/28/23	
A436	Enlarged Plans - Administration & Guidance Suites	D	12/28/23	
A437	Enlarged Plans - Nurse & Special Education Suites	D	12/28/23	
A438	Enlarged Plans - Media Center	D	12/28/23	
A439	Enlarged Plans – Teaching Academy	D	12/28/23	
A441	Int. Elevations - Auditorium	D	12/28/23	
A442	Int. Elevations – Auditorium & Details	D	12/28/23	
A443	Int. Elevations - Multi-Purpose Rooms	D	12/28/23	
A444	Int. Elevations Cafeteria	D	12/28/23	
A445	Int. Elevations - Cafeteria	D	12/28/23	
A446	Int. Elevations - Gym	D	12/28/23	
A447	Int. Elevations - Gym	D	12/28/23	
A448	Int. Elevations- Elevator and Shop Lobbies	D	12/28/23	
A449	Int. Elevations - Lobby E101 and Misc	D	12/28/23	
A450	Int. Elevations – Wrestling Room	D	12/28/23	
A451	Casework Elevations	D	12/28/23	
A452	Casework Elevations	D	12/28/23	
A453	Casework Elevations	D	12/28/23	
A454	Casework Elevations	D	12/28/23	
A456	Casework Elevations – Science Rooms	D	12/28/23	
A461	Casework Sections & Details	D	12/28/23	
A470	Millwork Details	D	12/28/23	
A500	Custom Masonry Shapes	D	12/28/23	
A501A	Exterior Plan Details - First Floor	D	12/28/23	
A502A	Exterior Plan Details - First Floor	D	12/28/23	
A503A	Exterior Plan Details - First Floor	D	12/28/23	
A504	Exterior Plan Details – Upper Gymnasium	D	12/28/23	
A504A	Exterior Plan Details - First Floor	D	12/28/23	
A505A	Exterior Plan Details - First Floor	D	12/28/23	
A505B	Exterior Plan Details – Upper Gymnasium	D	12/28/23	
A510A	Exterior Plan Details - First Floor	D	12/28/23	
A510B	Exterior Plan Details – Second Floor	D	12/28/23	
A511	Plan Details - Interior	D	12/28/23	
A512	Plan Details - Interior	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
A512A	Plan Details – Interior	D	12/28/23	
A513A	Exterior Plan Details - First Floor	D	12/28/23	
A513B	Exterior Plan Details – Second Floor	D	12/28/23	
A514A	Exterior Plan Details - First Floor	D	12/28/23	
A514B	Exterior Plan Details – Second Floor	D	12/28/23	
A515A	Exterior Plan Details - First Floor	D	12/28/23	
A515B	Exterior Plan Details – Second Floor	D	12/28/23	
A516A	Exterior Plan Details - First Floor	D	12/28/23	
A516B	Exterior Plan Details – Second Floor	D	12/28/23	
A517A	Exterior Plan Details - First Floor	D	12/28/23	
A517B	Exterior Plan Details – Second Floor	D	12/28/23	
A518A	Exterior Plan Details - First Floor	D	12/28/23	
A518B	Exterior Plan Details – Second Floor	D	12/28/23	
A519A	Exterior Plan Details - First Floor	D	12/28/23	
A519B	Exterior Plan Details – Second Floor	D	12/28/23	
A520A	Exterior Plan Details - First Floor	D	12/28/23	
A520B	Exterior Plan Details – Second Floor	D	12/28/23	
A521	Ceiling Details	D	12/28/23	
A522	Ceiling Section Details	D	12/28/23	
A523	Ceiling Section Details	D	12/28/23	
A531	Railing Details	D	12/28/23	
A532	Railing Details	D	12/28/23	
A541	Door Details - Interiors	D	12/28/23	
A542	Door Details - Interior	D	12/28/23	
A551	Section Details	D	12/28/23	
A560	Architectural Site Details	D	12/28/23	
A561	Architectural Site Details	D	12/28/23	
A562	Architectural Site Details	D	12/28/23	
A563	Architectural Site Details	D	12/28/23	
A564	Architectural Site Details	D	12/28/23	
A565	Architectural Site Details	D	12/28/23	
A590	Roofing Details	D	12/28/23	
A591	Roofing Details	D	12/28/23	
A601	Door Schedule	D	12/28/23	
A602	Door Schedule	D	12/28/23	
A603	Door Schedule - Exterior	D	12/28/23	
A604	Door and Frame Types	D	12/28/23	
A610	Exterior Storefront Types	D	12/28/23	
A611	Exterior Storefront Details	D	12/28/23	
A612	Exterior Storefront Details	D	12/28/23	
A613	Exterior Storefront Details	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
A614	Interior Storefront Types	D	12/28/23	
A621	Curtain Wall Types	D	12/28/23	
A631	Translucent Wall Panel Types & Louver Types	D	12/28/23	
A632	Translucent Wall Panel Types	D	12/28/23	
A633	Translucent Wall Panel Types	D	12/28/23	
A634	Translucent Wall Panel Types	D	12/28/23	
A641	Glazing Details - Interior	D	12/28/23	
A651	Exterior MCM Panel Schedule	D	12/28/23	
A701	Stair #1 & 8 - Plans and Sections	D	12/28/23	
A702	Stair #2 & 3 & 6 - Plans and Sections	D	12/28/23	
A703	Stair #4 & 7 - Plans and Sections	D	12/28/23	
A704	Monumental Stair in Lobby A102– Plans and Sections	D	12/28/23	
A705	Monumental Stair #5 – Plans and Sections (Add Alternate #7-BP-D)	D	12/28/23	
A706	Misc. Stairs, Ramps, and Details	D	12/28/23	
A707	Elevator #1 – Plans and Sections	D	12/28/23	
Interiors				
I-001	Finish Legend	D	12/28/23	
I-002	Overall First Floor Plan – Flooring Alternate	D	12/28/23	
I-111	First Floor Finish Plan - Keyplan 1	D	12/28/23	
I-112	First Floor Finish Plan - Keyplan 2	D	12/28/23	
I-113	First Floor Finish Plan - Keyplan 3	D	12/28/23	
I-114	First Floor Finish Plan - Keyplan 4	D	12/28/23	
I-115	First Floor Finish Plan - Keyplan 5	D	12/28/23	
I-116	First Floor Finish Plan - Keyplan 6	D	12/28/23	
I-116A	First Floor Finish Plan – Keyplan 6 – Alternate #3	D	12/28/23	
I-117	First Floor Finish Plan - Keyplan 7	D	12/28/23	
I-118	First Floor Finish Plan - Keyplan 8	D	12/28/23	
I-119	First Floor Finish Plan - Keyplan 9	D	12/28/23	
I-120	First Floor Finish Plan - Keyplan 10	D	12/28/23	
I-121	First Floor Finish Plan - Keyplan 11	D	12/28/23	
I-131	Second Floor Finish Plan – Keyplan 4	D	12/28/23	
I-132	Second Floor Finish Plan - Keyplan 5	D	12/28/23	
I-133	Second Floor Finish Plan - Keyplan 7	D	12/28/23	
I-134	Second Floor Finish Plan - Keyplan 8	D	12/28/23	
I-135	Second Floor Finish Plan - Keyplan 9	D	12/28/23	
I-136	Second Floor Finish Plan - Keyplan 10	D	12/28/23	
I-211	First Floor Furniture Plan - Keyplan 1	D	12/28/23	
I-212	First Floor Furniture Plan - Keyplan 2	D	12/28/23	
I-213	First Floor Furniture Plan - Keyplan 3	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
I-214	First Floor Furniture Plan - Keyplan4	D	12/28/23	
I-215	First Floor Furniture Plan - Keyplan 5	D	12/28/23	
I-216	First Floor Furniture Plan - Keyplan 6	D	12/28/23	
I-217	First Floor Furniture Plan - Keyplan 7	D	12/28/23	
I-218	First Floor Furniture Plan - Keyplan 8	D	12/28/23	
I-219	First Floor Furniture Plan - Keyplan 9	D	12/28/23	
I-220	First Floor Furniture Plan - Keyplan 10	D	12/28/23	
I-221	First Floor Furniture Plan - Keyplan 11	D	12/28/23	
I-231	Second Floor Furniture Plan - Keyplan 4	D	12/28/23	
I-232	Second Floor Furniture Plan - Keyplan 5	D	12/28/23	
I-233	Second Floor Furniture Plan - Keyplan 7	D	12/28/23	
I-234	Second Floor Furniture Plan - Keyplan 8	D	12/28/23	
I-235	Second Floor Furniture Plan - Keyplan 9	D	12/28/23	
I-236	Second Floor Furniture Plan - Keyplan 10	D	12/28/23	
Mechanical				
G001	Cover Sheet – Volume 3	D	12/28/23	
G002	Drawing List	D	12/28/23	
M001	Legend And Abbreviations - HVAC	D	12/28/23	
M111	First Floor – Keyplan 1 – HVAC	D	12/28/23	
M112	First Floor – Keyplan 2 – HVAC	D	12/28/23	
M113	First Floor – Keyplan 3 – HVAC	D	12/28/23	
M114	First Floor – Keyplan 4 – HVAC	D	12/28/23	
M115	First Floor – Keyplan 5 – HVAC	D	12/28/23	
M116	First Floor – Keyplan 6 – HVAC	D	12/28/23	
M117	First Floor – Keyplan 7 – HVAC	D	12/28/23	
M118	First Floor – Keyplan 8 – HVAC	D	12/28/23	
M119	First Floor – Keyplan 9 – HVAC	D	12/28/23	
M120	First Floor – Keyplan 10 – HVAC	D	12/28/23	
M121	First Floor – Keyplan 11 – HVAC	D	12/28/23	
M131	Second Floor – Keyplan 1 – HVAC	D	12/28/23	
M132	Second Floor – Keyplan 2 – HVAC	D	12/28/23	
M133	Second Floor – Keyplan 3 – HVAC	D	12/28/23	
M134	Second Floor – Keyplan 4 – HVAC	D	12/28/23	
M135	Second Floor – Keyplan 5 – HVAC	D	12/28/23	
M136	Second Floor – Keyplan 6 – HVAC	D	12/28/23	
M137	Second Floor – Keyplan 7 – HVAC	D	12/28/23	
M138	Second Floor – Keyplan 8 – HVAC	D	12/28/23	
M139	Second Floor – Keyplan 9 – HVAC	D	12/28/23	
M140	Second Floor – Keyplan 10 – HVAC	D	12/28/23	
M141	Second Floor – Keyplan 11 – HVAC	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
MP111	First Floor – Keyplan 1 – Mechanical Piping	D	12/28/23	
MP112	First Floor – Keyplan 2 – Mechanical Piping	D	12/28/23	
MP113	First Floor – Keyplan 3 – Mechanical Piping	D	12/28/23	
MP114	First Floor – Keyplan 4 – Mechanical Piping	D	12/28/23	
MP115	First Floor – Keyplan 5 – Mechanical Piping	D	12/28/23	
MP116	First Floor – Keyplan 6 – Mechanical Piping	D	12/28/23	
MP116A	First Floor – Keyplan 6 – Alternate - Mechanical Piping	D	12/28/23	
MP117	First Floor – Keyplan 7 – Mechanical Piping	D	12/28/23	
MP118	First Floor – Keyplan 8 – Mechanical Piping	D	12/28/23	
MP119	First Floor – Keyplan 9 – Mechanical Piping	D	12/28/23	
MP120	First Floor – Keyplan 10 – Mechanical Piping	D	12/28/23	
MP121	First Floor – Keyplan 11 – Mechanical Piping	D	12/28/23	
MP131	Second Floor – Keyplan 1 – Mechanical Piping	D	12/28/23	
MP132	Second Floor – Keyplan 2 – Mechanical Piping	D	12/28/23	
MP133	Second Floor – Keyplan 3 – Mechanical Piping	D	12/28/23	
MP134	Second Floor – Keyplan 4 – Mechanical Piping	D	12/28/23	
MP135	Second Floor – Keyplan 5 – Mechanical Piping	D	12/28/23	
MP136	Second Floor – Keyplan 6 – Mechanical Piping	D	12/28/23	
MP137	Second Floor – Keyplan 7 – Mechanical Piping	D	12/28/23	
MP138	Second Floor – Keyplan 8 – Mechanical Piping	D	12/28/23	
MP139	Second Floor – Keyplan 9 – Mechanical Piping	D	12/28/23	
MP140	Second Floor – Keyplan 10 – Mechanical Piping	D	12/28/23	
MP141	Second Floor – Keyplan 11 – Mechanical Piping	D	12/28/23	
M151	Roof – Areas 1 – HVAC	D	12/28/23	
M152	Roof – Areas 2 – HVAC	D	12/28/23	
M153	Roof – Areas 3 – HVAC	D	12/28/23	
M154	Roof – Areas 4 – HVAC	D	12/28/23	
M201	Part Plans – HVAC	D	12/28/23	
M202	Part Plans – HVAC	D	12/28/23	
M203	Part Plans – HVAC	D	12/28/23	
M204	Part Plans – HVAC	D	12/28/23	
M205	Part Plans – HVAC	D	12/28/23	
M301	Details - HVAC	D	12/28/23	
M302	Details - HVAC	D	12/28/23	
M303	Details - HVAC	D	12/28/23	
M304	Details - HVAC	D	12/28/23	
M305	Details - HVAC	D	12/28/23	
M306	Details - HVAC	D	12/28/23	
M307	Details - HVAC	D	12/28/23	
M308	Details - HVAC	D	12/28/23	
M309	Details - HVAC	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
M310	Details - HVAC	D	12/28/23	
M311	Details - HVAC	D	12/28/23	
M312	Details - HVAC	D	12/28/23	
M313	Details - HVAC	D	12/28/23	
M314	Details - HVAC	D	12/28/23	
M315	Details - HVAC	D	12/28/23	
M316	Details - HVAC	D	12/28/23	
M319	Details – HVAC	D	12/28/23	
M401	Automatic Temperature Controls	D	12/28/23	
M402	Automatic Temperature Controls	D	12/28/23	
M403	Automatic Temperature Controls	D	12/28/23	
M404	Automatic Temperature Controls	D	12/28/23	
M405	Automatic Temperature Controls	D	12/28/23	
M406	Automatic Temperature Controls	D	12/28/23	
M407	Automatic Temperature Controls	D	12/28/23	
M408	Automatic Temperature Controls	D	12/28/23	
M409	Automatic Temperature Controls	D	12/28/23	
M410	Automatic Temperature Controls	D	12/28/23	
M411	Automatic Temperature Controls	D	12/28/23	
M412	Automatic Temperature Controls	D	12/28/23	
M413	Automatic Temperature Controls	D	12/28/23	
M414	Automatic Temperature Controls	D	12/28/23	
M415	Automatic Temperature Controls	D	12/28/23	
M416	Automatic Temperature Controls	D	12/28/23	
M417	Automatic Temperature Controls	D	12/28/23	
M418	Automatic Temperature Controls	D	12/28/23	
M419	Automatic Temperature Controls	D	12/28/23	
M420	Automatic Temperature Controls	D	12/28/23	
M501	Schedules - HVAC	D	12/28/23	
M502	Schedules - HVAC	D	12/28/23	
M503	Schedules - HVAC	D	12/28/23	
M504	Schedules - HVAC	D	12/28/23	
M505	Schedules - HVAC	D	12/28/23	
M506	Schedules - HVAC	D	12/28/23	
M507	Schedules - HVAC	D	12/28/23	
M508	Schedules - HVAC	D	12/28/23	
M509	Schedules - HVAC	D	12/28/23	
M510	Schedules - HVAC	D	12/28/23	
M601	Site Plan – HVAC	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
Fire Protection				
F101	Fire Protection Zoning Plan – First Floor	D	12/28/23	
F102	Fire Protection Zoning Plan – Second Floor	D	12/28/23	
F111	First Floor - Keyplan 1 - Fire Protection	D	12/28/23	
F112	First Floor - Keyplan 2 - Fire Protection	D	12/28/23	
F113	First Floor - Keyplan 3 - Fire Protection	D	12/28/23	
F114	First Floor - Keyplan 4 - Fire Protection	D	12/28/23	
F115	First Floor - Keyplan 5 - Fire Protection	D	12/28/23	
F116	First Floor - Keyplan 6 - Fire Protection	D	12/28/23	
F117	First Floor - Keyplan 7 - Fire Protection	D	12/28/23	
F118	First Floor - Keyplan 8 - Fire Protection	D	12/28/23	
F119	First Floor - Keyplan 9 - Fire Protection	D	12/28/23	
F120	First Floor - Keyplan 10 - Fire Protection	D	12/28/23	
F121	First Floor - Keyplan 11 - Fire Protection	D	12/28/23	
F131	Second Floor Plan - Keyplan 1 - Fire Protection	D	12/28/23	
F132	Second Floor Plan - Keyplan 2 – Fire Protection	D	12/28/23	
F133	Second Floor Plan - Keyplan 3 - Fire Protection	D	12/28/23	
F134	Second Floor Plan - Keyplan 4 - Fire Protection	D	12/28/23	
F135	Second Floor Plan - Keyplan 5 - Fire Protection	D	12/28/23	
F136	Second Floor Plan - Keyplan 6 - Fire Protection	D	12/28/23	
F137	Second Floor Plan - Keyplan 7 - Fire Protection	D	12/28/23	
F138	Second Floor Plan - Keyplan 8 - Fire Protection	D	12/28/23	
F139	Second Floor Plan - Keyplan 9 - Fire Protection	D	12/28/23	
F140	Second Floor Plan - Keyplan 10 - Fire Protection	D	12/28/23	
F141	Second Floor Plan - Keyplan 11 - Fire Protection	D	12/28/23	
F301	Details – Fire Protection	D	12/28/23	
F302	Details & Schedules - Fire Protection	D	12/28/23	
Plumbing				
P001	Legend & Abbreviations – Plumbing	D	12/28/23	
P111	First Floor – Keyplan 1 – Plumbing	D	12/28/23	
P112	First Floor – Keyplan 2 – Plumbing	D	12/28/23	
P113	First Floor – Keyplan 3 – Plumbing	D	12/28/23	
P114	First Floor – Keyplan 4 – Plumbing	D	12/28/23	
P115	First Floor – Keyplan 5 – Plumbing	D	12/28/23	
P116	First Floor – Keyplan 6 – Plumbing	D	12/28/23	
P116A	First Floor – Keyplan 6 – Plumbing – Alternate - Plumbing	D	12/28/23	
P117	First Floor – Keyplan 7 – Plumbing	D	12/28/23	
P118	First Floor – Keyplan 8 – Plumbing	D	12/28/23	
P119	First Floor – Keyplan 9 – Plumbing	D	12/28/23	
P120	First Floor – Keyplan 10 – Plumbing	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
P121	First Floor – Keyplan 11 – Plumbing	D	12/28/23	
P131	Second Floor – Keyplan 1 – Plumbing	D	12/28/23	
P132	Second Floor – Keyplan 2 – Plumbing	D	12/28/23	
P133	Second Floor – Keyplan 3 – Plumbing	D	12/28/23	
P134	Second Floor – Keyplan 4 – Plumbing	D	12/28/23	
P135	Second Floor – Keyplan 5 – Plumbing	D	12/28/23	
P136	Second Floor – Keyplan 6 – Plumbing	D	12/28/23	
P137	Second Floor – Keyplan 7 – Plumbing	D	12/28/23	
P138	Second Floor – Keyplan 8 – Plumbing	D	12/28/23	
P139	Second Floor – Keyplan 9 – Plumbing	D	12/28/23	
P140	Second Floor – Keyplan 10 – Plumbing	D	12/28/23	
P141	Second Floor – Keyplan 11 – Plumbing	D	12/28/23	
P151	Roof - Areas 1 & 2 - Plumbing	D	12/28/23	
P152	Roof - Areas 3 & 6 - Plumbing	D	12/28/23	
P153	Roof - Areas 6, 8 & 11 - Plumbing	D	12/28/23	
P154	Roof - Areas 4, 5, 7, 8, 9 & 10 - Plumbing	D	12/28/23	
P201	Part Plans - Plumbing	D	12/28/23	
P202	Part Plans – Plumbing	D	12/28/23	
P203	Part Plans - Plumbing	D	12/28/23	
P204	Part Plan - Plumbing	D	12/28/23	
P205	Part Plans - Plumbing	D	12/28/23	
P206	Part Plans - Plumbing	D	12/28/23	
P207	Part Plans - Plumbing	D	12/28/23	
P301	Details – Plumbing	D	12/28/23	
P302	Details – Plumbing	D	12/28/23	
P303	Details – Plumbing	D	12/28/23	
P304	Details – Plumbing	D	12/28/23	
P305	Details – Plumbing	D	12/28/23	
P306	Details – Plumbing	D	12/28/23	
P307	Details – Plumbing	D	12/28/23	
P308	Details – Plumbing	D	12/28/23	
P309	Details – Plumbing	D	12/28/23	
P310	Details – Plumbing	D	12/28/23	
P311	Details – Plumbing	D	12/28/23	
P312	Details – Plumbing	D	12/28/23	
P313	Details – Plumbing	D	12/28/23	
P314	Details – Plumbing	D	12/28/23	
P315	Details – Plumbing	D	12/28/23	
P316	Details - Plumbing	D	12/28/23	
P317	Details - Plumbing	D	12/28/23	
P401	Schedules – Plumbing	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
P402	Schedules - Plumbing	D	12/28/23	
P501	Risers – Plumbing	D	12/28/23	
P502	Risers – Plumbing	D	12/28/23	
P503	Risers – Plumbing	D	12/28/23	
P504	Risers – Plumbing	D	12/28/23	
P505	Risers – Plumbing	D	12/28/23	
P506	Risers – Plumbing	D	12/28/23	
P507	Risers – Plumbing	D	12/28/23	
P508	Risers – Plumbing	D	12/28/23	
P509	Risers – Plumbing	D	12/28/23	
P510	Risers – Plumbing	D	12/28/23	
P511	Risers – Plumbing	D	12/28/23	
P512	Risers – Plumbing	D	12/28/23	
P513	Risers – Plumbing	D	12/28/23	
P514	Risers – Plumbing	D	12/28/23	
P515	Risers – Plumbing	D	12/28/23	
P516	Risers – Plumbing	D	12/28/23	
P517	Risers – Plumbing	D	12/28/23	
P518	Risers – Plumbing	D	12/28/23	
P519	Risers – Plumbing	D	12/28/23	
P520	Risers – Plumbing	D	12/28/23	
P521	Risers – Plumbing	D	12/28/23	
P522	Risers – Plumbing	D	12/28/23	
P523	Risers – Plumbing	D	12/28/23	
P524	Risers – Plumbing	D	12/28/23	
P525	Risers – Plumbing	D	12/28/23	
P526	Risers – Plumbing	D	12/28/23	
P527	Risers – Plumbing	D	12/28/23	
P528	Risers – Plumbing	D	12/28/23	
P529	Risers – Plumbing	D	12/28/23	
P530	Risers – Plumbing	D	12/28/23	
P531	Risers – Plumbing	D	12/28/23	
P532	Risers – Plumbing	D	12/28/23	
P533	Risers – Plumbing	D	12/28/23	
P534	Risers – Plumbing	D	12/28/23	
P535	Risers – Plumbing	D	12/28/23	
P536	Risers – Plumbing	D	12/28/23	
P537	Risers – Plumbing	D	12/28/23	
Electrical				
G001	Cover Sheet – Volume 4	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
G002	Drawing List	D	12/28/23	
E001	Electrical Legend, Schedules & Abbreviations	D	12/28/23	
E002	Lighting Fixture Schedule	D	12/28/23	
E003	Lighting Fixture Schedule	D	12/28/23	
E004	Site Plan Electrical	D	12/28/23	
E005	Site Plan Electrical	D	12/28/23	
E006	Site Plan Electrical	D	12/28/23	
E101	First Floor - Keyplan 1 - Power	D	12/28/23	
E102	First Floor - Keyplan 2 - Power	D	12/28/23	
E103	First Floor - Keyplan 3 - Power	D	12/28/23	
E104	First Floor - Keyplan 4 - Power	D	12/28/23	
E105	First Floor - Keyplan 5 - Power	D	12/28/23	
E106	First Floor - Keyplan 6 - Power	D	12/28/23	
E106A	First Floor - Keyplan 6A – Alternate #3 - Power	D	12/28/23	
E107	First Floor - Keyplan 7 - Power	D	12/28/23	
E108	First Floor - Keyplan 8 - Power	D	12/28/23	
E109	First Floor - Keyplan 9 - Power	D	12/28/23	
E110	First Floor - Keyplan 10 - Power	D	12/28/23	
E111	First Floor - Keyplan 11 - Power	D	12/28/23	
E121	Second Floor - Keyplan 4 - Power	D	12/28/23	
E122	Second Floor - Keyplan 5 - Power	D	12/28/23	
E123	Second Floor - Keyplan 6 - Power	D	12/28/23	
E124	Second Floor - Keyplan 7 - Power	D	12/28/23	
E125	Second Floor - Keyplan 8 - Power	D	12/28/23	
E126	Second Floor - Keyplan 9 - Power	D	12/28/23	
E127	Second Floor - Keyplan 10 - Power	D	12/28/23	
E128	Second Floor - Keyplan 11 - Power	D	12/28/23	
E129	Roof Plan - Overall - Power	D	12/28/23	
E201	First Floor - Keyplan 1 - Lighting	D	12/28/23	
E202	First Floor - Keyplan 2 - Lighting	D	12/28/23	
E203	First Floor - Keyplan 3 - Lighting	D	12/28/23	
E204	First Floor - Keyplan 4 - Lighting	D	12/28/23	
E205	First Floor - Keyplan 5 - Lighting	D	12/28/23	
E206	First Floor - Keyplan 6 - Lighting	D	12/28/23	
E206A	First Floor – Keyplan 6A – Alternate #3 Lighting	D	12/28/23	
E207	First Floor - Keyplan 7 - Lighting	D	12/28/23	
E208	First Floor - Keyplan 8 - Lighting	D	12/28/23	
E209	First Floor - Keyplan 9 - Lighting	D	12/28/23	
E210	First Floor - Keyplan 10 - Lighting	D	12/28/23	
E211	First Floor - Keyplan 11 - Lighting	D	12/28/23	
E221	Second Floor - Keyplan 4 - Lighting	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
E222	Second Floor - Keyplan 5 - Lighting	D	12/28/23	
E223	Second Floor - Keyplan 6 - Lighting	D	12/28/23	
E224	Second Floor - Keyplan 7 - Lighting	D	12/28/23	
E225	Second Floor - Keyplan 8 - Lighting	D	12/28/23	
E226	Second Floor - Keyplan 9 - Lighting	D	12/28/23	
E227	Second Floor - Keyplan 10 - Lighting	D	12/28/23	
E228	Second Floor - Keyplan 11 - Lighting	D	12/28/23	
E301	First Floor - Keyplan 1 - Fire Alarm	D	12/28/23	
E302	First Floor - Keyplan 2 - Fire Alarm	D	12/28/23	
E303	First Floor - Keyplan 3 - Fire Alarm	D	12/28/23	
E304	First Floor - Keyplan 4 - Fire Alarm	D	12/28/23	
E305	First Floor - Keyplan 5 - Fire Alarm	D	12/28/23	
E306	First Floor - Keyplan 6 - Fire Alarm	D	12/28/23	
E306A	Firs Floor – Keyplan 6A – Alternate #3 – Fire Alarm	D	12/28/23	
E307	First Floor - Keyplan 7 - Fire Alarm	D	12/28/23	
E308	First Floor - Keyplan 8 - Fire Alarm	D	12/28/23	
E309	First Floor - Keyplan 9 - Fire Alarm	D	12/28/23	
E310	First Floor - Keyplan 10 - Fire Alarm	D	12/28/23	
E311	First Floor - Keyplan 11 - Fire Alarm	D	12/28/23	
E321	Second Floor - Keyplan 4 - Fire Alarm	D	12/28/23	
E322	Second Floor - Keyplan 5 - Fire Alarm	D	12/28/23	
E323	Second Floor - Keyplan 6 - Fire Alarm	D	12/28/23	
E324	Second Floor - Keyplan 7 - Fire Alarm	D	12/28/23	
E325	Second Floor - Keyplan 8 - Fire Alarm	D	12/28/23	
E326	Second Floor - Keyplan 9 - Fire Alarm	D	12/28/23	
E327	Second Floor - Keyplan 10 - Fire Alarm	D	12/28/23	
E328	Second Floor - Keyplan 11 - Fire Alarm	D	12/28/23	
E401	Part Plan - Main Electrical/Mechanical Room	D	12/28/23	
E402	Electrical Part Plans	D	12/28/23	
E403	Electrical Part Plans	D	12/28/23	
E404	Part Plan - Kitchen E105	D	12/28/23	
E405	Part Plan - Culinary Lab D101	D	12/28/23	
E406	Part Plan - Electrical Shop D110	D	12/28/23	
E407	Part Plan - Masonry Shop - D114	D	12/28/23	
E408	Part Plan - Plumbing Shop D116	D	12/28/23	
E409	Part Plan - Carpentry Shop C101	D	12/28/23	
E410	Part Plan - Cosmetology Lab C102B & C102K	D	12/28/23	
E411	Part Plan - Industrial Millwright C118	D	12/28/23	
E412	Part Plan - Autobody Shop C120	D	12/28/23	
E413	Part Plan - Auto Tech Shop C124	D	12/28/23	
E414	Part Plans - Mezzanine	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
E415	Part Plans - Mezzanine	D	12/28/23	
E416	Part Plans - Mezzanine	D	12/28/23	
E417	Part Plan – Auditorium Theater Equipment Rough-Ins	D	12/28/23	
E418	Part Plan – Auditorium Theater Equipment Lighting Rough-Ins	D	12/28/23	
E419	Part Plan – Auditorium Theater Elevations	D	12/28/23	
E501	Schematic Power Riser Diagram	D	12/28/23	
E502	Schematic Power Riser Diagram	D	12/28/23	
E503	Schematic Power Riser Diagram	D	12/28/23	
E504	Schematic Power Riser Diagram	D	12/28/23	
E505	Schematic Power Riser Diagram	D	12/28/23	
E506	Schematic Fire Alarm Riser Diagram	D	12/28/23	
E507	Fire Alarm Static Graphic Annunciator	D	12/28/23	
E601	Panel Schedules	D	12/28/23	
E602	Panel Schedules	D	12/28/23	
E603	Panel Schedules	D	12/28/23	
E604	Panel Schedules	D	12/28/23	
E605	Panel Schedules	D	12/28/23	
E606	Panel Schedules	D	12/28/23	
E607	Panel Schedules	D	12/28/23	
E608	Panel Schedules	D	12/28/23	
E609	Panel Schedules	D	12/28/23	
E610	Panel Schedules	D	12/28/23	
E611	Panel Schedules	D	12/28/23	
E612	Panel Schedules	D	12/28/23	
E613	Panel Schedules	D	12/28/23	
E614	Panel Schedules	D	12/28/23	
E615	Panel Schedules	D	12/28/23	
E616	Panel Schedules	D	12/28/23	
E617	Panel Schedules	D	12/28/23	
E618	Panel Schedules	D	12/28/23	
E619	Panel Schedules	D	12/28/23	
E620	Mechanical Equipment Connection Schedule	D	12/28/23	
E621	Mechanical Equipment Connection Schedule	D	12/28/23	
E622	Mechanical Equipment Connection Schedule	D	12/28/23	
E623	Mechanical Equipment Connection Schedule	D	12/28/23	
E624	Mechanical Equipment Connection Schedule	D	12/28/23	
E625	Mechanical Equipment Connection Schedule	D	12/28/23	
E626	Kitchen Equipment Connection Schedule	D	12/28/23	
E701	Electrical Details	D	12/28/23	
E702	Electrical Details	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
E703	Electrical Details	D	12/28/23	
E704	Electrical Details	D	12/28/23	
E705	Electrical Details	D	12/28/23	
E706	Electrical Details	D	12/28/23	
E707	Electrical Details	D	12/28/23	
E708	Electrical Details	D	12/28/23	
E709	Electrical Details	D	12/28/23	
E710	Electrical Details	D	12/28/23	
E711	Electrical Details	D	12/28/23	
E712	Electrical Details	D	12/28/23	
E713	Electrical Details	D	12/28/23	
E714	Electrical Details	D	12/28/23	
E715	Electrical Details	D	12/28/23	
E716	Corridor Lighting Control Zones	D	12/28/23	
E717	Switched Receptacle Control Zones	D	12/28/23	
Theater				
G001	Cover Sheet – Volume 5	D	12/28/23	
G002	Drawing List	D	12/28/23	
AV-001	AV Systems - Schedules	D	12/28/23	
AV-002	AV Systems - Technical Power Concept	D	12/28/23	
AV-101	AV Systems - Level 1 Plan	D	12/28/23	
AV-201	AV Systems - Loudspeaker & Projection Centerline	D	12/28/23	
AV-301	AV Systems - Combo Panel Details	D	12/28/23	
AV-302	AV Systems - SVC Device Details	D	12/28/23	
AV-303	AV Systems - Rack Panel Details	D	12/28/23	
AV-304	AV Systems - Rack Elevations	D	12/28/23	
AV-401	AV Systems – Signal Flows 1	D	12/28/23	
AV-402	AV Systems – Signal Flows 2	D	12/28/23	
TE-110	Performance Lighting Systems	D	12/28/23	
TE-120	Performance Lighting Systems	D	12/28/23	
TE-130	Performance Lighting Systems	D	12/28/23	
TE-140	Performance Lighting Systems	D	12/28/23	
TE-150	Performance Lighting Systems	D	12/28/23	
TE-160	Performance Lighting Systems	D	12/28/23	
TR-101	Keyplan 2 – Stage Rigging Plan	D	12/28/23	
TR-201	Keyplan 2 – Stage Rigging Section	D	12/28/23	
TR-301	Keyplan 2 – Stage Rigging Elevations	D	12/28/23	
TR-302	Keyplan 2 – Stage Rigging Elevations	D	12/28/23	
TR-401	Keyplan 2 – Stage Rigging Details	D	12/28/23	
TR-402	Keyplan 2 - Stage Rigging Details	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
TS-101	Keyplan 2 – Auditorium Seating Plan	D	12/28/23	
TS-102	Keyplan 2 – Auditorium Seating Centerline Section	D	12/28/23	
Kitchen				
FS-1.0	Foodservice Equipment Plan - Overall	D	12/28/23	
FS-1.1	Foodservice Equipment Plan - Cafeteria	D	12/28/23	
FS-1.2	Foodservice Equipment Plan - Food Lab	D	12/28/23	
FS-1.3	Foodservice Equipment Schedule	D	12/28/23	
FS-1.4	Foodservice Electrical Schedule	D	12/28/23	
FS-1.5	Foodservice Plumbing Schedule	D	12/28/23	
FS-1.6	Foodservice Details	D	12/28/23	
FS-1.7	Foodservice Plumbing Plan - Cafeteria	D	12/28/23	
FS-1.8	Foodservice Plumbing Plan - Food Lab	D	12/28/23	
FS-1.9	Foodservice Plumbing Schedule	D	12/28/23	
FS-1.10	Foodservice Details	D	12/28/23	
FS-2.0	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.1	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.2	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.3	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.4	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.5	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.6	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.7	Foodservice Exhaust Hood Details	D	12/28/23	
FS-2.8	Foodservice Utility Distribution System Details	D	12/28/23	
FS-2.9	Foodservice Utility Distribution System Details	D	12/28/23	
FS-2.10	Foodservice Utility Distribution System Details	D	12/28/23	
FS-2.11	Foodservice Utility Distribution System Details	D	12/28/23	
FS-3.0	Foodservice Walk-In Details	D	12/28/23	
FS-3.1	Foodservice Walk-In Details	D	12/28/23	
FS-3.2	Foodservice Walk-In Details	D	12/28/23	
FS-3.3	Foodservice Walk-In Details	D	12/28/23	
FS-4.0	Foodservice Equipment Plan – Support Kitchen	D	12/28/23	
Technology				
T000	Symbols And Notes	D	12/28/23	
T100	Site Plan	D	12/28/23	
T101	Overall First Floor Plan	D	12/28/23	
T102	Overall Second Floor Plan	D	12/28/23	
T103	Floor Plan - Shops - Mezzanine Level	D	12/28/23	
T111	First Floor Plan - Keyplan 1	D	12/28/23	
T112	First Floor Plan - Keyplan 2	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
T113	First Floor Plan - Keyplan 3	D	12/28/23	
T114	First Floor Plan - Keyplan 4	D	12/28/23	
T115	First Floor Plan - Keyplan 5	D	12/28/23	
T116	First Floor Plan - Keyplan 6	D	12/28/23	
T116A	First Floor Plan - Keyplan 6 Alternate	D	12/28/23	
T117	First Floor Plan - Keyplan 7	D	12/28/23	
T118	First Floor Plan - Keyplan 8	D	12/28/23	
T119	First Floor Plan - Keyplan 9	D	12/28/23	
T120	First Floor Plan - Keyplan 10	D	12/28/23	
T121	First Floor Plan - Keyplan 11	D	12/28/23	
T131	Second Floor Plan - Keyplan 4	D	12/28/23	
T132	Second Floor Plan - Keyplan 5	D	12/28/23	
T133	Second Floor Plan - Keyplan 7	D	12/28/23	
T134	Second Floor Plan - Keyplan 8	D	12/28/23	
T135	Second Floor Plan - Keyplan 9	D	12/28/23	
T136	Second Floor Plan - Keyplan 10	D	12/28/23	
T500	Main Telecom Room Details	D	12/28/23	
T501	Telecom Rooms First Floor 1	D	12/28/23	
T502	Telecom Rooms First Floor 2	D	12/28/23	
T503	Telecom Rooms Second Floor 1	D	12/28/23	
T504	Pathways	D	12/28/23	
T505	Faceplates	D	12/28/23	
T507	Intercom & Clock System	D	12/28/23	
T508	Cafeteria Audio System	D	12/28/23	
T509	Gymnasium Audio System	D	12/28/23	
T510	Demo Camera System	D	12/28/23	
Security				
TY000	Security Symbols and Notes	D	12/28/23	
TY100	Site Security Plan	D	12/28/23	
TY101	Overall First Floor Security Plan	D	12/28/23	
TY102	Overall Second Floor Security Plan	D	12/28/23	
TY103	Floor Plan - Shops - Mezzanine Level Security	D	12/28/23	
TY111	First Floor Security Plan - Keyplan 1	D	12/28/23	
TY112	First Floor Security Plan - Keyplan 2	D	12/28/23	
TY113	First Floor Security Plan - Keyplan 3	D	12/28/23	
TY114	First Floor Security Plan - Keyplan 4	D	12/28/23	
TY115	First Floor Security Plan - Keyplan 5	D	12/28/23	
TY116	First Floor Security Plan - Keyplan 6	D	12/28/23	
TY116A	First Floor Security Plan - Keyplan 6 Alternate	D	12/28/23	
TY117	First Floor Security Plan - Keyplan 7	D	12/28/23	

DRWG NO.	DRAWING NAME	BID PACKS	ISSUE DATE	LATEST REV. DATE
TY118	First Floor Security Plan - Keyplan 8	D	12/28/23	
TY119	First Floor Security Plan - Keyplan 9	D	12/28/23	
TY120	First Floor Security Plan - Keyplan 10	D	12/28/23	
TY121	First Floor Security Plan - Keyplan 11	D	12/28/23	
TY131	Second Floor Security Plan - Keyplan 4	D	12/28/23	
TY132	Second Floor Security Plan - Keyplan 5	D	12/28/23	
TY133	Second Floor Security Plan - Keyplan 7	D	12/28/23	
TY134	Second Floor Security Plan - Keyplan 8	D	12/28/23	
TY135	Second Floor Security Plan - Keyplan 9	D	12/28/23	
TY136	Second Floor Security Plan - Keyplan 10	D	12/28/23	
TY500	Intrusion Detection System	D	12/28/23	
TY501	Access Control System	D	12/28/23	
TY502	Video Surveillance System	D	12/28/23	

END OF SECTION

SECTION 001116 - INVITATION TO BID

Receipt of Bids

Public notice is hereby given that sealed bids for the following prime contracts will be received for the construction of New Castle County Vocational Technical School District Hodgson Vo-Tech High School Sitework and Utilities located in Wilmington, Delaware. **Bids will be received at the office of New Castle County Vo-Tech School District, 1417 Newport Road, Wilmington, DE 19804 until 3:00 local time on Wednesday January 17, 2024**, at which time they will be publicly opened and read aloud. The outer envelope should clearly indicate: "NEW CASTLE COUNTY VOCATIONAL TECHNICAL SCHOOL DISTRICT - HODGSON VO-TECH HIGH SCHOOL- BUILDING ENVELOPE AND FITOUT BP-D CONTRACT #_____ SEALED BID-DO NOT OPEN." ***Bidder bears the risk of late delivery. Any bids received after the stated time will be returned unopened.***

Contract D-01: Unit Masonry
Contract D-02: Miscellaneous Metals, Stairs, and Rails
Contract D-03: Exterior Structural Stud Assembly
Contract D-04: Carpentry and General Work
Contract D-05: Exterior Metal Panels
Contract D-06: Drywall and Interior Metal Framing
Contract D-07: General Labor and Clean-up
Contract D-08: Roofing
Contract D-09: Fireproofing
Contract D-10: Joint Sealants and Preformed Joint Assemblies
Contract D-11: Hollow Metal, Wood Doors, and Finish Hardware
Contract D-12: Overhead Coiling Doors
Contract D-13: Curtainwall/Glazing/Storefronts
Contract D-14: Tiling
Contract D-15: Acoustical and Specialty Ceilings
Contract D-16: Flooring
Contract D-17: Resilient Athletic Flooring
Contract D-18: Resinous Matrix Terrazzo Flooring
Contract D-19: Fluid Applied Flooring
Contract D-20: Paint and VWC
Contract D-21: Wood Strip Flooring-Gym Flooring
Contract D-22: Specialties
Contract D-23: Food Service Equipment
Contract D-24: Window Shades and Roller Shades
Contract D-25: Laminate Clad Casework, Countertops, and Sills
Contract D-26: Stage Rigging, Lighting, and Accessories
Contract D-27: Fixed Auditorium Seating
Contract D-28: Telescoping Bleachers and Platforms
Contract D-29: Hydraulic Holeless Passenger Elevator
Contract D-30: Fire Protection
Contract D-31: Plumbing
Contract D-32: Mechanical Piping - HVAC
Contract D-33: Testing, Adjusting, and Balancing

Contract D-34: Electrical, Lighting and Fire Alarm Systems
Contract D-35: Special Systems
Contract D-36: Vertical Retracting Walls
Contract D-37: Miscellaneous Concrete and Grouting

This project is a pilot project authorized by SB 160, Section 34, in which seven percent (7%) of the contractors for the project are DBEs. Non-DBE contractors may achieve the seven percent (7%) by hiring DBE firms as subcontractors or having their subcontractors hire DBE firms. All DBE firms must be registered with either the Delaware Department of Transportation or the Delaware Office of Supplier Diversity. The percentage requirement and the registration requirements will remain in place for the length of the project.

The selected project, New Castle County Vocational Technical School District's Hodgson Vo-Tech, includes a cooperative program in which students from Vocational Technical schools will work on the project in compliance with 19 Del. C. ch. 5.

Bids will be evaluated based on a best value process that is described in the Instruction to Bidders.

Bidding Documents

1. It is the responsibility of each bidder to review and coordinate all Project Documents. This includes plans, specifications, and addendums.
2. Documents, for review only, may be examined on or after **December 19, 2023** on the State of Delaware Online Bid Solicitation Directory, http://bids.delaware.gov, or at the office of the Construction Manager, EDIS Company, 110 S. Poplar Street, Suite 400, Wilmington, Delaware 19801;.
3. Bid documents will be available on the EDiS FTP site. In order to obtain access to biddable documents on the EDiS FTP site, bidders must download and complete the Plans Request form from http://bids.delaware.gov, and submit to: planrequests@delaware.gov for approval. Once the plans request is approved and you want to receive the biddable plans submit your request for access to the FTP site via email to Jackie McKee at jmckee@ediscompany.com. Your request should include the following information: your company name, contact name, email address, phone number, fax number, and postal mailing address.

Bid Security

A bid security in the amount of ten percent (10%) of the bid, plus a consent of surety must accompany each bid. Bid Security shall specify the Owner as the obligee. Owner: New Castle County Vo-Tech School District, 1417 Newport Road, Wilmington, DE 19804.

Pre-Bid Meeting

A **NON-mandatory** pre-bid meeting will be held at the **New Castle County Vocational Technical School District Hodgson Vo-Tech, 2575 Glasgow Ave, Newark, DE 19702 on Wednesday, December 27, 2023 at 9:00 AM local time.** A site visit will be conducted immediately following the pre-bid meeting. This site visit will be the only opportunity for the bidders to visit the existing building and review existing conditions affecting the work. Attendance is highly suggested but not mandatory.

Questions

Please contact EDiS Company, Kevin Lucas at klucas@ediscompany.com, and copy Jackie McKee at jmckee@ediscompany.com (302) 420-3083 with questions and RFI submissions. All bid questions must be submitted electronically. All bid questions must be submitted by **Wednesday January 10, 2023.**

Conformance to the Delaware Architectural Accessibility Act and the standards of the Architectural Accessibility Board is required on the Project.

Prevailing Wage Rates

Prevailing Wage Rates, as directed by Delaware Law, must be adhered to where applicable. Davis-Bacon Act wages, in accordance with Subchapter IV of Chapter 31 of Title 40USC, must be adhered to. Contractors must pay the higher of the two rates.

Drug Testing Requirements

Pursuant to the Office of Management and Budget (OMB) "4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects" required that Contractors and Subcontractors who work on Large Public Works Contracts funded all or in part with public funds implement a Mandatory Drug Testing Program. The latest regulation can be downloaded from the following website: http://regulations.delaware.gov/AdminCode/title19/4000/4100/4104.pdf

Craft Training for Public Works Procurement

In accordance with Delaware Code, Title 29, Chapter 69, Section 6962, requires: A public works contract must include a requirement that the contractor provide craft training for journeyman and apprentice levels if all of the following apply:

A. The project requires prevailing wages and,
B. The contractor or subcontractor employs 10 or more people and,
C. It is not a federal highway project.

The craft training may be provided by any of the following:

A. The contractor, or
B. The subcontractor, or
C. A program registered pursuant under Section 1101-4.0 of Title 19 of the Delaware Administrative Code.

Subsection 6902 defines "Craft Training" as "an apprenticeship program approved by and registered with any state apprenticeship agency or the United States Department of Labor. The Secretary of the Department of Labor shall maintain a list of crafts for which there are approved and registered training programs."

Delaware's Contractor Registration Act Is Effective July 1, 2021

https://labor.delaware.gov/divisions/industrial-affairs/labor-law/contractor-registration-act/

Bidders will not be subject to discrimination on the basis of race, creed, color, sex, sexual orientation, gender identity or national origin in consideration of this award, and Minority Business Enterprises,

Disadvantaged Business Enterprises, Women-Owned Business Enterprises and Veteran-Owned Business Enterprises will be afforded full opportunity to submit bids on this contract. Each bid must be accompanied by a bid security equivalent to ten percent of the bid amount and all additive alternates. The successful bidder must post a performance bond and payment bond in a sum equal to 100 percent of the contract price upon execution of the contract. The Owner reserves the right to reject any or all bids and to waive any informalities therein. The Owner may extend the time and place for the opening of the bids from that described in the advertisement, with not less than two calendar days' notice by certified delivery, facsimile machine, or other electronic means to those bidders receiving plans.

END OF SECTION

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

SECTION 00 21 13

INSTRUCTIONS TO BIDDERS

TABLE OF ARTICLES

1. GENERAL

2. BIDDER'S REPRESENTATION

3. BIDDING DOCUMENTS

4. BIDDING PROCEDURES

5. CONSIDERATION OF BIDS

6. POST-BID INFORMATION

7. PERFORMANCE BOND AND PAYMENT BOND

8. FORM OF AGREEMENT BETWEEN OWNER AND CONTRACTOR

ARTICLE 1: GENERAL

1.0 This project is a pilot project authorized by SB 160, Section 34, in which seven (7) percent of the contractors for the project are DBEs. Non-DBE contractors may achieve the 7% by hiring DBE firms as subcontractors or having their subcontractors hire DBE firms. All DBE firms must be registered with either the Delaware Department of Transportation or the Delaware Office of Supplier Diversity. The percentage requirement and the registration requirements will remain in place for the length of the project.

The selected project, New Castle County Vocational Technical School District's Hodgson Vo-Tech, includes a cooperative program in which students from Vocational Technical schools will work on the project in compliance with Title 19, Chapter 5 of the Delaware Code. The wage rate has been established by the Office of Management and Budget (OMB) and the New Castle County Vocational Technical School District and shall appear in the project specifications. So that you are aware, this wage rate shall be recognized by the Delaware Department of Labor as "OMB Pilot Program Coop Student Rate" in lieu of a Prevailing Wage rate on the pilot project. This Student Rate is applicable to this pilot project only.

Bids will be evaluated based on a best value process that is described in Article 5 of these Instructions to Bidders.

Bidders should be aware that OMB is required to provide annual reports by January 1 to the Joint Committee on Capital Improvement that includes OMB's assessment of the pilot, including, but not limited to, employee hiring statistics, cost savings, project quality, worker safety, and the effectiveness of contracting disadvantaged businesses, including but not limited to, subcontractors. To that end, awarded contractors shall be required to provide reports to the Construction Managers for this project. The awarded contractors will be provided a report form to be completed quarterly over of the life of the project that includes: (i) number of DBEs; (ii) total amount paid to each DBE as of the date of reporting; (iii) confirmation that the DBE listed is still registered; and (iv) whether the DBE's work is completed or still in progress at the time of reporting.

1.1 DEFINITIONS

1.1.1 Whenever the following terms are used, their intent and meaning shall be interpreted as follows:

1.2 STATE: The State of Delaware.

1.3 AGENCY: Contracting State Agency as noted on cover sheet.

1.4 DESIGNATED OFFICIAL: The agent authorized to act for the Agency.

1.5 BIDDING DOCUMENTS: Bidding Documents include the Bidding Requirements and the proposed Contract Documents. The Bidding Requirements consist of the Advertisement for Bid, Invitation to Bid, Instructions to Bidders, Supplementary Instructions to Bidders (if any), General Conditions, Supplementary General Conditions, General Requirements, Special Provisions (if any), the Bid Form (including the Non-collusion Statement), and other sample bidding and contract forms. The proposed Contract Documents consist of the form of Agreement between the Owner and Contractor, as well as the Drawings, Specifications (Project Manual) and all Addenda issued prior to execution of the Contract.

1.6 CONTRACT DOCUMENTS: The Contract Documents consist of the Instructions to Bidders, Supplementary Instructions to Bidders (if any), General Conditions, Supplementary General Conditions, General Requirements, Special Provisions (if any), the form of agreement between the Owner and the Contractor, Drawings (if any), Specifications (Project Manual), and all addenda.

1.7 AGREEMENT: The form of the Agreement shall be AIA Document A132, Standard Form of Agreement Between Owner and Contractor, *Construction Manager as Adviser Edition* where the basis of payment is a STIPULATED SUM. In the case of conflict between the instructions contained therein and the General Requirements herein, the General Requirements shall prevail.

1.8 GENERAL REQUIREMENTS (or CONDITIONS): General Requirements (or conditions) are instructions pertaining to the Bidding Documents and to contracts in general. They contain, in summary, requirements of laws of the State, policies of the Agency and instructions to bidders.

1.9 SPECIAL PROVISIONS: Special Provisions are specific conditions or requirements peculiar to the bidding documents and to the contract under consideration and are supplemental to the General Requirements. Should the Special Provisions conflict with the General Requirements, the Special Provisions shall prevail.

1.10 ADDENDA: Written or graphic instruments issued by the Owner/Architect prior to the execution of the contract which modify or interpret the Bidding Documents by additions, deletions, clarifications or corrections.

1.11 BIDDER OR VENDOR: A person or entity who formally submits a Bid for the material or Work contemplated, acting directly or through a duly authorized representative who meets the requirements set forth in the Bidding Documents.

1.12 SUB-BIDDER: A person or entity who submits a Bid to a Bidder for materials or labor, or both for a portion of the Work.

1.13 BID: A complete and properly executed proposal to do the Work for the sums stipulated therein, submitted in accordance with the Bidding Documents.

1.14 BASE BID: The sum stated in the Bid for which the Bidder offers to perform the Work described in the Bidding Documents as the base, to which Work may be added or from which Work may be deleted for sums stated in Alternate Bids (if any are required to be stated in the bid).

1.15 ALTERNATE BID (or ALTERNATE): An amount stated in the Bid, where applicable, to be added to or deducted from the amount of the Base Bid if the corresponding change in the Work, as described in the Bidding Documents is accepted.

1.16 UNIT PRICE: An amount stated in the Bid, where applicable, as a price per unit of measurement for materials, equipment or services or a portion of the Work as described in the Bidding Documents.

1.17 SURETY: The corporate body which is bound with and for the Contract, or which is liable, and which engages to be responsible for the Contractor's payments of all debts pertaining to and for his acceptable performance of the Work for which he has contracted.

1.18 BIDDER'S DEPOSIT: The security designated in the Bid to be furnished by the Bidder as a guaranty of good faith to enter into a contract with the Agency if the Work to be performed or the material or equipment to be furnished is awarded to him.

1.19 CONTRACT: The written agreement covering the furnishing and delivery of material or work to be performed.

1.20 CONTRACTOR: Any individual, firm or corporation with whom a contract is made by the Agency.

1.21 SUBCONTRACTOR: An individual, partnership or corporation which has a direct contract with a contractor to furnish labor and materials at the job site, or to perform construction labor and furnish material in connection with such labor at the job site.

1.22 CONTRACT BOND: The approved form of security furnished by the contractor and his surety as a guaranty of good faith on the part of the contractor to execute the work in accordance with the terms of the contract.

1.23 DISADVANTAGED BUSINESS ENTERPRISE (DBE): A for-profit businesses in which at least 51 percent of the business is owned by one or more individuals who are both socially and economically disadvantaged; and whose daily operations are managed by one or more individuals who are both socially and economically disadvantaged.

1.24 BEST VALUE PROCESS: The bid evaluation process for this project, which will include the price and the percentage of DBEs identified in the bid. In addition, all bids are subject to an evaluation for responsiveness and responsibility.

1.25 CONSTRUCTION MANAGER: EDiS Company, who was hired by the New Castle County Vocational Technical School District for this project.

1.26 CUSTOM FABRICATION: As defined in 29 Del. C. § 6902, the term "custom fabrication" means the offsite fabrication, assembly, or other production of non-standard goods or materials, including components, fixtures or parts thereof, specifically for a public works project. Such goods and materials shall include those used in the following trades or systems: (1) Plumbing or pipe fitting systems, including heating, ventilating, air-conditioning,
refrigeration systems, sheet metal or other duct systems; (2) Electrical systems; (3) Mechanical insulation work; (4) Ornamental iron work; and (5) Commercial signage that does not attempt or appear to direct the movement of traffic on highways or roadways or interfere with, imitate, or resemble any official traffic sign, signal or device.

ARTICLE 2: BIDDER'S REPRESENTATION

2.1 PRE-BID MEETING

2.1.1 A pre-bid meeting for this project will be held at the time and place designated. Attendance at this meeting is a pre-requisite for submitting a Bid, unless this requirement is specifically waived elsewhere in the Bid Documents.

2.2 By submitting a Bid, the Bidder represents that:

2.2.1 The Bidder has read and understands the Bidding Documents and that the Bid is made in accordance therewith.

2.2.2 The Bidder has visited the site, become familiar with existing conditions under which the Work is to be performed, and has correlated the Bidder's personal observations with the requirements of the proposed Contract Documents.

2.2.3 The Bid is based upon the materials, equipment, and systems required by the Bidding Documents without exception.

2.3 JOINT VENTURE REQUIREMENTS

2.3.1 For Public Works Contracts, each Joint Venturer shall be qualified and capable to complete the Work with their own forces.

2.3.2 Included with the Bid submission, and as a requirement to bid, a copy of the executed Joint Venture Agreement shall be submitted and signed by all Joint Venturers involved.

2.3.3 All required Bid Bonds, Performance Bonds, Material and Labor Payment Bonds must be executed by both Joint Venturers and be placed in both of their names.

2.3.4 All required insurance certificates shall name both Joint Venturers.

2.3.5 Both Joint Venturers shall sign the Bid Form.

2.3.6 Both Joint Venturers shall include their Federal E.I. Number with the Bid.

2.3.7 In the event of a mandatory Pre-bid Meeting, each Joint Venturer shall have a representative in attendance.

2.3.8 Due to exceptional circumstances and for good cause shown, one or more of these provisions may be waived at the discretion of the State.

2.4 ASSIGNMENT OF ANTITRUST CLAIMS

2.4.1 As consideration for the award and execution by the Owner of this contract, the Contractor hereby grants, conveys, sells, assigns and transfers to the State of Delaware all of its right, title and interests in and to all known or unknown causes of action it presently has or may now or hereafter acquire under the antitrust laws of the United States and the State of Delaware, relating to the particular goods or services purchased or acquired by the Owner pursuant to this contract.

ARTICLE 3: BIDDING DOCUMENTS

3.1 COPIES OF BID DOCUMENTS

3.1.1 Bidders may obtain complete sets of the Bidding Documents from the Architectural/Engineering firm designated in the Advertisement or Invitation to Bid in the number and for the deposit sum, if any, stated therein.

3.1.2 Bidders shall use complete sets of Bidding Documents for preparation of Bids. The issuing Agency nor the Architect assumes no responsibility for errors or misinterpretations resulting from the use of incomplete sets of Bidding Documents.

3.1.3 Any errors, inconsistencies or omissions discovered shall be reported to the Architect immediately.

3.1.4 The Agency and Architect may make copies of the Bidding Documents available on the above terms for the purpose of obtaining Bids on the Work. No license or grant of use is conferred by issuance of copies of the Bidding Documents.

3.2 INTERPRETATION OR CORRECTION OF BIDDING DOCUMENTS

3.2.1 The Bidder shall carefully study and compare the Bidding Documents with each other, and with other work being bid concurrently or presently under construction to the extent that it relates to the Work for which the Bid is submitted, shall examine the site and local conditions, and shall report any errors, inconsistencies, or ambiguities discovered to the Architect.

3.2.2 Bidders or Sub-bidders requiring clarification or interpretation of the Bidding Documents shall make a written request to the Architect at least seven days prior to the date for receipt of Bids. Interpretations, corrections, and changes to the Bidding Documents will be made by written Addendum. Interpretations, corrections, or changes to the Bidding Documents made in any other manner shall not be binding.

3.2.3 The apparent silence of the specifications as to any detail, or the apparent omission from it of detailed description concerning any point, shall be regarded as meaning that only the best commercial practice is to prevail and only material and workmanship of the first quality are to be used. Proof of specification compliance will be the responsibility of the Bidder.

3.2.4 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for all permits, labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for the proper execution and completion of the Work.

3.2.5 The Owner will bear the costs for all impact and user fees associated with the project.

3.3 SUBSTITUTIONS

3.3.1 The materials, products and equipment described in the Bidding Documents establish a standard of quality, required function, dimension, and appearance to be met by any proposed substitution. The specification of a particular manufacturer or model number is not intended to be proprietary in any way. Substitutions of products for those named will be considered, providing that the Vendor certifies that the function, quality, and performance characteristics of the material offered is equal or superior to that specified. It shall be the Bidder's responsibility to assure that the proposed substitution will not affect the intent of the design, and to make any installation modifications required to accommodate the substitution.

3.3.2 Requests for substitutions shall be made in writing to the Architect at least ten days prior to the date of the Bid Opening. Such requests shall include a complete description of the proposed substitution, drawings, performance and test data, explanation of required installation modifications due the substitution, and any other information necessary for an evaluation. The burden of proof of the merit of the proposed substitution is upon the proposer. The Architect’s decision of approval or disapproval shall be final. The Architect is to notify Owner prior to any approvals.

3.3.3 If the Architect approves a substitution prior to the receipt of Bids, such approval shall be set forth in an Addendum. Approvals made in any other manner shall not be binding.

3.3.4 The Architect shall have no obligation to consider any substitutions after the Contract award.

3.4 ADDENDA

3.4.1 Addenda will be mailed or delivered to all who are known by the Architect to have received a complete set of the Bidding Documents.

3.4.2 Copies of Addenda will be made available for inspection wherever Bidding Documents are on file for that purpose.

3.4.3 No Addenda will be issued later than 2 calendar days prior to the date for receipt of Bids except an Addendum withdrawing the request for Bids or one which extends the time or changes the location for the opening of bids.

3.4.4 Each bidder shall ascertain prior to submitting his Bid that they have received all Addenda issued and shall acknowledge their receipt in their Bid in the appropriate space. Not acknowledging an issued Addenda could be grounds for determining a bid to be non-responsive.

ARTICLE 4: BIDDING PROCEDURES

4.1 PREPARATION OF BIDS

4.1.1 Submit the bids on the Bid Forms included with the Bidding Documents.

4.1.2 Submit the original Bid Form for each bid. Bid Forms may be removed from the project manual for this purpose.

4.1.3 Execute all blanks on the Bid Form in a non-erasable medium (typewriter or manually in ink).

4.1.4 Where so indicated by the makeup on the Bid Form, express sums in both words and figures, in case of discrepancy between the two, the written amount shall govern.

4.1.5 Interlineations, alterations or erasures must be initialed by the signer of the Bid.

4.1.6 BID ALL REQUESTED ALTERNATES AND UNIT PRICES, IF ANY. If there is no change in the Base Bid for an Alternate, enter “No Change”. The Contractor is responsible for verifying that they have received all addenda issued during the bidding period. Work required by Addenda shall automatically become part of the Contract.

4.1.7 Make no additional stipulations on the Bid Form and do not qualify the Bid in any other manner.

4.1.8 Each copy of the Bid shall include the legal name of the Bidder and a statement whether the Bidder is a sole proprietor, a partnership, a corporation, or any legal entity, and each copy shall be signed by the person or persons legally authorized to bind the Bidder to a contract. A Bid by a corporation shall further give the state of incorporation and have the corporate seal affixed. A Bid submitted by an agent shall have a current Power of Attorney attached, certifying agent's authority to bind the Bidder.

4.1.9 Bidder shall complete the Non-Collusion Statement form included with the Bid Forms and include it with their Bid.

4.1.10 In the construction of all Public Works projects for the State of Delaware or any agency thereof, preference in employment of laborers, workers or mechanics shall be given to bona

fide legal citizens of the State who have established citizenship by residence of at least 90 days in the State.

4.1.11 Each bidder shall include a signed Affidavit for the Bidder certifying compliance with OMB Regulation 4104 - "Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on "Large Public Works Projects." "Large Public Works" is based upon the current threshold required for bidding Public Works as set by the Purchasing and Contracting Advisory Council.

4.2 BID SECURITY

4.2.1 All bids shall be accompanied by a deposit of either a good and sufficient bond to the agency for the benefit of the agency, with corporate surety authorized to do business in this State, the form of the bond and the surety to be approved by the agency, or a security of the bidder assigned to the agency, for a sum equal to at least 10% of the bid plus all add Alternates, or in lieu of the bid bond a security deposit in the form of a certified check, bank treasurer's check, cashier's check, money order, or other prior approved secured deposit assigned to the State. The bid bond need not be for a specific sum but may be stated to be for a sum equal to 10% of the bid plus all add Alternates to which it relates and not to exceed a certain stated sum, if said sum is equal to at least 10% of the bid. The Bid Bond form used shall be the standard OMB form (attached).

4.2.2 The Agency has the right to retain the bid security of Bidders to whom an award is being considered until either a formal contract has been executed and bonds have been furnished or the specified time has elapsed so the Bids may be withdrawn, or all Bids have been rejected.

4.2.3 In the event of any successful Bidder refusing or neglecting to execute a formal contract and bond within 20 days of the awarding of the contract, the bid bond or security deposited by the successful bidder shall be forfeited.

4.3 SUBCONTRACTOR LIST

4.3.1 In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, each Bidder shall submit with their Bid a completed List of Sub-Contractors included with the Bid Form. NAME ONLY ONE SUBCONTRACTOR FOR EACH TRADE. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the Bidder will be using to perform the work and provide material for that subcontractor category. Should the Bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the Bidder shall list that third-tier contractor's full name and address (City & State). **If the Bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the Bidder intends to perform the work themselves, the Bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

4.3.1.1 For the purposes of this project, the Bidder shall also identify, on a separate form, those subcontractor, third-tier, or providers of material on the bidder's Subcontractor List,

which, if any, are DBEs. To be able to calculate the percentage of DBE representation, the Bidder must identify all subcontractors, third-tier contractors or providers of material that will be hired for this project.

4.3.2 It is the responsibility of the Contractor to ensure that their Subcontractors are in compliance with the provisions of this law. Also, if a Contractor elects to list themselves as a Subcontractor for any category, they must specifically name themselves on the Bid Form and be able to document their capability to act as Subcontractor in that category in accordance with this law.

4.4 AFFIDAVIT OF CONTRACTOR QUALIFICATIONS

4.4.1 In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, each Bidder shall submit with their Bid the Affidavit of Contractor Qualifications certifying that the Bidder will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term. After a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

4.5 AFFIDAVIT OF CRAFT TRAINING COMPLIANCE

4.5.1 In accordance with Title 29, Chapter 69, Section 6962(c)(13) of the Delaware Code, contractors and subcontractors must provide craft training for journeyman and apprentice levels if **all** of the following apply:

A. A project meets the prevailing wage requirement under Title 29, Chapter 69, Section 6960 of the Delaware Code.
B. The contractor employs 10 or more total employees.
C. The project is not a federal highway project

Failure to provide required craft training on the project may subject the successful contractor and/or subcontractor(s) to penalties as outlined in Title 29, Chapter 69, Section 6962(c)(13) of the Delaware Code.

Bidders shall submit the Affidavit of Craft Training Compliance prior to contract execution.

4.6 EQUALITY OF EMPLOYMENT OPPORTUNITY ON PUBLIC WORKS

4.6.1 During the performance of this contract, the contractor agrees as follows:

A. The Contractor will not discriminate against any employee or applicant for employment because of race, creed, sex, color, sexual orientation, gender identity or national origin. The Contractor will take affirmative action to ensure the applicants are employed, and that employees are treated during employment, without regard to their race, creed, sex, color, sexual orientation, gender identity or national origin. Such action shall include, but not be limited to, the following: Employment, upgrading, demotion or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places available to employees and applicants for employment notices to be provided by the contracting agency setting forth this nondiscrimination clause.

B. The Contractor will, in all solicitations or advertisements for employees placed by or on behalf of the Contractor, state that all qualified applicants will receive consideration for employment without regard to race, creed, sex, color, sexual orientation, gender identity or national origin."

4.7 PREVAILING WAGE REQUIREMENT

4.7.1 Wage Provisions: For renovation and new construction projects whose costs exceed the thresholds contained in Delaware Code, Title 29, Section 6960, the minimum wage rates for various classes of laborers and mechanics shall be as determined by the Department of Labor, Division of Industrial Affairs of the State of Delaware.

4.7.2 The employer shall pay all mechanics and labors employed directly upon the site of work, unconditionally and not less often than once a week and without subsequent deduction or rebate on any account, the full amounts accrued at time of payment, computed at wage rates not less than those stated in the specifications, regardless of any contractual relationship which may be alleged to exist between the employer and such laborers and mechanics.

4.7.3 The scale of the wages to be paid shall be posted by the employer in a prominent and easily accessible place at the site of the work.

4.7.4 Every contract based upon these specifications shall contain a stipulation that sworn payroll information, as required by the Department of Labor, be furnished weekly. The Department of Labor shall keep and maintain the sworn payroll information for a period of 6 months from the last day of the work week covered by the payroll.

4.8 SUBMISSION OF BIDS

4.8.1 Enclose the Bid, the Bid Security, and any other documents required to be submitted with the Bid in a sealed opaque envelope. Address the envelope to the party receiving the Bids. Identify with the project name, project number, and the Bidder's name and address. If the Bid is sent by mail, enclose the sealed envelope in a separate mailing envelope with the notation "BID ENCLOSED" on the face thereof. The State is not responsible for the opening of bids prior to bid opening date and time that are not properly marked.

4.8.2 Deposit Bids at the designated location prior to the time and date for receipt of bids indicated in the Advertisement for Bids. Bids received after the time and date for receipt of bids will be marked “LATE BID” and returned.

4.8.3 Bidder assumes full responsibility for timely delivery at location designated for receipt of bids.

4.8.4 Oral, telephonic or telegraphic bids are invalid and will not receive consideration.

4.8.5 Withdrawn Bids may be resubmitted up to the date and time designated for the receipt of Bids, provided that they are then fully in compliance with these Instructions to Bidders.

4.9 MODIFICATION OR WITHDRAW OF BIDS

4.9.1 Prior to the closing date for receipt of Bids, a Bidder may withdraw a Bid by personal request and by showing proper identification to the Architect. A request for withdraw by letter or fax, if the Architect is notified in writing prior to receipt of fax, is acceptable. A fax directing a

modification in the bid price will render the Bid informal, causing it to be ineligible for consideration of award. Telephone directives for modification of the bid price shall not be permitted and will have no bearing on the submitted proposal in any manner.

4.9.2 Bidders submitting Bids that are late shall be notified as soon as practicable and the bid shall be returned.

4.9.3 A Bid may not be modified, withdrawn or canceled by the Bidder during a thirty (30) day period following the time and date designated for the receipt and opening of Bids, and Bidder so agrees in submitting their Bid. Bids shall be binding for 30 days after the date of the Bid opening.

ARTICLE 5: CONSIDERATION OF BIDS

5.0 BEST VALUE PROCESS

Bidders shall provide their bids on the forms provided and shall indicate the percent of DBEs that the Bidder will be utilizing to complete the scope of work for the Prime Contract for which it is bidding. The DBE may be a subcontractor, a third-tier contractor, or a provider of material. The Winning Bidder may be expected to include students from the New Castle County Vocational Training School District as identified in the individual contract Scopes of Work.

The Best Value Process will evaluate the bids as a weighted average in the following manner:

1. The Bid Amount, including any Alternates that are expected to be awarded.
2. A discount on the Bidder's Bid Amount assigned based on the chart below based on the percentage of DBE firms being hired by Bidder.

Once calculated, the Lowest Adjusted Bid will be awarded to the Bidder that is also found to be responsive and responsible. For clarification, the discount will be used for evaluation purposes only. The contract award will be based on the amount the Bidder provided in its bidding package.

DISCOUNT FOR DBE% PARTICIPATION
0% = -2% discount
1% to 2% = -1.5% discount
>2% to 3% = -1% discount
>3% to 4% = 0% discount
>4% to 5% = 1% discount
>5% to 6% = 2% discount
>6% to <7% = 3% discount
7% = 4% discount
>7% to 20% = 5% discount on bid price
>20% to 30% = 6% discount on bid price
>30% to 40% = 7% discount on bid price
>40% to 50% = 8% discount on bid price
> 50% = 10% discount on bid price

5.1 OPENING/REJECTION OF BIDS

5.1.1 Unless otherwise stated, Bids received on time will be publicly opened and will be read aloud. An abstract of the Bids will be made available to Bidders.

5.1.2 The Agency shall have the right to reject any and all Bids. A Bid not accompanied by a required Bid Security or by other data required by the Bidding Documents, or a Bid which is in any way incomplete, or irregular is subject to rejection.

5.1.3 If the Bids are rejected, it will be done within thirty (30) calendar day of the Bid opening.

5.2 COMPARISON OF BIDS

5.2.1 After the Bids have been opened and read, the bids will be evaluated using the Best Value Process in Article 5.0. the result of such evaluations will be made available to the public. The evaluation of the Bids will be based on the Base Bid plus desired Alternates. The Agency shall have the right to accept Alternates in any order or combination.

5.2.2 The Agency reserves the right to waive technicalities, to reject any or all Bids, or any portion thereof, to advertise for new Bids, to proceed to do the Work otherwise, or to abandon the Work, if in the judgment of the Agency or its agent(s), it is in the best interest of the State.

5.2.3 An increase or decrease in the quantity for any item is not sufficient grounds for an increase or decrease in the Unit Price.

5.2.4 The prices quoted are to be those for which the material will be furnished F.O.B. Job Site and include all charges that may be imposed during the period of the Contract.

5.2.5 No qualifying letter or statements in or attached to the Bid, or separate discounts will be considered in determining the low Bid except as may be otherwise herein noted. Cash or separate discounts should be computed and incorporated into Unit Bid Price(s).

5.3 DISQUALIFICATION OF BIDDERS

5.3.1 An agency shall determine that each Bidder on any Public Works Contract is responsible before awarding the Contract. Factors to be considered in determining the responsibility of a Bidder include:

A. The Bidder's financial, physical, personnel or other resources including Subcontracts;

B. The Bidder's record of performance on past public or private construction projects, including, but not limited to, defaults and/or final adjudication or admission of violations of the Prevailing Wage Laws in Delaware or any other state;

C. The Bidder's written safety plan;

D. Whether the Bidder is qualified legally to contract with the State;

E. Whether the Bidder supplied all necessary information concerning its responsibility; and,

F. Any other specific criteria for a particular procurement, which an agency may establish; provided however, that, the criteria be set forth in the Invitation to Bid and is otherwise in conformity with State and/or Federal law.

5.3.2 If an agency determines that a Bidder is nonresponsive and/or nonresponsible, the determination shall be in writing and set forth the basis for the determination. A copy of

the determination shall be sent to the affected Bidder within five (5) working days of said determination.

5.3.3 In addition, any one or more of the following causes may be considered as sufficient for the disqualification of a Bidder and the rejection of their Bid or Bids.

5.3.3.1 More than one Bid for the same Contract from an individual, firm or corporation under the same or different names.

5.3.3.2 Evidence of collusion among Bidders.

5.3.3.3 Unsatisfactory performance record as evidenced by past experience.

5.3.3.4 If the Unit Prices are obviously unbalanced either in excess or below reasonable cost analysis values.

5.3.3.5 If there are any unauthorized additions, interlineation, conditional or alternate bids or irregularities of any kind which may tend to make the Bid incomplete, indefinite or ambiguous as to its meaning.

5.3.3.6 If the Bid is not accompanied by the required Bid Security and other data required by the Bidding Documents.

5.3.3.7 If any exceptions or qualifications of the Bid are noted on the Bid Form.

5.4 ACCEPTANCE OF BID AND AWARD OF CONTRACT

5.4.1 A formal Contract shall be executed with the successful Bidder within twenty (20) calendar days after the award of the Contract.

5.4.2 Per Section 6962(d)(13)a., Title 29, Delaware Code, “The contracting agency shall award any public works contract within thirty (30) days of the bid opening to the lowest responsive and responsible Bidder, unless the Agency elects to award on the basis of best value, in which case the election to award on the basis of best value shall be stated in the Invitation To Bid. Any public school district and its board shall award public works contracts in accordance with this section’s requirements except it shall award the contract within 60 days of the bid opening.”

5.4.3 Each Bid on any Public Works Contract must be deemed responsive by the Agency to be considered for award. A responsive Bid shall conform in all material respects to the requirements and criteria set forth in the Contract Documents and specifications.

5.4.4 The Agency shall have the right to accept Alternates in any order or combination, and to determine the low Bidder on the basis of the sum of the Base Bid, plus accepted Alternates

5.4.5 The successful Bidder shall execute a formal contract, submit the required Insurance Certificate, and furnish good and sufficient bonds, unless specifically waived in the General Requirements, in accordance with the General Requirement, within twenty (20) days of official notice of contract award. The successful Bidder shall provide, at least two business days prior to contract execution, copies of the Employee Drug Testing Program for the Bidder and all listed Subcontractors. Bonds shall be for the benefit of the Agency with surety in the amount of 100% of the total contract award. Said Bonds shall be conditioned upon the faithful performance of the contract. Bonds shall remain in affect for period of two (2) years after the date of the Certificate of Final Payment.

5.4.6 If the successful Bidder fails to execute the required Contract, Bond and all required information, as aforesaid, within twenty (20) calendar days after the date of official Notice of the Award of the Contract, their Bid guaranty shall immediately be taken and become the property of the State for the benefit of the Agency as liquidated damages, and not as a forfeiture or as a penalty. Award will then be made to the next lowest qualified Bidder of the Work or readvertised, as the Agency may decide.

5.4.7 Each bidder shall supply with its bid its taxpayer identification number (i.e., federal employer identification number or social security number) and should the vendor be awarded a contract, such vendor shall provide to the agency the taxpayer identification license numbers of such subcontractors. Such numbers shall be provided on the later of the date on which such subcontractor is required to be identified or the time the contract is executed. The successful Bidder shall provide to the agency to which it is contracting, within 30 days of entering into such public works contract, copies of all Delaware Business licenses of subcontractors and/or independent contractors that will perform work for such public works contract. However, if a subcontractor or independent contractor is hired or contracted more than 20 days after the Bidder entered the public works contract the Delaware Business license of such subcontractor or independent contractor shall be provided to the agency within 10 days of being contracted or hired.

5.4.8 The Bid Security shall be returned to the successful Bidder upon the execution of the formal contract. The Bid Securities of unsuccessful bidders shall be returned within thirty (30) calendar days after the opening of the Bids.

ARTICLE 6: POST-BID INFORMATION

6.1 CONTRACTOR'S QUALIFICATION STATEMENT

6.1.1 Bidders to whom an award of a Contract is under consideration shall, if requested by the Agency, submit a properly executed AIA Document A305-2020, Contractor's Qualification Statement, unless such a statement has been previously required and submitted.

6.2 Bidders to whom an award of a Contract has been made must produce their Delaware Business License before the Contract can be executed.

ARTICLE 7: PERFORMANCE BOND AND PAYMENT BOND

7.1 BOND REQUIREMENTS

7.1.1 The cost of furnishing the required Bonds, that are stipulated in the Bidding Documents, shall be included in the Bid.

7.1.2 If the Bidder is required by the Agency to secure a bond from other than the Bidder's usual sources, changes in cost will be adjusted as provide in the Contract Documents.

7.1.3 The Performance and Payment Bond forms used shall be the standard OMB forms (attached).

7.2 TIME OF DELIVERY AND FORM OF BONDS

7.2.1 The bonds shall be dated on or after the date of the Contract.

7.2.2 The Bidder shall require the attorney-in-fact who executes the required bonds on behalf of the surety to affix a certified and current copy of the power of attorney.

ARTICLE 8: FORM OF AGREEMENT BETWEEN OWNER AND CONTRACTOR

8.1 Unless otherwise required in the Bidding Documents, the Agreement for the Work will be written on AIA Document A132, Standard Form of Agreement Between Owner and Contractor, *Construction Manager as Adviser Edition*.

END OF SECTION

SECTION 003132 – GEOTECHNICAL DATA

1. GENERAL

A. Owner's Disclaimer

1. Site Information: Data on subsurface conditions are made available in the Bidding Documents as a convenience to Bidders and the Contractor. They are not intended as representations or warrants of continuity of such conditions between soil borings. It shall be expressly understood that the Owner will not be responsible for interpretations or conclusions drawn there from by the Contractor. Additional test borings and other exploratory operations may be made by the Contractor at no additional cost to the Owner, provided such operations are acceptable to the Architect and Construction Manager.

B. SOIL BORING DATA

1. Boring logs and location plans are available for review at Construction Manager's office. All Contractors are strongly urged to review this information. The following Geotechnical Reports are attached following this page:

- February 9, 2023 GTA Report of Final Geotechnical Exploration
- January 10, 2023 GTA Report of Geotechnical Exploration
- June 17, 2022 GTA Report of Geotechnical Exploration

END OF SECTION

GEO-TECHNOLOGY ASSOCIATES, INC.

GEOTECHNICAL AND
ENVIRONMENTAL CONSULTANTS

A Practicing Geoprofessional Business Association Member Firm

February 9, 2023

New Castle County Vo-Tech School District
1703 School Lane
Wilmington, Delaware 19808

Attn: Mr. Al Schrum; Supervisor of Facilities and Special Projects

Re: Report of Final Geotechnical Exploration
NCCVT New Hodgson Vo-tech High School
New Castle County, Delaware

Dear Mr. Schrum:

In accordance with our agreements dated April 5, 2022, Geo-Technology Associates, Inc. (GTA) has performed a geotechnical exploration for the new NCCVT New Hodgson Vo-tech High School located in New Castle County, Delaware. The exploration consisted of performing Standard Penetration Test borings and Cone Penetration Test soundings across the site to evaluate the encountered materials for engineering properties. Final geotechnical recommendations regarding design and construction of the proposed buildings and pavements are included in this report. Recommendations related to the proposed stormwater management facilities will be provided under separate cover. GTA appreciates the opportunity to have been of assistance to you on this project. Should you have questions or require additional information, please contact our office at (302) 326-2100.

Sincerely,
GEO-TECHNOLOGY ASSOCIATES, INC.

Alison R. Schoch, P.E.
Senior Geotechnical Engineer

Meghan McDonough, P.E.
Principal

AJC/MM/mt
220791
Attachments

REPORT OF FINAL GEOTECHNICAL EXPLORATION

NCCVT NEW HODGSON VO-TECH HIGH SCHOOL

New Castle County, Delaware

FEBRUARY 2023

Prepared For:

NEW CASTLE COUNTY VO-TECH SCHOOL DISTRICT
1703 School Lane
Wilmington, Delaware 19808

Attn: Mr. Al Schrum

Prepared By:

GEO-TECHNOLOGY ASSOCIATES, INC.
Geotechnical and Environmental Consultants
18 Boulden Circle, Suite 36
New Castle, Delaware 19720
(302) 326-2100

GTA Job No: 220791

TABLE OF CONTENTS

PAGE

INTRODUCTION 1

SITE CONDITIONS 1

PROPOSED CONSTRUCTION 2

SITE GEOLOGY 2

SUBSURFACE EXPLORATION 3

SUBSURFACE CONDITIONS 5

CONCLUSIONS AND RECOMMENDATIONS 6

- Demolition and Earthwork Considerations 6
- Site Preparation 9
- Site Grading 9
- Foundations 11
- Seismic Information 12
- Floor Slabs 12
- Subsurface Utilities 14
- Pavements 14

ADDITIONAL SERVICES 15

LIMITATIONS 16

GBA—Important Information About Your Geotechnical Engineering Report

APPENDICES

Appendix A – Figures
- Figure No. 1 – Site Location Map
- Figure No. 2 – Exploration Location Plan

Appendix B – Subsurface Exploration Data
- Notes For Exploration Logs
- Exploration Logs (B-1 to B-16; CPT-1 to CPT-19)

Appendix C – Soil Laboratory Test Data
- Figure Nos. 3 to 5 – Particle Size Distribution Reports (3 Sheets)
- Figure No. 6 – Standard Proctor Moisture-Density Relationship (1 Sheet)

REPORT OF FINAL GEOTECHNICAL EXPLORATION

NCCVT NEW HODGSON VO-TECH HIGH SCHOOL
NEW CASTLE COUNTY, DELAWARE
FEBRUARY 2023

INTRODUCTION

This report presents the results of the geotechnical exploration performed for the New Hodgson Vo-tech High School, located in New Castle County, Delaware. GTA was provided with an untitled plan indicating the locations of existing and proposed site features, as well as existing grading, prepared by Landmark Science and Engineering.

In April 2022, Geo-Technology Associates, Inc. (GTA) was retained to perform a preliminary geotechnical exploration at the site. This exploration included 4 Standard Penetration Test (SPT) borings and 9 Cone Penetration Test (CPT) soundings across the site. The results of the preliminary exploration were summarized in our report dated June 2022. Following further site concept development, GTA was retained to perform additional SPT borings and CPT soundings in the vicinity of the proposed buildings as well as pavement cores near the existing entrance roadway to the school. Conclusions and recommendations regarding design and construction of the proposed buildings and infrastructure were derived from engineering analysis of fieldwork.

SITE CONDITIONS

The approximate 65.0± acre site is located at 2575 Glasgow Avenue in New Castle County, Delaware as shown on the *Site Location Map, Figure 1*, included in Appendix A. The site is located within the NCCVT New Hodgson Vo-tech High School and consists of a one-story building, athletic fields, open grass areas, parking lots, and drive aisles. The exploration areas were located within the existing athletic fields, open grass areas, and the east parking lot. The site is bound by Glasgow Avenue to the west, Summit Bridge Trail and an undeveloped wooded area to the north, Summit Bridge Road to the east and south.

The north half of the site is relatively flat, with existing grades ranging between approximate elevation (EL) 83 to EL 80, with isolated mounded areas within landscaped areas which grade as high as EL 86. Along the east side of the site, east of parking lot areas, the site grades range between

EL 74 to EL 73. In the south half of the site, existing grades in this area range between EL 84 to EL 73.

PROPOSED CONSTRUCTION

Proposed construction will consist of redeveloping the existing high school campus to include a new 2-story high school building as well as proposed parking lots and access drives, a field house building, athletic fields, and associated SWM facilities. The proposed building is to be located within an area of the site currently occupied by athletic fields and the proposed athletic facilities are located within an area of the existing building. At this time, there are five locations where SWM facilities are proposed throughout the campus. The results of infiltration testing have been provided under separate cover.

The 2-story high school will consist of masonry and steel-framing and will be constructed at-grade (i.e., no basement level is proposed). The finished floor elevation for the building is anticipated to be EL 84.0. Existing grades in the proposed building area range from EL 79 to EL 83, which will require fills of up to approximately 5 feet to achieve the proposed building pad subgrade elevation. For our analysis, we have assumed structural loads on the order of 3 to 5 kips per linear foot for walls and 100 to 150 kips for columns.

The athletic facilities will include an 11,000 square-foot field house and football stadium located north of the proposed school building. We have assumed structural loads for the field house will be on the order of 2 kips per linear foot for walls and 75 kips for columns and a finished floor elevation within 2 to 3 feet of current grades in this area. The proposed pavements will include access drives throughout the site to parking lots surrounding the school and nearby the athletic fields and football stadium. A loading area was noted near the northeast corner of the school.

SITE GEOLOGY

According to the *Geologic Map of New Castle County Delaware* (GM13, 2005), published by the Delaware Geological Survey, the site vicinity is situated in the Coastal Plain. Physiographic Province. The Coastal Plain is characterized by undifferentiated and interlayered sedimentary deposits derived from eroded rock formations to the north and west. Specifically, the site is mapped

as underlain by a 30-to-50-foot thickness of the Pleistocene Age Columbia Formation. The Pleistocene deposits generally consist of quartz sand and gravel, with lenses of silt and clay. Beneath the surficial sediments of the Columbia Formation, the geologic map indicates the soils of the Potomac Formation are present.

Groundwater mapping provided by the Delaware Geologic Information Resource (DGIR) indicate that groundwater levels at the site during wet seasonal conditions will be 9 to 16 feet below grade throughout the north and west most area of the site, with an area along the south half of the site with groundwater levels of 6 to 9 feet. During normal and dry seasonal conditions groundwater levels will be 9 to 16 feet throughout the majority of the site, with areas within the north side of the site with water levels between 16 and 20 feet deep.

SUBSURFACE EXPLORATION

The field exploration consisted of drilling Standard Penetration Test (SPT) borings and Cone Penetration Test (CPT) soundings throughout the site. Between December 19 and 21, 2022, GTA performed 12 SPT borings and 10 CPT soundings in the area of the proposed school. The SPT borings were performed to depths of 20 to 25 feet below grade. The CPT soundings were performed to depths ranging between approximately 12 to 36 feet below grade. In addition, 4 pavement cores were performed through the pavement section within the entrance area driveway to the existing school. The explorations were field located by GTA via hand-held GPS and measuring from existing site features, with the approximate locations indicated on *Figure 2: Exploration Location Plan*, included in Appendix B.

Standard Penetration Testing was performed in the boreholes, with nearly continuous sampling performed in the upper 10 feet of drilling and at 5-foot intervals thereafter. Standard Penetration Testing involves driving a 2-inch outside diameter (O.D.), 1⅜-inch inside diameter (I.D.) split-spoon sampler with a 140-pound hammer free-falling 30 inches. The number of blows required to drive the sampler was recorded in intervals of 6 inches. The total number of hammer blows required to drive the sampler from the 6- to 18-inch interval is the SPT N-value. Split spoon samples retrieved from the test borings were returned to GTA's laboratory for limited testing.

The CPT soundings were performed using a 20-ton, 15 cm² single-element cone capable of measuring pore pressures at the u_2 position. The soundings were performed by pushing an electronically instrumented cone shaped probe into the soil with the hydraulic system of a track-mounted reaction device. The cone is equipped with an instrumented tip and friction sleeve that measures tip resistance and soil-to-steel friction, respectively, as the cone is being pushed. In addition, the pore water pressure response to cone penetration is measured. Measurements of tip resistance, sleeve friction, and pore pressure were taken at approximately 1-inch depth intervals. This data was transmitted to recording devices at the ground surface. Graphical cone sounding logs were constructed to show the variations of tip resistance, local friction, friction ratio, and pore pressure with depth. These values can be correlated to soil strength, compressibility, and classification. The tip resistance profile graphically presents the relative strength of the soil strata. The friction ratio, the numerical ratio of the local friction to the tip resistance, was computed for each depth interval. This ratio is an indicator of the material type, i.e. sand, silt, or clay. The friction, friction ratio, and pore pressure profiles are used primarily to interpret soil type. Refer to the attached CPT sounding logs for detailed graphical interpretation of the subsurface conditions.

GTA performed 4 pavement cores within the driveway area near the entrance to the school to evaluate the pavement section. The following table indicates the pavement section thicknesses.

PAVEMENT CORE SECTION THICKNESSES

LOCATION	ASPHALT SURFACE COURSE	ASPHALT BASE COURSE	GRADED AGGREGATE
P-1	2 inches	4 ½ inches	1 inch
P-2	1 ½ inches	3 inches	2 inches
P-3	2 inches	3 inches	2 ¼ inches
P-4	1 ½ inches	3 inches	2 inches

It should be noted that an instrument survey for elevation or location was not performed and the elevations indicated on the logs were interpolated from the site topography indicated on the referenced plan. Therefore, it should be understood that all elevations, as well as transitions in soil strata indicated on the logs are approximate.

SUBSURFACE CONDITIONS

Beneath a layer of topsoil, the subsurface conditions at the site can generally be described as a layer of fill underlain by natural soils consistent with the Columbia Formation descriptions to the completion depths of the explorations. Topsoil measured 3 to 12 inches at the ground surface. Fill material was observed in Borings B-5, B-7, B-8, B-10, B-13, B-14, and B-15 to depths of 2 to 4 feet and was likely placed during previous site development. The fill material consisted of sandy silt material with varying amounts of gravel. Beneath the fill, the natural soils generally consisted of fine-grained soils underlain by granular soils to the extent of the explorations. The fine-grained soils consisted of lean clay and silt with varying amounts of sand and gravel. The granular soils consisted of silty sand, clayey sand, and poorly-graded sand with silt. In locations B-5, B-7, and B-14, a layer of fine-grained soils was interlayered within the sand stratum.

Uncorrected SPT N-values for the encountered fine-grained soils ranged from 3 to 16 blows per foot (bpf), averaging 7 bpf, indicating these soils range from soft to stiff, and are generally medium stiff. Uncorrected SPT N-values for the coarse-grained soils ranged from 3 to 19 bpf, averaging 9 bpf, indicating these soils range from very loose to medium dense, and are generally loose to medium dense.

Cone tip resistances in the CPT logs were variable across the site. The surface fine-grained materials generally had cone tip resistances if up to approximately 50 tons per square foot (tsf) indicating soft to medium stiff materials to depths ranging between 2 to 12 feet below grade. The granular soils in the upper approximately 30 feet of generally ranged from 50 to 100 tsf, indicating medium dense or denser soils. Isolated areas throughout the sand stratum were greater than 100 tsf indicating dense soils. Based on the seismic CPT data and the site geologic profile, average shear wave velocities of more than 400 feet per second and less than 1,200 feet per second are estimated for the upper 100 feet of materials at the site. Accordingly, the site can be assigned to Site Class D – Stiff Soil Profile.

Groundwater was observed in the borings during drilling at depths ranging between approximately 8 and 15 feet below existing grades, corresponding to approximate EL 64 to EL 73. Following completion of drilling, water levels through the augers were observed to range between

approximately 7 to 20 feet below grade, corresponding to approximate EL 61 to EL 74. The boreholes were backfilled upon completion and therefore, 24-hour water level readings were not determined. In the CPT soundings, groundwater levels were observed at depths ranging from approximately 5½ to 16½ feet below grade, corresponding to approximate EL 59 to 72. The groundwater table will fluctuate several feet due to variations in precipitation and surface runoff.

LABORATORY ANALYSES

Selected samples obtained from the borings were tested for grain size analysis, Atterberg Limits, and natural moisture contents. The testing was performed to determine the Unified Soil Classification System (USCS) designation for the soil. The USCS classifications provide information regarding soil-engineering behavior. In addition, one Standard Proctor test was done to determine the moisture-density relationship of potential structural fill material. The results of the testing are summarized in the table below and in *Appendix C*.

SUMMARY OF LABORATORY TESTING

LOCATION	DEPTH (ft)	USCS CLASSIFICATION	NMC (%)	% <200 Sieve	LL (%)	PI (%)
B-15	4.0 – 6.0	Clayey SAND (SC)	15.0	45.2	29	12
B-22	2.0 – 4.0	Clayey SAND (SC)	15.0	26.1	32	12
SWM-5	0.0 – 5.0	Lean CLAY with Sand (CL)	18.2	83.6	29	10

Note: LL=Liquid Limit; PI=Plastic Index; NMC=Natural Moisture Content

CONCLUSIONS AND RECOMMENDATIONS

Based upon the results of this exploration, it is our opinion that the proposed construction is generally feasible, given that the geotechnical recommendations are followed, and that the standard level of care is maintained during construction. The potential geotechnical issues related to site development will be demolition of existing site features and impact on new construction, moisture sensitive fine-grained soils, existing fill and obstructions, and perched water. A discussion of these issues, as well as general foundation design parameters, are included in the following paragraphs.

Demolition and Earthwork Considerations

As previously mentioned, the location of the proposed building is currently occupied by the

football field, track, and other existing athletic facility features. The existing building and pavements are located where proposed athletic facility construction is proposed. Therefore, redevelopment will include demolition of the existing structures including the existing school building, pavement and sidewalk areas, track, several football stadium structures and bleachers, various fences throughout the site, and existing utilities.

Pavements will require removal and replacement or retrofit to accompany the new construction. Asphalt millings should be segregated from the graded-aggregate base course, and should not be used as structural fill. Graded aggregate base course (GABC) can be removed and stockpiled for future use. The GABC can remain in-place in proposed parking and drive areas. GTA recommends the complete removal of all obstructions, foundations/slabs, and retaining walls from the proposed construction area. Alternately, these elements can remain in place if they are at least 20 feet from any proposed structure and removed to a minimum depth of 2 feet below final grading, provided their location does not conflict with utility installation, foundation construction or retaining wall construction. This will need to be further evaluated as design progresses.

GTA recommends that the existing utilities be removed and/or relocated to areas outside of the planned construction zone. The base of all excavations resulting from the removal of existing features and utilities, if situated below the proposed finished floor elevation, should be evaluated by the representative of the Geotechnical Engineer of Record to confirm stabilization prior to backfilling. Following confirmation of a stable subgrade, the excavations should be backfilled as specified in the *Site Grading* section of this report.

A portable crushing plant capable of handling a variety of materials of non-uniform size or composition will be required to process the building materials for re-use as structural fill. Metal and waste materials must be detected and removed at the start of processing by manual or magnetic separation. If the concrete contains steel reinforcement it will be necessary to remove this reinforcement. All reinforcing steel should be removed from the salvaged concrete either before or during the crushing operation. Any reinforcing steel not removed previously must be separated from the recycled concrete after it is processed through the primary crusher.

The recycling of the building rubble waste consists of concrete, asphalt, wood, fixtures, rebar, metals, drywall, roofing, and other materials. Appropriately labeled cans should be provided by the demolition contractor for the various materials. The concrete, masonry, brick and rebar shall be segregated and stockpiled separately. Proper separation of unsuitable materials from the crushed aggregate feedstock is important. We recommend that the feedstock slabs be processed to slabs measuring no more than 4 feet by 4 feet.

The recycled concrete aggregate shall consist of Portland Cement Concrete or other concrete containing pozzolanic binder material from only on-site sources. The recycled concrete material shall be free of reinforcing steel, expansion material, gypsum, organic substances (wood, textile fabric, paper, joint sealants, paints, etc.), chlorides, and glass. The recycled concrete aggregate for re-use as structural fill should consist of at least 70 percent, by weight, Portland cement concrete, with the following materials making up the remaining 30 percent; wood shall be no more than 0.1 percent maximum, and brick, glass, concrete masonry units, on-site soils, or other friable materials shall be no more than 29.9 percent maximum.

The percentage of wood, brick, glass, concrete masonry units, on-site soils, and other friable materials shall be determined by weighing that material retained on the No. 4 sieve, and dividing by the total weight of recycled concrete aggregate material retained on the No. 4 sieve. Fine aggregate passing the No. 4 (4.75-mm) sieve shall consist of fines from the operation of crushing the recycled concrete aggregate. The processed materials should have a unit weight of at least 110 pounds per cubic foot.

Recycled concrete aggregate samples for preliminary testing shall be furnished by the Contractor prior to the start of backfill. Samples of recycled concrete aggregate shall be furnished by the Contractor at the start of production and at intervals during production. The sampling points and intervals will be designated by the Engineer. The samples will be the basis of approval of specific lots of recycled concrete aggregate for the quality requirements.

Additionally, if any foundations fall within a sloped excavation, the foundation bearing level be lowered below the excavation support grade or supported on compacted structural fill after

completion of the foundation walls.

Site Preparation

Concluding demolition and after removal of the bituminous concrete, site preparation should include the stripping of all vegetation and other deleterious material from within and a minimum of 10 feet beyond the proposed construction limits following demolition. Topsoil thicknesses ranged between 3 and 12 inches; however actual stripping thickness will be dependent on localized topsoil development, precipitation, soil moisture, construction traffic disturbance and contractor care. The topsoil may be stockpiled for future use in landscaped areas but would not be suitable for reuse in structural areas.

Existing fill was encountered within the upper 2 to 4 feet of the ground surface. The fill materials primarily consisted of medium stiff to very stiff fine-grained materials or loose to medium dense granular materials. Fill containing organic material may not be used in structural areas and should be removed if encountered during construction. Based on the proposed finished floor elevation of 84.0 feet, fills on the order of 1 to 5 feet will be required in the building pad area. We recommend that GTA further evaluate the fill at the time of construction to determine its suitability to remain in-place for support of proposed structures. The further evaluation should consist of at a minimum the excavation of test pits, proof-rolling with a loaded tri-axle dump truck, and/or performing in-place density testing. If unsuitable conditions are encountered, they can be undercut and replaced with structural fill in accordance with the *Site Grading* section of this report. Alternatively, under suitable weather conditions, soft/loose or unstable areas which are the result of excessive moisture can be aerated, dried in-place, and recompacted. The lateral extent, depth, and method of stabilization will be dependent on actual site conditions and should be determined at the time of construction by a representative of the Geotechnical Engineer of Record.

Site Grading

Upon satisfactory evaluation of the subgrade, structural fill should be placed in lifts and compacted in accordance with the specifications included in this report. Fill materials will typically need to be within 2 to 3 percentage points of the optimum moisture content before compactive effort is applied. Moisture conditioning of the soils should be anticipated in order to obtain the

recommended degree of compaction and to provide stable subgrades. Excavated soil materials will generally need to be within 2 to 3 percentage points of the optimum moisture content before compactive effort is applied. Moisture contents for the fine-grained soils in the upper 6 feet of the surface ranged from 13 to 20 percent moisture compared to optimum moisture contents in the 14 to 16 percent range. Moisture contents for the granular materials ranged from 6 to13 percent moisture. The contractor should be prepared to moisture condition soils by discing and aerating, or cutting and blending the on-site soils with imported cohesionless granular materials that are dry of optimum if the moisture content of the excavated soils for re-use as structural fill is above the working range of optimum for compaction.

We recommend that positive drainage be maintained across the site during construction to minimize ponding of water, since the exposed subgrades could destabilize in combination with construction traffic and precipitation. Furthermore, heavy construction traffic should generally be run on designated haul roads during periods of wet weather to reduce the potential for destabilization of more subgrade areas than necessary. If the subgrade is disturbed by construction traffic and becomes unstable, undercutting and replacement of these surficial materials will likely be required.

Based on the proposed finished floor elevation of EL 84.0 for the school building pad, it is anticipated that fills on the order of 1 to 5 feet will be required in the building area. The available "cut" material from the proposed SWM areas consisted of primarily of fine-grained soils at the surface with some granular soils at deeper depths. These materials may be suitable for re-use as structural fill if they are at a moisture content at which compaction can be achieved. It should be anticipated that moisture the moisture content of the potential fill will be wetter than the optimum and some drying may be required. Proper moisture-conditioning of these soils require time and warm, dry weather. The shallow fine-grained soils are susceptible to moisture-related compaction problems and as such are considered less desirable for reuse as controlled compacted fill compared with granular materials. It should be noted that even if the soils are successfully compacted to the required densities, they can easily become unstable from excess moisture and construction equipment traffic and subsequent over-excavation of unstable soils should be expected.

If sufficient quantities of suitable on-site soils are not available for structural fill, imported borrow consisting of predominantly granular soils conforming to the requirements of DelDOT Standard Specifications Borrow Type C (Backfill) should be utilized. Other granular sources will be considered provided they are within working range of optimum moisture content for compaction at the point of placement.

Structural fill should meet USCS designation CL, ML, SM, SC, GP-GM, GM, or GW-GM and be approved by the Geotechnical Engineer prior to use. All structural fill should be constructed in maximum 8-inch thick, loose lifts and be compacted to the following specifications:

COMPACTION SPECIFICATIONS

Structure / Fill Location	Compaction / Moisture Specification
Below foundations, floor slabs, and within wall backfill or slopes steeper than 5H:1V	95 percent of ASTM D698 Moisture: ± 3% of optimum
Top 1-foot of pavement subgrade	98 percent of ASTM D698 Moisture: ± 2% of optimum
Fills below 1-foot of pavement subgrade	95 percent of ASTM D698 Moisture: ± 3% of optimum

Backfill placed in confined areas, such as foundation and utility excavations, should be spread in thinner layers and compacted to the same degree using manually operated compaction equipment.

All compactive effort should be verified by in-place density testing by a representative of GTA. The 2018/2021 IBC requires that fill subgrades and each lift of fill be observed and tested.

Foundations

The proposed school and field house buildings may be supported on shallow spread footings designed for a maximum net allowable bearing pressure of 3,000 pounds per square foot (psf). Minimum widths for wall footings of 24 inches and column footings of 36 inches are recommended when design based on 3,000 psf results in a narrower footing. For the school building, settlement on

the order of 1-inch total and ½-inch differential can be anticipated, based on the assumed loads of 3 to 5 kips per linear foot for walls and maximum column loads of 100 to 150 kips. For the field house, settlement on the order of ¾-inch total and ½ inch differential can be anticipated, based on the assumed loads of 2 kips per linear foot for walls and 75 kips for columns. Exterior footings should be founded a minimum of 32 inches below the final exterior grades to provide protection from frost action.

Footings should be supported on new compacted structural fill or medium dense/stiff natural soils. If loose or soft natural soils or undocumented, uncontrolled fill are encountered at the footing subgrade elevation, these soils should be undercut to suitable materials. The undercut volume should be backfilled with compacted structural fill, AASHTO No. 57 aggregate, or additional concrete. The aggregate should be placed in 1- to 2-foot-thick layers and be tamped with the equipment bucket with the last lift compacted with a small walk behind vibratory roller or large vibra-plate. GTA recommends that footing excavations be filled with concrete the same day the excavations are performed to prevent destabilization and softening of the subgrade soils.

Detailed foundation excavation evaluations should be performed in each footing excavation prior to the placement of crushed stone, reinforcing steel, or concrete. These evaluations should be performed by a representative of the registered Geotechnical Engineer to confirm that the design allowable soil bearing pressure is available. The foundation bearing surface evaluations should be performed using a combination of visual observation, hand-rod probing, comparison with the borings, and Dynamic Cone Penetrometer (DCP) testing, as applicable.

Seismic Information

Based on the SPT data, and the site geologic profile, the site should be assigned to Site Class D, in accordance with *Chapter 20 of the American Society of Civil Engineers (ASCE) Standard 7-20 Minimum Design Loads for Buildings and Other Structures* and *2018/2021 International Building Code*. This categorization is based on the near surface test boring results, general geologic information for the region, and the information contained in the standard.

Floor Slabs

Where floor slab loads are 100 psf or less, the floor slab can be designed as a concrete slab

on-grade using a design modulus of subgrade reaction (k) of 175 pounds per cubic inch (pci). GTA recommends that the concrete floor slabs supported on grade be founded on a 6-inch (minimum) thickness coarse granular layer. A vapor retarder should be used in occupied spaces with moisture sensitive floor finished to interrupt the rise of capillary moisture through the slab. Crushed stone or washed gravel meeting the gradation of AASHTO Size No. 57 or dense-graded aggregate can be used for the granular layer. The slabs may bear on footing projections; however, they should be jointed so that the foundations can settle without affecting the slab.

Utility and footing backfill below floor slabs should meet the compaction requirements specified herein. Open trenches should be backfilled at the end of the day with suitable structural fill, and trenches should not remain open to the elements or instability will occur. Construction activities and exposure to weather often cause deterioration of slab subgrades. The plumbing, masonry, and foundation subcontractors should exercise care prior to floor slab preparation to limit disturbance to exposed subgrades turned over to the general contractor by the earthwork contractor. It will be each subcontractors responsible to "dress" their work area and fine-grade upon completion of each's day work. Each subcontractor will be responsible for returning the slab subgrade to the approved, stable condition it was prior to the start of their work.

We recommend that the slab subgrade soils be evaluated by a representative of the Geotechnical Engineer immediately prior to stone and concrete placement. This evaluation may include a combination of visual observations, hand-rod probing, and field density tests to verify that the subgrade soils have been prepared properly. It is unlikely that proofrolling will be possible across the majority of the pad due to plumbing stick-ups and interior bearing walls, therefore observation will be mostly visual methods. If soft or loose soils, ice, or muddy conditions are encountered, recommendations for remedial measures should be provided by the Geotechnical Engineer at the time construction is performed prior to placement of stone.

Utility and footing backfill below floor slabs should meet the compaction requirements specified herein. Depending on depth of trench and bedding and cover over pipe, light weight hand operated compaction equipment may need to be utilized. Lifts within these trenches should not exceed 6-inch loose thickness.

Subsurface Utilities

The natural soils are considered suitable for support of the subsurface utilities. However, if loose/soft soils are encountered, it may be necessary to undercut the subgrade and provide a minimum 6-inch-thick granular bedding to provide uniform support, as dictated by site conditions. Backfill for the new structures should be free of organic material, rubble, and other deleterious materials. New subsurface utilities that run parallel to foundations should be set so that they fall outside of the zone of influence of the foundations (1H:1V) and conform to the plumbing code specifications.

Water was encountered at depths ranging from approximately 8 to 17 feet below existing grades within the explorations and is not anticipated to impact construction of shallower utilities. However, seepage may impact utility construction especially during the wet season or periods of prolonged precipitation. Problems associated with seepage into the excavation include loss of stability, sidewall collapse, and sloughing of soils. These problems can be reduced through the use of dewatering techniques. Dewatering through the use of "sump and pump" techniques may be required in some areas to remove perched or trapped water seepage.

All construction excavations should be sloped and shored in accordance with OSHA excavation regulations or stricter local governing safety codes. It is our opinion that the undisturbed natural soils would generally be classified as "Type C" soils under the OSHA excavation regulations. Significantly flatter excavation side-slopes will be required where groundwater seepage occurs. Utility pipe systems below pavement and other structural areas should be backfilled using controlled fill compacted in accordance with the *Site Grading* section of this report.

Pavements

GTA recommends that the upper 12 to 18 inches of roadway subgrade be constructed with the following characteristics if possible:

PAVEMENT SUBGRADE SPECIFICATIONS

Liquid Limit	35 percent or less

Plasticity Index	15 percent or less
Maximum Dry Density	110 pcf or greater
California Bearing Ratio	5 or greater

The fine-grained surface soils and on-site material to be used for fill are relatively weak and some of the materials are not expected to be suitable as pavement subgrade. Therefore, all pavement subgrade areas should be proof-rolled and evaluated for stability and to determine if they meet the specifications above. Soils that are unstable or unsuitable, will need to be stabilized for pavement support. Soils can be selectively excavated, and the resultant excavations backfilled with controlled, compacted fill or reworked, dried, and recompacted.

Prepared subgrades soils may become disturbed and softened from excess moisture and construction equipment traffic. Contractors should anticipate that remedial work could be required to achieve a stable subgrade prior to paving, even if the subgrade soils had previously been compacted to the required densities. Prudent planning and earthwork procedures will reduce the potential necessity for remedial work.

Heavy construction traffic should not be allowed on partial pavement sections since such traffic can damage the pavement. The paving contractor should be advised that they must control construction traffic to limit disturbance of previously approved subgrade, stone base course, or completed asphalt. Some patching and repair may be necessary prior to placement of the final wearing surface layer of asphalt due to construction traffic.

Proper drainage will be an important consideration for the overall performance of the pavement. Proper grading should be provided for suitable runoff from the pavement surface and beyond the limits of the paved areas. Underdrains should be considered to extend the life of the bituminous concrete pavements.

ADDITIONAL SERVICES

We recommend that during final design and construction of the subject project, a geotechnical engineer be retained to provide services for the following items.

- Perform supplemental testing including infiltration testing to confirm with local, and state regulations.
- Review final site, structural plans, and specifications to evaluate if they conform with the intent of this report.
- Review excavated footings for compliance with the project drawings and the intent of this geotechnical report.
- Provide observation and testing services during wall construction to evaluate if the earthwork is being performed in accordance with the intent of this report and project plans and specifications.
- Provide other Special Inspections as required by the project specifications and the New Castle County Department of Land Use.

LIMITATIONS

This report, including all supporting exploration logs, field data, field notes, calculations, estimates and other documents prepared by GTA in connection with this Project have been prepared for the exclusive use of New Castle County Vo-tech School District (Client) pursuant to agreements between GTA and Client in accordance with generally accepted engineering practice. All terms and conditions set forth in the Agreement and the General Provisions attached thereto are incorporated herein by reference. No warranty, express or implied, is made herein. Use and reproduction of this report by any other person without the expressed written permission of GTA and Client is unauthorized and such use is at the sole risk of the user.

The analysis and recommendations contained in this report are based on the data obtained from limited observation and testing of the encountered materials. Explorations indicate soil conditions only at specific locations and times, and only at the depths penetrated. They do not necessarily reflect strata or variations that may exist between test boring locations. Consequently, the analysis and recommendations must be considered preliminary until the subsurface conditions can be verified by direct observation at the time of construction. If variations of subsurface conditions from those described in this report are noted during construction, recommendations in this report may need to be re-evaluated.

In the event that any changes in the nature, design, or location of the facilities are planned, the conclusions and recommendations contained in this report should not be considered valid unless the changes are reviewed and conclusions of this report are verified in writing. Geo-Technology Associates, Inc. is not responsible for any claims, damages, or liability associated with interpretation of subsurface data or reuse of the subsurface data or engineering analysis without the expressed written authorization of Geo-Technology Associates, Inc.

The scope of our services for this geotechnical exploration did not include any environmental assessment or investigation for the presence or absence of wetlands, or hazardous or toxic materials in the soil, surface water, groundwater or air, on or below or around this site. Any statements in this report or on the logs regarding odors or unusual or suspicious items or conditions observed are strictly for the information of our Client.

This report and the attached logs are instruments of service. The subject matter of this report is limited to the facts and matters stated herein. Absence of a reference to any other conditions or subject matter shall not be construed by the reader to imply approval by the writer.

220791 **GEO-TECHNOLOGY ASSOCIATES, INC.**

Important Information about This

Geotechnical-Engineering Report

Subsurface problems are a principal cause of construction delays, cost overruns, claims, and disputes.

While you cannot eliminate all such risks, you can manage them. The following information is provided to help.

The Geoprofessional Business Association (GBA) has prepared this advisory to help you – assumedly a client representative – interpret and apply this geotechnical-engineering report as effectively as possible. In that way, you can benefit from a lowered exposure to problems associated with subsurface conditions at project sites and development of them that, for decades, have been a principal cause of construction delays, cost overruns, claims, and disputes. If you have questions or want more information about any of the issues discussed herein, contact your GBA-member geotechnical engineer. Active engagement in GBA exposes geotechnical engineers to a wide array of risk-confrontation techniques that can be of genuine benefit for everyone involved with a construction project.

Understand the Geotechnical-Engineering Services Provided for this Report

Geotechnical-engineering services typically include the planning, collection, interpretation, and analysis of exploratory data from widely spaced borings and/or test pits. Field data are combined with results from laboratory tests of soil and rock samples obtained from field exploration (if applicable), observations made during site reconnaissance, and historical information to form one or more models of the expected subsurface conditions beneath the site. Local geology and alterations of the site surface and subsurface by previous and proposed construction are also important considerations. Geotechnical engineers apply their engineering training, experience, and judgment to adapt the requirements of the prospective project to the subsurface model(s). Estimates are made of the subsurface conditions that will likely be exposed during construction as well as the expected performance of foundations and other structures being planned and/or affected by construction activities.

The culmination of these geotechnical-engineering services is typically a geotechnical-engineering report providing the data obtained, a discussion of the subsurface model(s), the engineering and geologic engineering assessments and analyses made, and the recommendations developed to satisfy the given requirements of the project. These reports may be titled investigations, explorations, studies, assessments, or evaluations. Regardless of the title used, the geotechnical-engineering report is an engineering interpretation of the subsurface conditions within the context of the project and does not represent a close examination, systematic inquiry, or thorough investigation of all site and subsurface conditions.

Geotechnical-Engineering Services are Performed for Specific Purposes, Persons, and Projects, and At Specific Times

Geotechnical engineers structure their services to meet the specific needs, goals, and risk management preferences of their clients. A geotechnical-engineering study conducted for a given civil engineer will not likely meet the needs of a civil-works constructor or even a different civil engineer. Because each geotechnical-engineering study is unique, each geotechnical-engineering report is unique, prepared *solely* for the client.

Likewise, geotechnical-engineering services are performed for a specific project and purpose. For example, it is unlikely that a geotechnical-engineering study for a refrigerated warehouse will be the same as one prepared for a parking garage; and a few borings drilled during a preliminary study to evaluate site feasibility will not be adequate to develop geotechnical design recommendations for the project.

Do not rely on this report if your geotechnical engineer prepared it:

- for a different client;
- for a different project or purpose;
- for a different site (that may or may not include all or a portion of the original site); or
- before important events occurred at the site or adjacent to it; e.g., man-made events like construction or environmental remediation, or natural events like floods, droughts, earthquakes, or groundwater fluctuations.

Note, too, the reliability of a geotechnical-engineering report can be affected by the passage of time, because of factors like changed subsurface conditions; new or modified codes, standards, or regulations; or new techniques or tools. *If you are the least bit uncertain* about the continued reliability of this report, contact your geotechnical engineer before applying the recommendations in it. A minor amount of additional testing or analysis after the passage of time – if any is required at all – could prevent major problems.

Read this Report in Full

Costly problems have occurred because those relying on a geotechnical-engineering report did not read the report in its entirety. Do not rely on an executive summary. Do not read selective elements only. *Read and refer to the report in full.*

You Need to Inform Your Geotechnical Engineer About Change

Your geotechnical engineer considered unique, project-specific factors when developing the scope of study behind this report and developing the confirmation-dependent recommendations the report conveys. Typical changes that could erode the reliability of this report include those that affect:

- the site's size or shape;
- the elevation, configuration, location, orientation, function or weight of the proposed structure and the desired performance criteria;
- the composition of the design team; or
- project ownership.

As a general rule, *always* inform your geotechnical engineer of project or site changes – even minor ones – and request an assessment of their impact. *The geotechnical engineer who prepared this report cannot accept*

responsibility or liability for problems that arise because the geotechnical engineer was not informed about developments the engineer otherwise would have considered.

Most of the "Findings" Related in This Report Are Professional Opinions

Before construction begins, geotechnical engineers explore a site's subsurface using various sampling and testing procedures. *Geotechnical engineers can observe actual subsurface conditions only at those specific locations where sampling and testing is performed.* The data derived from that sampling and testing were reviewed by your geotechnical engineer, who then applied professional judgement to form opinions about subsurface conditions throughout the site. Actual sitewide-subsurface conditions may differ – maybe significantly – from those indicated in this report. Confront that risk by retaining your geotechnical engineer to serve on the design team through project completion to obtain informed guidance quickly, whenever needed.

This Report's Recommendations Are Confirmation-Dependent

The recommendations included in this report – including any options or alternatives – are confirmation-dependent. In other words, they are not final, because the geotechnical engineer who developed them relied heavily on judgement and opinion to do so. Your geotechnical engineer can finalize the recommendations *only after observing actual subsurface conditions* exposed during construction. If through observation your geotechnical engineer confirms that the conditions assumed to exist actually do exist, the recommendations can be relied upon, assuming no other changes have occurred. *The geotechnical engineer who prepared this report cannot assume responsibility or liability for confirmation-dependent recommendations if you fail to retain that engineer to perform construction observation.*

This Report Could Be Misinterpreted

Other design professionals' misinterpretation of geotechnical-engineering reports has resulted in costly problems. Confront that risk by having your geotechnical engineer serve as a continuing member of the design team, to:

- confer with other design-team members;
- help develop specifications;
- review pertinent elements of other design professionals' plans and specifications; and
- be available whenever geotechnical-engineering guidance is needed.

You should also confront the risk of constructors misinterpreting this report. Do so by retaining your geotechnical engineer to participate in prebid and preconstruction conferences and to perform construction-phase observations.

Give Constructors a Complete Report and Guidance

Some owners and design professionals mistakenly believe they can shift unanticipated-subsurface-conditions liability to constructors by limiting the information they provide for bid preparation. To help prevent the costly, contentious problems this practice has caused, include the complete geotechnical-engineering report, along with any attachments or appendices, with your contract documents, *but be certain to note conspicuously that you've included the material for information purposes only.* To avoid misunderstanding, you may also want to note that "informational purposes" means constructors have no right to rely on the interpretations, opinions, conclusions, or recommendations in the report. Be certain that constructors know they may learn about specific project requirements, including options selected from the report, *only* from the design drawings and specifications. Remind constructors that they may perform their own studies if they want to, and *be sure to allow enough time* to permit them to do so. Only then might you be in a position to give constructors the information available to you, while requiring them to at least share some of the financial responsibilities stemming from unanticipated conditions. Conducting prebid and preconstruction conferences can also be valuable in this respect.

Read Responsibility Provisions Closely

Some client representatives, design professionals, and constructors do not realize that geotechnical engineering is far less exact than other engineering disciplines. This happens in part because soil and rock on project sites are typically heterogeneous and not manufactured materials with well-defined engineering properties like steel and concrete. That lack of understanding has nurtured unrealistic expectations that have resulted in disappointments, delays, cost overruns, claims, and disputes. To confront that risk, geotechnical engineers commonly include explanatory provisions in their reports. Sometimes labeled "limitations," many of these provisions indicate where geotechnical engineers' responsibilities begin and end, to help others recognize their own responsibilities and risks. *Read these provisions closely.* Ask questions. Your geotechnical engineer should respond fully and frankly.

Geoenvironmental Concerns Are Not Covered

The personnel, equipment, and techniques used to perform an environmental study – e.g., a "phase-one" or "phase-two" environmental site assessment – differ significantly from those used to perform a geotechnical-engineering study. For that reason, a geotechnical-engineering report does not usually provide environmental findings, conclusions, or recommendations; e.g., about the likelihood of encountering underground storage tanks or regulated contaminants. *Unanticipated subsurface environmental problems have led to project failures.* If you have not obtained your own environmental information about the project site, ask your geotechnical consultant for a recommendation on how to find environmental risk-management guidance.

Obtain Professional Assistance to Deal with Moisture Infiltration and Mold

While your geotechnical engineer may have addressed groundwater, water infiltration, or similar issues in this report, the engineer's services were not designed, conducted, or intended to prevent migration of moisture – including water vapor – from the soil through building slabs and walls and into the building interior, where it can cause mold growth and material-performance deficiencies. Accordingly, ***proper implementation of the geotechnical engineer's recommendations will not of itself be sufficient to prevent moisture infiltration. Confront the risk of moisture infiltration*** by including building-envelope or mold specialists on the design team. ***Geotechnical engineers are not building-envelope or mold specialists.***

GEOPROFESSIONAL BUSINESS ASSOCIATION

Telephone: 301/565-2733
e-mail: info@geoprofessional.org www.geoprofessional.org

Copyright 2019 by Geoprofessional Business Association (GBA). Duplication, reproduction, or copying of this document, in whole or in part, by any means whatsoever, is strictly prohibited, except with GBA's specific written permission. Excerpting, quoting, or otherwise extracting wording from this document is permitted only with the express written permission of GBA, and only for purposes of scholarly research or book review. Only members of GBA may use this document or its wording as a complement to or as an element of a report of any kind. Any other firm, individual, or other entity that so uses this document without being a GBA member could be committing negligent

APPENDIX A



Notes:

1) Base map obtained from Google Earth Imagery, Inc. from June 24, 2022.
2) Site Location Map should be reviewed in conjunction with GTA Report NCCVT New Hodgson Vo-tech High School, Job No. 220791

N


GEO-TECHNOLOGY ASSOCIATES, INC.
Geotechnical and Environmental Consultants
18 Boulden Circle, Suite 36
New Castle, Delaware 19720
(302) 326-2100

SITE LOCATION MAP

NCCVT NEW HODGSON VO-TECH HIGH SCHOOL

NEW CASTLE COUNTY, DELAWARE

SCALE	DATE	DRAWN BY	REVIEW BY	JOB NO.	FIGURE NO.
NTS	FEB 2023	GOOGLE	MM	220791	1

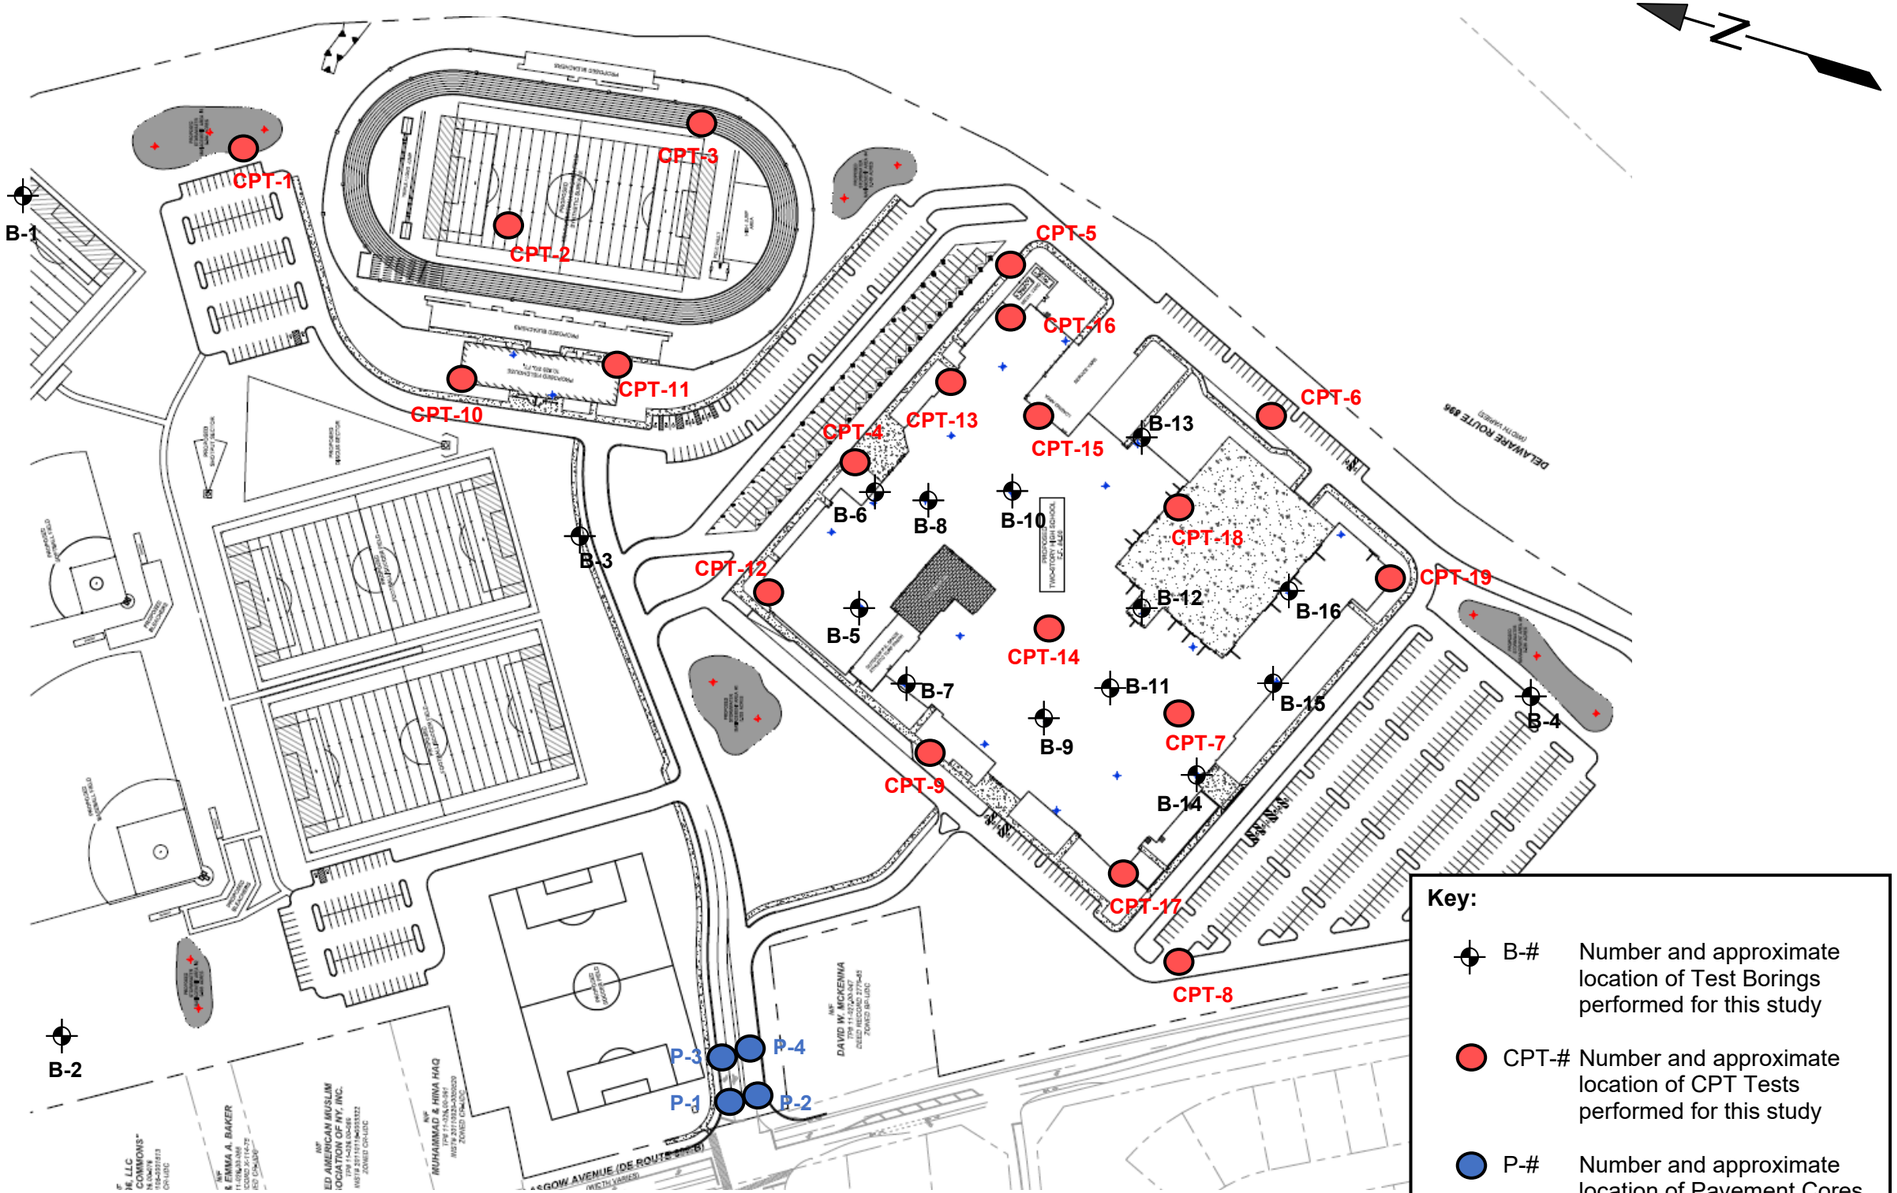

Notes: (1) Base map prepared by Landmark Science and Engineering and use of this diagram by GTA is limited to illustration of the approximate locations of our explorations.
(2) Exploration Location Plan should be read together with GTA Report NCCVT New Hodgson Vo-tech High School, Job No. 220791 for complete evaluation. Use of the diagram is limited illustration of the approximate locations of the explorations.
(3) The approximate locations of the explorations were measured from site features and should be considered accurate to the degree implied by this method.

JOB NUMBER.:
220791

FIGURE:
2

REVIEW BY:
MM

SCALE:
NTS

DATE:
FEB 2023

EXPLORATION LOCATION PLAN
NCCVT
NEW HODGSON VO-TECH HIGH SCHOOL
NEW CASTLE COUNTY, DELAWARE

GEO-TECHNOLOGY ASSOCIATES, INC.
Geotechnical and Environmental Consultants
18 Boulden Circle, Suite 3'6
New Castle, Delaware 19720
(302) 326-2100

APPENDIX B

NOTES FOR EXPLORATION LOGS

KEY TO USCS TERMINOLOGY AND GRAPHIC SYMBOLS

MAJOR DIVISIONS (BASED UPON ASTM D 2488)			SYMBOLS GRAPHIC	SYMBOLS LETTER
COARSE - GRAINED SOILS MORE THAN 50% OF MATERIAL IS LARGER THAN NO. 200 SIEVE SIZE	GRAVEL AND GRAVELY SOILS MORE THAN 50% OF COARSE FRACTION RETAINED ON NO. 4 SIEVE	CLEAN GRAVELS (LESS THAN 5% PASSING THE NO. 200 SIEVE)		GW
				GP
		GRAVELS WITH FINES (MORE THAN 15% PASSING THE NO. 200 SIEVE)		GM
				GC
	SAND AND SANDY SOILS MORE THAN 50% OF COARSE FRACTION PASSING ON NO. 4 SIEVE	CLEAN SANDS (LESS THAN 5% PASSING THE NO. 200 SIEVE)		SW
				SP
		SANDS WITH FINES (MORE THAN 15% PASSING THE NO. 200 SIEVE)		SM
				SC
FINE - GRAINED SOILS MORE THAN 50% OF MATERIAL IS SMALLER THAN NO. 200 SIEVE SIZE	SILTS AND CLAYS LIQUID LIMIT LESS THAN 50	SILT OR CLAY (<15% RETAINED THE NO. 200 SIEVE)		ML
		SILT OR CLAY WITH SAND OR GRAVEL (15% TO 30% RETAINED THE NO. 200 SIEVE)		CL
		SANDY OR GRAVELY SILT OR CLAY (>30% RETAINED THE NO. 200 SIEVE)		OL
	SILTS AND CLAYS LIQUID LIMIT GREATER THAN 50	SILT OR CLAY (<15% RETAINED THE NO. 200 SIEVE)		MH
		SILT OR CLAY WITH SAND OR GRAVEL (15% TO 30% RETAINED THE NO. 200 SIEVE)		CH
		SANDY OR GRAVELY SILT OR CLAY (>30% RETAINED THE NO. 200 SIEVE)		OH
HIGHLY ORGANIC SOILS				PT

NOTE: DUAL SYMBOLS ARE USED TO INDICATE COARSE-GRAINED SOILS CONTAINING AN ESTIMATED 10% FINES BY VISUAL CLASSIFICATION OR WHEN THE SOIL HAS BETWEEN 5 AND 12 PERCENT FINES FROM LABORATORY TESTS; AND FOR FINE-GRAINED SOILS WHEN THE PLOT OF LIQUID LIMIT & PLASTICITY INDEX VALUES FALLS IN THE PLASTICITY CHART'S CROSSHATCHED AREA. RESULTS OF LABORATORY TESTING ARE USED TO SUPPLEMENT THE CLASSIFICATION OF THE SOILS BASED ON THE VISUAL-MANUAL PROCEDURES OF ASTM D2488.

ADDITIONAL TERMINOLOGY AND GRAPHIC SYMBOLS

	DESCRIPTION		GRAPHIC SYMBOLS
ADDITIONAL DESIGNATION	TOPSOIL		
	MAN-MADE FILL		
	GLACIAL TILL		
	COBBLES AND BOULDERS		
RESIDUAL SOIL DESIGNATION	DESCRIPTION	"N" VALUE	
	HIGHLY WEATHERED ROCK	50 TO 50/1"	
	PARTIALLY WEATHERED ROCK	MORE THAN 50 BLOWS FOR 1" PENETRATION, AUGER PENETRABLE	

COARSE-GRAINED SOILS
(GRAVEL AND SAND)

DESIGNATION	BLOWS PER FOOT (BPF) "N"
VERY LOOSE	0 - 4
LOOSE	5 - 10
MEDIUM DENSE	11 - 30
DENSE	31 - 50
VERY DENSE	>50

NOTE: "N" VALUE DETERMINED AS PER ASTM D1586

FINE-GRAINED SOILS
(SILT AND CLAY)

CONSISTENCY	BPF "N"
VERY SOFT	<2
SOFT	2 - 4
MEDIUM STIFF	5 - 8
STIFF	9 - 15
VERY STIFF	16 - 30
HARD	>30

NOTE: ADDITIONAL DESIGNATIONS TO ADVANCE SAMPLER INDICATED IN BLOW COUNT COLUMN:
WOH = WEIGHT OF HAMMER
WOR = WEIGHT OF ROD(S)

SAMPLE TYPE

DESIGNATION	SYMBOL
SPLIT-SPOON	S-
SHELBY TUBE	U-
ROCK CORE	R-

WATER DESIGNATION

DESCRIPTION	SYMBOL
ENCOUNTERED DURING DRILLING	▽
UPON COMPLETION OF DRILLING	▼
24 HOURS AFTER COMPLETION	⧩

NOTE: WATER OBSERVATIONS WERE MADE AT THE TIME INDICATED. POROSITY OF SOIL STRATA, WEATHER CONDITIONS, SITE TOPOGRAPHY, ETC. MAY CAUSE WATER LEVEL CHANGES.

LOG OF BORING NO. B-1

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	12.7	Dry	BOC
DATE:	4/20/22	4/20/22	
CAVED (ft):	In Augers	9.0	

DATE STARTED: **4/20/22**
DATE COMPLETED: **4/20/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **13.0**
GROUND SURFACE ELEVATION: **77.0**
DATUM: **Google Earth**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **A. Carta**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					77.0	0			Topsoil +/- 6 Inches	
S-1	0.0	10	1-2-1-2	3	76.5		FILL		Dark brown, moist, soft, sandy silt FILL	
S-2	2.0	19	3-6-5-4	11	75.0		ML		Light brown, moist, stiff, Sandy SILT	
S-3	4.0	19	1-2-1-2	3	73.0	5	CL		Tan, moist, soft, Sandy Lean CLAY	
S-4	6.0	19	2-3-5-5	8	71.0		SM		Light tan, moist, loose, Silty SAND, contains gravel	
S-5	8.0	16	1-3-4-4	7					Same	
						10				
S-6	13.0	21	2-4-3-3	7					Same, wet	▽
						15				
S-7	18.0	20	2-3-5-5	8					Brown, moist, loose, Silty SAND, contains gravel	
					57.0	20			Boring terminated at 20.0 feet.	
						25				

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-1

LOG OF BORING NO. B-2

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	12.7	Dry	BOC
DATE:	4/20/22	4/20/22	
CAVED (ft):	In Augers	9.0	

DATE STARTED: **4/20/22**
DATE COMPLETED: **4/20/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **13.0**
GROUND SURFACE ELEVATION: **78.0**
DATUM: **Google Earth**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **A. Carta**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					78.0	0			Topsoil +/- 7 Inches	
S-1	0.0	18	1-2-3-5	5	77.4		FILL		Brown, moist, sandy SILT FILL	
S-2	2.0	14	4-4-3-3	7	76.0		SC		Tan, moist, loose, Clayey SAND, contains gravel	
S-3	4.0	19	3-5-5-6	10	74.0	5	SM		Tan, moist, loose, Silty SAND	
S-4	6.0	17	3-5-5-6	10					Tan, moist, loose, Silty SAND	
S-5	8.0	21	4-5-5-4	10		10			Dark orange, moist, loose, Silty SAND, contains gravel	
S-6	13.0	16	2-3-5-4	8	65.0		SP-SM		Dark orange, wet, loose, Poorly-graded SAND with SILT, contains gravel	
						15				
S-7	18.0	24	2-3-3-4	6	60.0		SM		Dark orange, moist, loose, Silty SAND	
					58.0	20			Boring terminated at 20.0 feet.	
						25				

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-2

LOG OF BORING NO. B-3

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	13.0	Dry	BOC
DATE:	4/20/22	4/20/22	
CAVED (ft):	In Augers	7.9	

DATE STARTED: **4/20/22**
DATE COMPLETED: **4/20/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **13.0**
GROUND SURFACE ELEVATION: **78.0**
DATUM: **Google Earth**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **A. Carta**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					78.0	0			Topsoil +/- 6 Inches	
S-1	0.0	16	1-1-2-3	3	77.5		FILL		Dark brown and brown, moist, sandy SILT FILL	
S-2	2.0	22	3-6-9-11	15					Dark brown and brown, moist, stiff, sandy silt FILL, contains gravel	
					74.0					
S-3	4.0	19	1-5-3-4	8		5	ML		Tan, moist, medium stiff, Sandy SILT	
S-4	6.0	22	3-5-7-7	12					Same, stiff	
					70.0					
S-5	8.0	16	3-6-6-5	12			SM		Brown, moist, medium dense, Silty SAND, contains gravel	
						10				
S-6	13.0	18	2-3-4-4	7					Dark brown and brown, wet, loose, Silty SAND, contains gravel	▼
						15				
S-7	18.0	14	2-4-6-7	10					Brown, moist, loose, Silty SAND, contains gravel	
					58.0	20			Boring terminated at 20.0 feet.	
						25				

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-3

LOG OF BORING NO. B-4

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	7.2	5.7	BOC
DATE:	4/20/22	4/20/22	
CAVED (ft):	In Augers	5.9	

DATE STARTED: **4/20/22**
DATE COMPLETED: **4/20/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **8.0**
GROUND SURFACE ELEVATION: **81**
DATUM: **Google Earth**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **A. Carta**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
S-1	0.0	20	1-2-6-5	8	81.0 80.7	0	SC		Topsoil +/- 4 Inches Tan, moist, loose, Clayey SAND	
S-2	2.0	18	2-4-6-8	10					Same	
S-3	4.0	20	3-3-5-6	8		5			Same, brown	
S-4	6.0	21	5-7-6-6	13					Brown, moist, medium dense, Clayey SAND, contains gravel	
S-5	8.0	20	2-3-3-3	6	73.0		SM		Brown, wet, loose, Silty SAND, contains gravel	
						10				
S-6	13.0	24	1-4-5-5	9	68.0		SP-SM		Brown, moist, loose, Poorly-graded SAND with SILT, contains gravel	
						15				
S-7	18.0	24	2-3-3-3	6					Same	
					61.0	20			Boring terminated at 20.0 feet.	
						25				

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-4

LOG OF BORING NO. B-5

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	20.2	Dry	BOC
DATE:	12/21/22	12/21/22	
CAVED (ft):	In Augers	11.3	

DATE STARTED: **12/21/22**
DATE COMPLETED: **12/21/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **15.0**
GROUND SURFACE ELEVATION: **83.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					83.0	0			Topsoil +/- 9 Inches	
S-1	0.0	12	1-1-3-2	4	82.2		FILL		Brown, moist, soft, sandy silt FILL, contains organic material	
S-2	2.0	13	2-3-3-3	6	81.0		SC		Brown, moist, loose, Clayey SAND, contains gravel	
S-3	4.0	16	2-4-5-8	9	79.0	5	SM		Dark gray, moist, loose, Silty SAND	
S-4	6.0	15	3-6-6-7	12	77.0		SP-SM		Brown, moist, medium dense, Poorly-graded SAND with Silt, contains gravel	
S-5	8.0	19	2-3-3-6	6	75.0	10	CL		Gray and brown, moist, medium stiff, Lean CLAY with Sand	
S-6	13.0	21	2-2-4-5	6	70.0		SM		Orange-brown, wet, loose, Silty SAND, contains gravel	
S-7	18.0	15	1-2-4-6	6		15			Orange, moist, loose, Silty SAND, contains gravel	
S-8	23.0	24	5-5-5-6	10		20			Same	
					58.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-5

LOG OF BORING NO. B-6

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	17.7	9.5	BOC
DATE:	12/29/22	12/29/22	
CAVED (ft):	In Augers	11.5	

DATE STARTED: **12/29/22**
DATE COMPLETED: **12/29/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **13.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 6 Inches	
S-1	0.0	16	2-2-2-2	4	81.5		ML		Brown, moist, soft, Sandy SILT	
S-2	2.0	15	2-2-3-2	5					Brown, moist, medium stiff, Sandy SILT, contains gravel	
S-3	4.0	15	1-1-2-5	3	78.0	5	CL		Dark brown, moist, soft, Sandy Lean CLAY, contains gravel	
S-4	6.0	20	8-5-6-6	11	76.0		ML		Gray and orange, moist, stiff, SILT with sand, contains gravel	
S-5	8.0	17	2-3-6-7	9	74.0		CL		Gray and orange, moist, stiff, Sandy Lean CLAY, contains gravel	▽
						10				
					69.0		SM		Orange, wet, very loose, Silty SAND, contains gravel	▽
S-6	13.0	16	1-2-2-2	4						
						15				
S-7	18.0	24	2-1-2-2	3					Tan, moist, very loose, Silty SAND	▽
						20				
S-8	23.0	11	2-3-6-9	9					Brown, moist, loose, Silty SAND	
					57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-6

LOG OF BORING NO. B-7

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	16.7	Dry	BOC
DATE:	12/21/22	12/21/22	
CAVED (ft):	In Augers	9.7	

DATE STARTED: **12/21/22**
DATE COMPLETED: **12/21/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 9 Inches	
S-1	0.0	18	1-2-2-4	4	81.2		FILL		Brown, moist, soft, silt with sand FILL	
					80.0		SM		Brown, moist, loose, Silty SAND	
S-2	2.0	20	2-3-4-3	7						
									Brown, moist, very loose, Silty SAND, contains gravel	
S-3	4.0	16	1-2-2-4	4		5				
									Tan, moist, medium dense, Silty SAND	
S-4	6.0	16	2-4-8-11	12						
					74.0		CL		Light brown and gray, moist, medium stiff, Lean CLAY with sand	
S-5	8.0	22	2-3-2-4	5		10				
					69.0		SM		Light brown, wet, very loose, Silty SAND	▽
S-6	13.0	14	2-1-3-3	4		15				
										▽
									Light brown, moist, loose, Silty SAND, contains gravel	
S-7	18.0	12	1-3-3-3	6		20				
					59.0		SP-SM		Orange-brown, moist, medium dense, Poorly-graded SAND with silt, contains gravel	
S-8	23.0	12	4-4-9-11	13	57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-7

LOG OF BORING NO. B-8

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	16.5	11.0	BOC
DATE:	12/29/22	12/29/22	
CAVED (ft):	In Augers	11.5	

DATE STARTED: **12/29/22**
DATE COMPLETED: **12/29/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 5 Inches	
S-1	0.0	15	1-2-2-1	4	81.6		FILL		Brown, moist, soft, sandy silt FILL, contains organic material	
					80.0		CL		Brown, moist, soft, Sandy Lean CLAY, contains gravel	
S-2	2.0	13	2-1-2-2	3						
S-3	4.0	14	1-2-2-3	4		5			Dark gray, moist, soft, Sandy Lean CLAY	
S-4	6.0	17	3-3-4-7	7					Gray and orange, medium stiff, Sandy Lean CLAY, contains gravel	
					74.0		SM		Brown, moist, loose, Silty SAND, contains gravel	
S-5	8.0	14	2-4-5-4	9		10				
S-6	13.0	18	1-1-1-2	2					Orange, moist, very loose, Silty SAND, contains gravel	
						15				
S-7	18.0	24	1-4-4-5	8					Light brown, moist, loose, Silty SAND, contains gravel	
						20				
S-8	23.0	24	3-4-6-7	10					Same, orange-brown	
					57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-8

LOG OF BORING NO. B-9

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	20.0	Dry	BOC
DATE:	12/19/22	12/19/22	
CAVED (ft):	In Augers	9.8	

DATE STARTED: **12/19/22**
DATE COMPLETED: **12/19/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **81.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					81.0	0			Topsoil +/- 8 Inches	
S-1	0.0	19	1-3-2-3	5	80.3		CL		Tan, moist, medium stiff, Lean CLAY, contains gravel and organic material	
S-2	2.0	13	2-6-7-9	13	79.0		ML		Gray and brown, moist, stiff, SILT	
S-3	4.0	24	3-6-9-9	15		5			Same, gray	
S-4	6.0	11	6-7-9-9	16					Gray, moist, very stiff, SILT, contains gravel	
S-5	8.0	21	1-1-2-3	3	73.0		SM		Tan and orange, moist, very loose, Silty SAND, contains gravel	
						10				
S-6	13.0	17	1-2-2-3	4					Light brown, wet, very loose, Silty SAND, contains gravel	▽
						15				
S-7	18.0	24	1-2-4-5	6					Brown, moist, loose, Silty SAND, contains gravel	
						20				▽
S-8	23.0	24	3-4-6-8	10					Same	
					56.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-9

LOG OF BORING NO. B-10

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	16.5	10.0	BOC
DATE:	12/29/22	12/29/22	
CAVED (ft):	In Augers	12.0	

DATE STARTED: **12/29/22**
DATE COMPLETED: **12/29/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **13.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 5 Inches	
S-1	0.0	14	1-2-2-2	4	81.6		FILL		Brown, moist, soft, sandy silt FILL, contains organic material	
S-2	2.0	22	3-4-6-6	10	80.0		SC		Brown, moist, loose, Clayey SAND, contains gravel	
S-3	4.0	18	2-4-2-6	6		5			Brown, moist, loose, Clayey SAND	
S-4	6.0	20	6-4-4-6	8					Same	
S-5	8.0	17	2-5-6-4	11	74.0		SM		Brown, moist, medium dense, Silty SAND, contains gravel	
						10				▽
S-6	13.0	17	1-3-3-3	6					Orange, wet, loose, Silty SAND	▽
						15				▽
S-7	18.0	24	1-2-3-5	5					Yellow-brown, moist, loose, Silty SAND, contains gravel	
						20				
S-8	23.0	24	3-4-7-9	11					Orange-brown, moist, medium dense, Silty SAND, contains gravel	
					57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-10

LOG OF BORING NO. B-11

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	16.0	Dry	BOC
DATE:	12/19/22	12/19/22	
CAVED (ft):	In Augers	9.8	

DATE STARTED: **12/19/22**
DATE COMPLETED: **12/19/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **81.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					81.0	0			Topsoil +/- 4 Inches	
S-1	0.0	21	1-3-2-3	5	80.7		CL		Brown, moist, medium stiff, Lean CLAY with sand	
					79.0		SM		Light brown, moist, loose, Silty SAND, contains gravel and clay	
S-2	2.0	16	1-3-6-6	9						
S-3	4.0	24	3-6-10-8	16		5			Brown, moist, medium dense, Silty SAND, contains gravel	
S-4	6.0	15	5-8-8-8	16					Same	
S-5	8.0	20	2-4-4-4	8					Same, loose	
						10				
S-6	13.0	18	1-3-3-3	6					Orange-brown, wet, loose, Silty SAND, contains gravel	▽
						15				▽
S-7	18.0	24	2-2-5-7	7					Light brown, moist, loose, Silty SAND	
						20				
S-8	23.0	24	6-8-11-12	19					Light brown, moist, medium dense, Silty SAND	
					56.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-11

LOG OF BORING NO. B-12

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	15.3	Dry	BOC
DATE:	12/21/22	12/21/22	
CAVED (ft):	In Augers	9.5	

DATE STARTED: **12/21/22**
DATE COMPLETED: **12/21/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 7 Inches	
S-1	0.0	12	1-2-4-3	6	81.4		ML		Brown, moist, medium stiff, SILT	
S-2	2.0	15	2-2-3-6	5					Same, contains gravel	
					78.0		SM		Light brown, moist, loose, Silty SAND	
S-3	4.0	17	2-3-4-7	7		5				
					76.0		SP-SM		Light brown, moist, medium dense, Poorly-graded SAND with Silt, contains gravel	
S-4	6.0	19	4-9-9-9	18						
					74.0		SM		Light brown, loose, Silty SAND, contains gravel	
S-5	8.0	16	2-3-3-4	6		10				
									Orange-brown, wet, loose, Silty SAND, contains gravel	▽
S-6	13.0	15	1-2-3-3	5		15				▽
									Same, moist	
S-7	18.0	24	1-2-3-4	5		20				
									Same, moist	
S-8	23.0	24	2-2-3-5	5						
					57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-12

LOG OF BORING NO. B-13

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	19.2	Dry	BOC
DATE:	12/29/22	12/29/22	
CAVED (ft):	In Augers	8.8	

DATE STARTED: **12/29/22**
DATE COMPLETED: **12/29/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 3 Inches	
S-1	0.0	13	1-2-1-1	3	81.8		FILL		Brown, moist, soft, sandy silt FILL, contains gravel	
S-2	2.0	22	4-4-5-5	9	80.0		SC		Brown, moist, loose, Clayey SAND, contains gravel	
S-3	4.0	13	1-1-2-2	3	78.0	5	SM		Tan, moist, very loose, Silty SAND	
S-4	6.0	19	2-4-7-7	11					Dark brown and tan, moist, medium dense, Silty SAND, contains gravel	
S-5	8.0	17	2-6-6-7	12					Same, orange-brown	
						10				
S-6	13.0	14	1-2-3-5	5					Orange, wet, loose, Silty SAND	▽
						15				
S-7	18.0	24	1-4-6-8	10					Orange-brown, moist, loose, Silty SAND, contains gravel	▽
						20				
S-8	23.0	24	2-3-6-7	9					Orange-brown, moist, loose, Silty SAND	
					57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-13

LOG OF BORING NO. B-14

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	15.0	Dry	BOC
DATE:	12/19/22	12/19/22	
CAVED (ft):	In Augers	9.0	

DATE STARTED: **12/19/22**
DATE COMPLETED: **12/19/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **14.0**
GROUND SURFACE ELEVATION: **82.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					82.0	0			Topsoil +/- 5 Inches	
S-1	0.0	18	1-1-2-5	3	81.6		FILL		Light brown, moist, very loose, sandy silt FILL, contains organic material	
					80.0		SC		Orange, moist, loose, Clayey SAND	
S-2	2.0	17	3-3-6-6	9						
									Same, contains gravel	
S-3	4.0	21	3-3-4-4	7		5				
									Same	
S-4	6.0	17	2-2-3-3	5						
					74.0		ML		Light brown, moist, medium stiff, Sandy SILT	
S-5	8.0	21	2-2-3-5	5		10				
					69.0		SM		Light brown, wet, loose, Silty SAND, contains gravel	
S-6	13.0	18	2-3-4-4	7						
						15				
									Same	
S-7	18.0	24	1-4-4-6	8						
						20				
									Same, medium dense	
S-8	23.0	24	4-5-7-8	12						
					57.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-14

LOG OF BORING NO. B-15

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	14.0	Dry	BOC
DATE:	12/19/22	12/19/22	
CAVED (ft):	In Augers	10.5	

DATE STARTED: **12/19/22**
DATE COMPLETED: **12/19/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **13.0**
GROUND SURFACE ELEVATION: **81.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					81.0	0			Topsoil +/- 12 Inches	
S-1	0.0	22	1-2-3-3	5	80.0		FILL		Dark brown, moist, medium stiff, silt with sand FILL	
S-2	2.0	9	2-2-5-5	7	79.0		CL		Tan, moist, medium stiff, Lean CLAY with sand	
S-3	4.0	21	3-8-8-10	16	77.0	5	SM		Light brown, moist, medium dense, Silty SAND, contains gravel	
S-4	6.0	11	4-6-8-8	14					Same	
S-5	8.0	17	2-4-5-4	9		10			Same, loose	
S-6	13.0	18	1-2-2-3	4		15			Light brown, wet, very loose, Silty SAND, contains gravel	
S-7	18.0	24	2-5-5-5	10		20			Light brown and dark brown, moist, loose, Silty SAND, contains gravel	
S-8	23.0	24	3-5-7-8	12					Same, light brown	
					56.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-15

LOG OF BORING NO. B-16

PROJECT: **NCCVT New Hodgson Vo-Tech High School**
PROJECT NO.: **220791**
PROJECT LOCATION: **New Castle County, Delaware**

WATER LEVEL (ft):	8.5	8.5	BOC
DATE:	12/19/22	12/19/22	
CAVED (ft):	In Augers	10.8	

DATE STARTED: **12/19/22**
DATE COMPLETED: **12/19/22**
DRILLING CONTRACTOR: **GTA**
DRILLER: **D. Hans, Jr.**
DRILLING METHOD: **Hollow Stem Auger**
SAMPLING METHOD: **Split Spoon**

WATER ENCOUNTERED DURING DRILLING (ft) **8.0**
GROUND SURFACE ELEVATION: **79.0**
DATUM: **Topo**
EQUIPMENT: **Diedrich D50**
LOGGED BY: **M.DiBartolomeo**
CHECKED BY: **M.McDonough**

SAMPLE NUMBER	SAMPLE DEPTH (ft.)	SAMPLE RECOVERY (in.)	SAMPLE BLOWS/6 inches	N (blows/ft.)	ELEVATION (ft.)	DEPTH (ft.)	USCS	GRAPHIC SYMBOL	DESCRIPTION	REMARKS
					79.0	0			Topsoil +/- 7 Inches	
S-1	0.0	21	1-2-7-9	9	78.4		SM		Orange-brown, moist, loose, Silty SAND, contains clay	
S-2	2.0	1	5-8-8-5	16					Orange-brown, moist, medium dense, Silty SAND	
S-3	4.0	15	3-6-7-5	13		5			Same, light brown	
S-4	6.0	15	4-6-7-7	13					Same, light brown	
S-5	8.0	16	2-3-5-4	8					Light brown, wet, loose, Silty SAND, contains gravel	▽
						10				
S-6	13.0	24	2-3-5-3	8					Same	
						15				
S-7	18.0	24	2-3-7-5	10					Same	
						20				
S-8	23.0	24	6-7-10-9	17					Light brown, moist, medium dense, Silty SAND, contains gravel	
					54.0	25			Boring terminated at 25.0 feet.	

NOTES: **Elevation and location should be considered approximate.**


GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

LOG OF BORING NO. B-16


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 1
Total depth: 29.20 ft, Date: 4/20/2022
Surface Elevation: 76.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

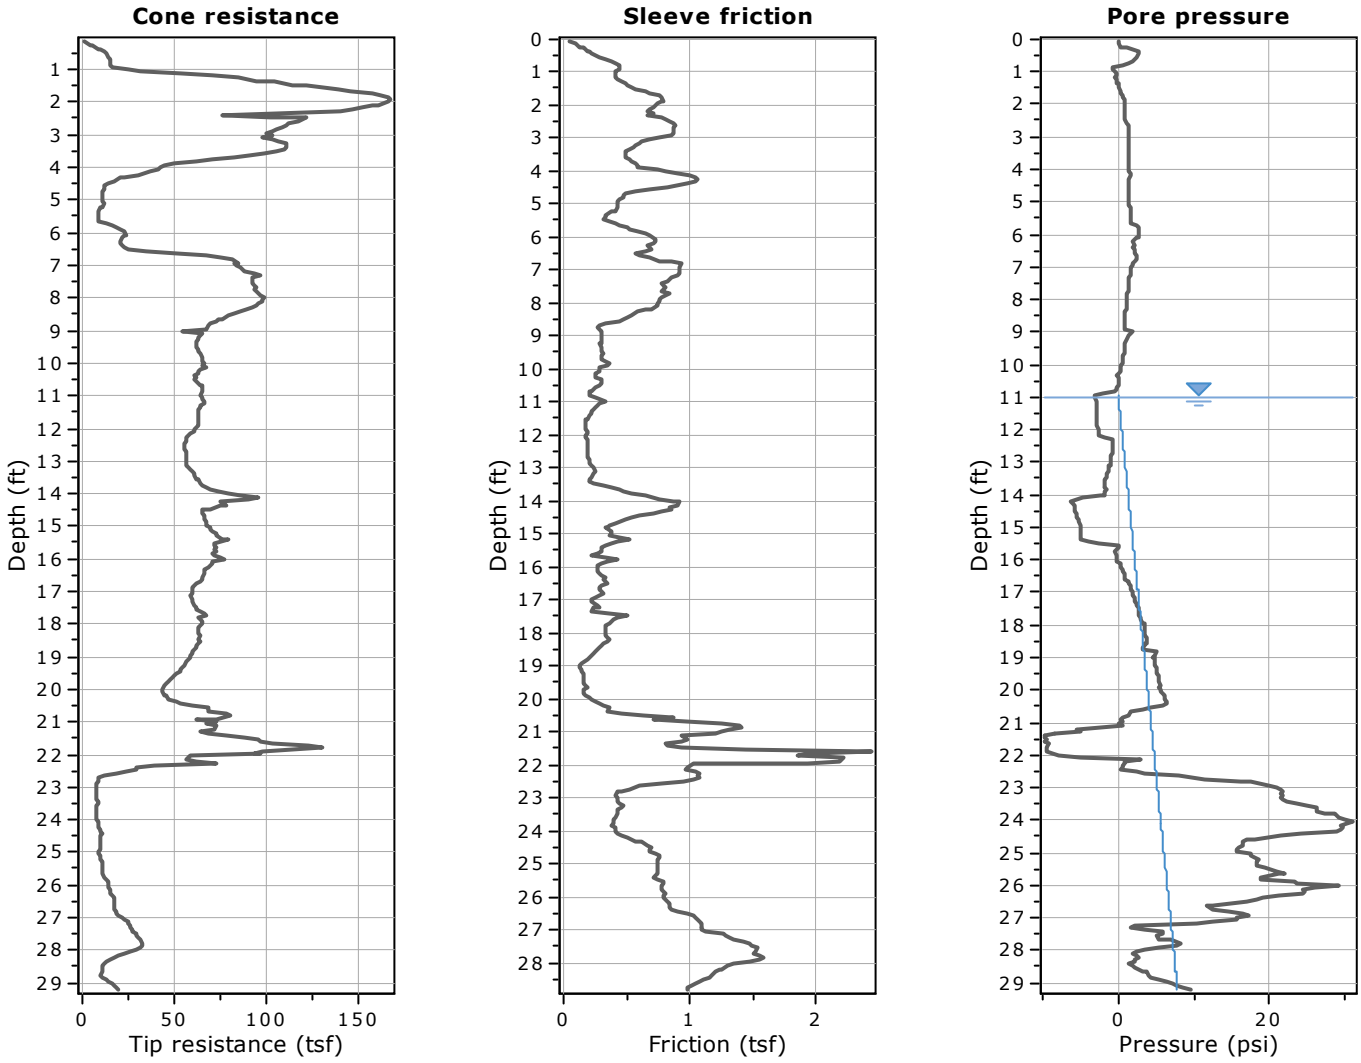


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

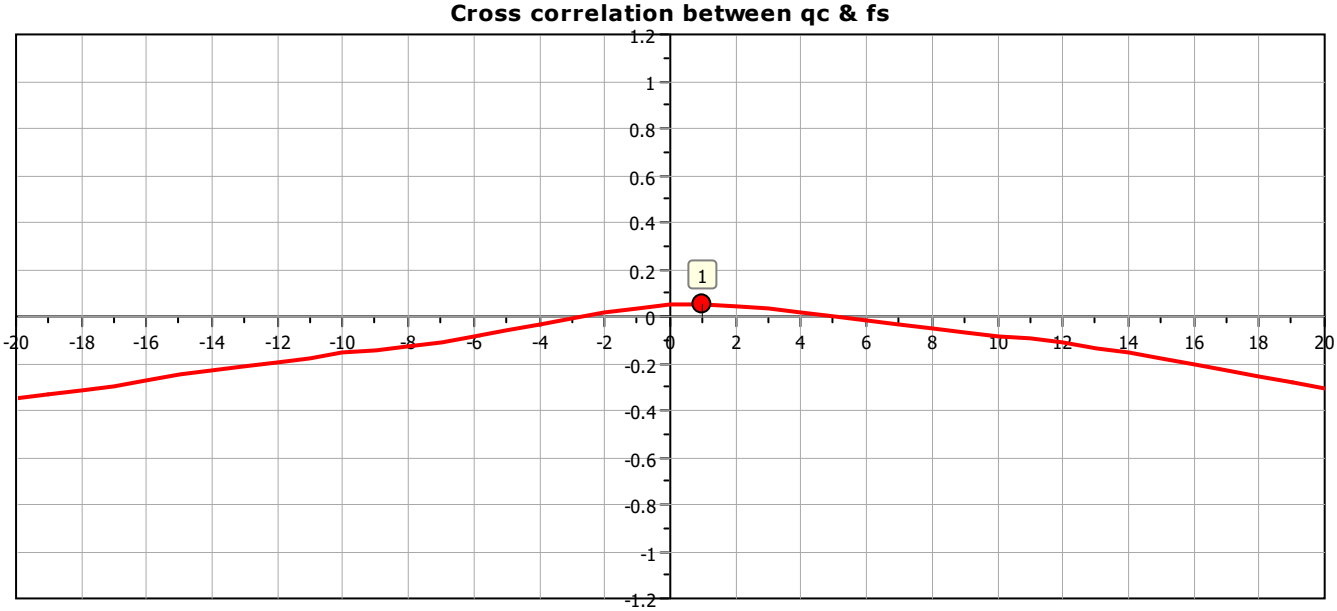

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 1
Total depth: 29.20 ft, Date: 4/20/2022
Surface Elevation: 76.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

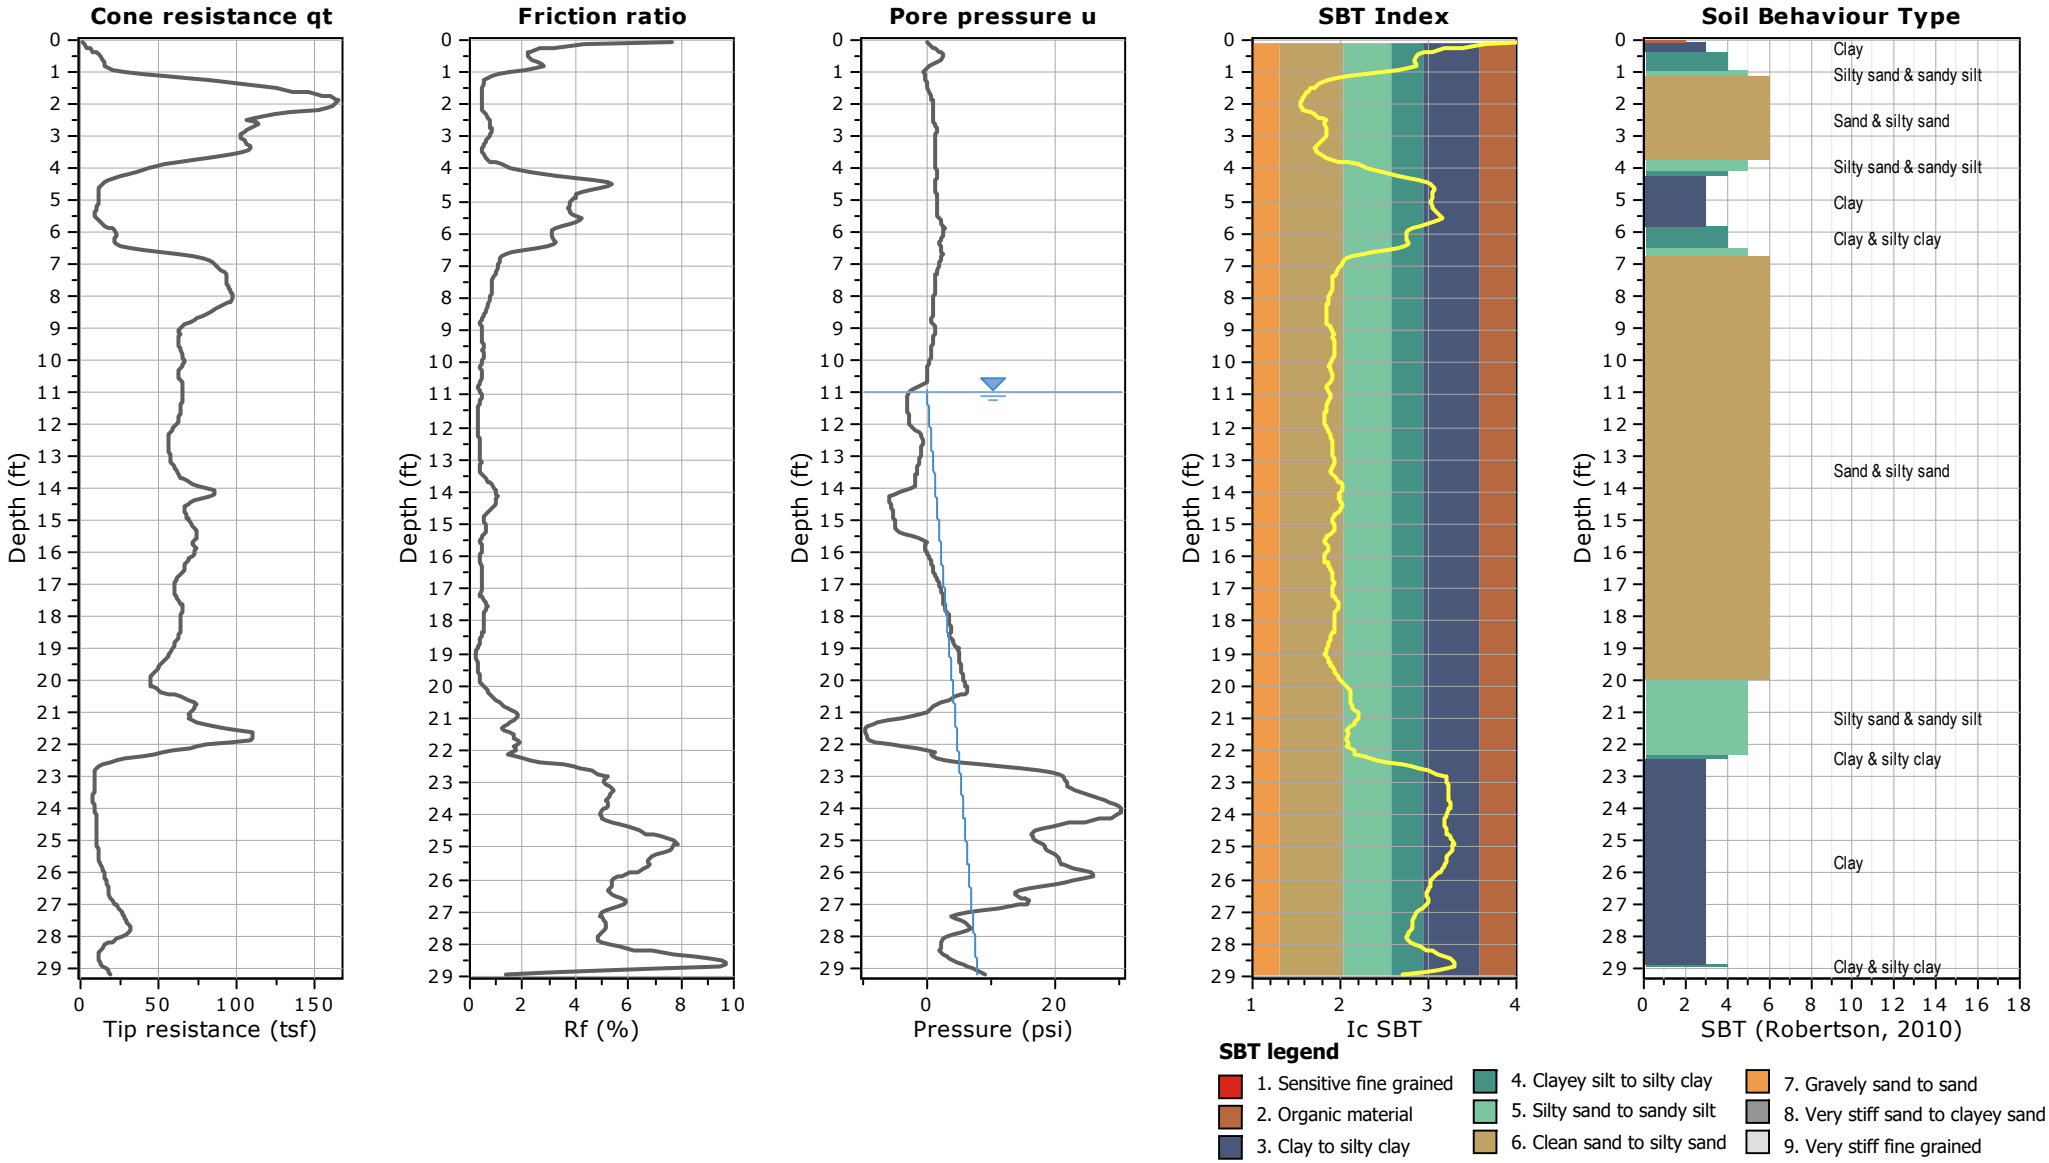



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 1
Total depth: 29.20 ft, Date: 4/20/2022
Surface Elevation: 76.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

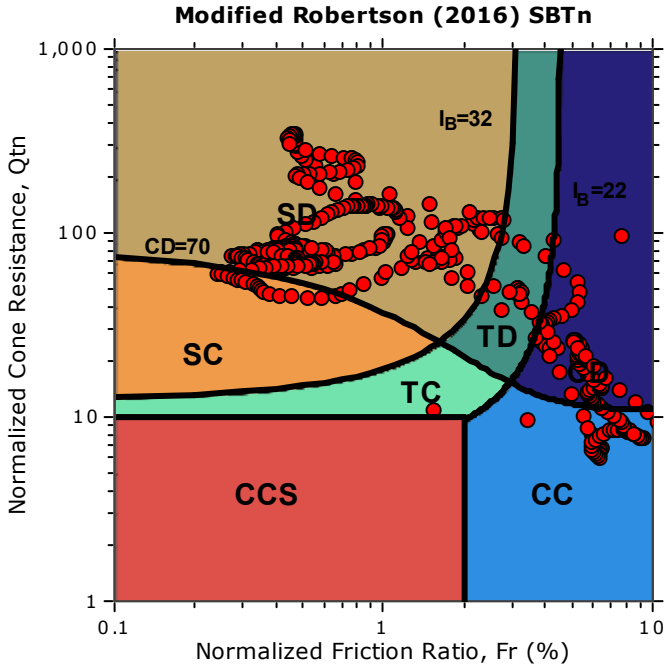

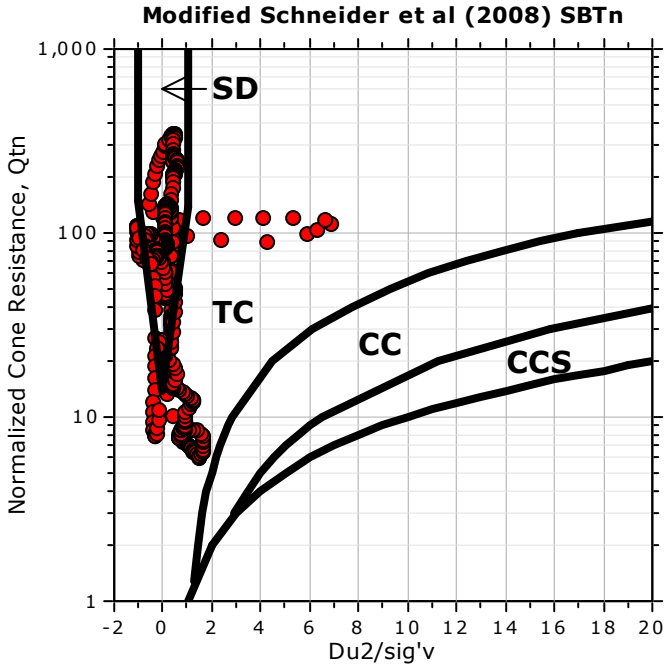

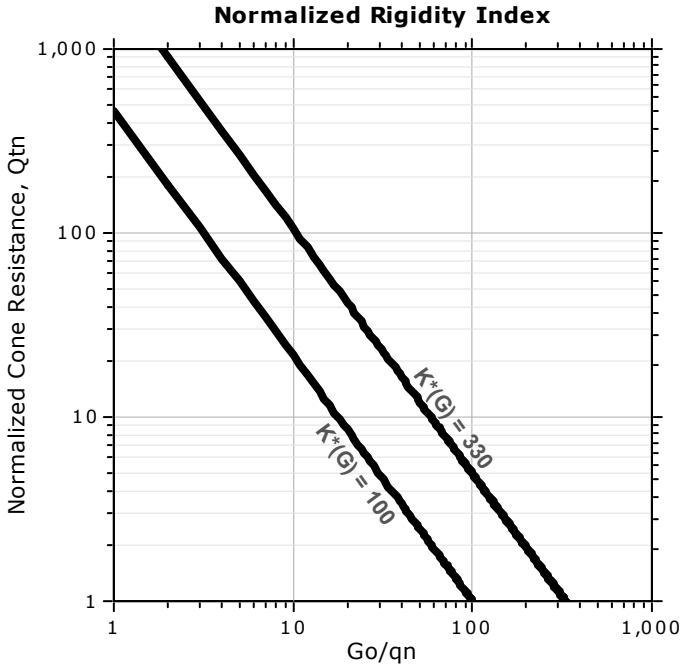


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 1
Total depth: 29.20 ft, Date: 4/20/2022
Surface Elevation: 76.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

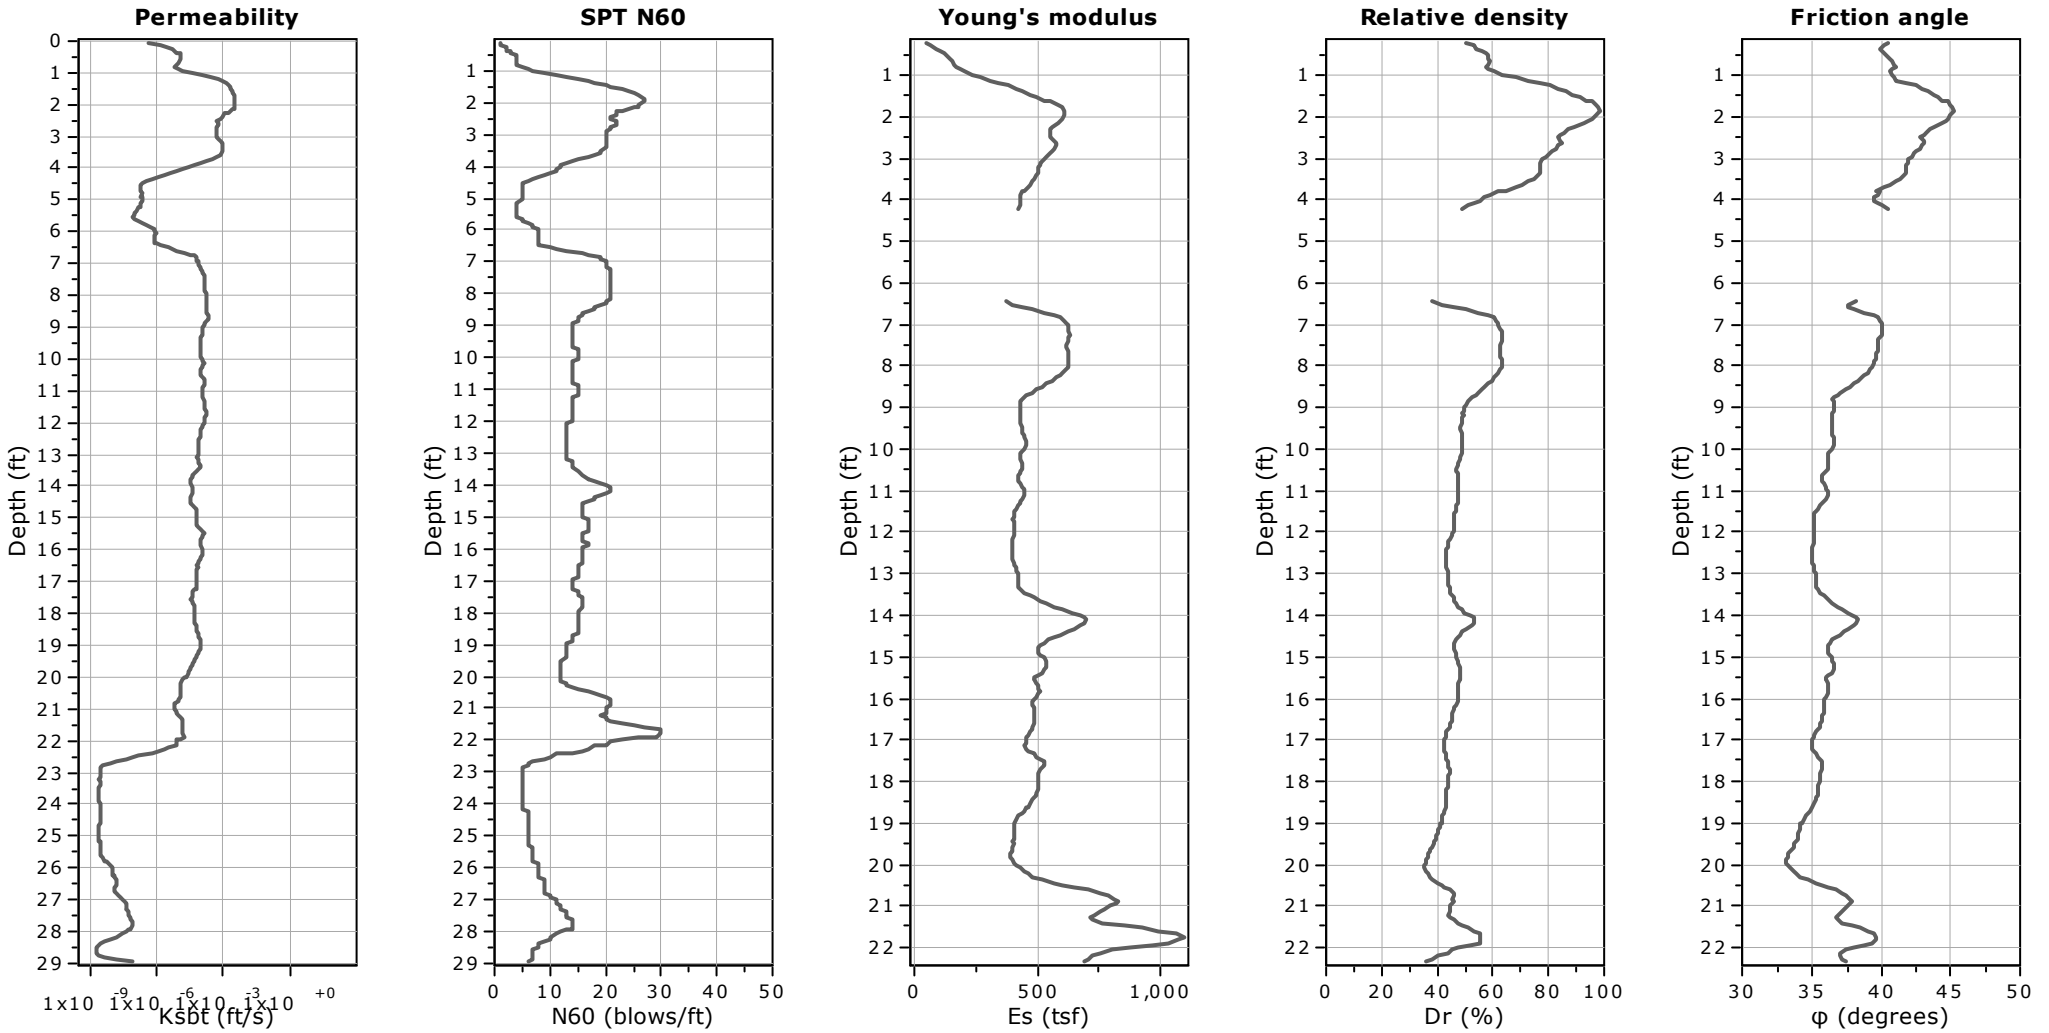


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 1
Total depth: 29.20 ft, Date: 4/20/2022
Surface Elevation: 76.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

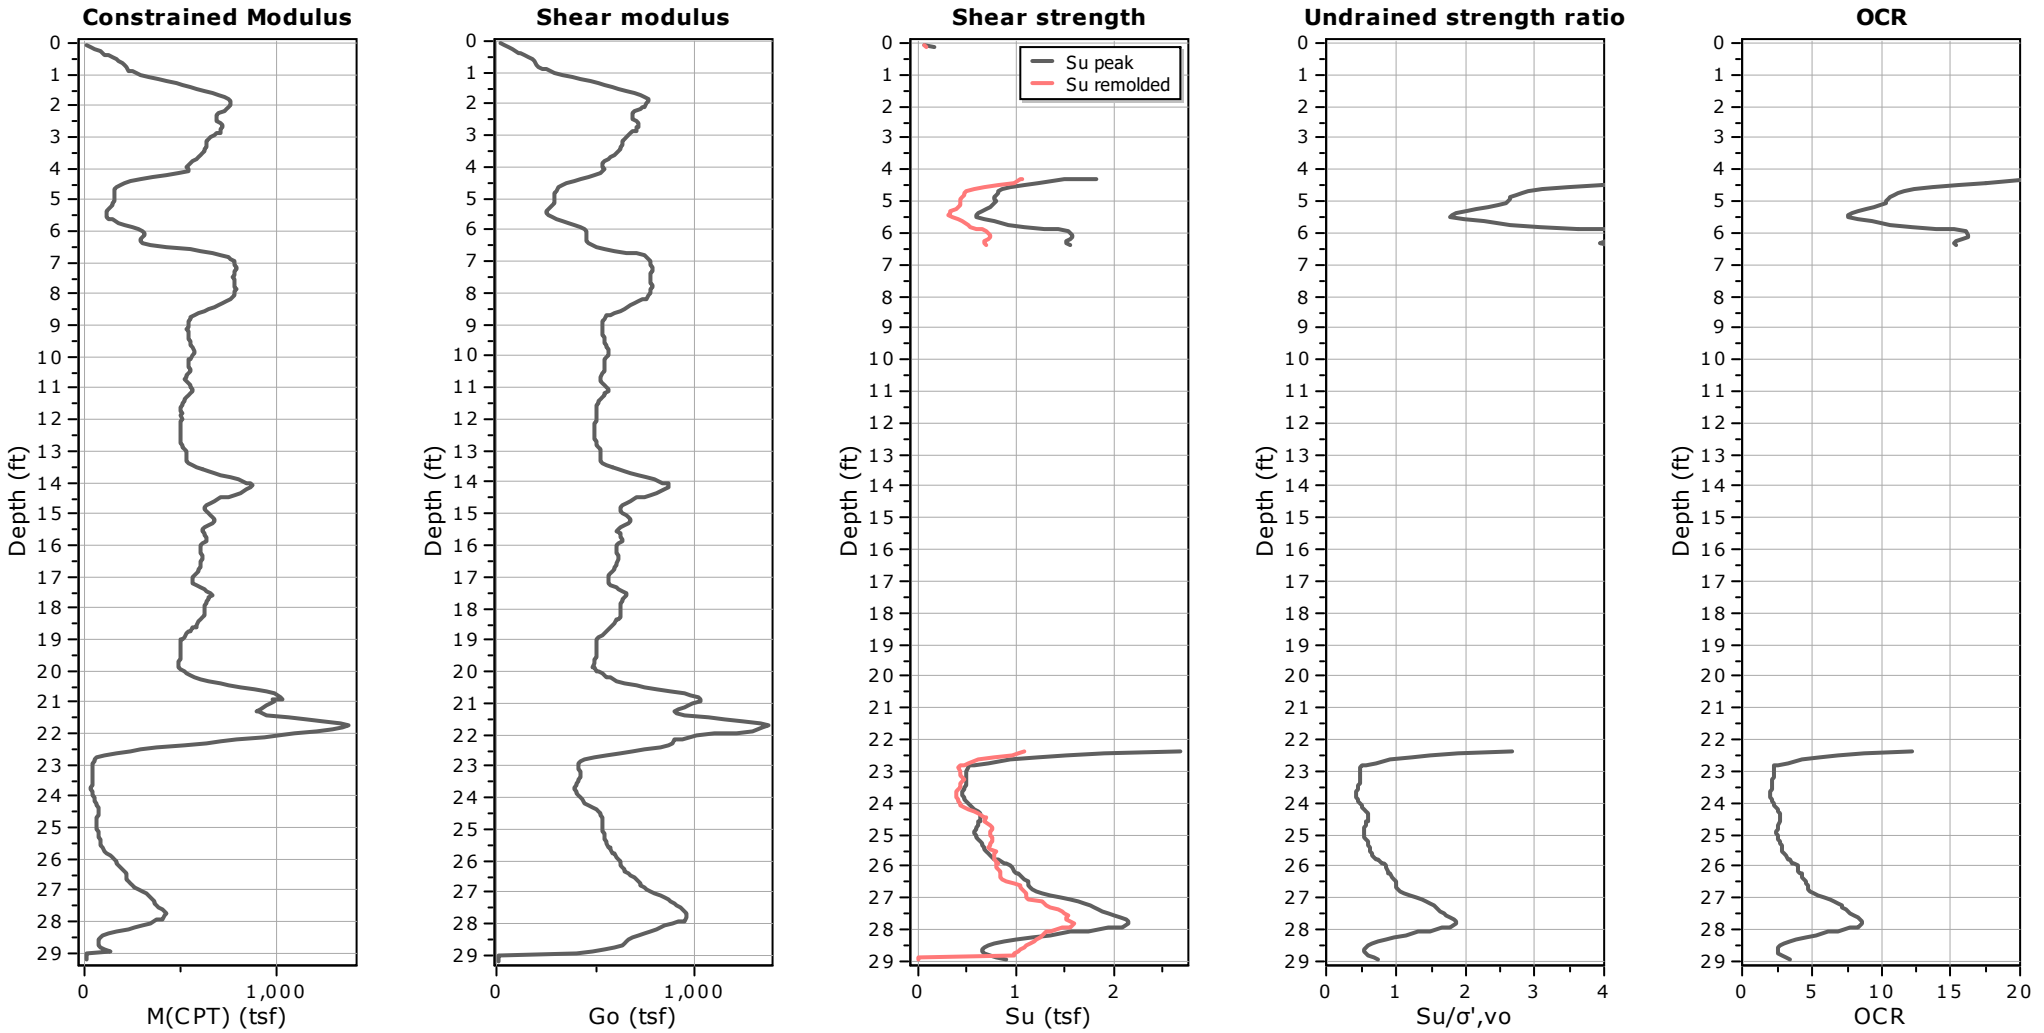


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 1
Total depth: 29.20 ft, Date: 4/20/2022
Surface Elevation: 76.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

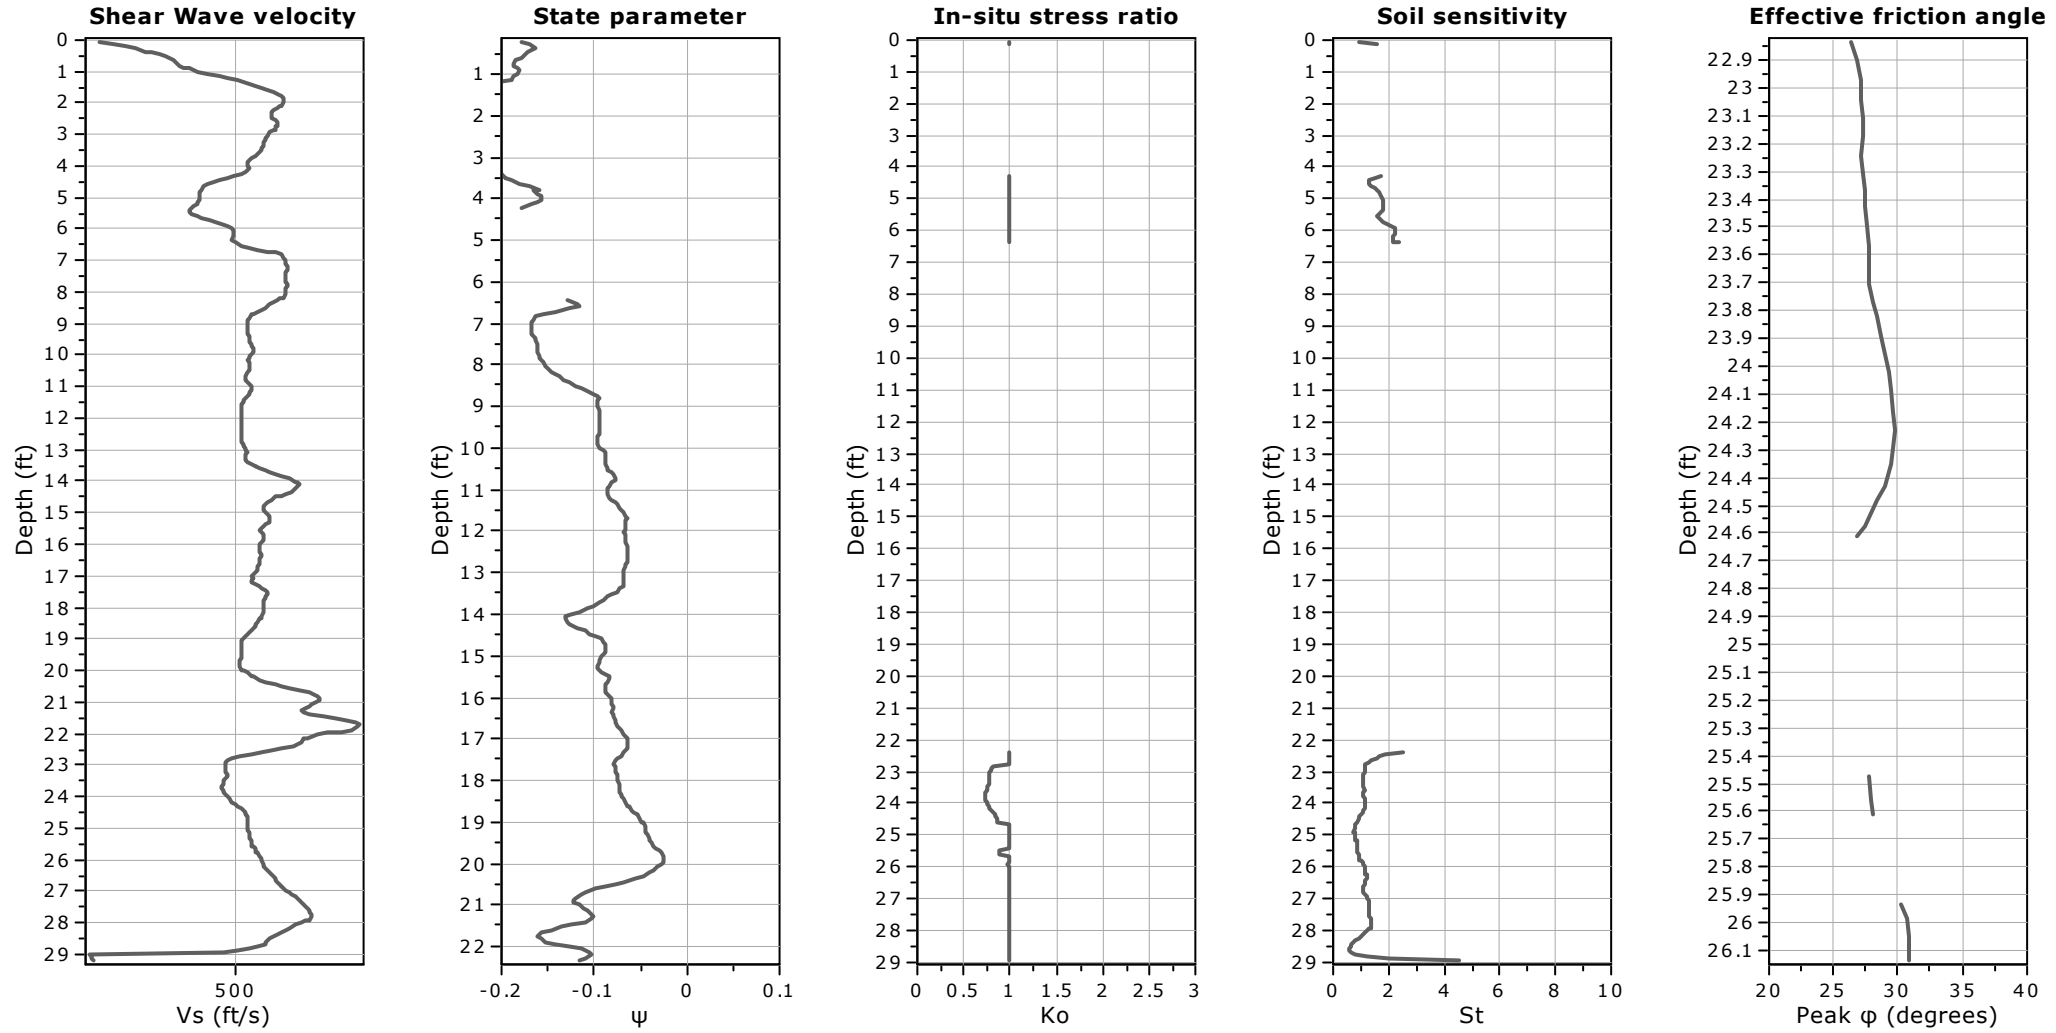

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 2
Total depth: 26.06 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

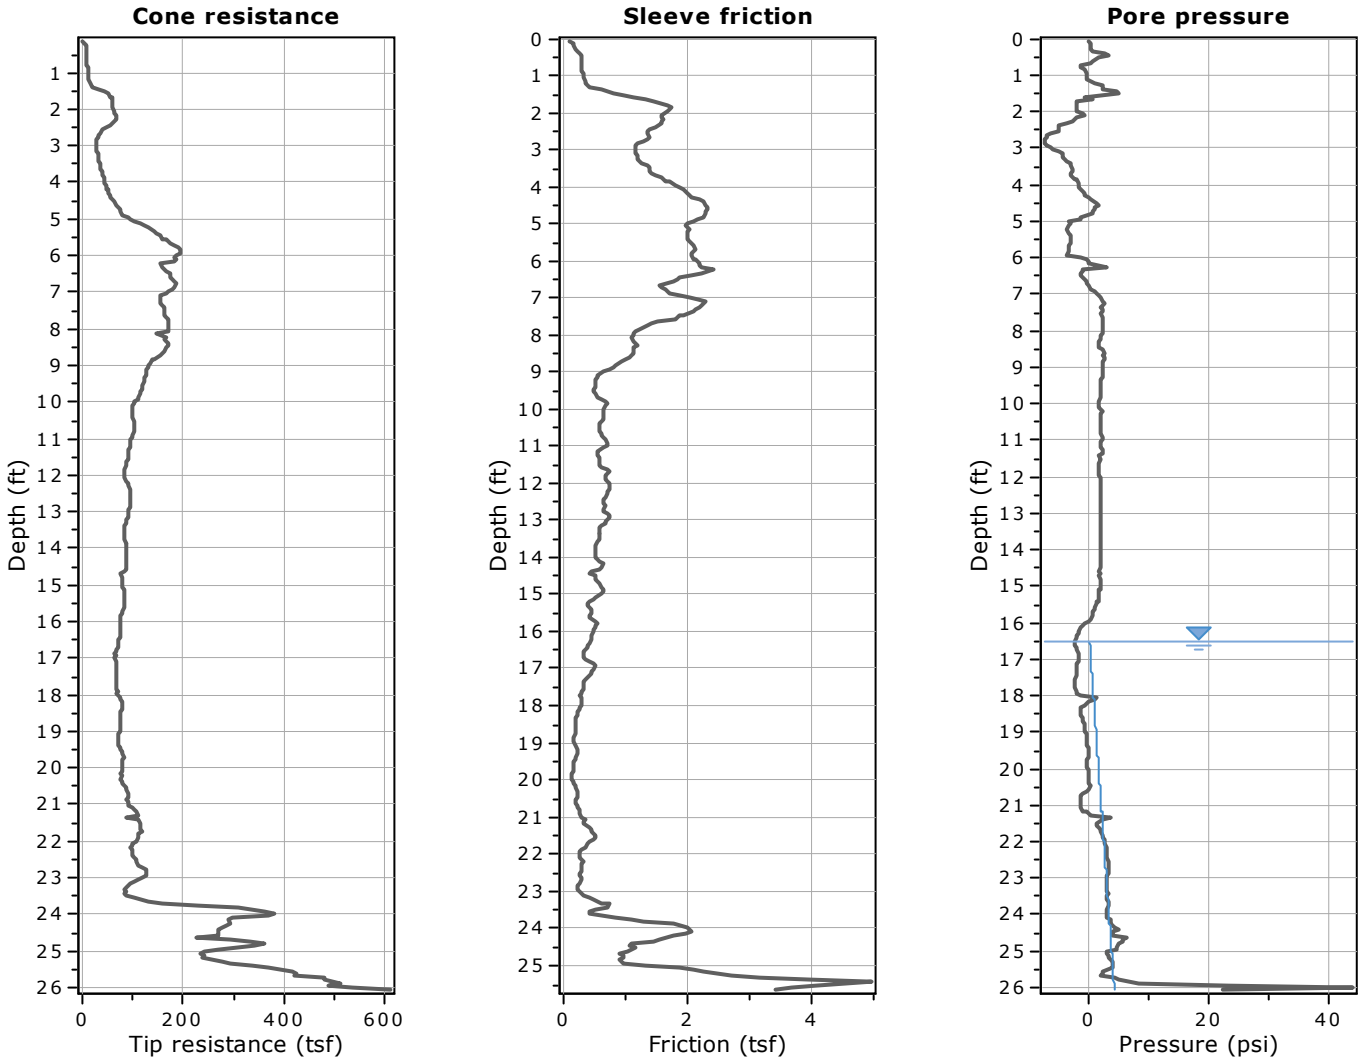


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

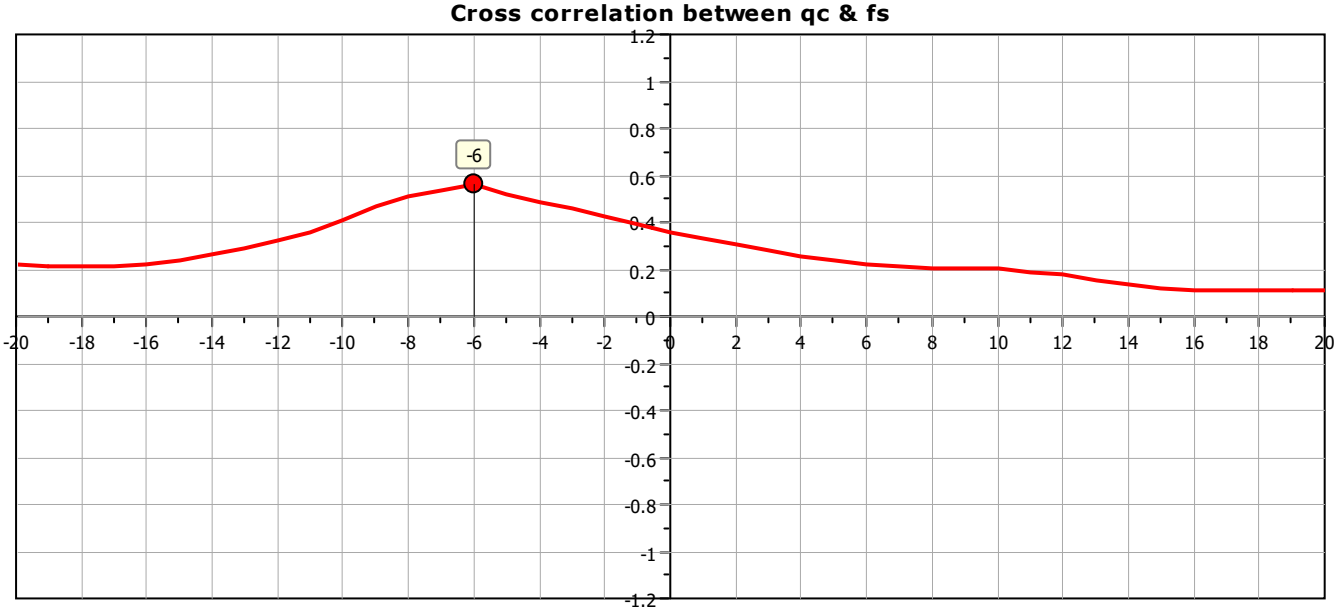

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 2
Total depth: 26.06 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

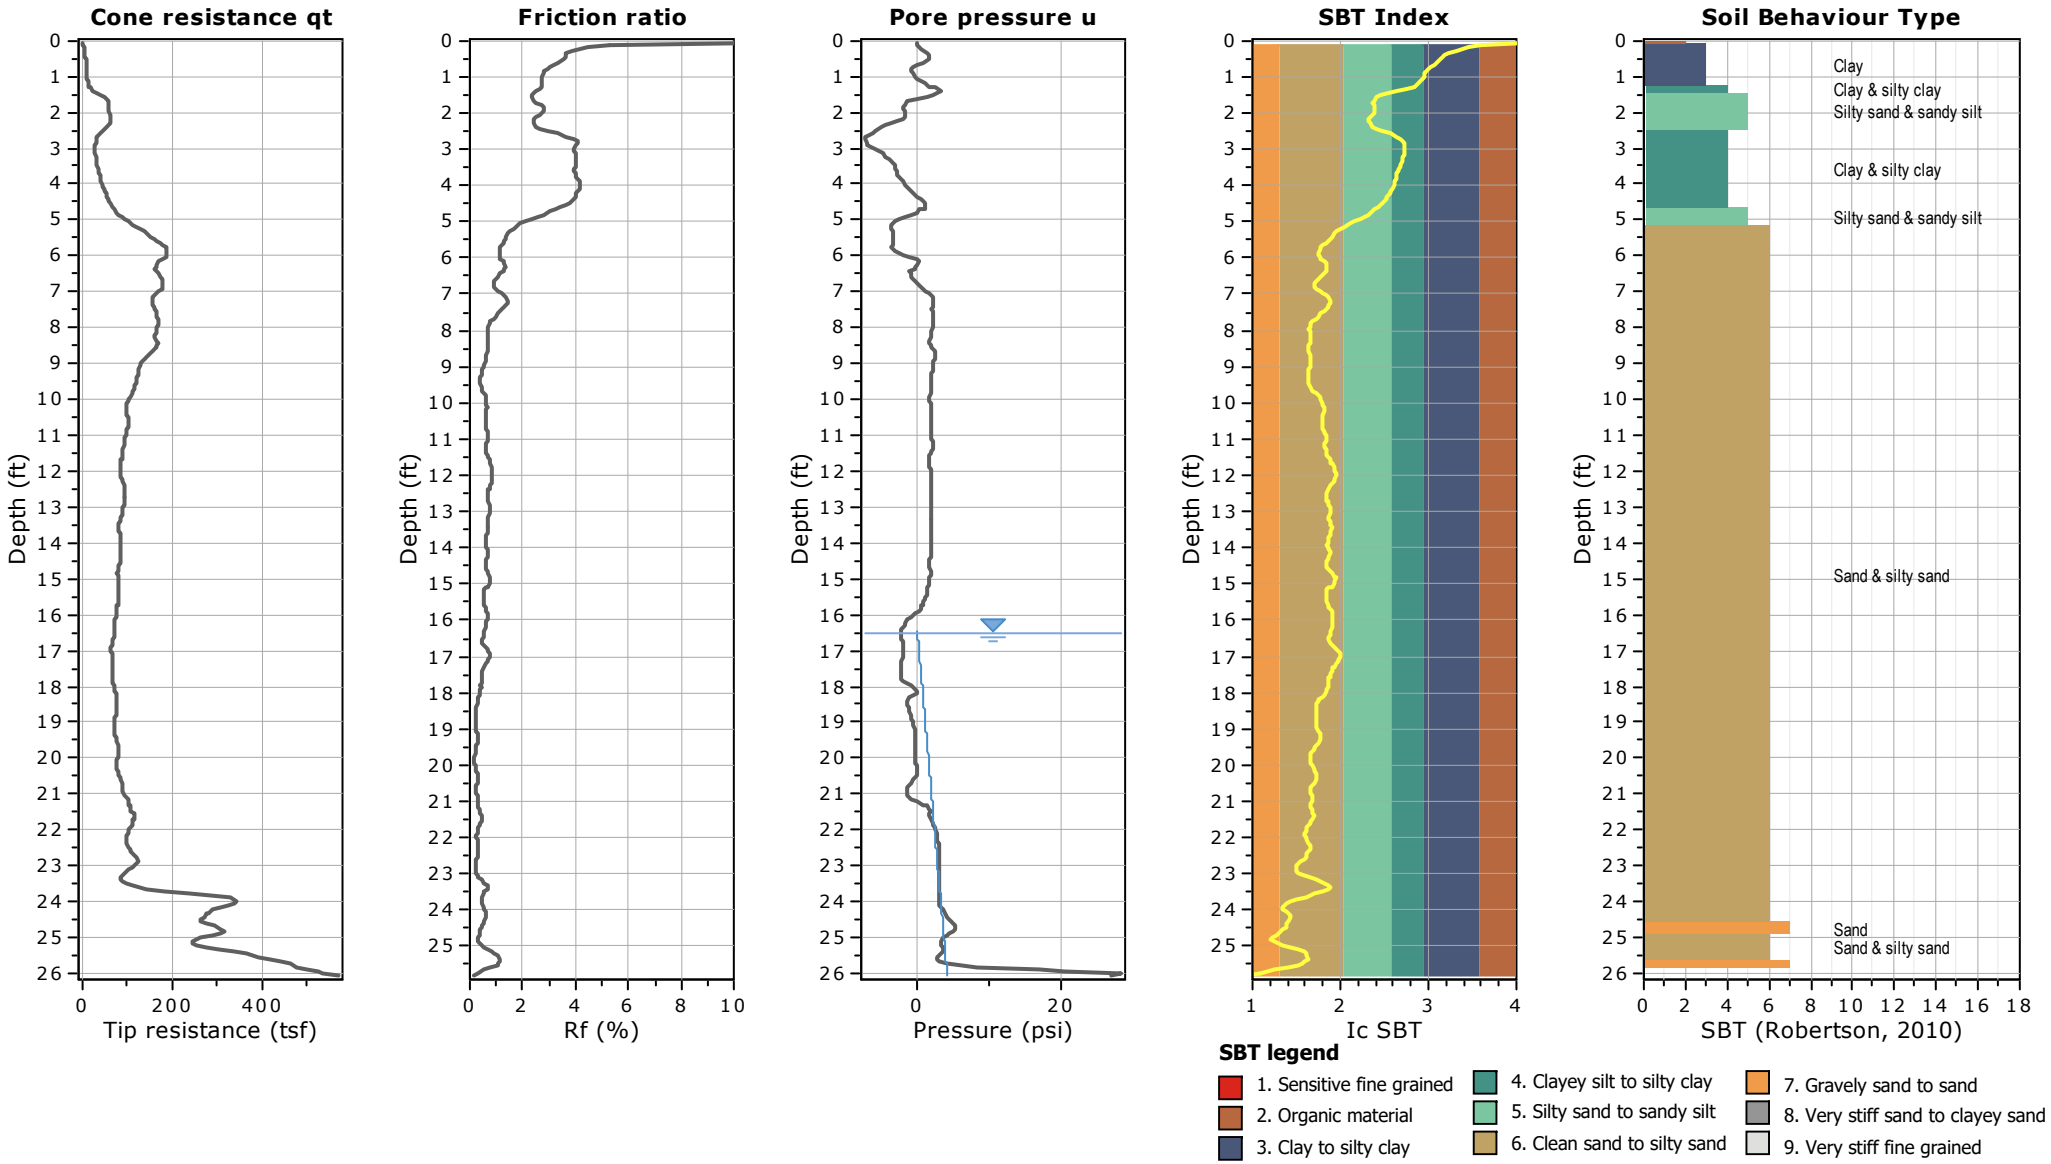



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 2
Total depth: 26.06 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

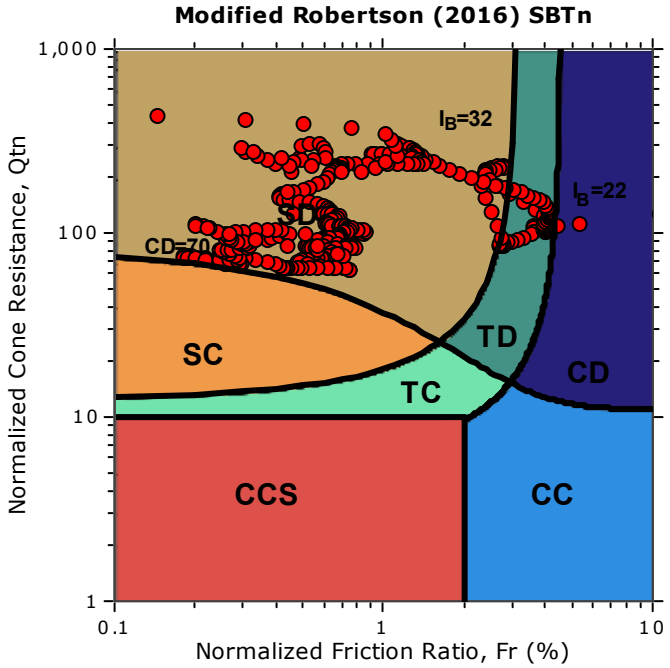

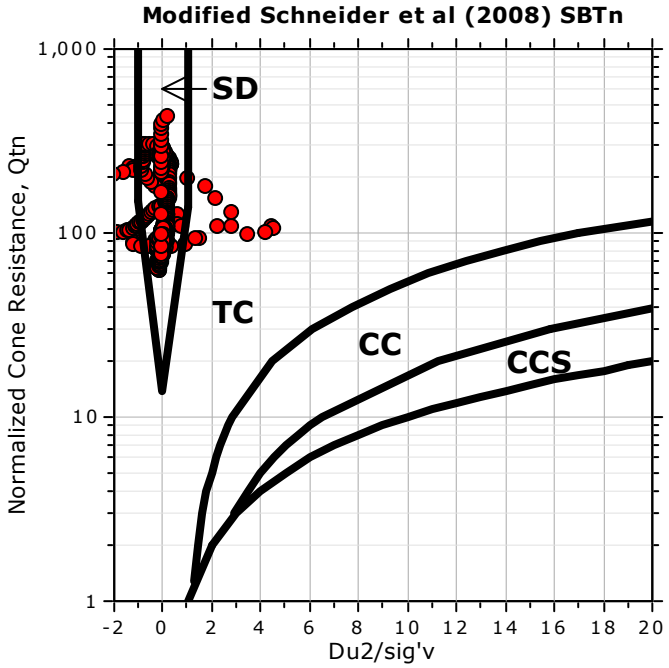

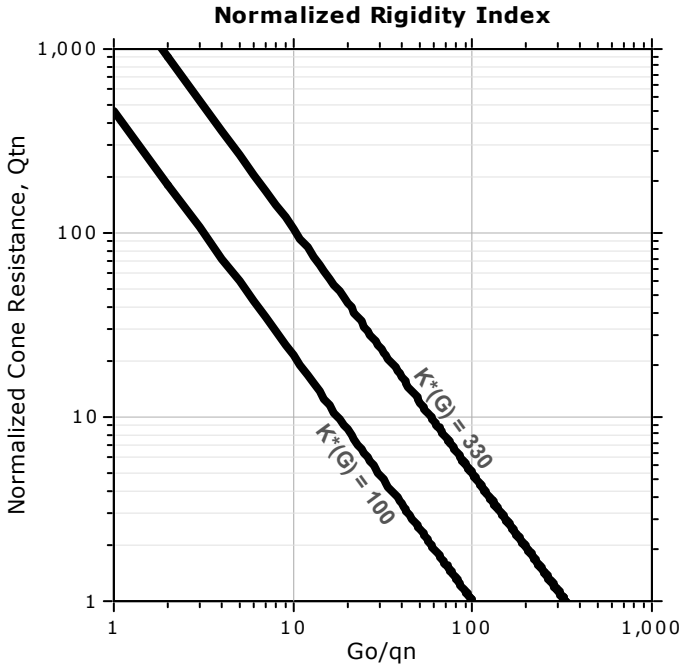


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 2
Total depth: 26.06 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

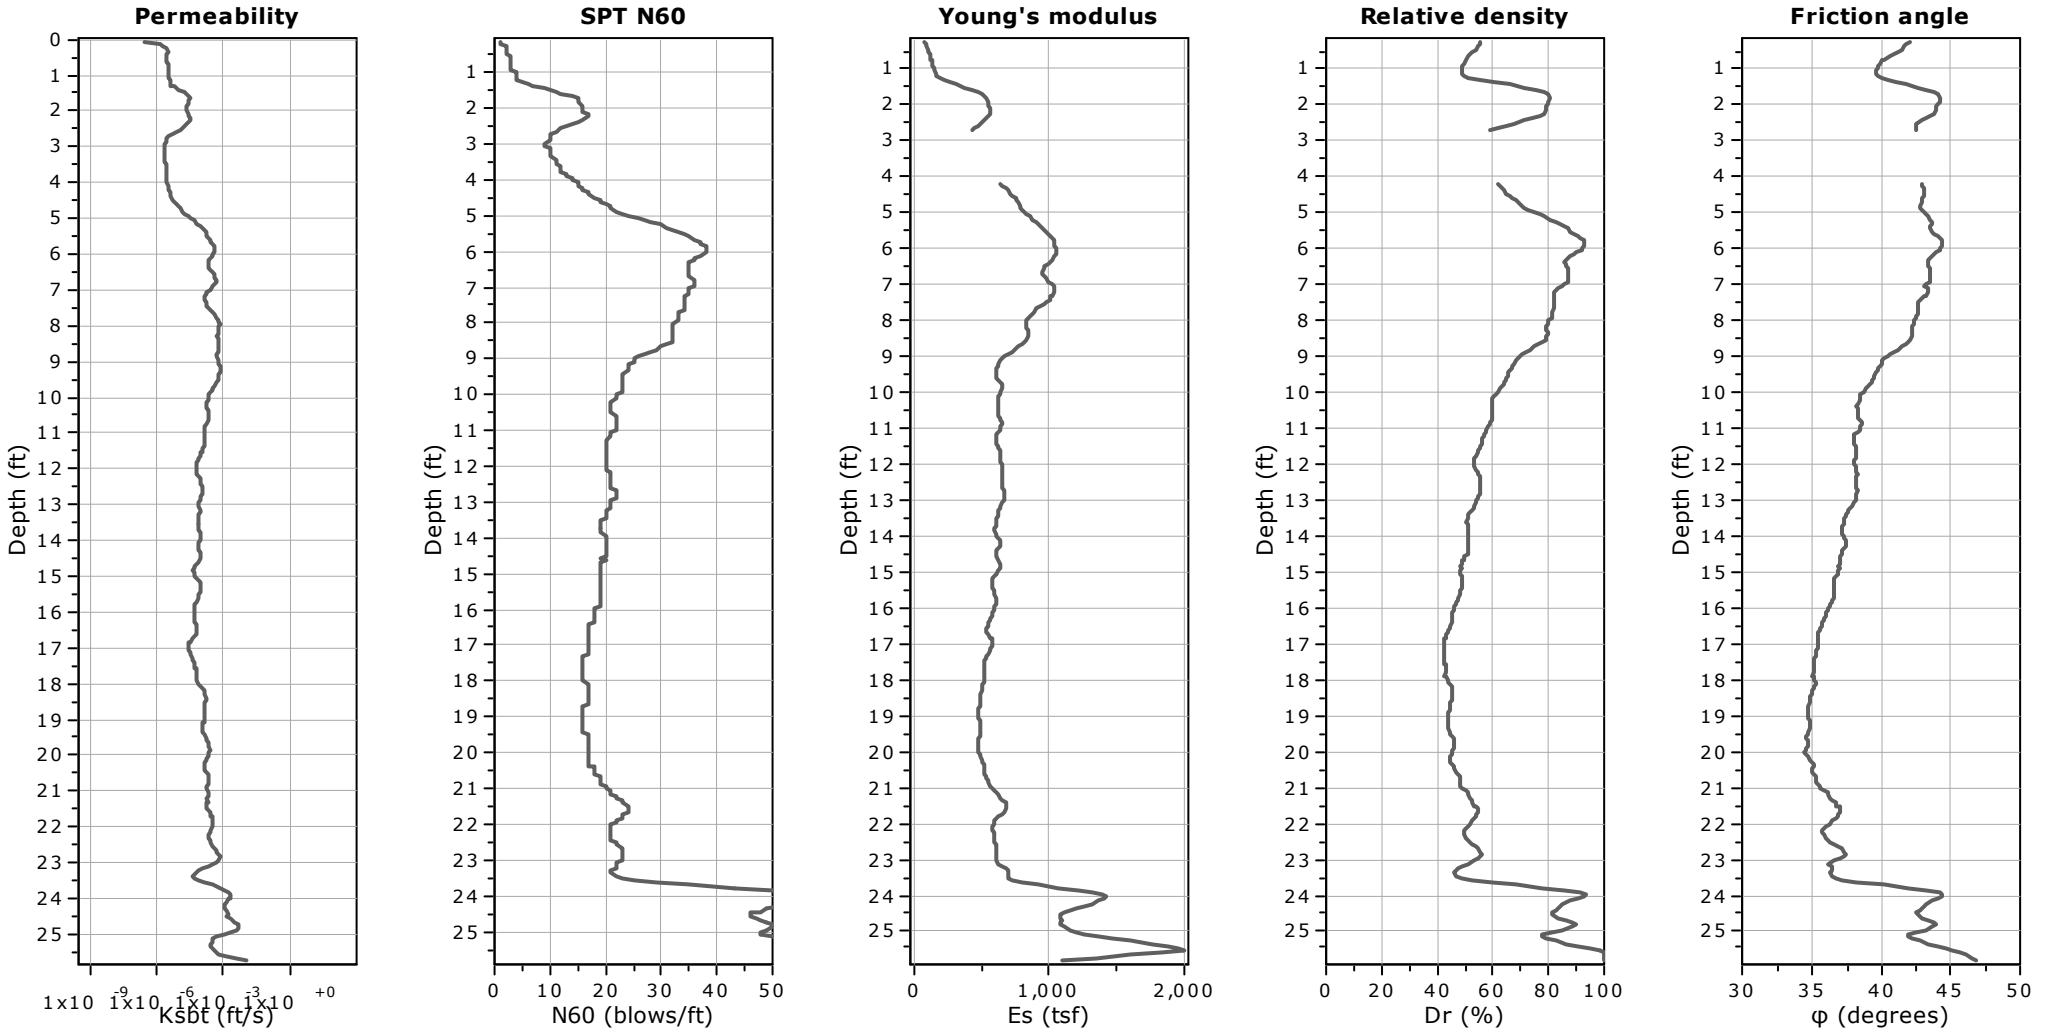


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 2
Total depth: 26.06 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

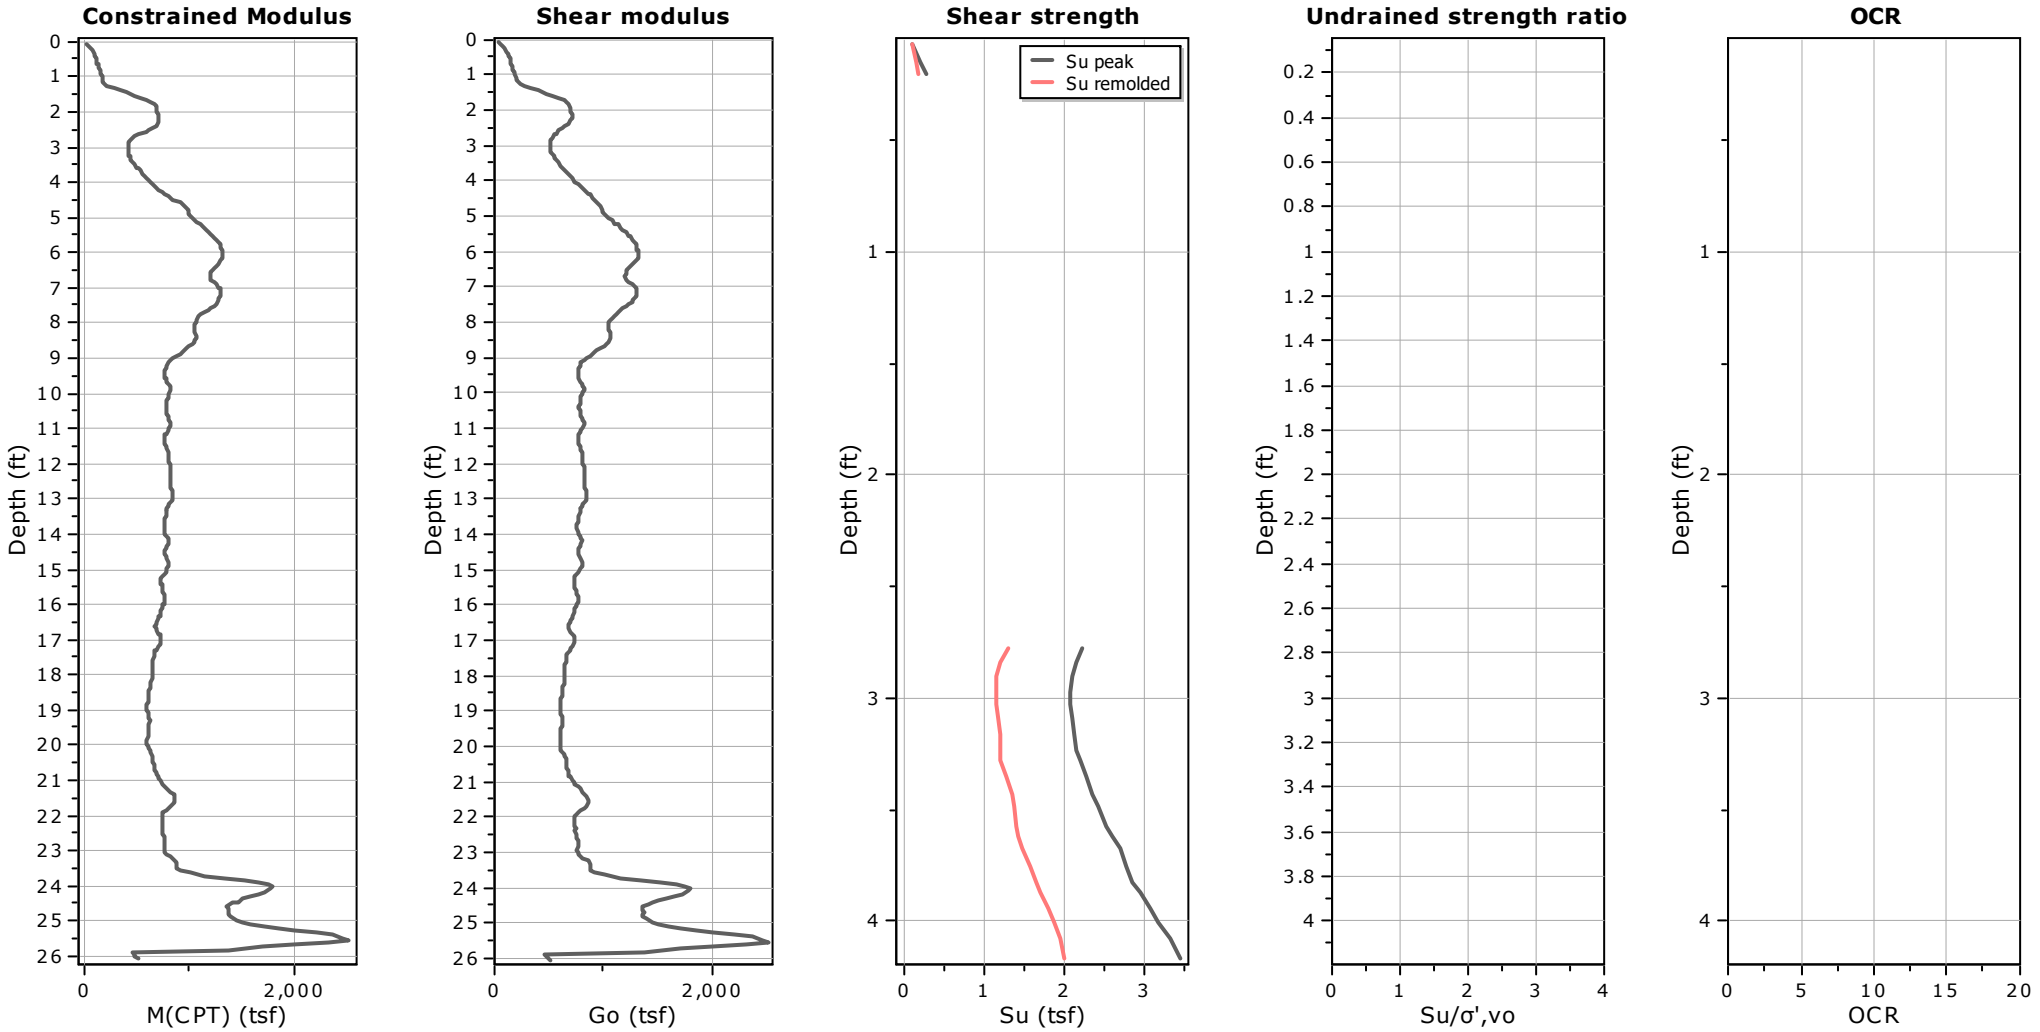


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 2
Total depth: 26.06 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

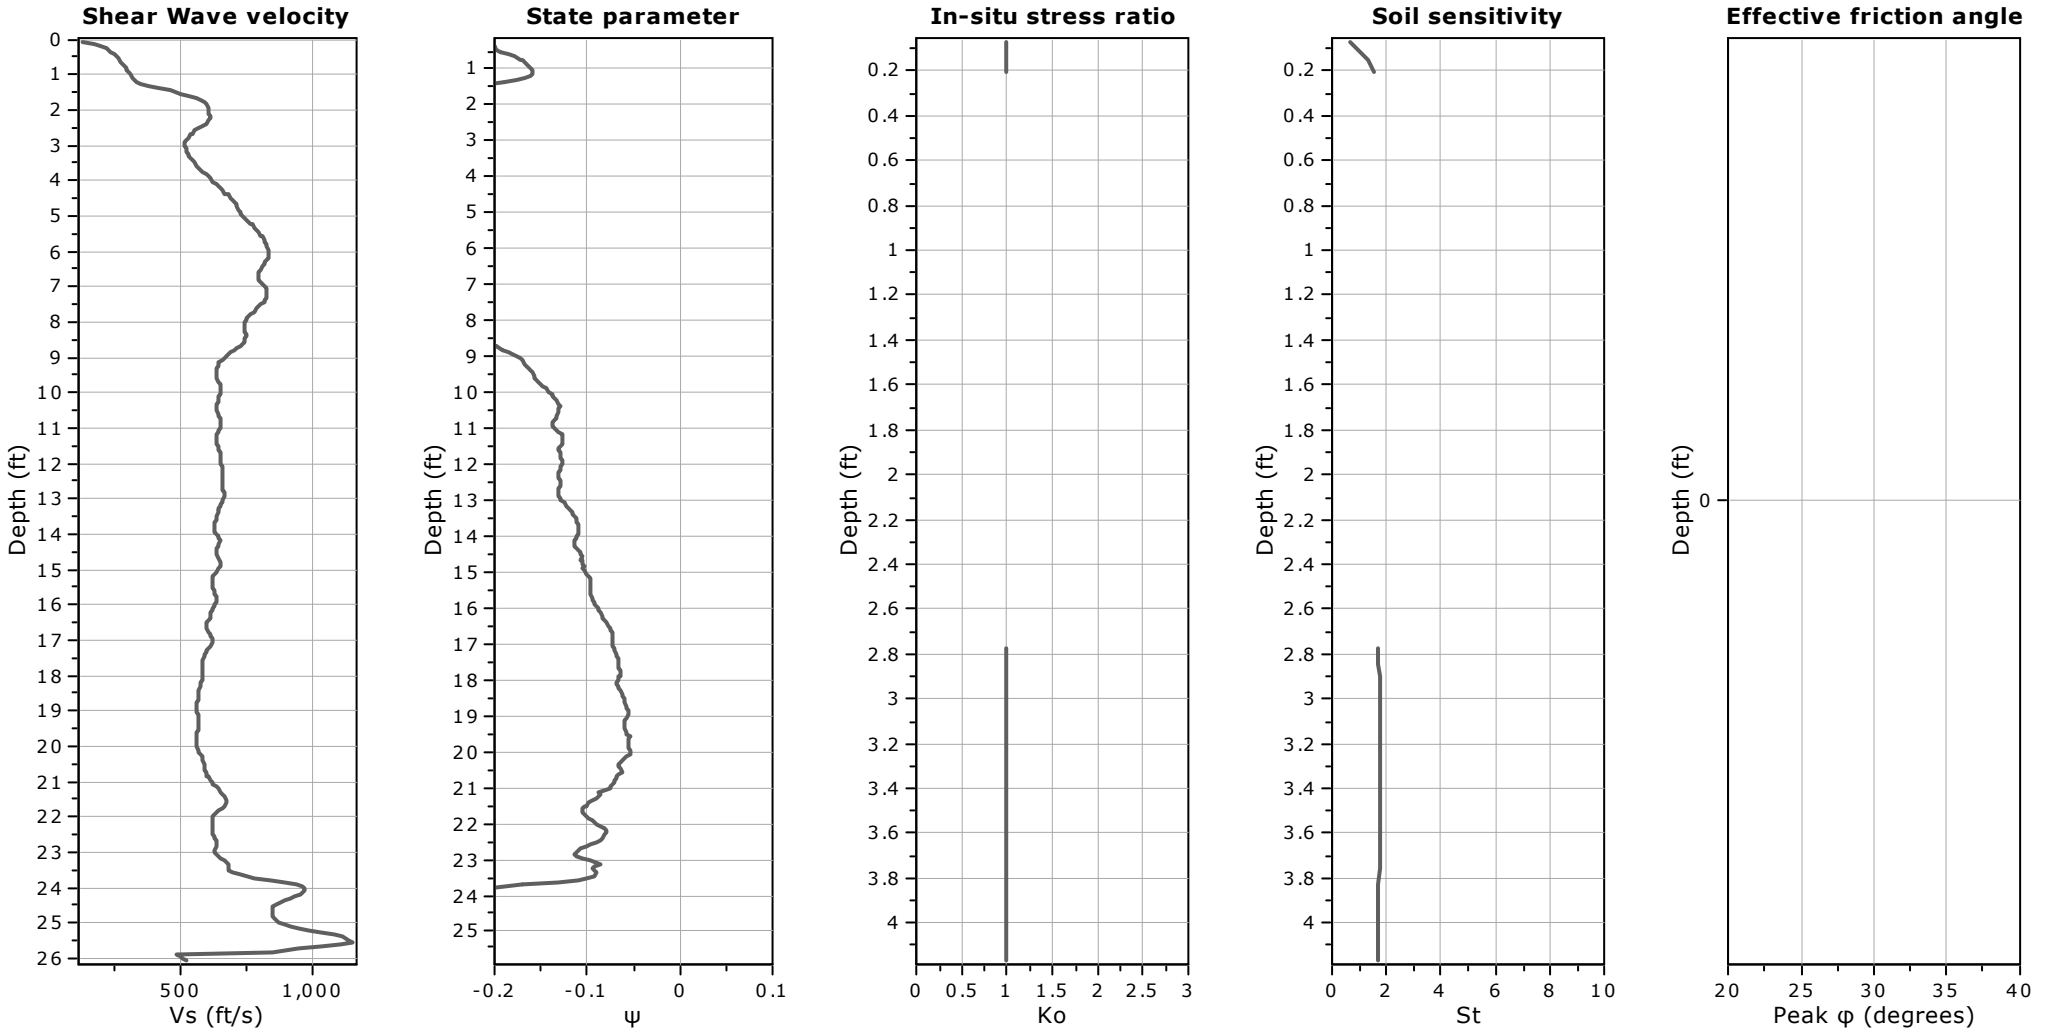

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 3
Total depth: 24.87 ft, Date: 4/20/2022
Surface Elevation: 71.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

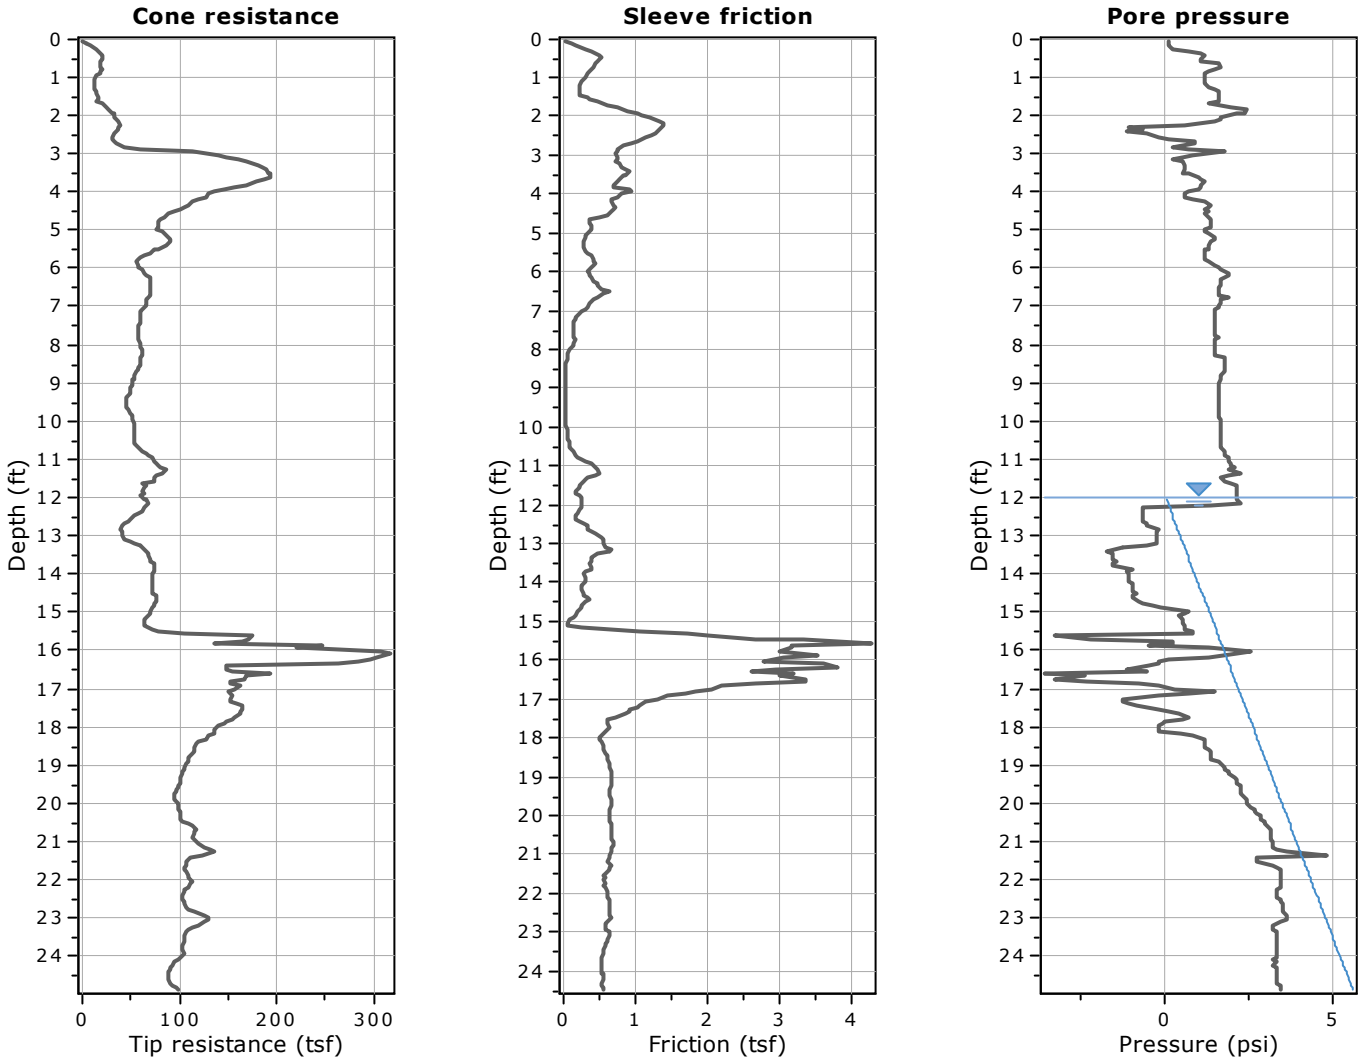


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

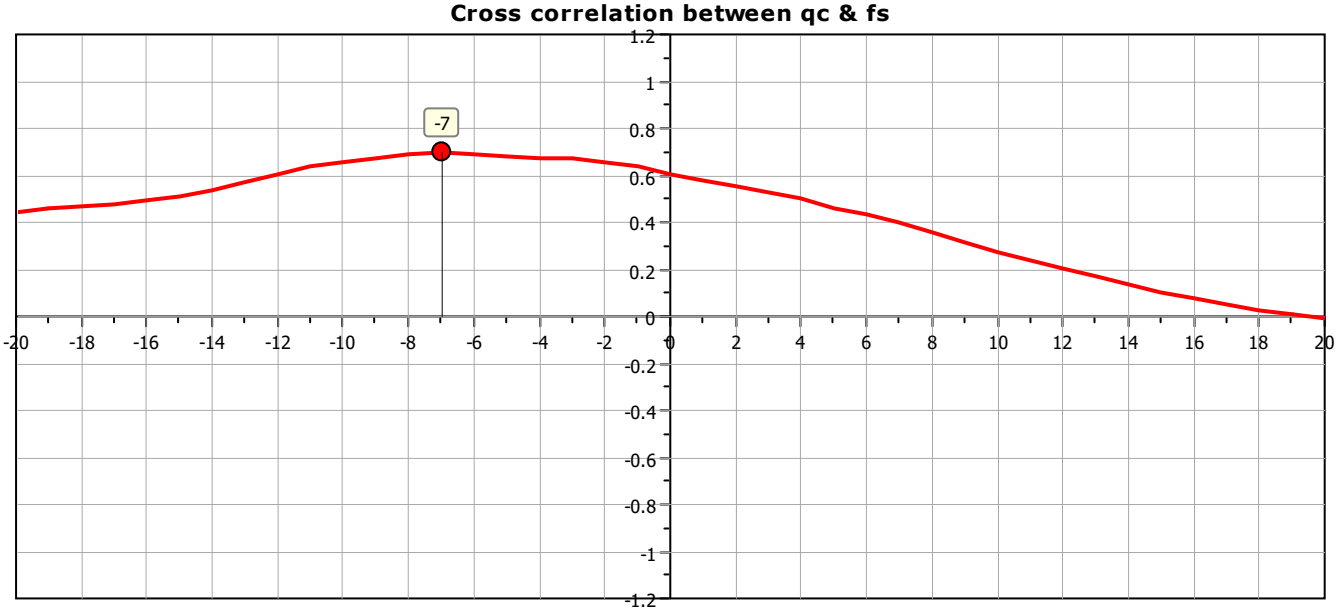

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 3
Total depth: 24.87 ft, Date: 4/20/2022
Surface Elevation: 71.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

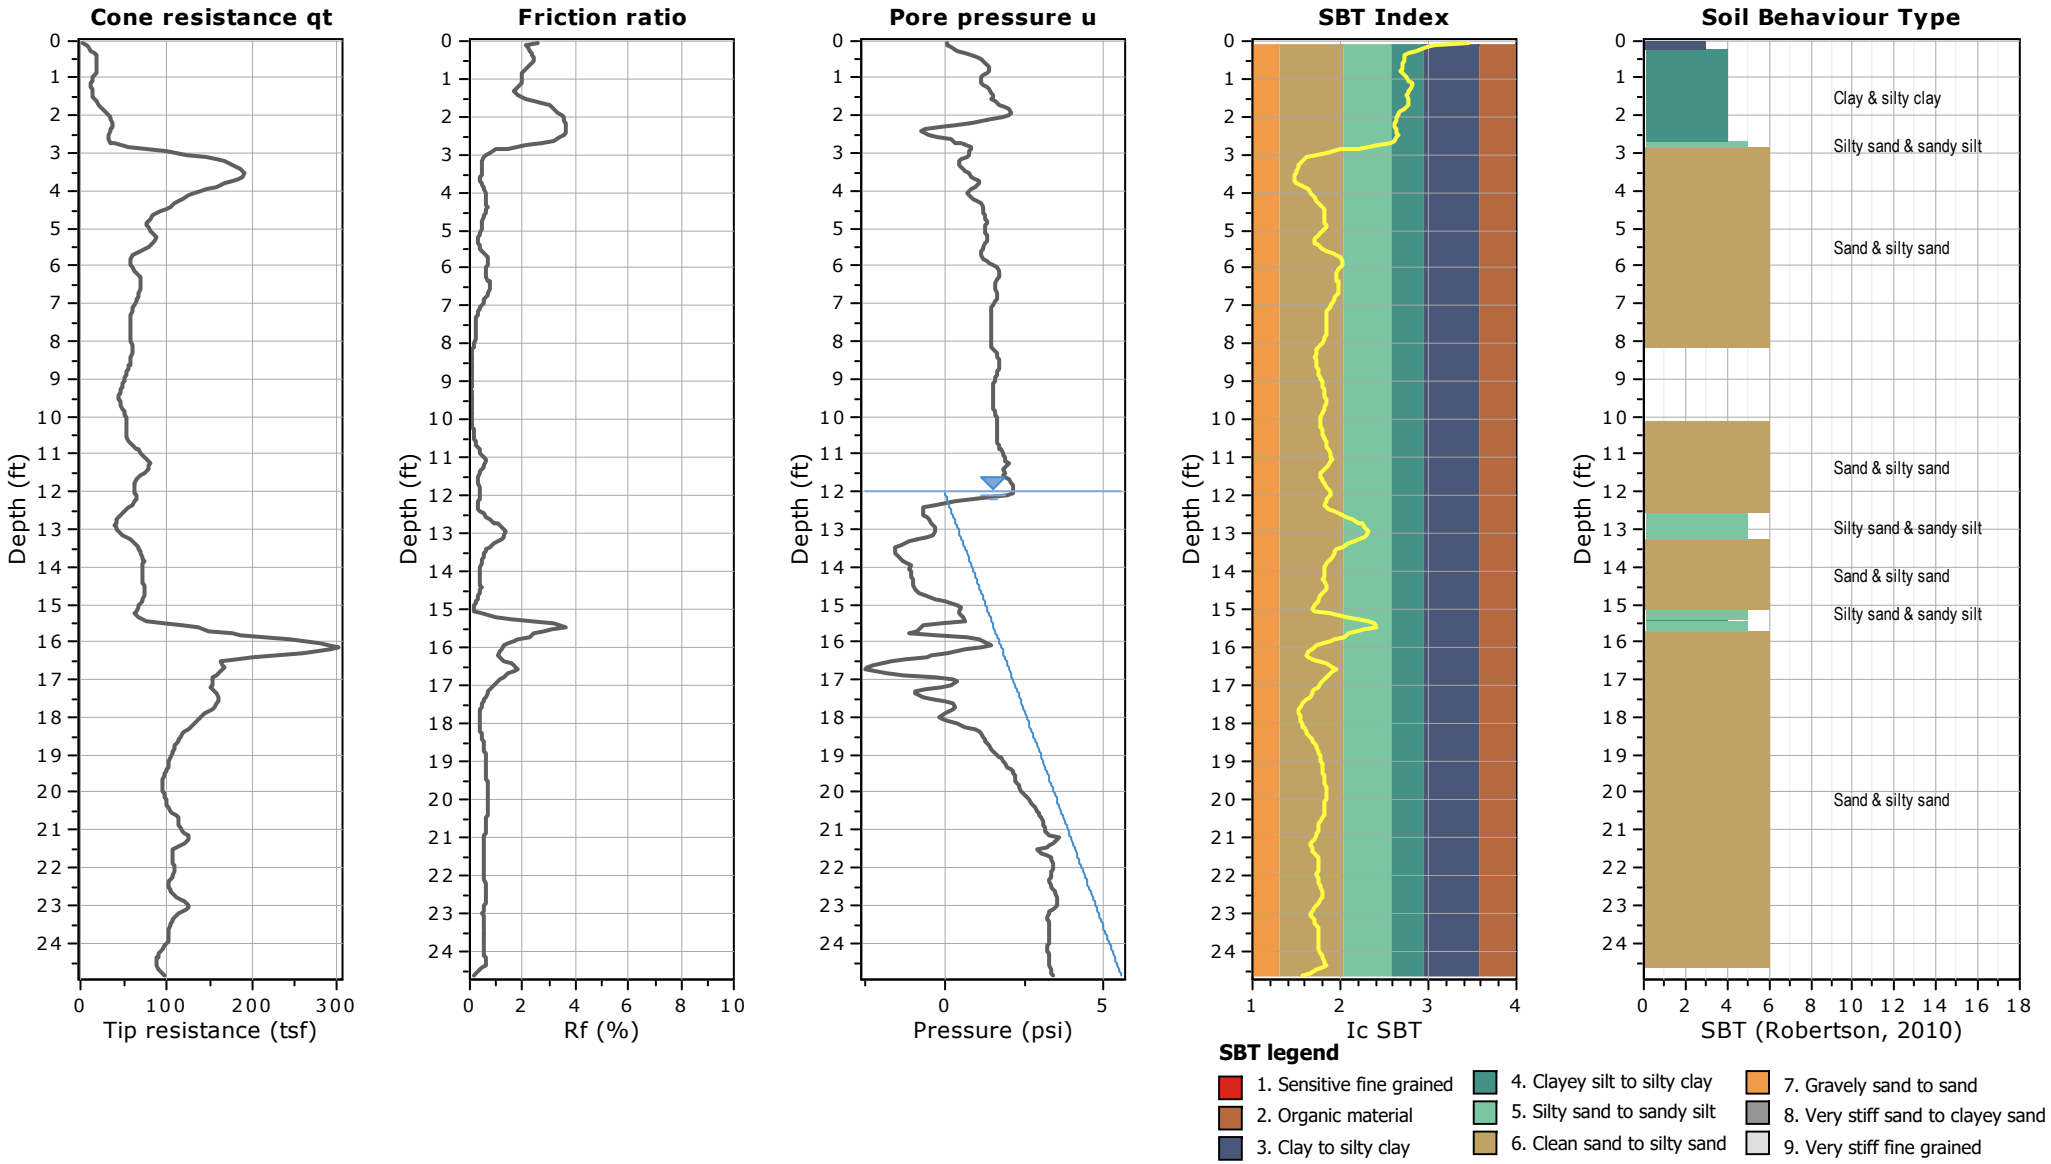



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 3
Total depth: 24.87 ft, Date: 4/20/2022
Surface Elevation: 71.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

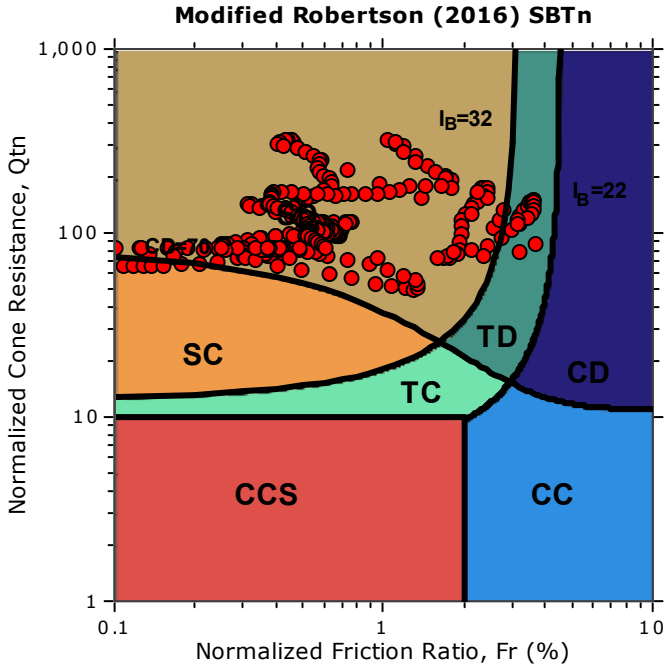

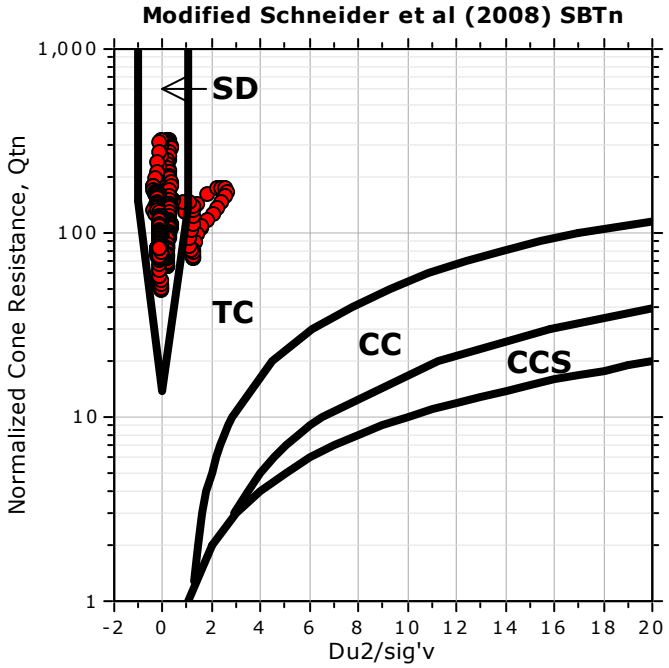

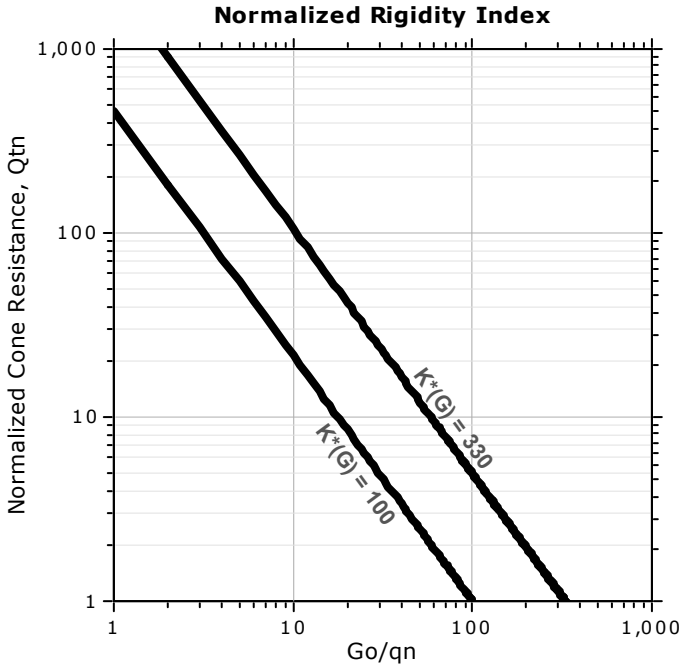


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 3
Total depth: 24.87 ft, Date: 4/20/2022
Surface Elevation: 71.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

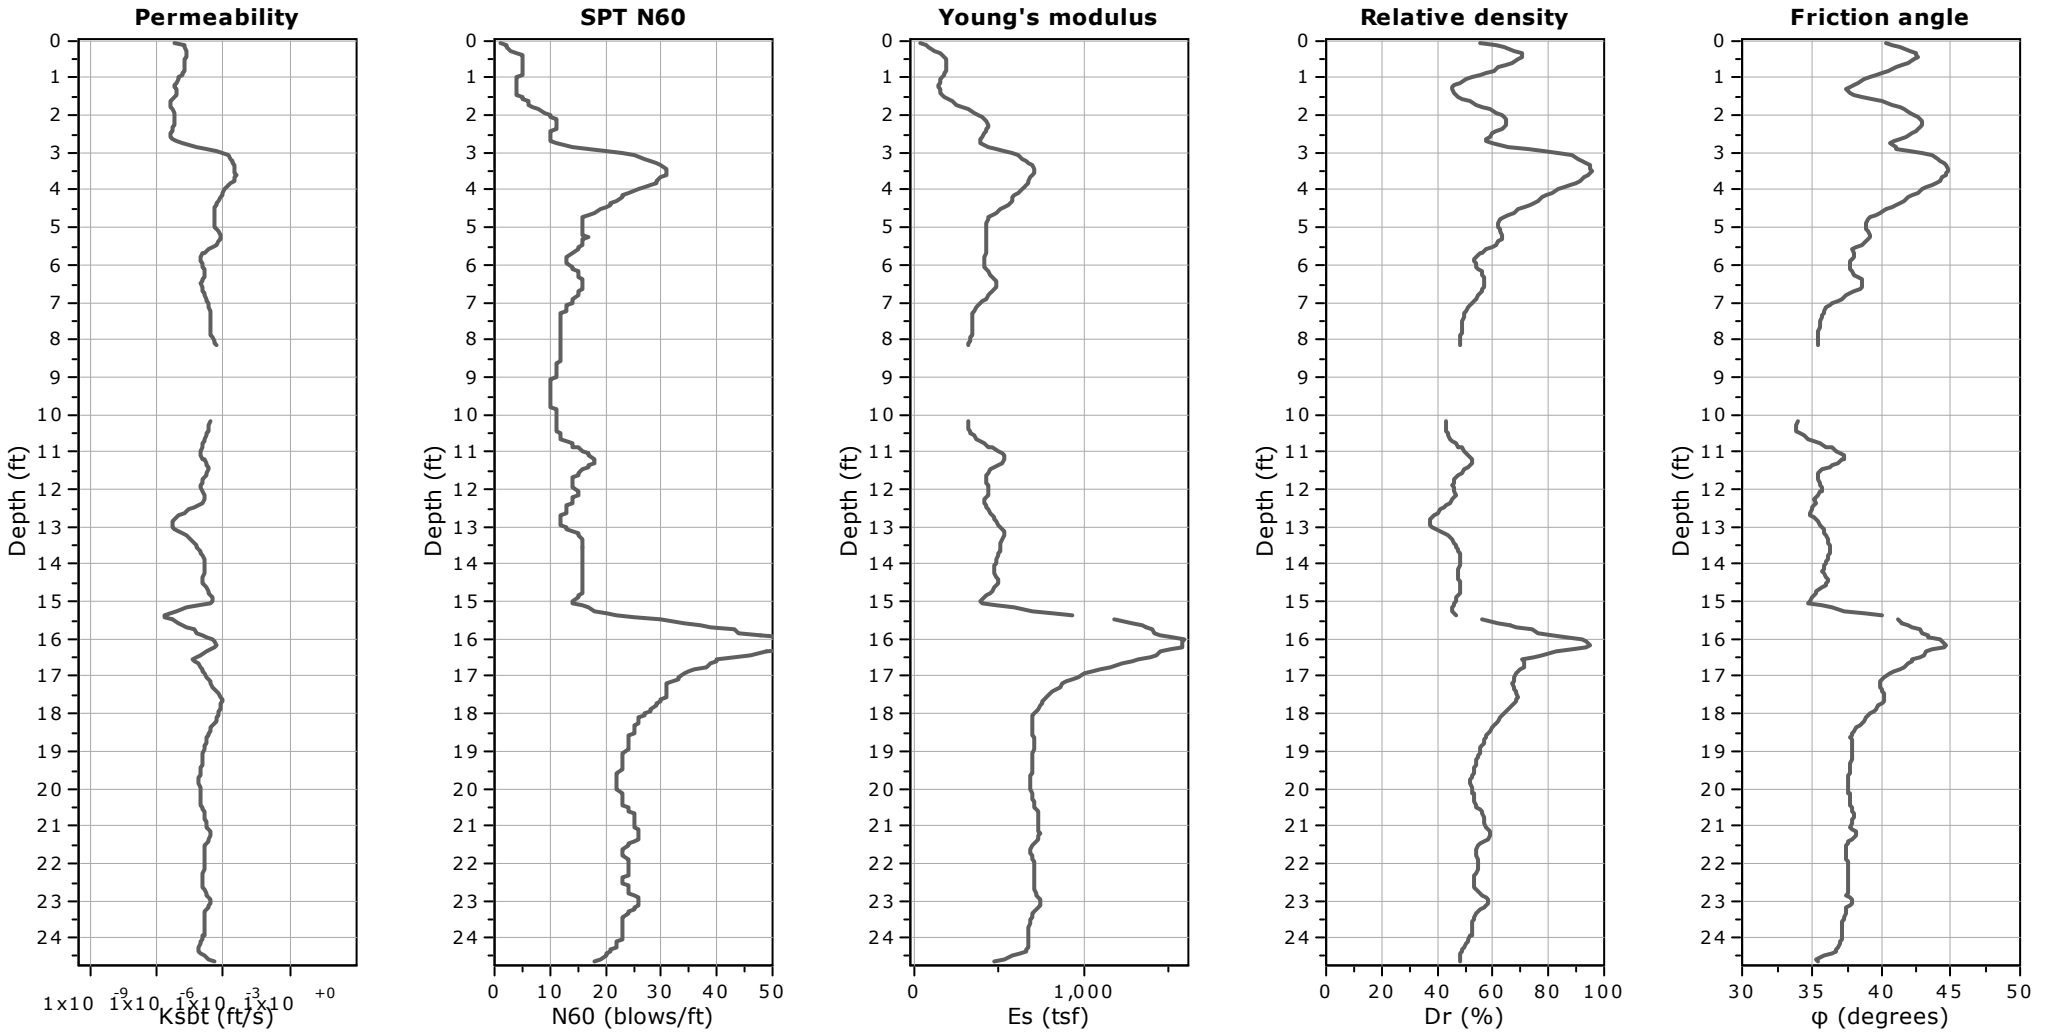


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 3
Total depth: 24.87 ft, Date: 4/20/2022
Surface Elevation: 71.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

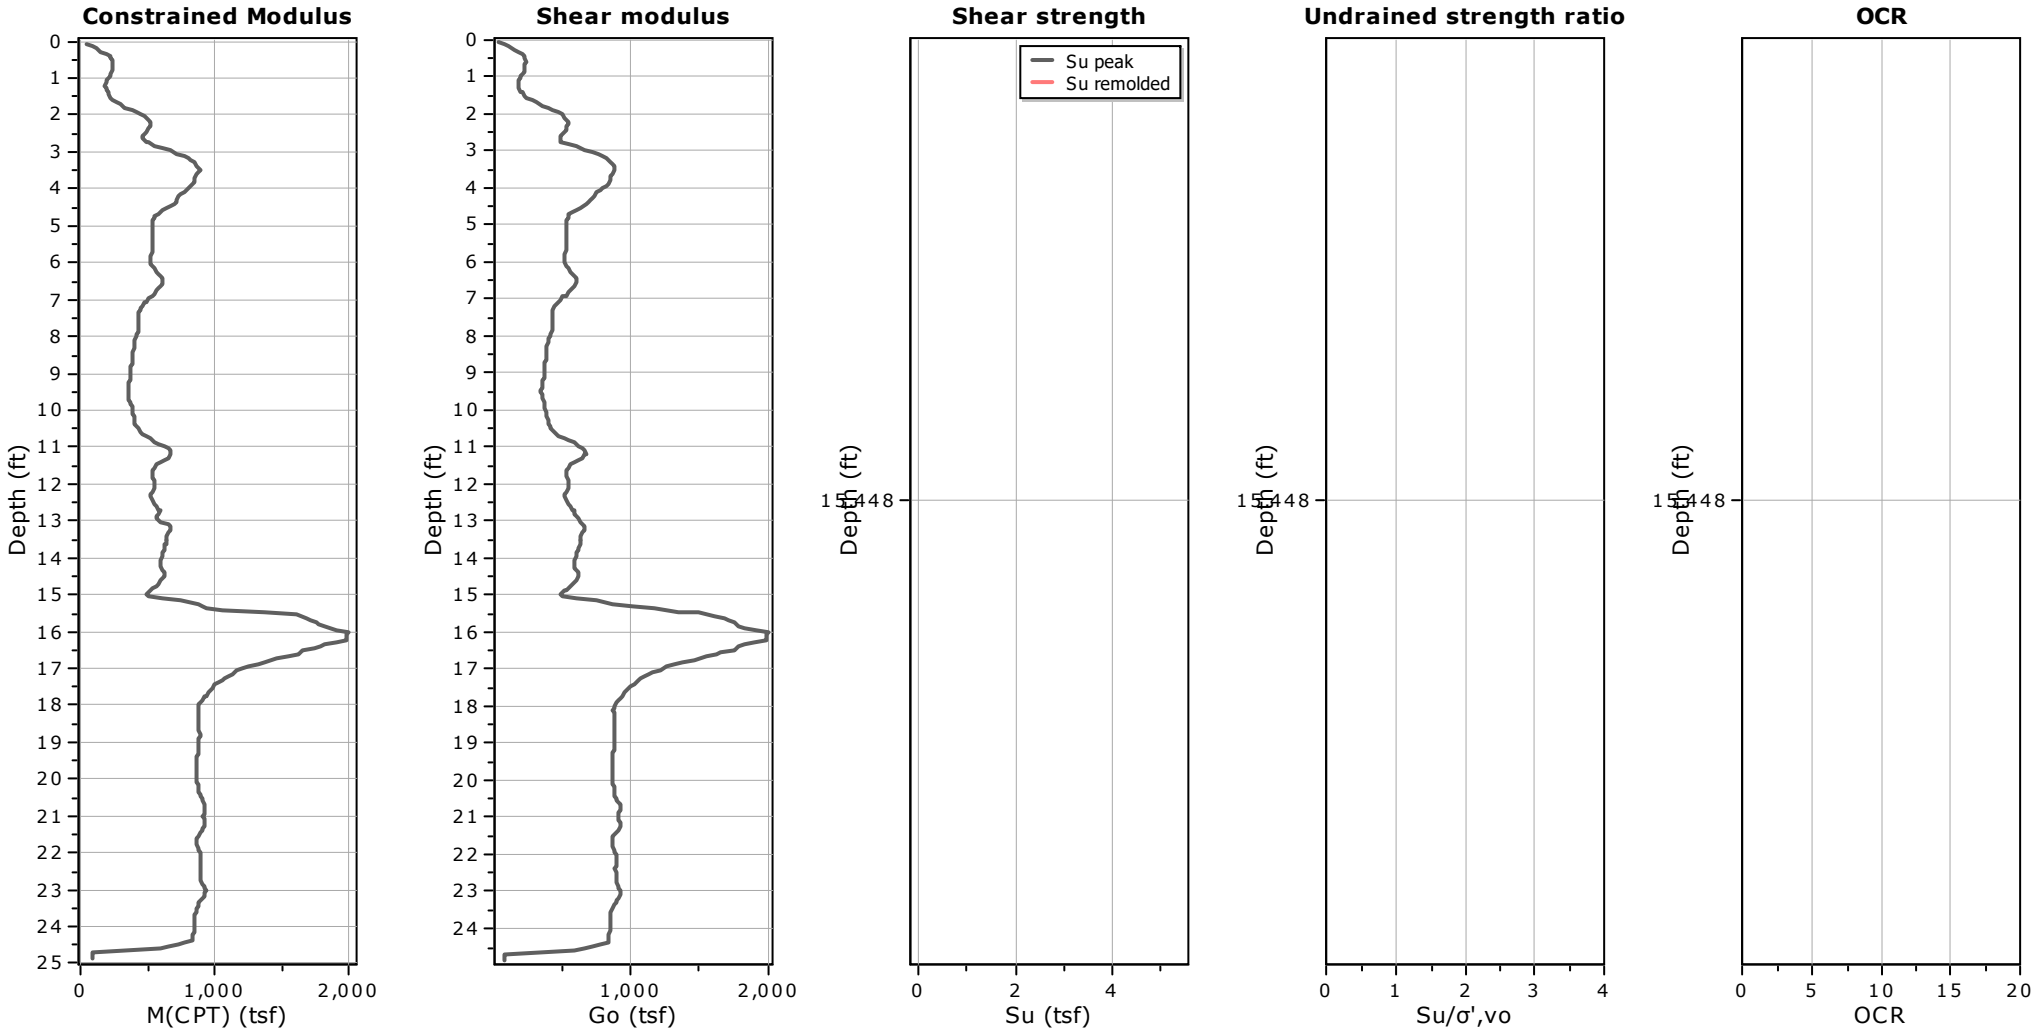


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 3
Total depth: 24.87 ft, Date: 4/20/2022
Surface Elevation: 71.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

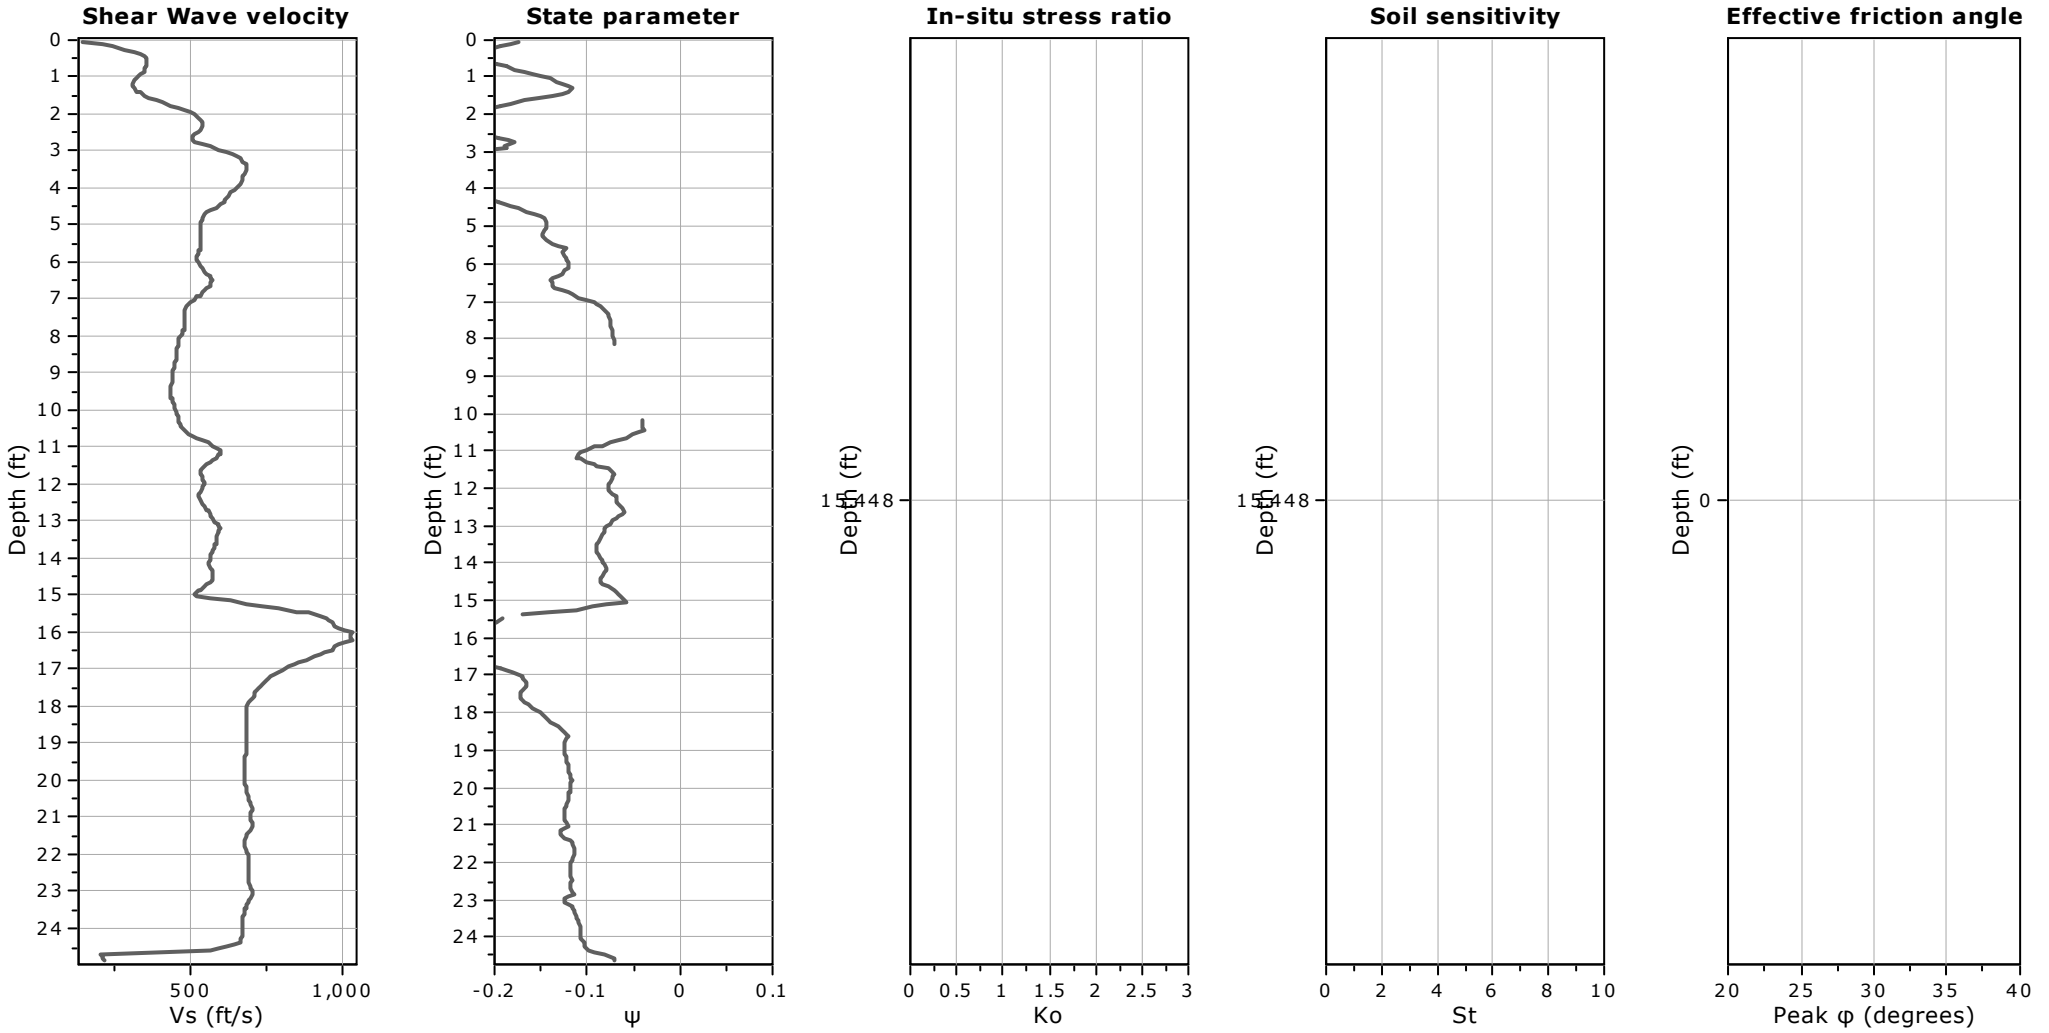

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 4
Total depth: 31.31 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

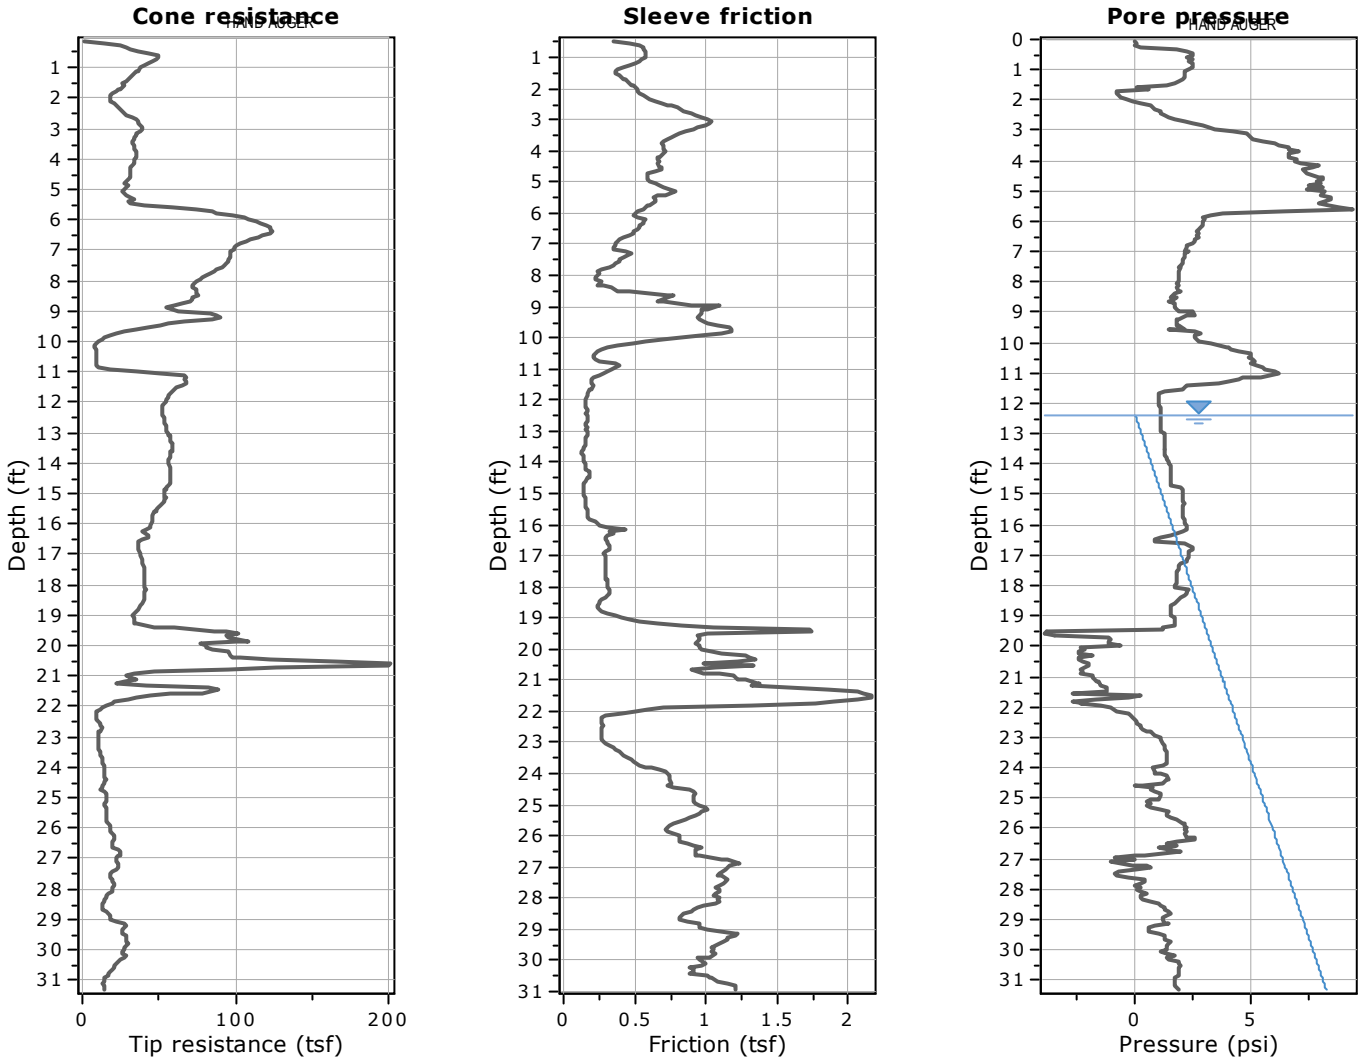


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

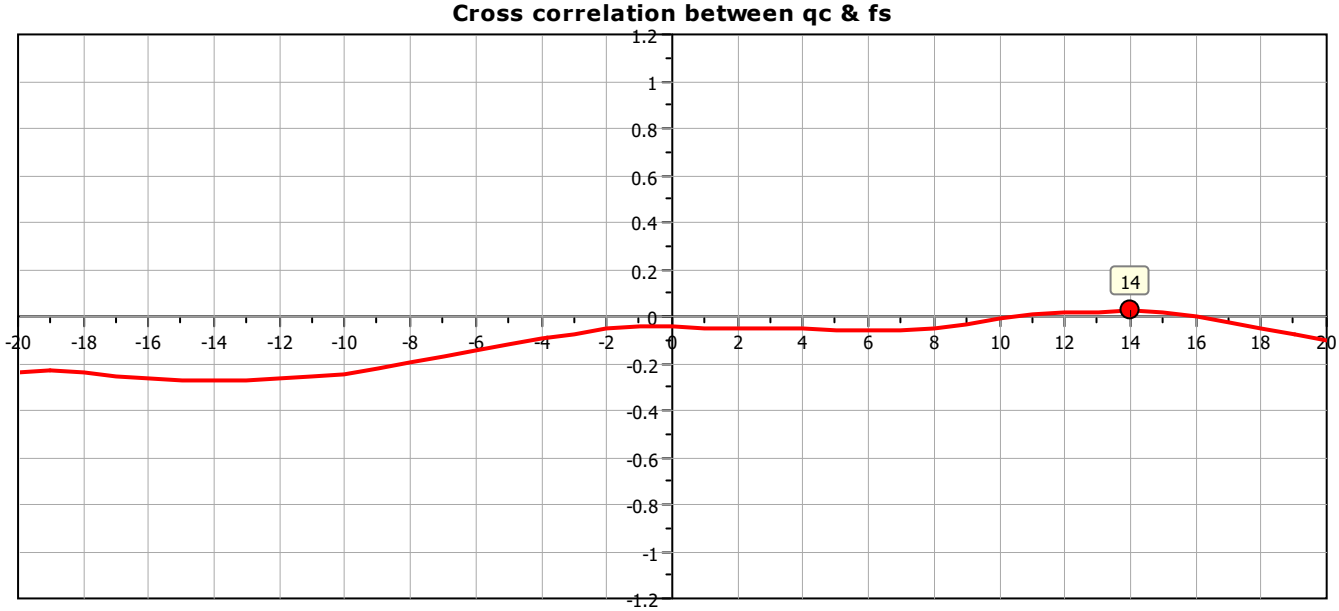

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 4
Total depth: 31.31 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

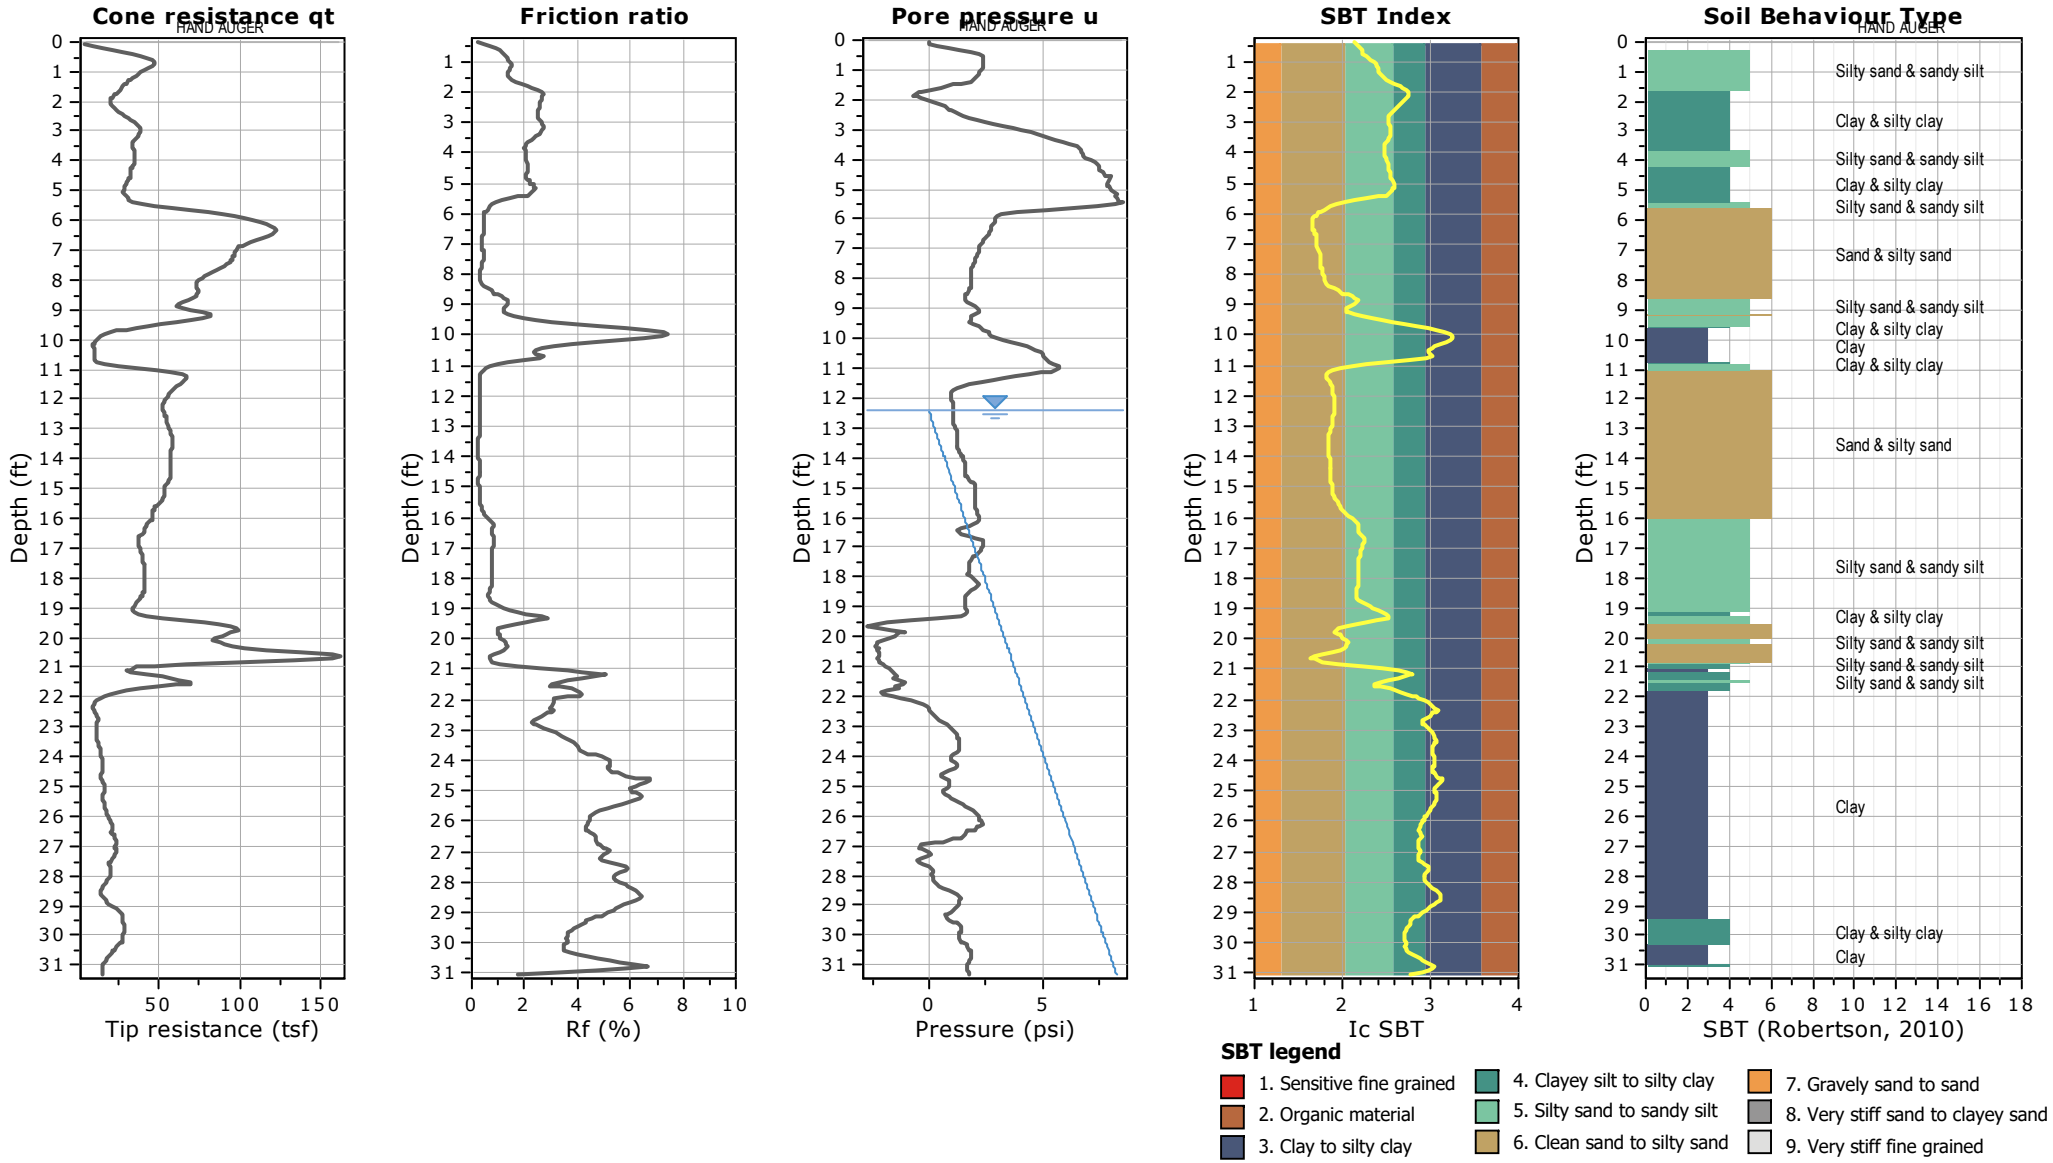



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 4
Total depth: 31.31 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

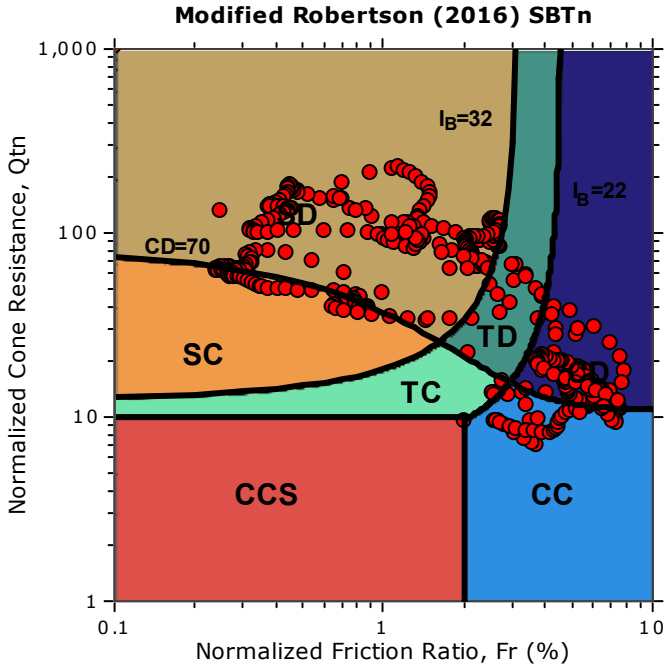

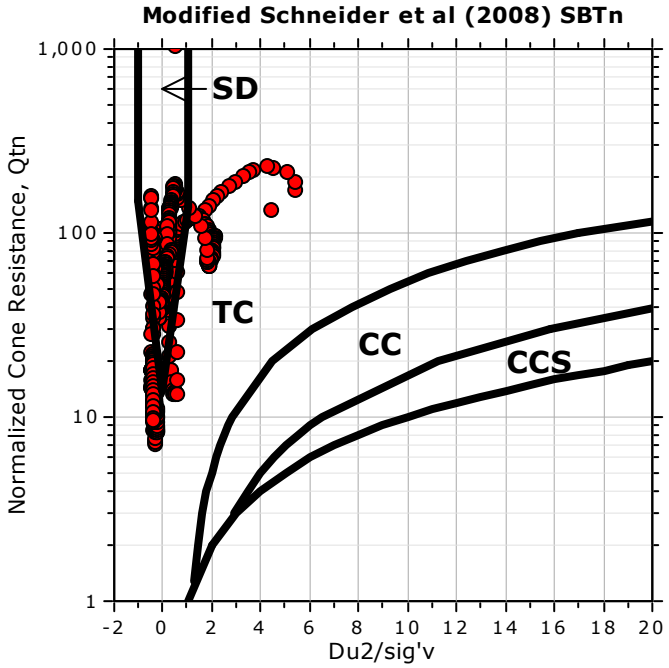

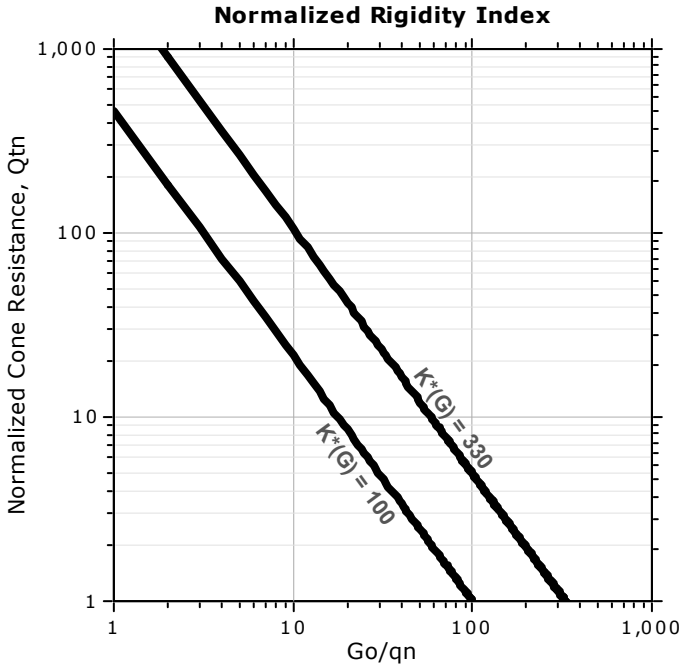


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 4
Total depth: 31.31 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

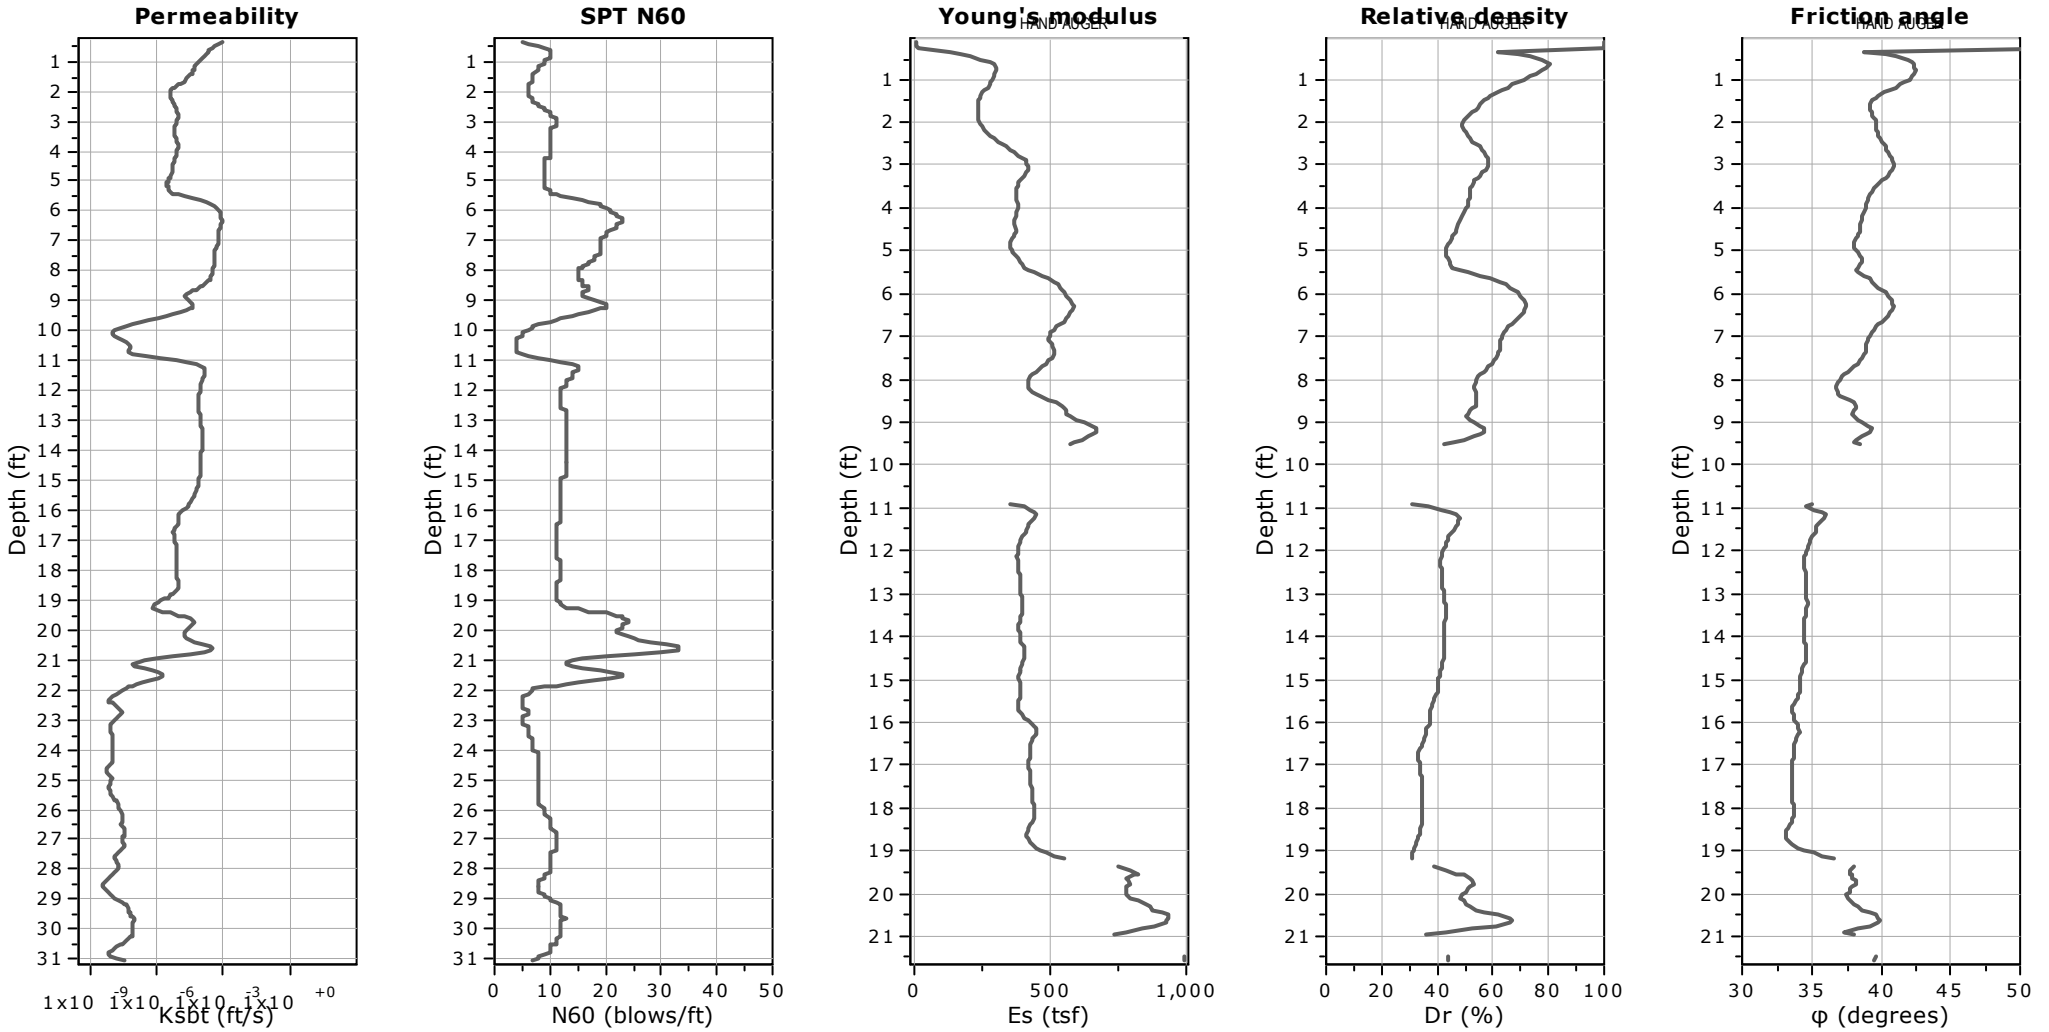


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 4
Total depth: 31.31 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

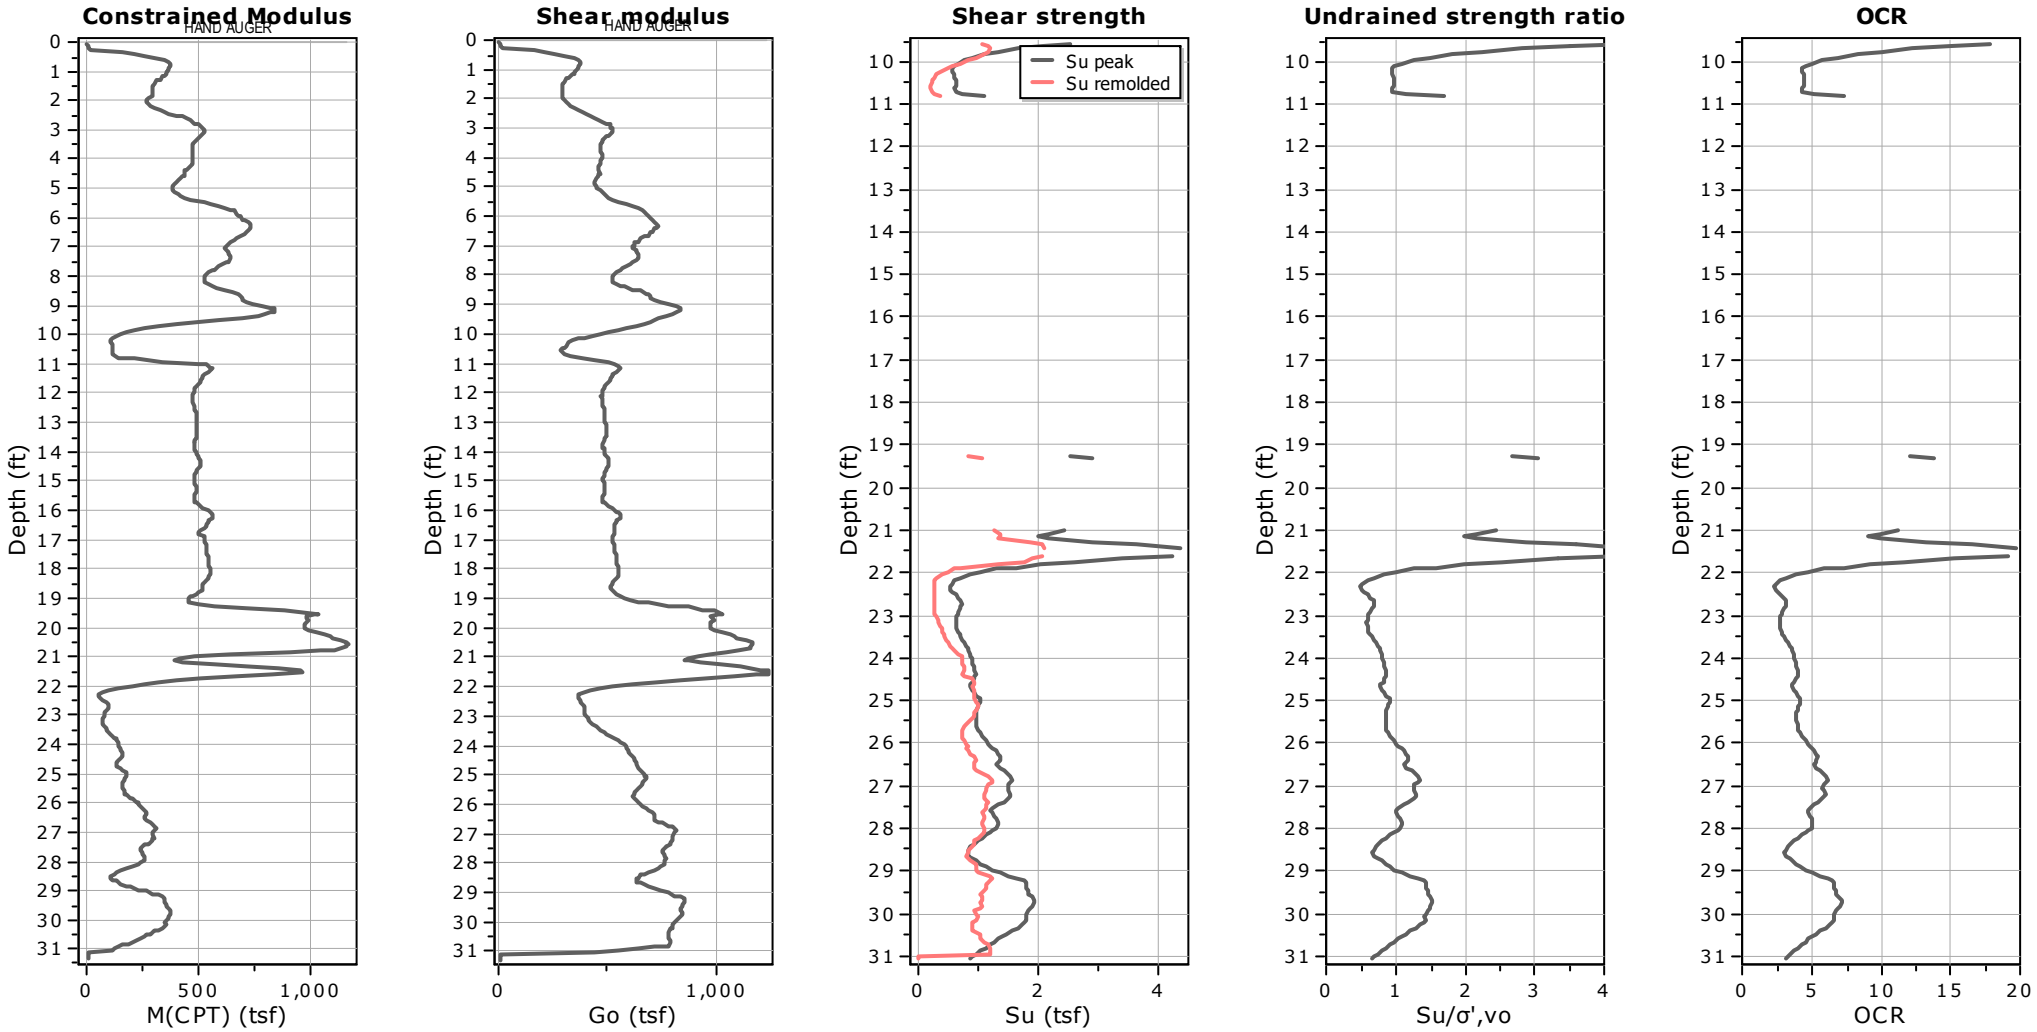


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 4
Total depth: 31.31 ft, Date: 4/20/2022
Surface Elevation: 75.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

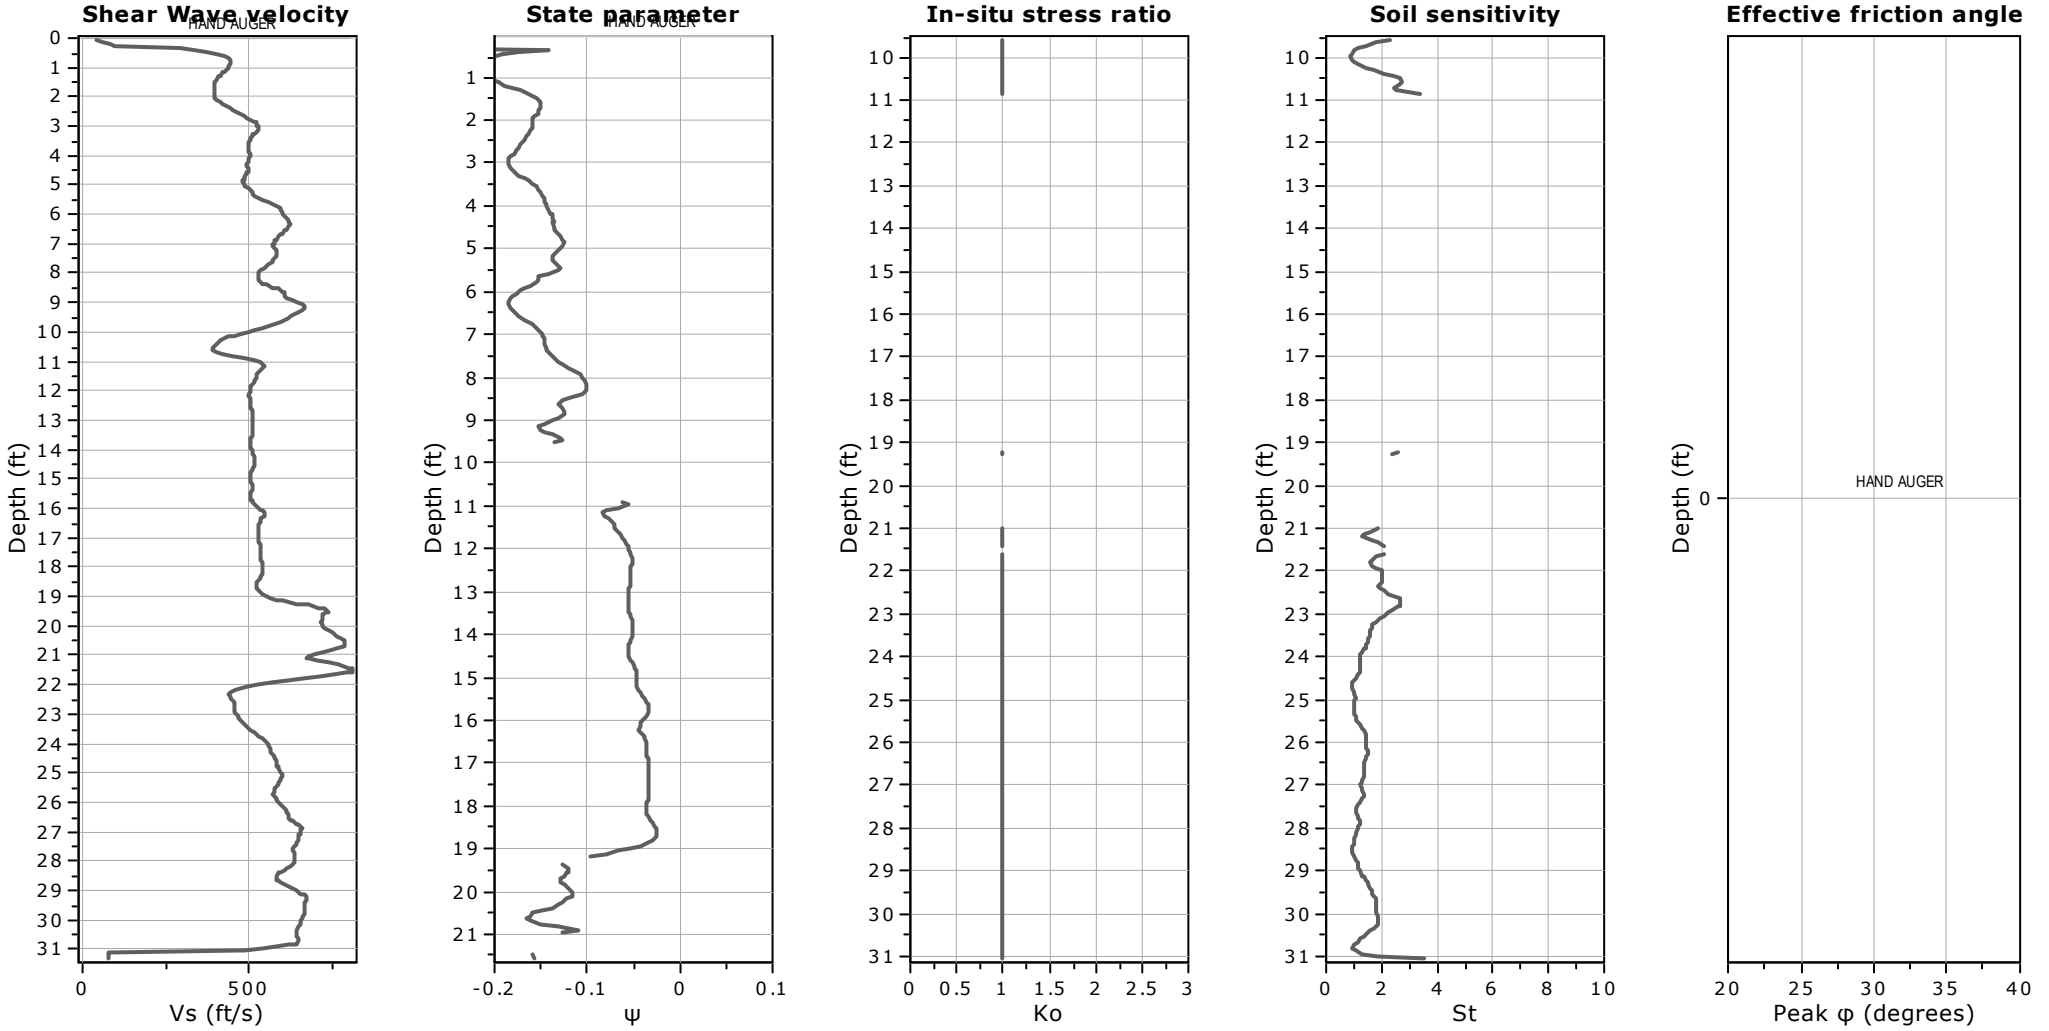

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 5
Total depth: 27.05 ft, Date: 4/20/2022
Surface Elevation: 73.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

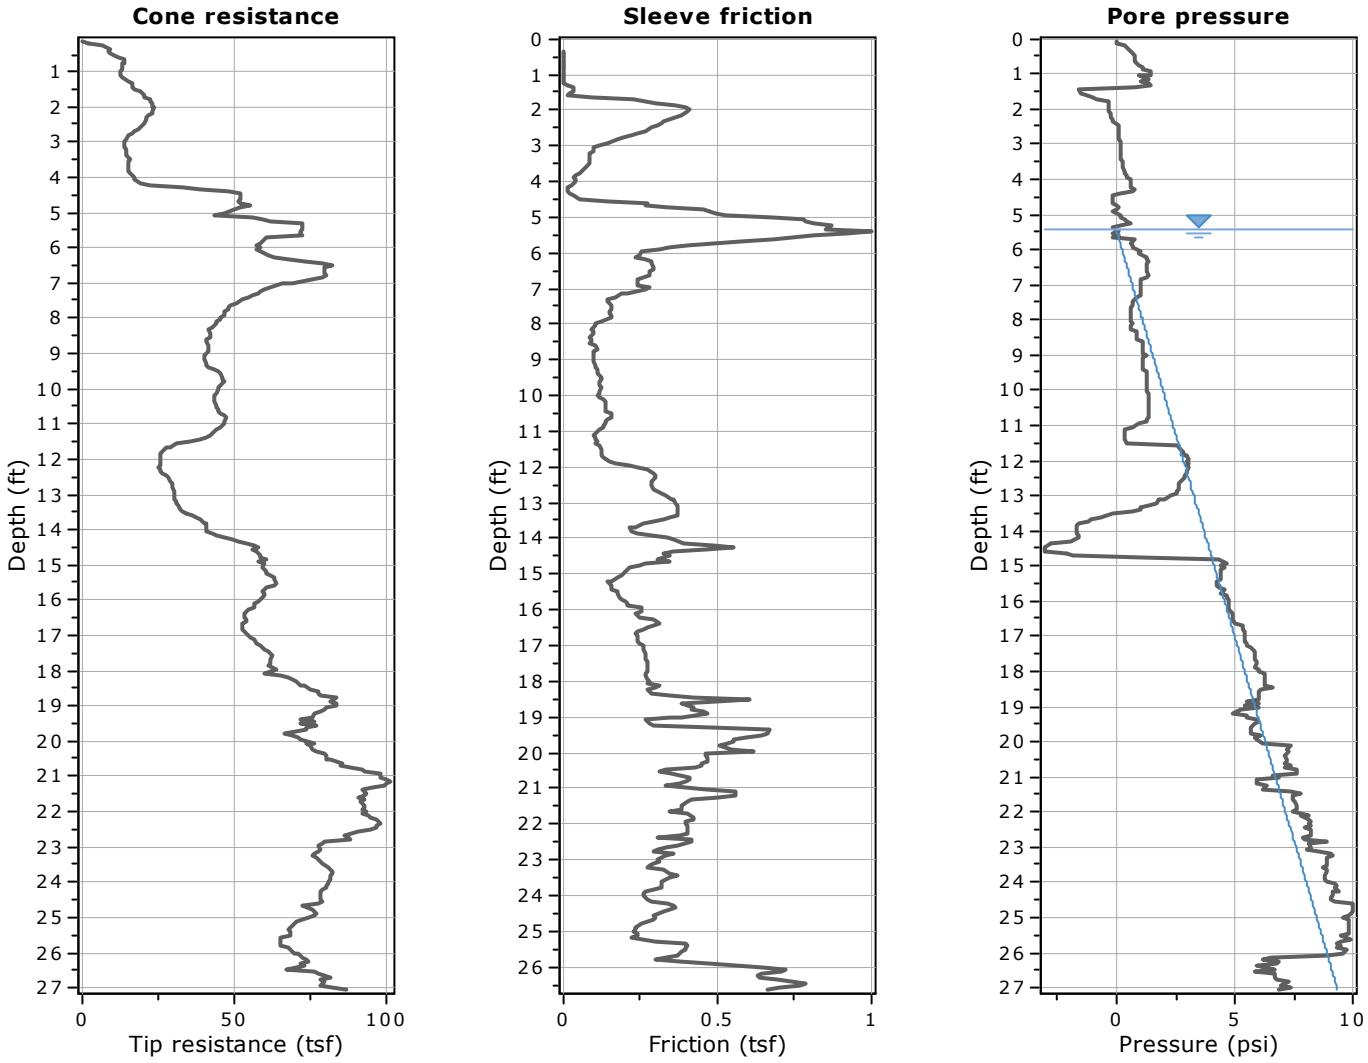


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

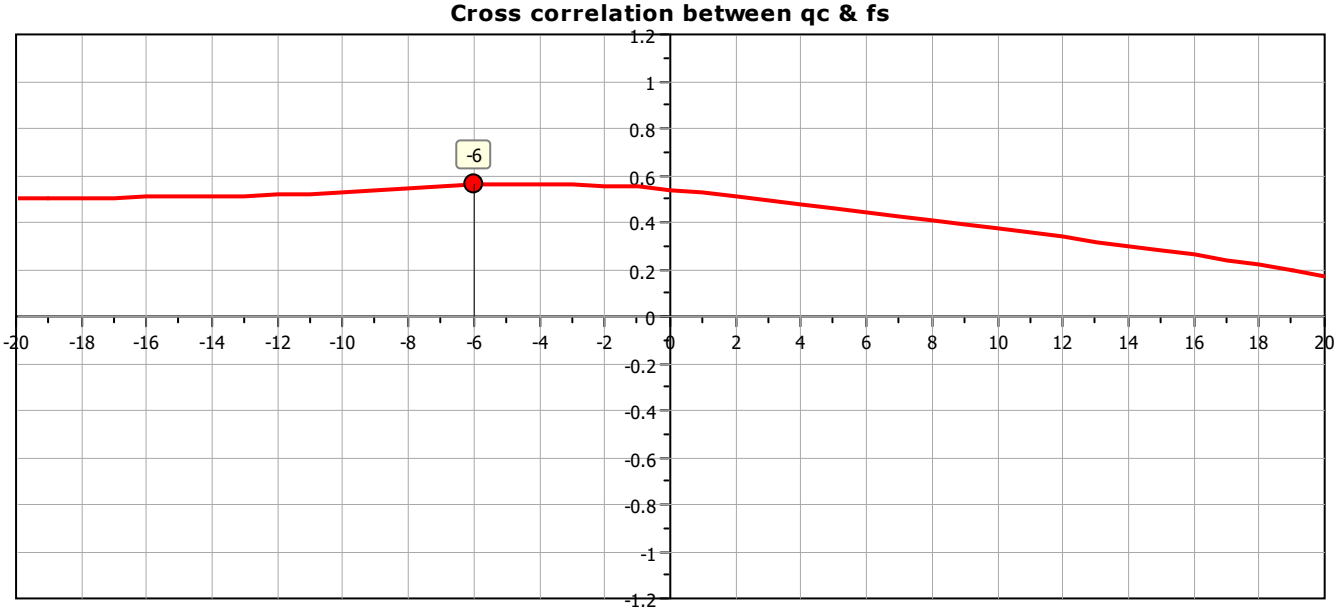

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 5
Total depth: 27.05 ft, Date: 4/20/2022
Surface Elevation: 73.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

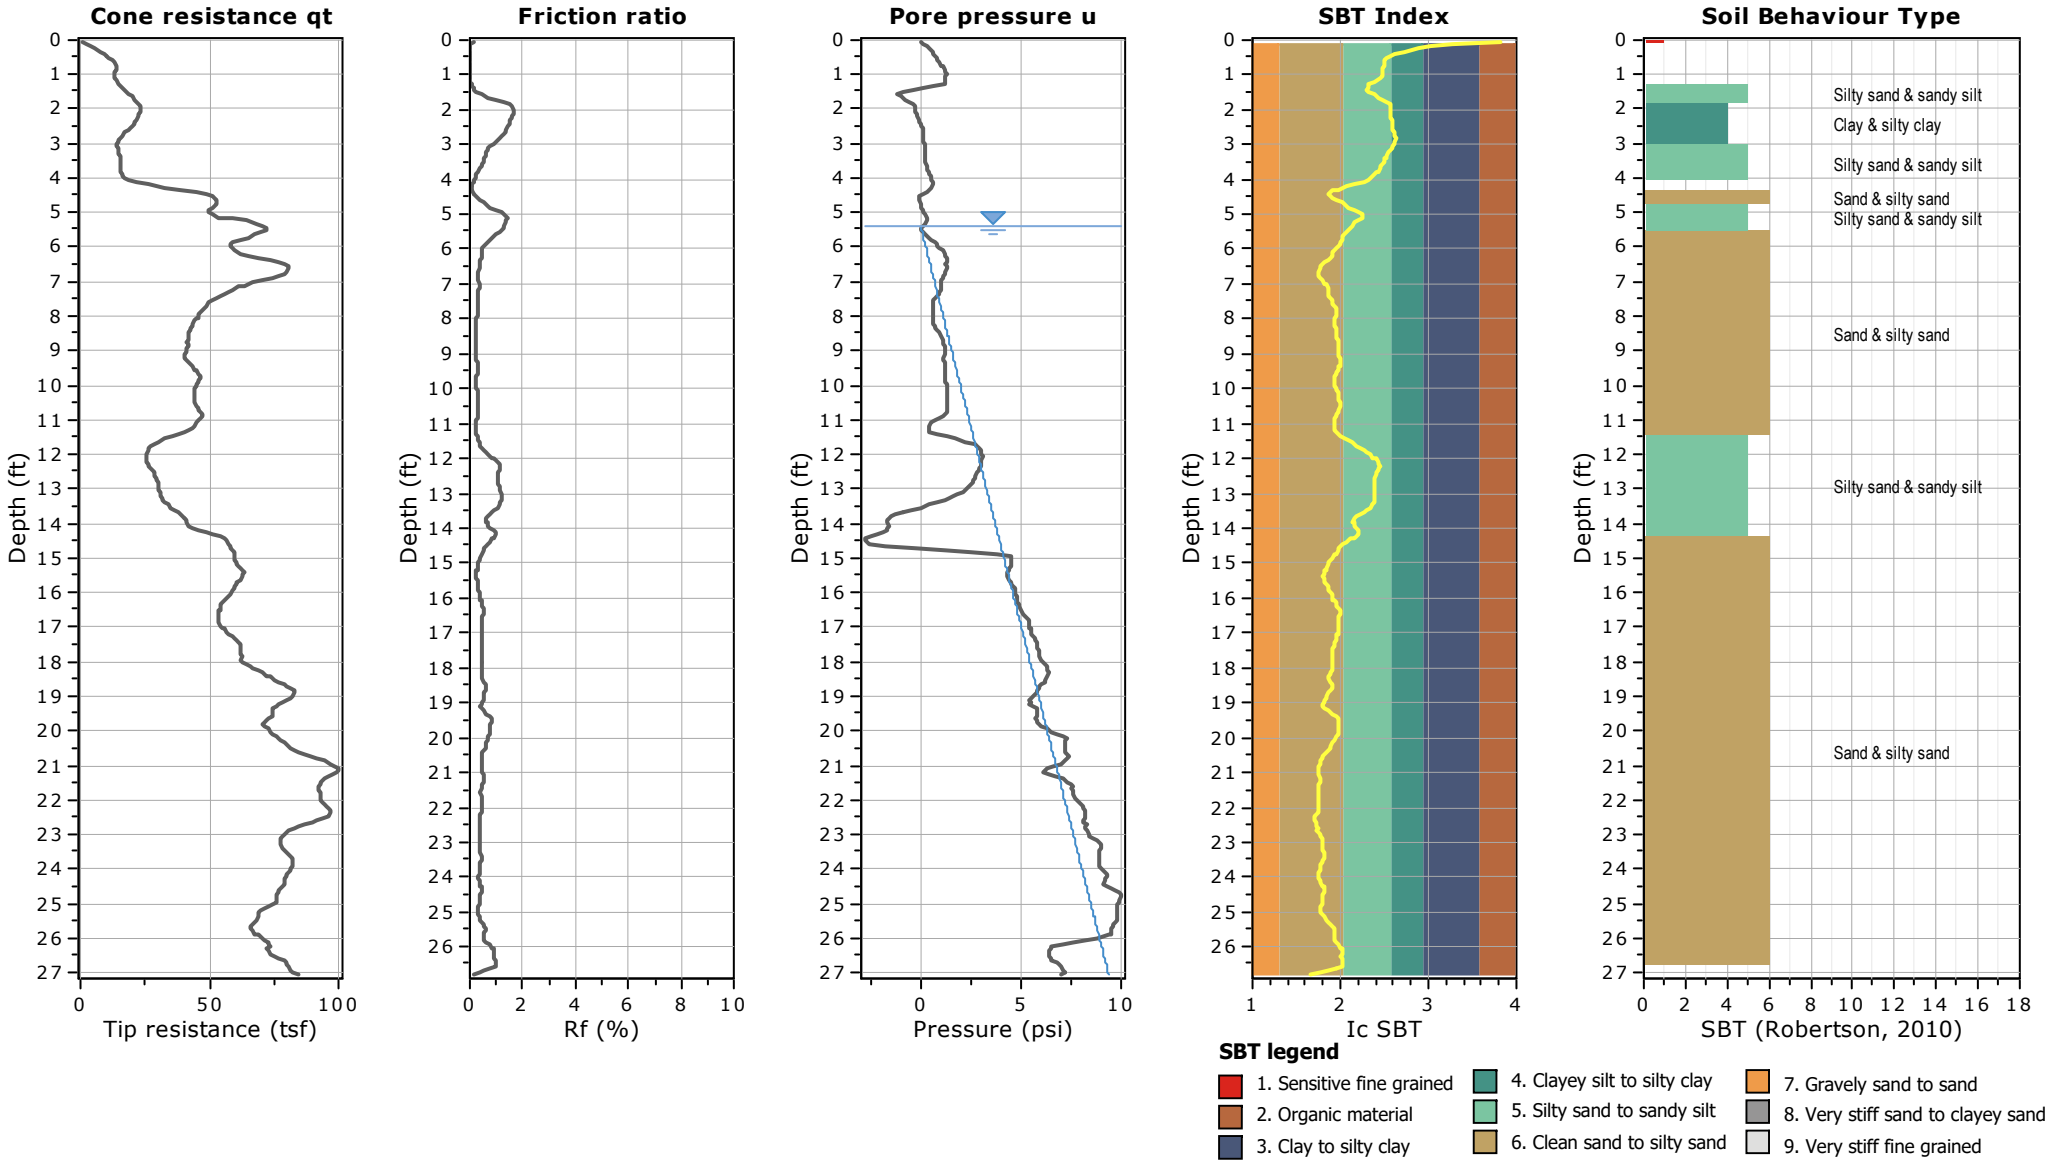



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 5
Total depth: 27.05 ft, Date: 4/20/2022
Surface Elevation: 73.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

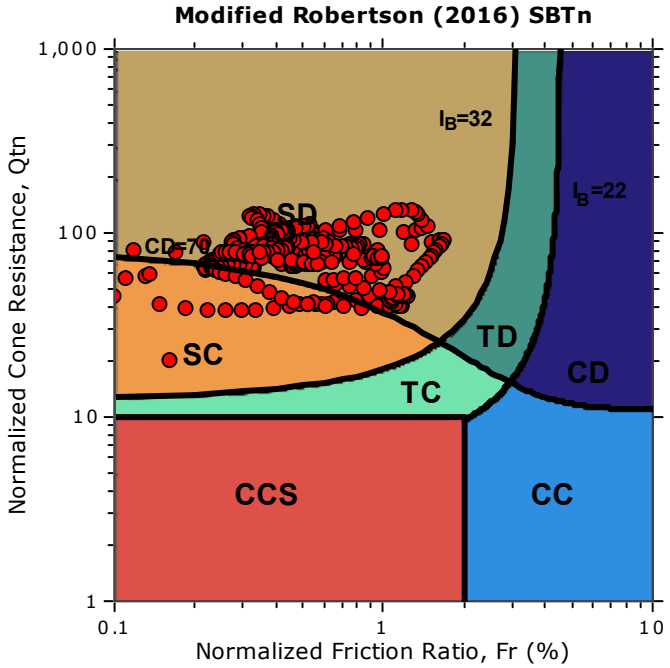

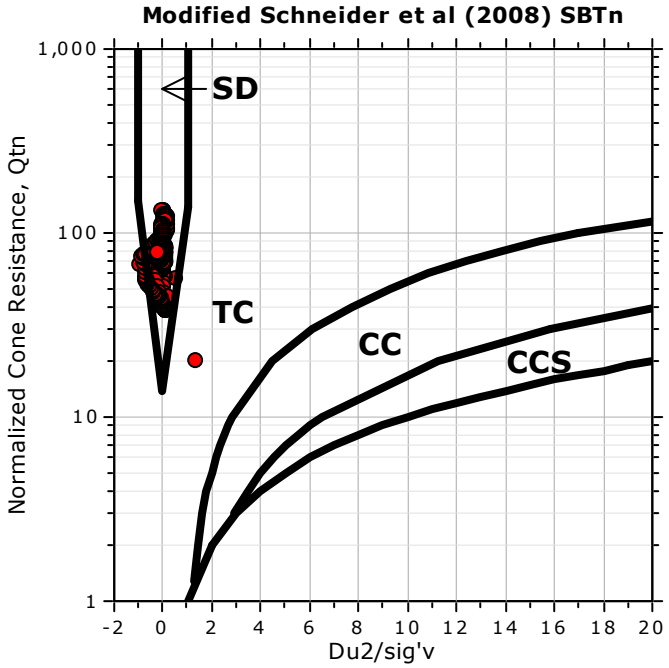

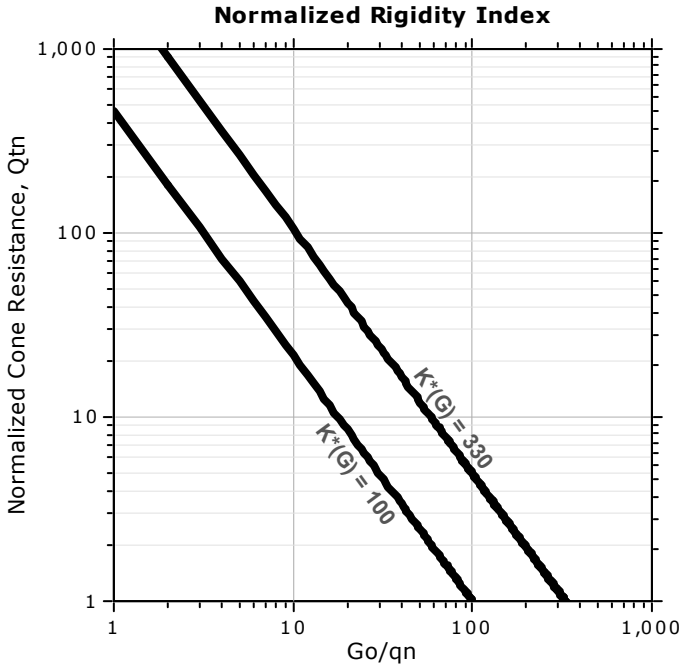


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 5
Total depth: 27.05 ft, Date: 4/20/2022
Surface Elevation: 73.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

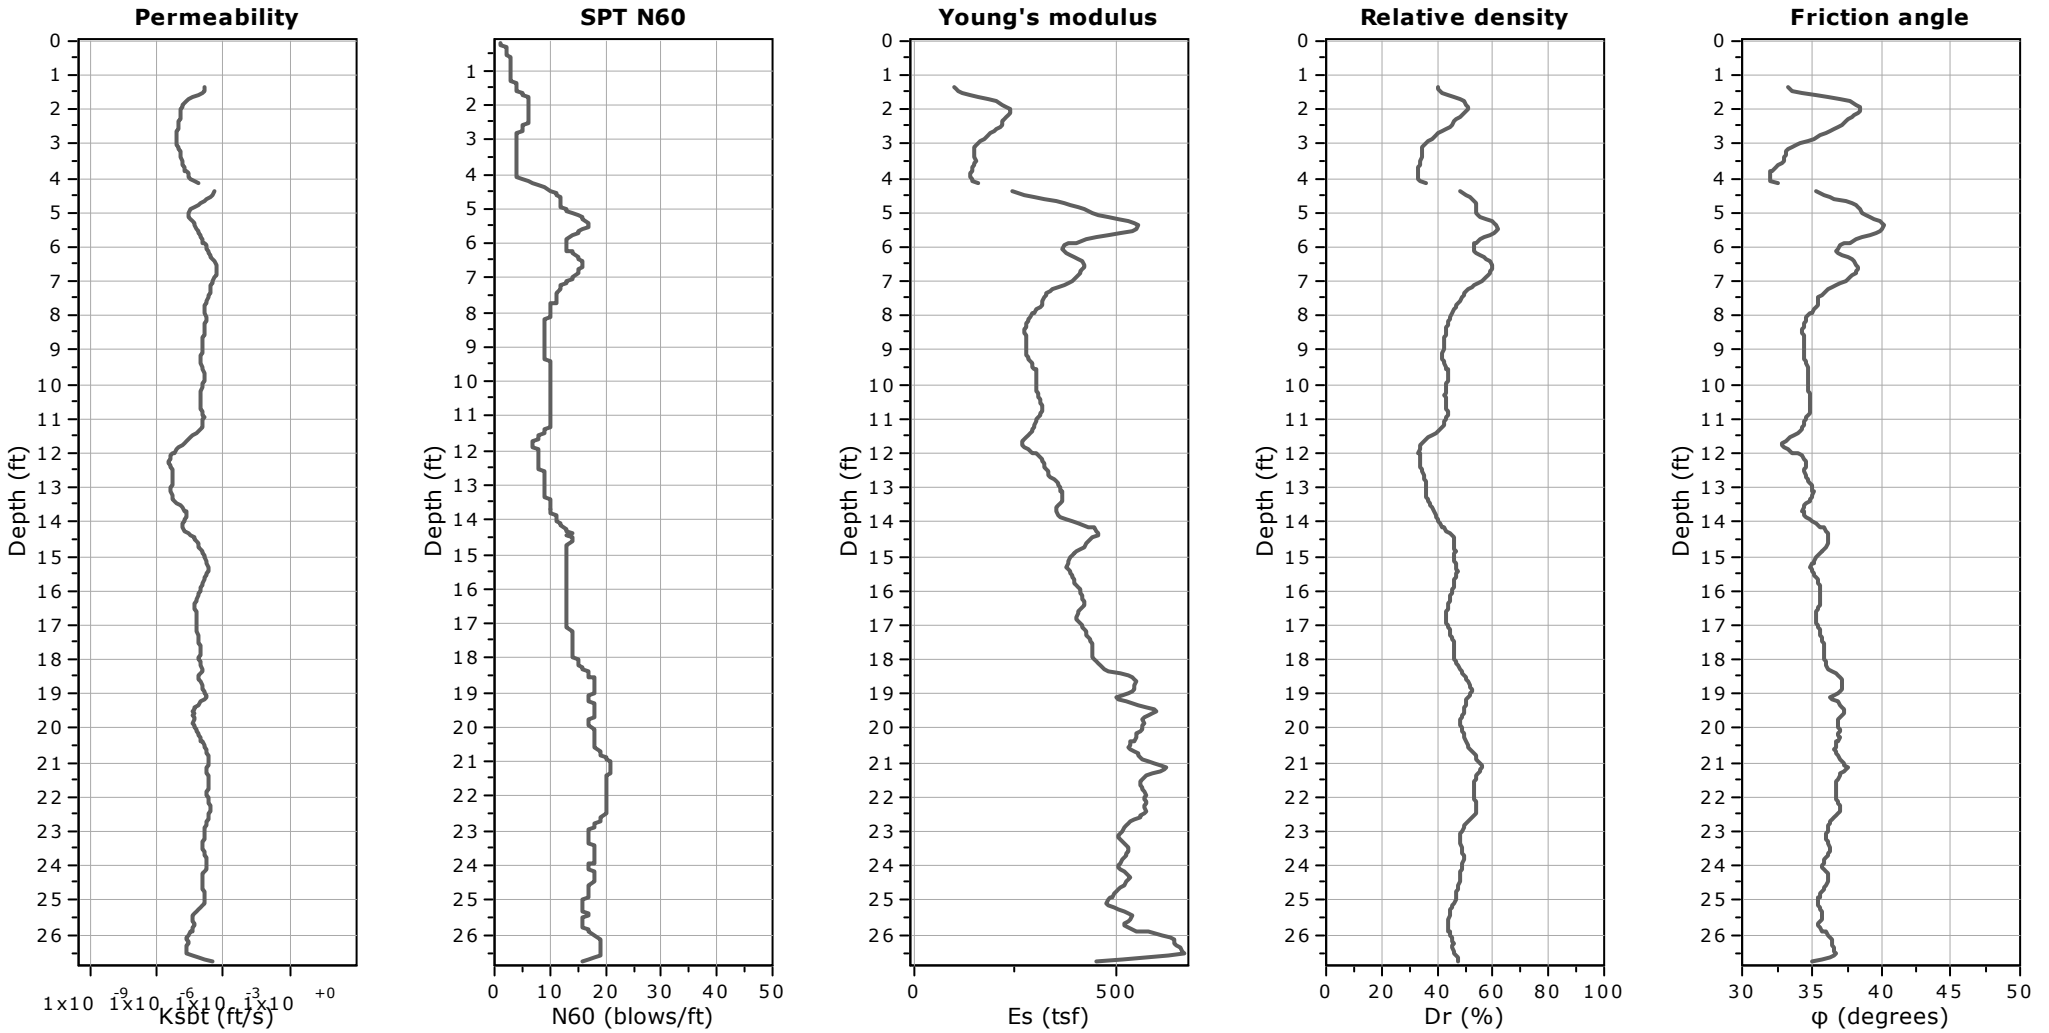


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 5
Total depth: 27.05 ft, Date: 4/20/2022
Surface Elevation: 73.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

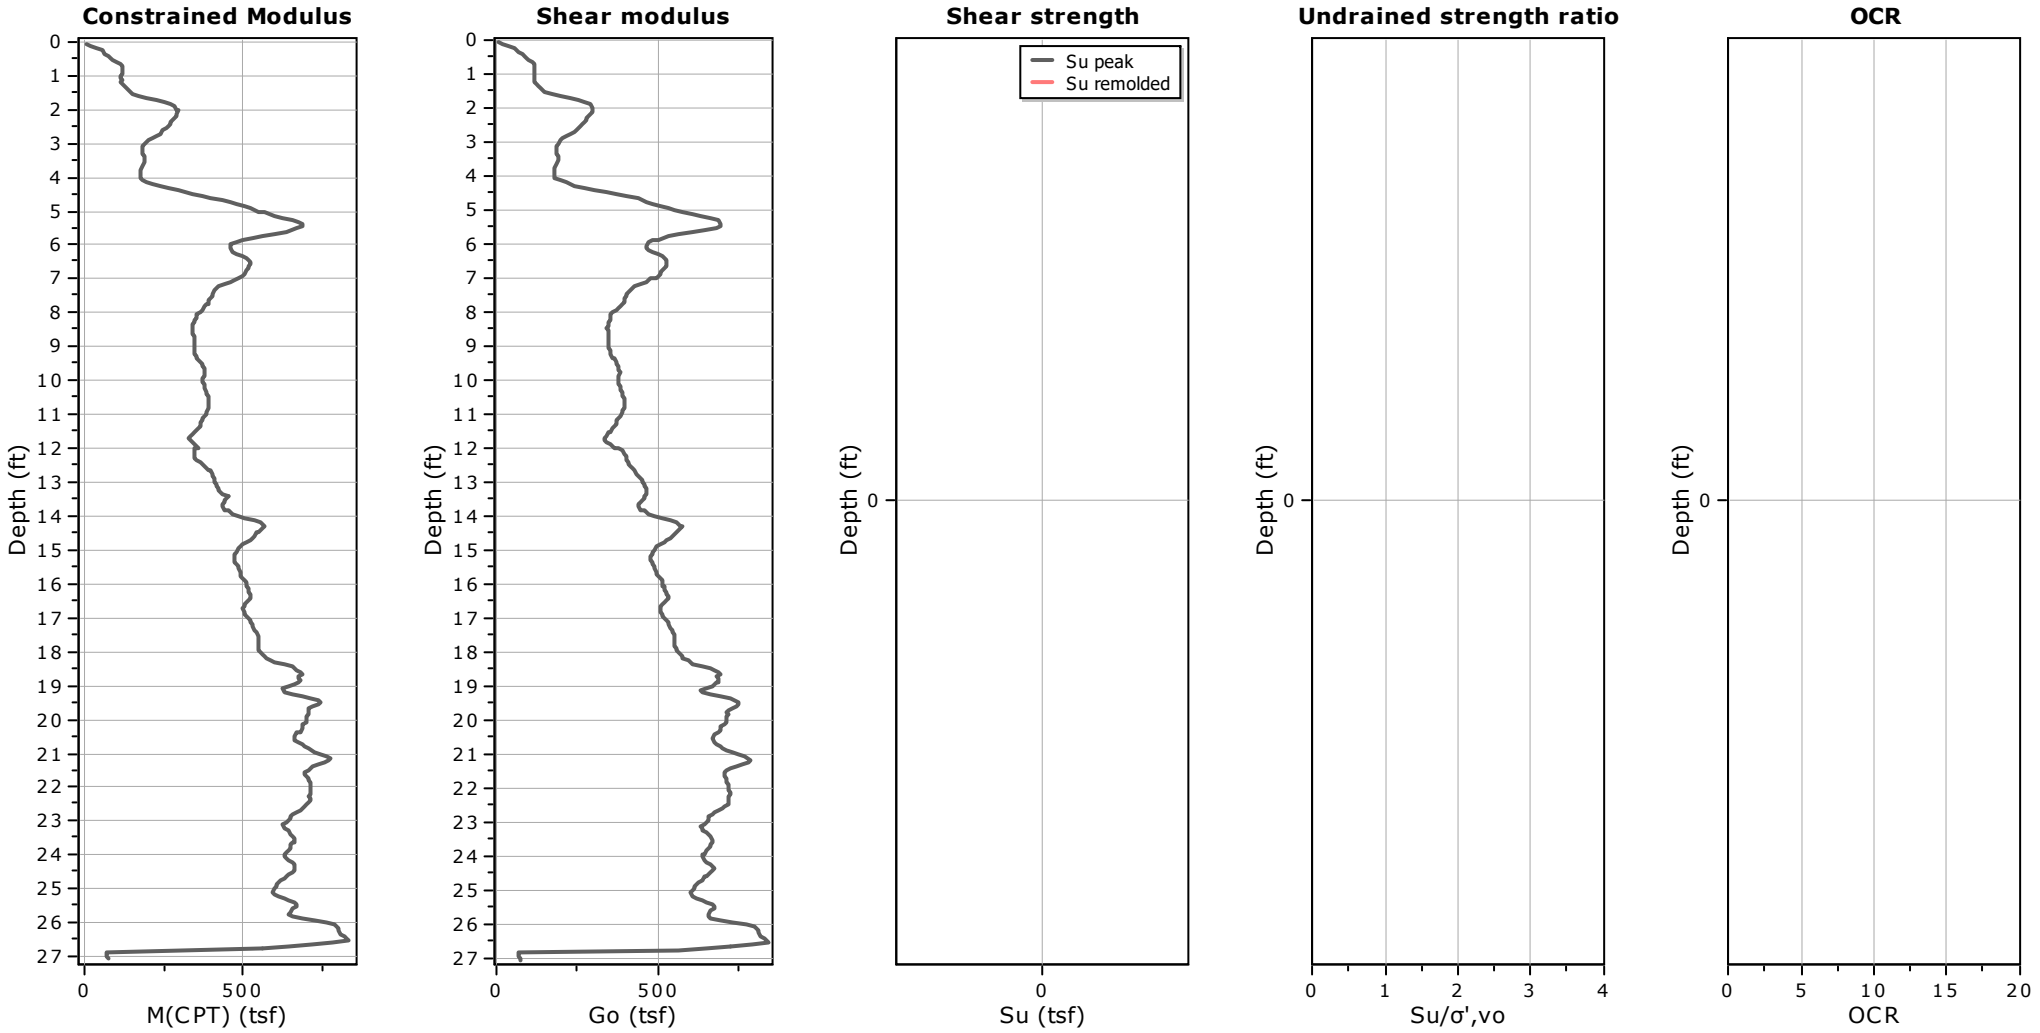


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 5
Total depth: 27.05 ft, Date: 4/20/2022
Surface Elevation: 73.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

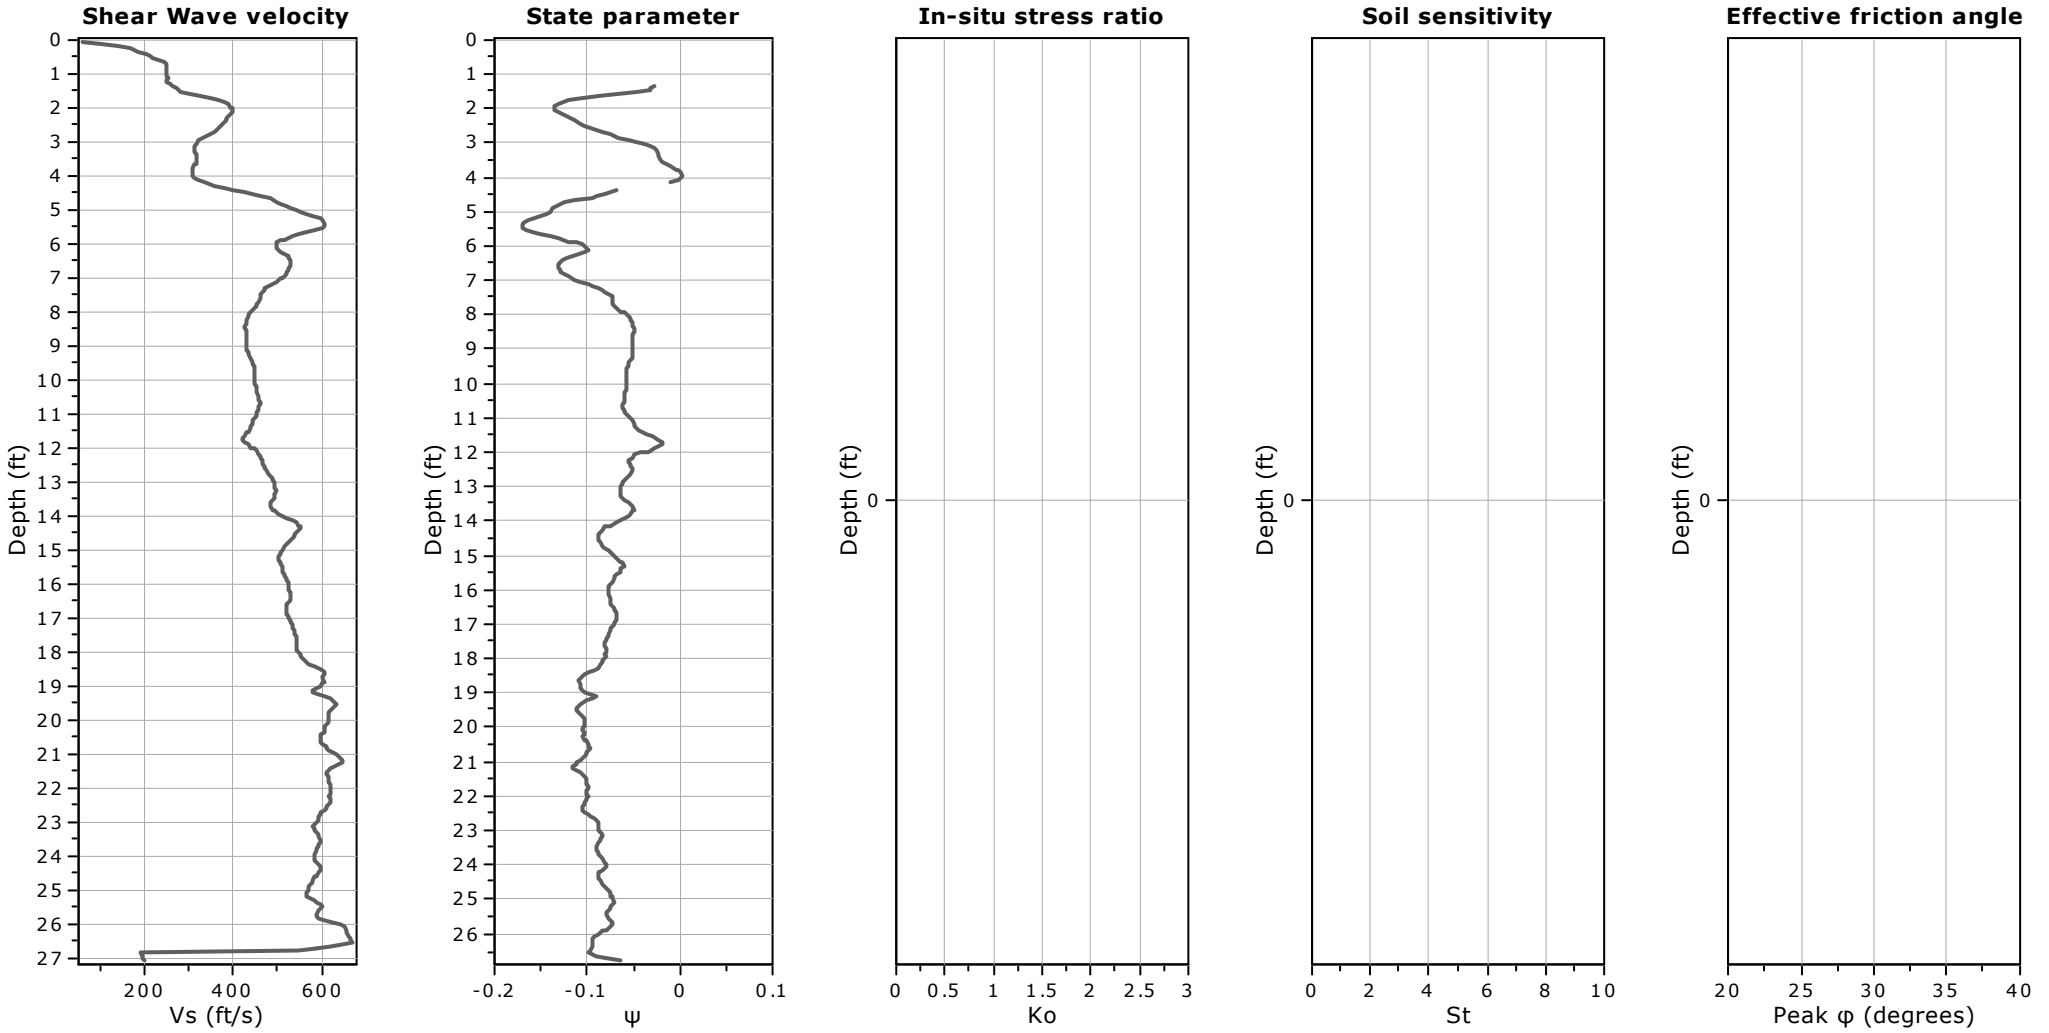

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 6
Total depth: 27.06 ft, Date: 4/20/2022
Surface Elevation: 78.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

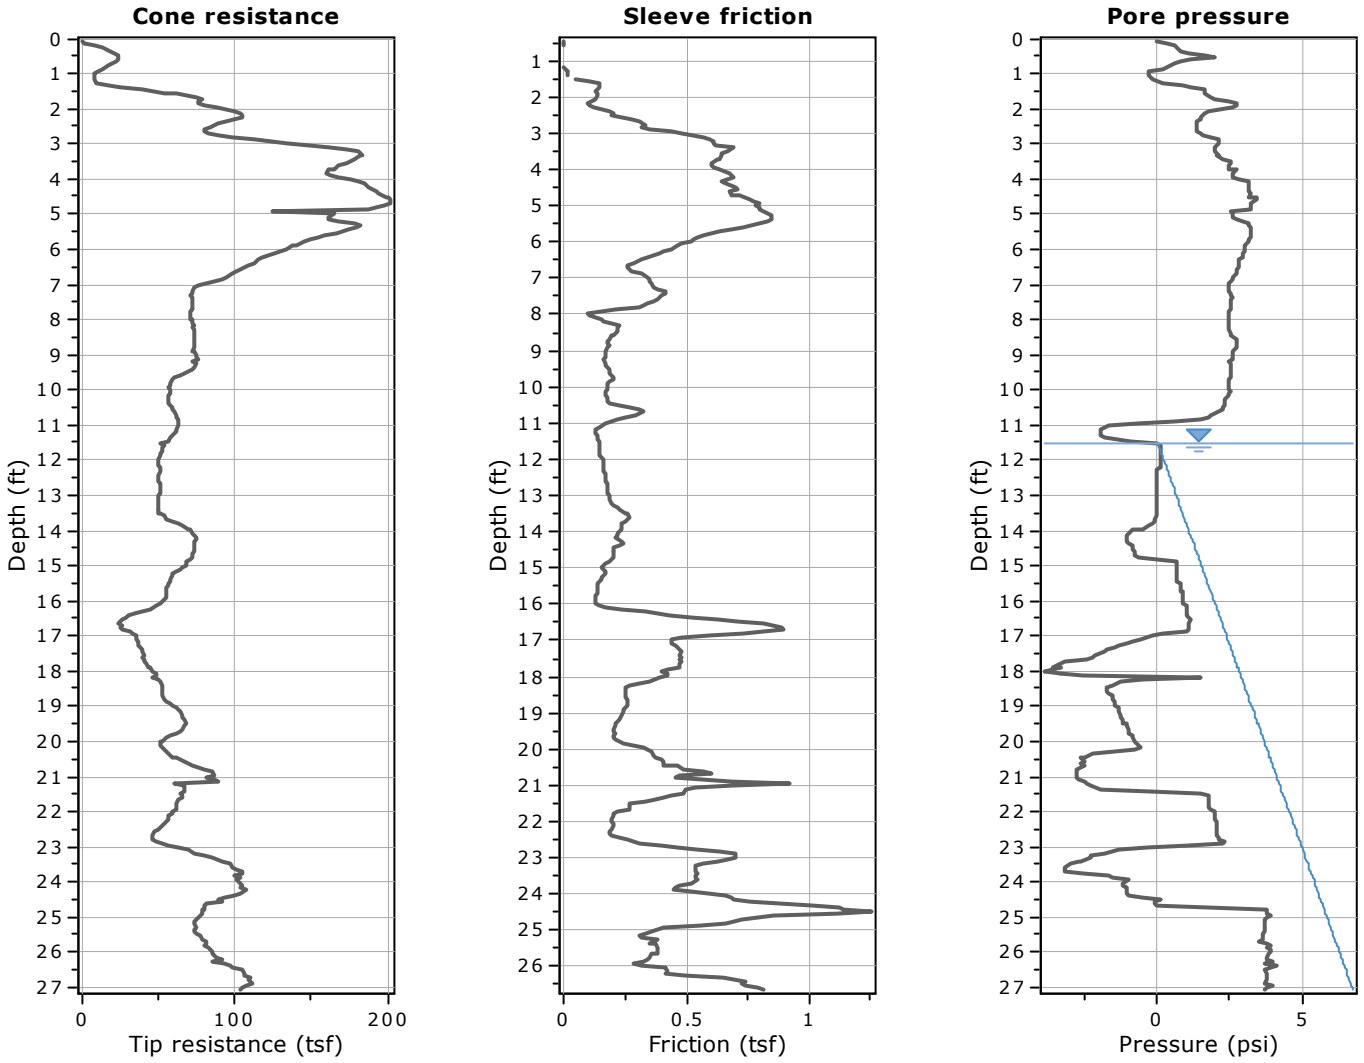


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

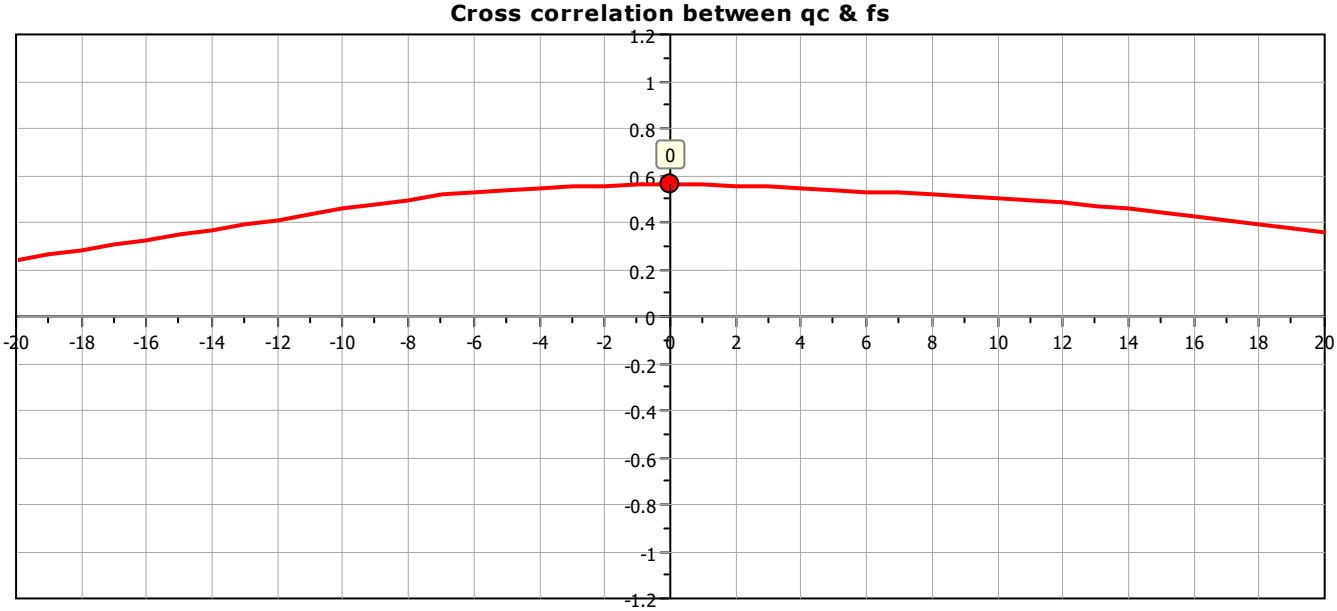

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 6
Total depth: 27.06 ft, Date: 4/20/2022
Surface Elevation: 78.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

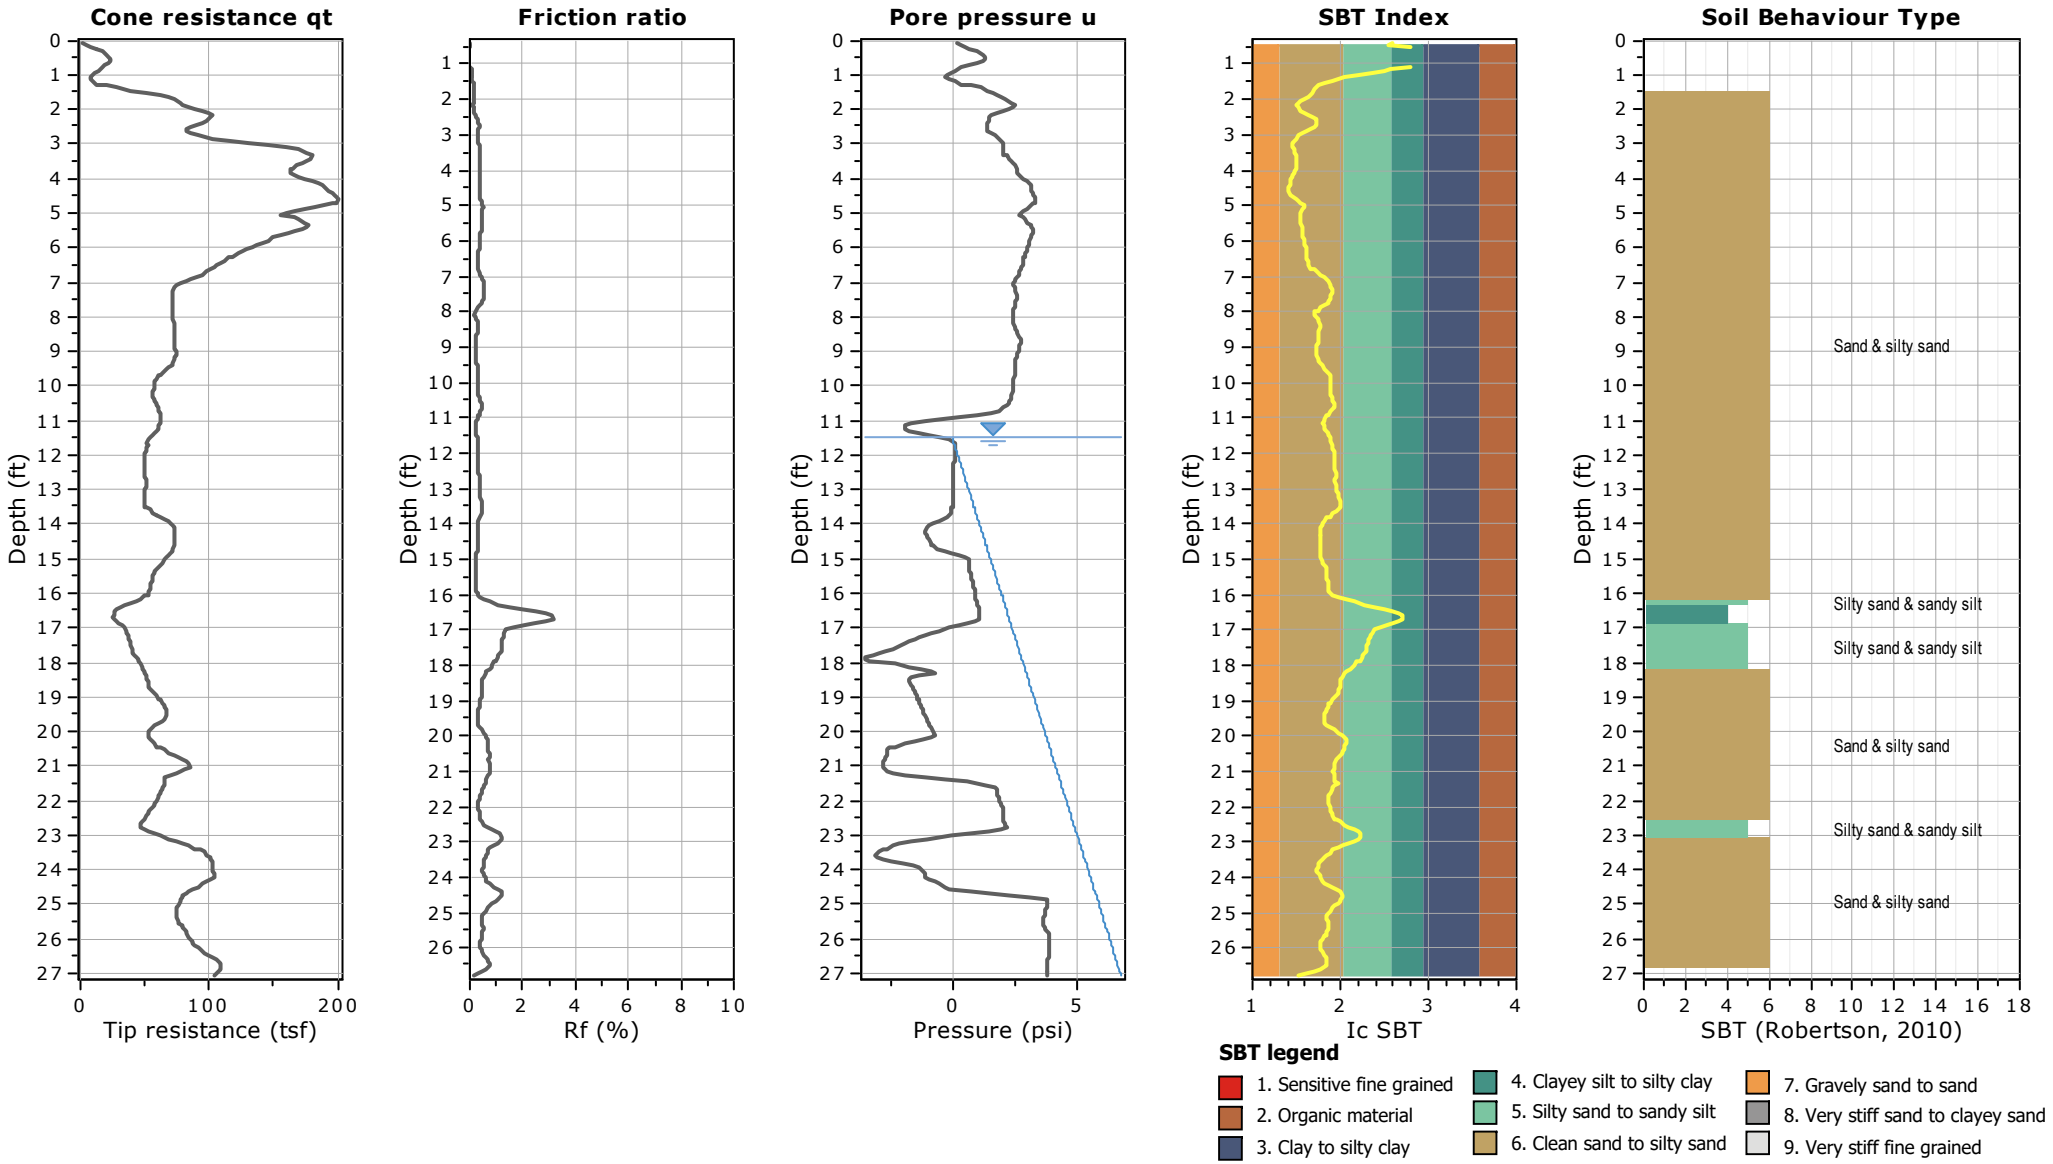



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 6
Total depth: 27.06 ft, Date: 4/20/2022
Surface Elevation: 78.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

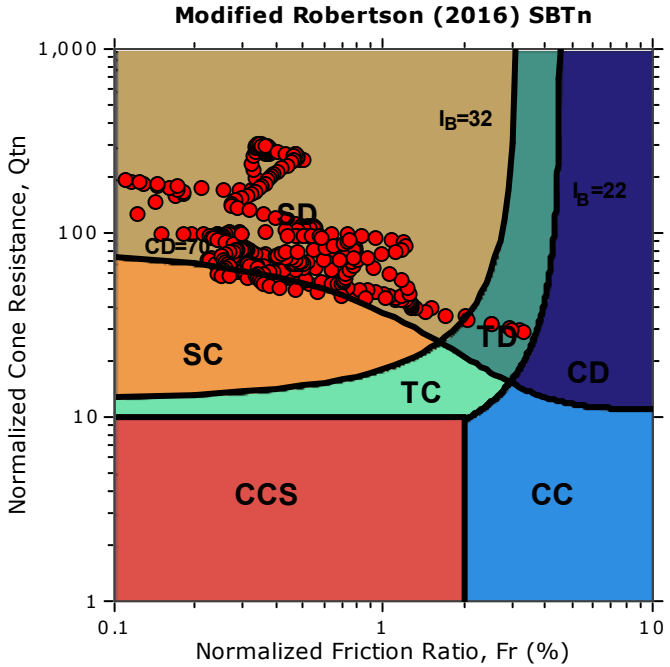

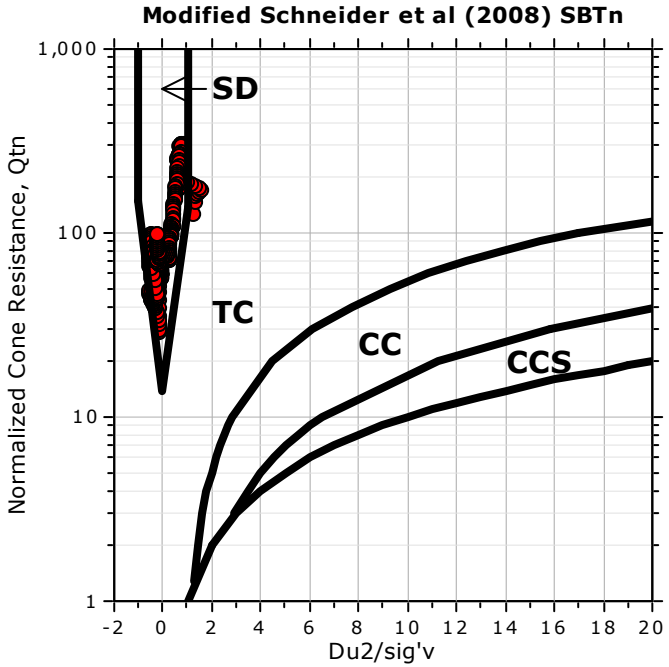

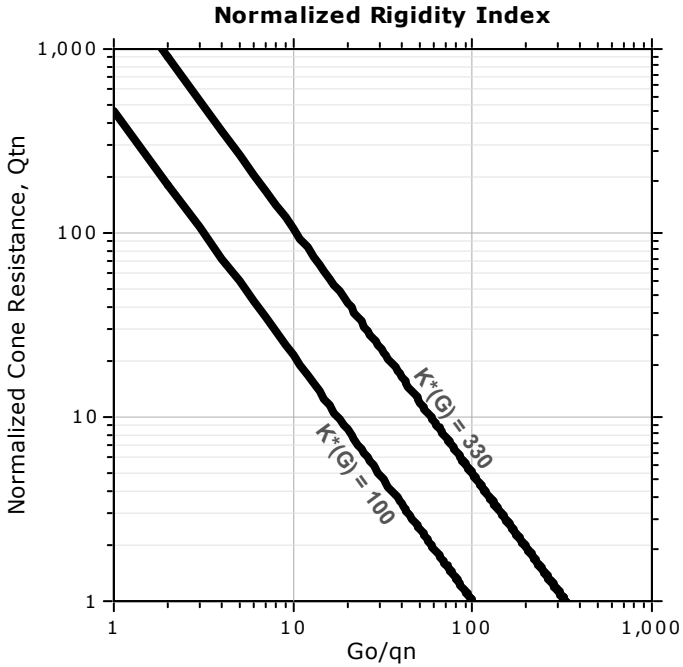


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 6
Total depth: 27.06 ft, Date: 4/20/2022
Surface Elevation: 78.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

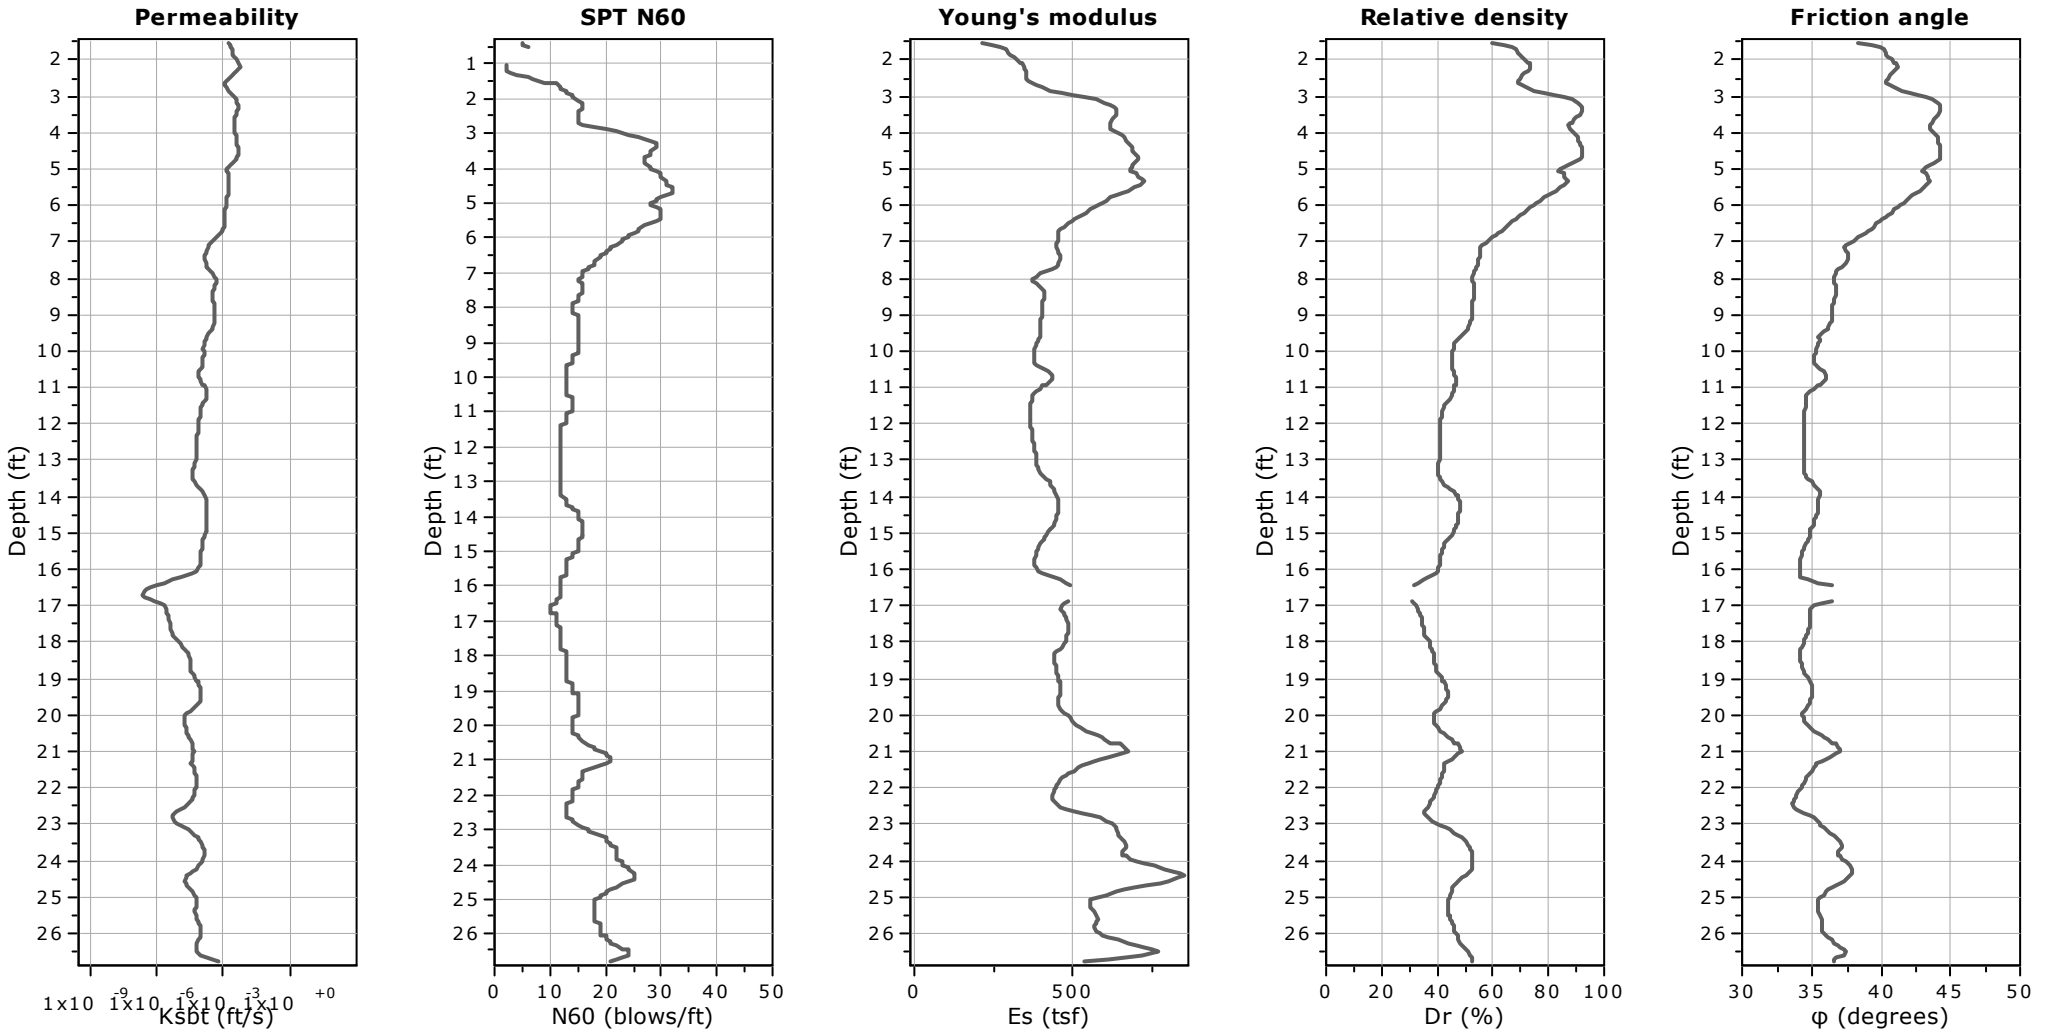


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 6
Total depth: 27.06 ft, Date: 4/20/2022
Surface Elevation: 78.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

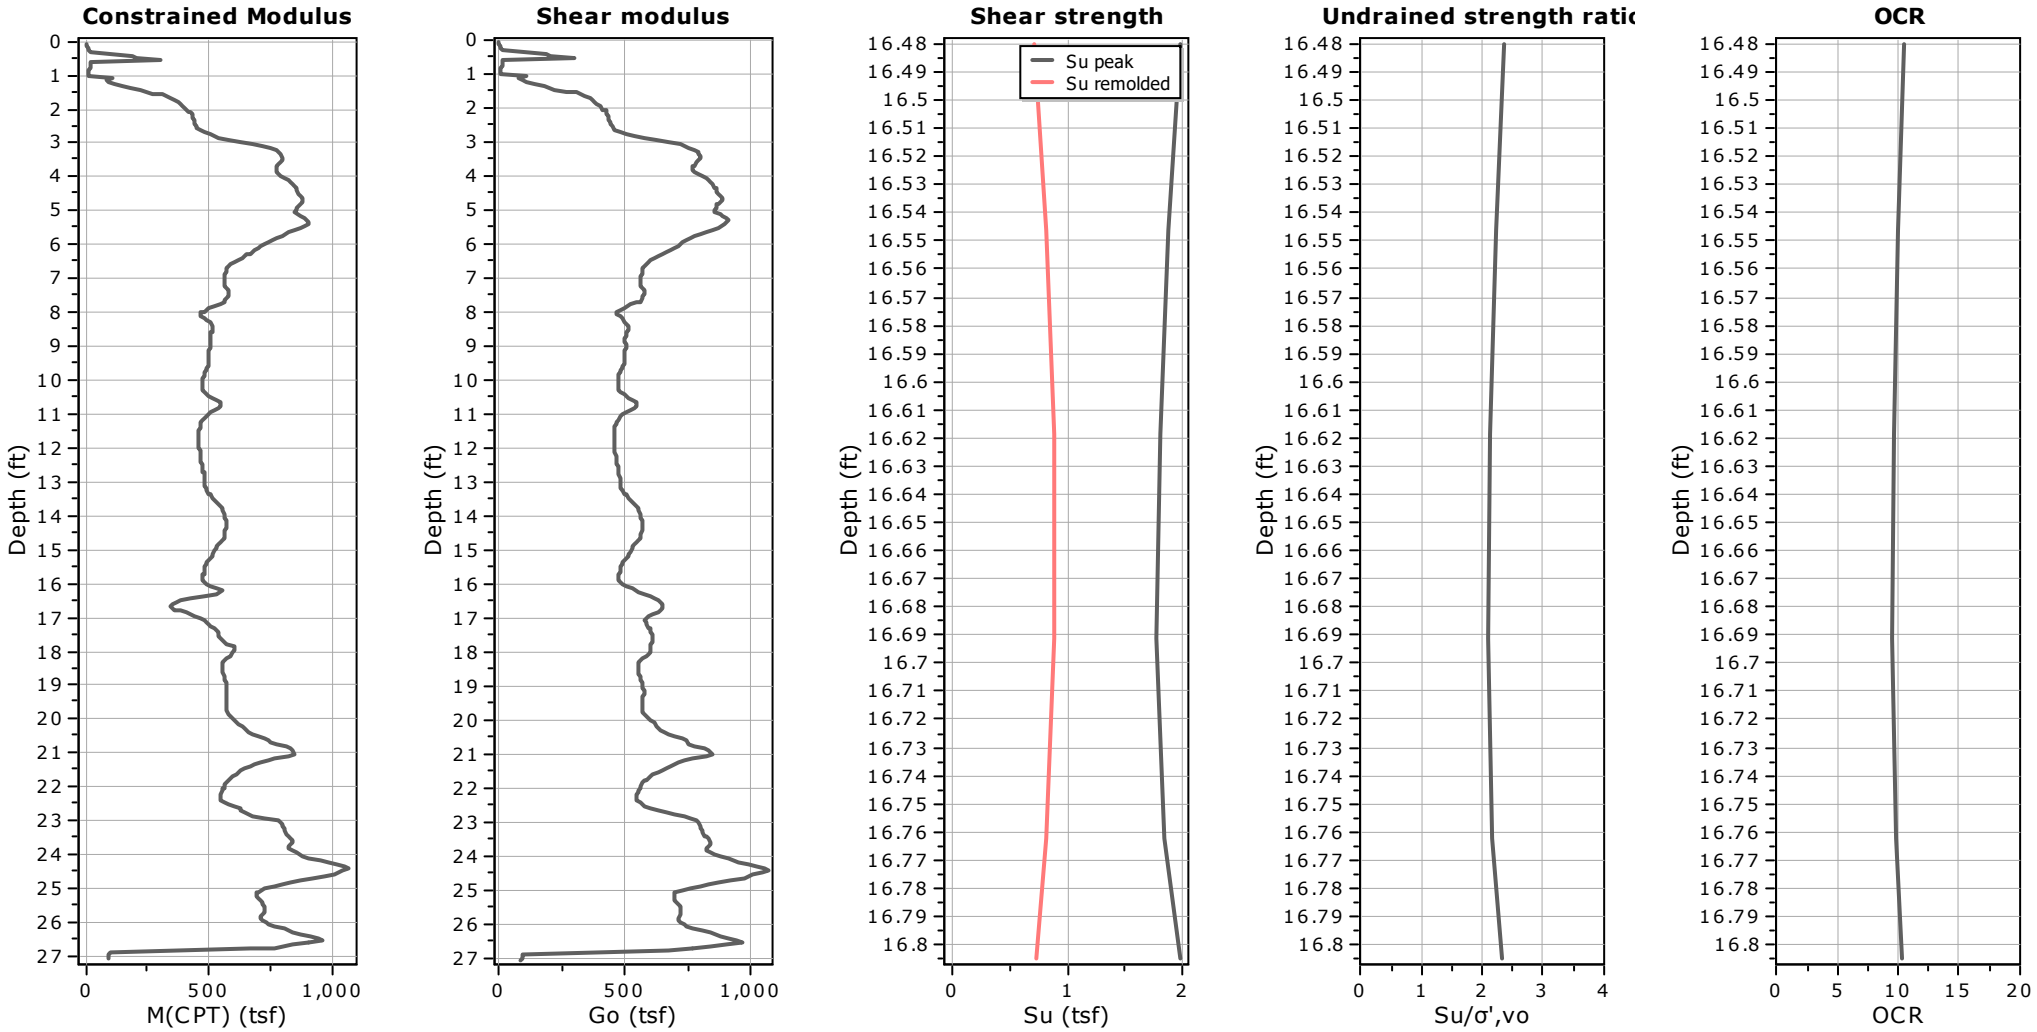


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 6
Total depth: 27.06 ft, Date: 4/20/2022
Surface Elevation: 78.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

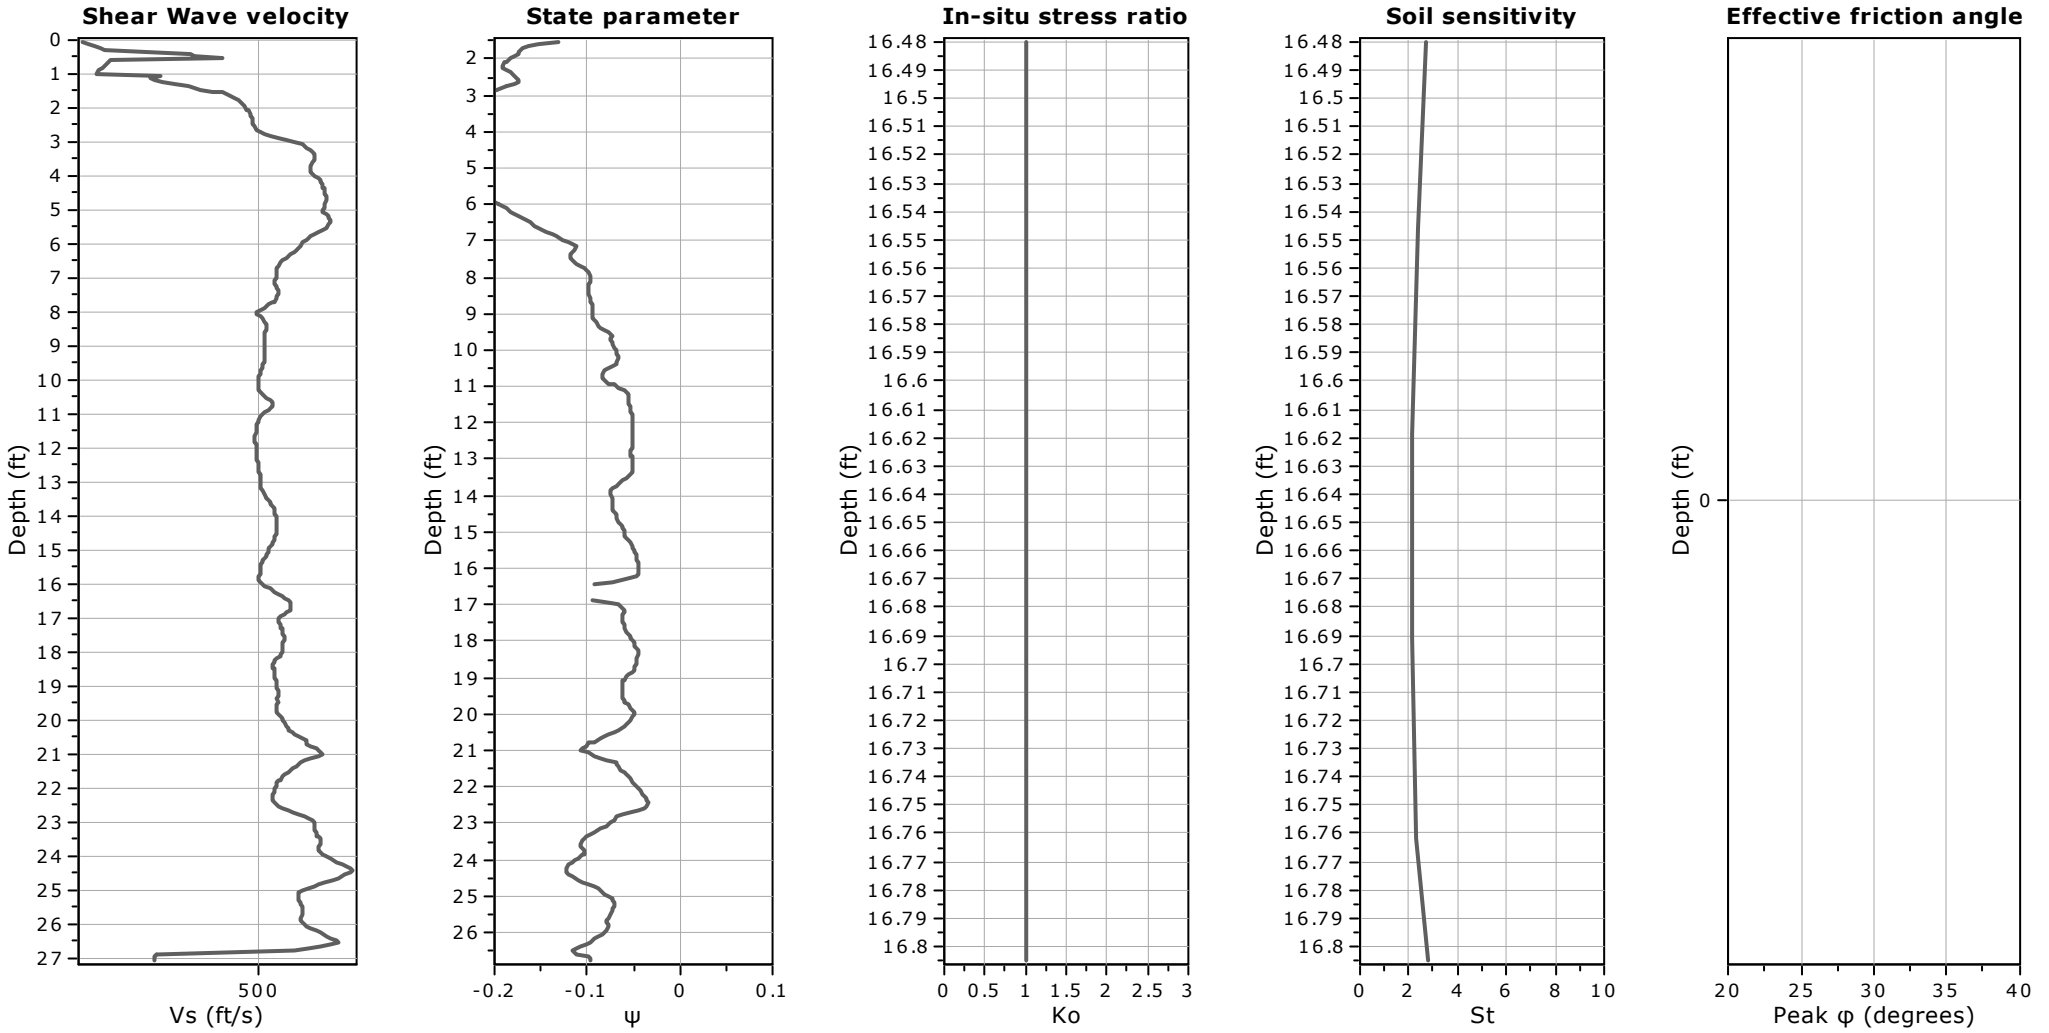

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 7
Total depth: 24.82 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

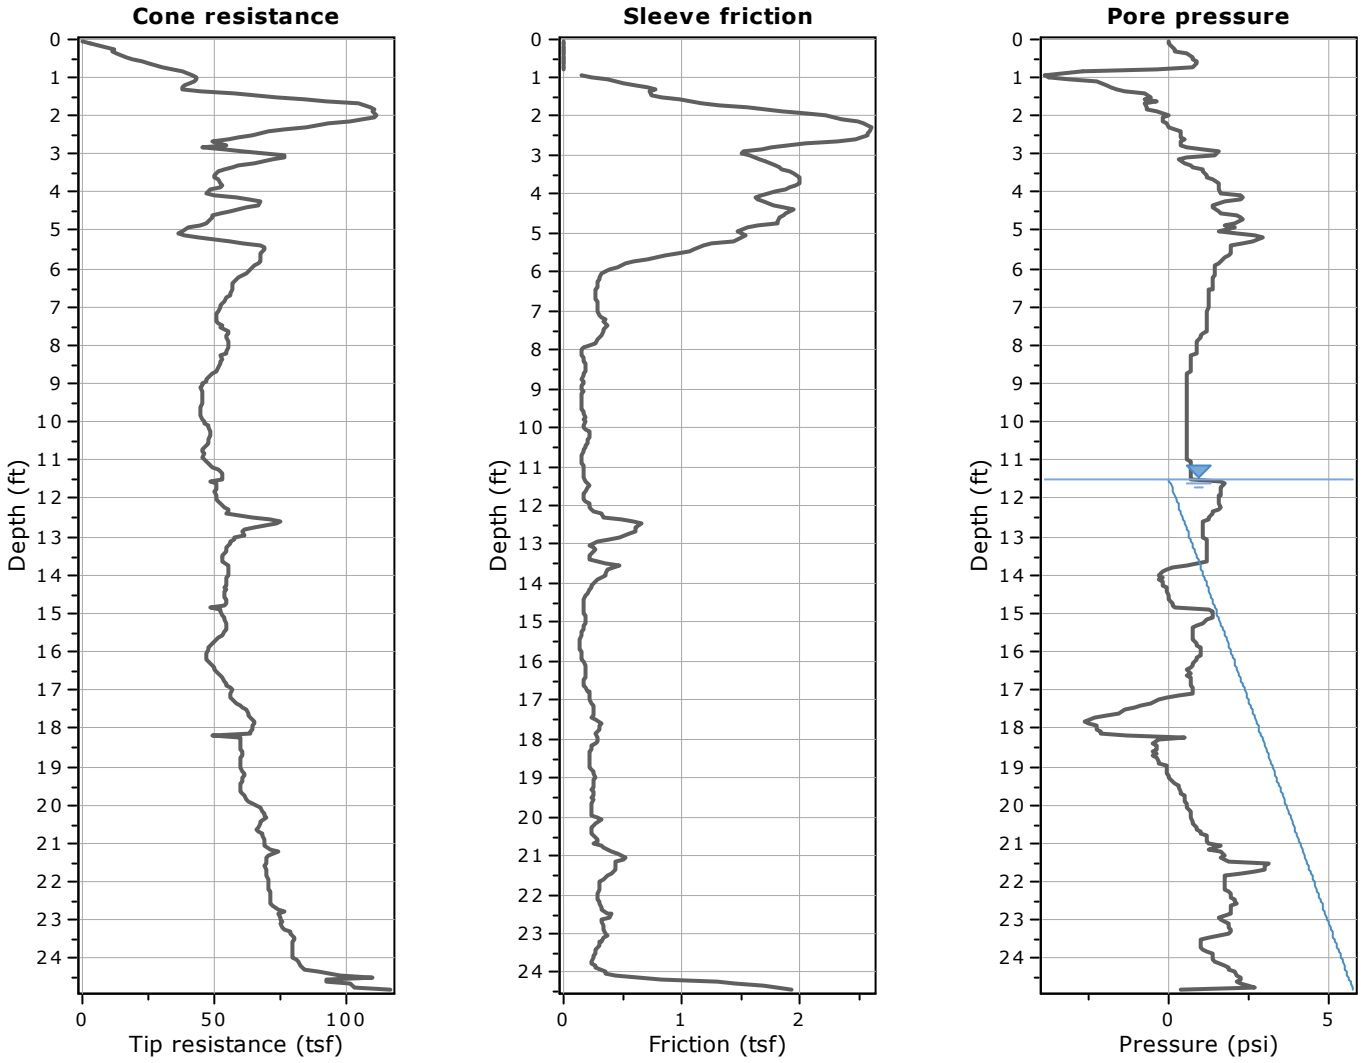


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

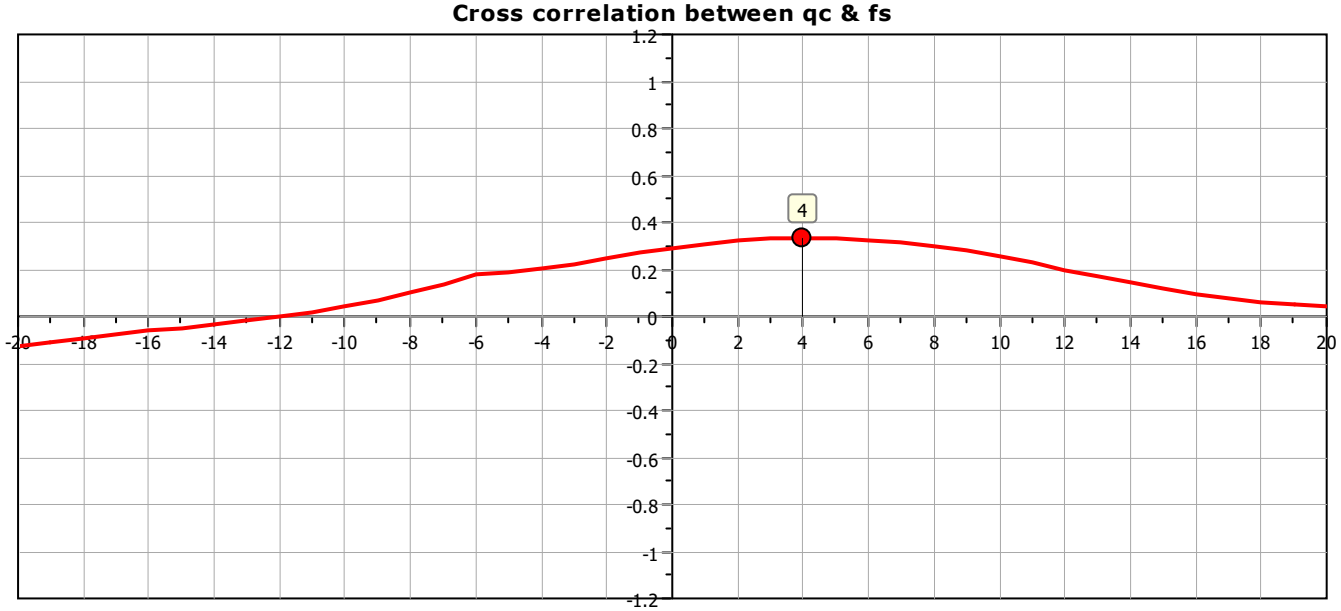

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 7
Total depth: 24.82 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

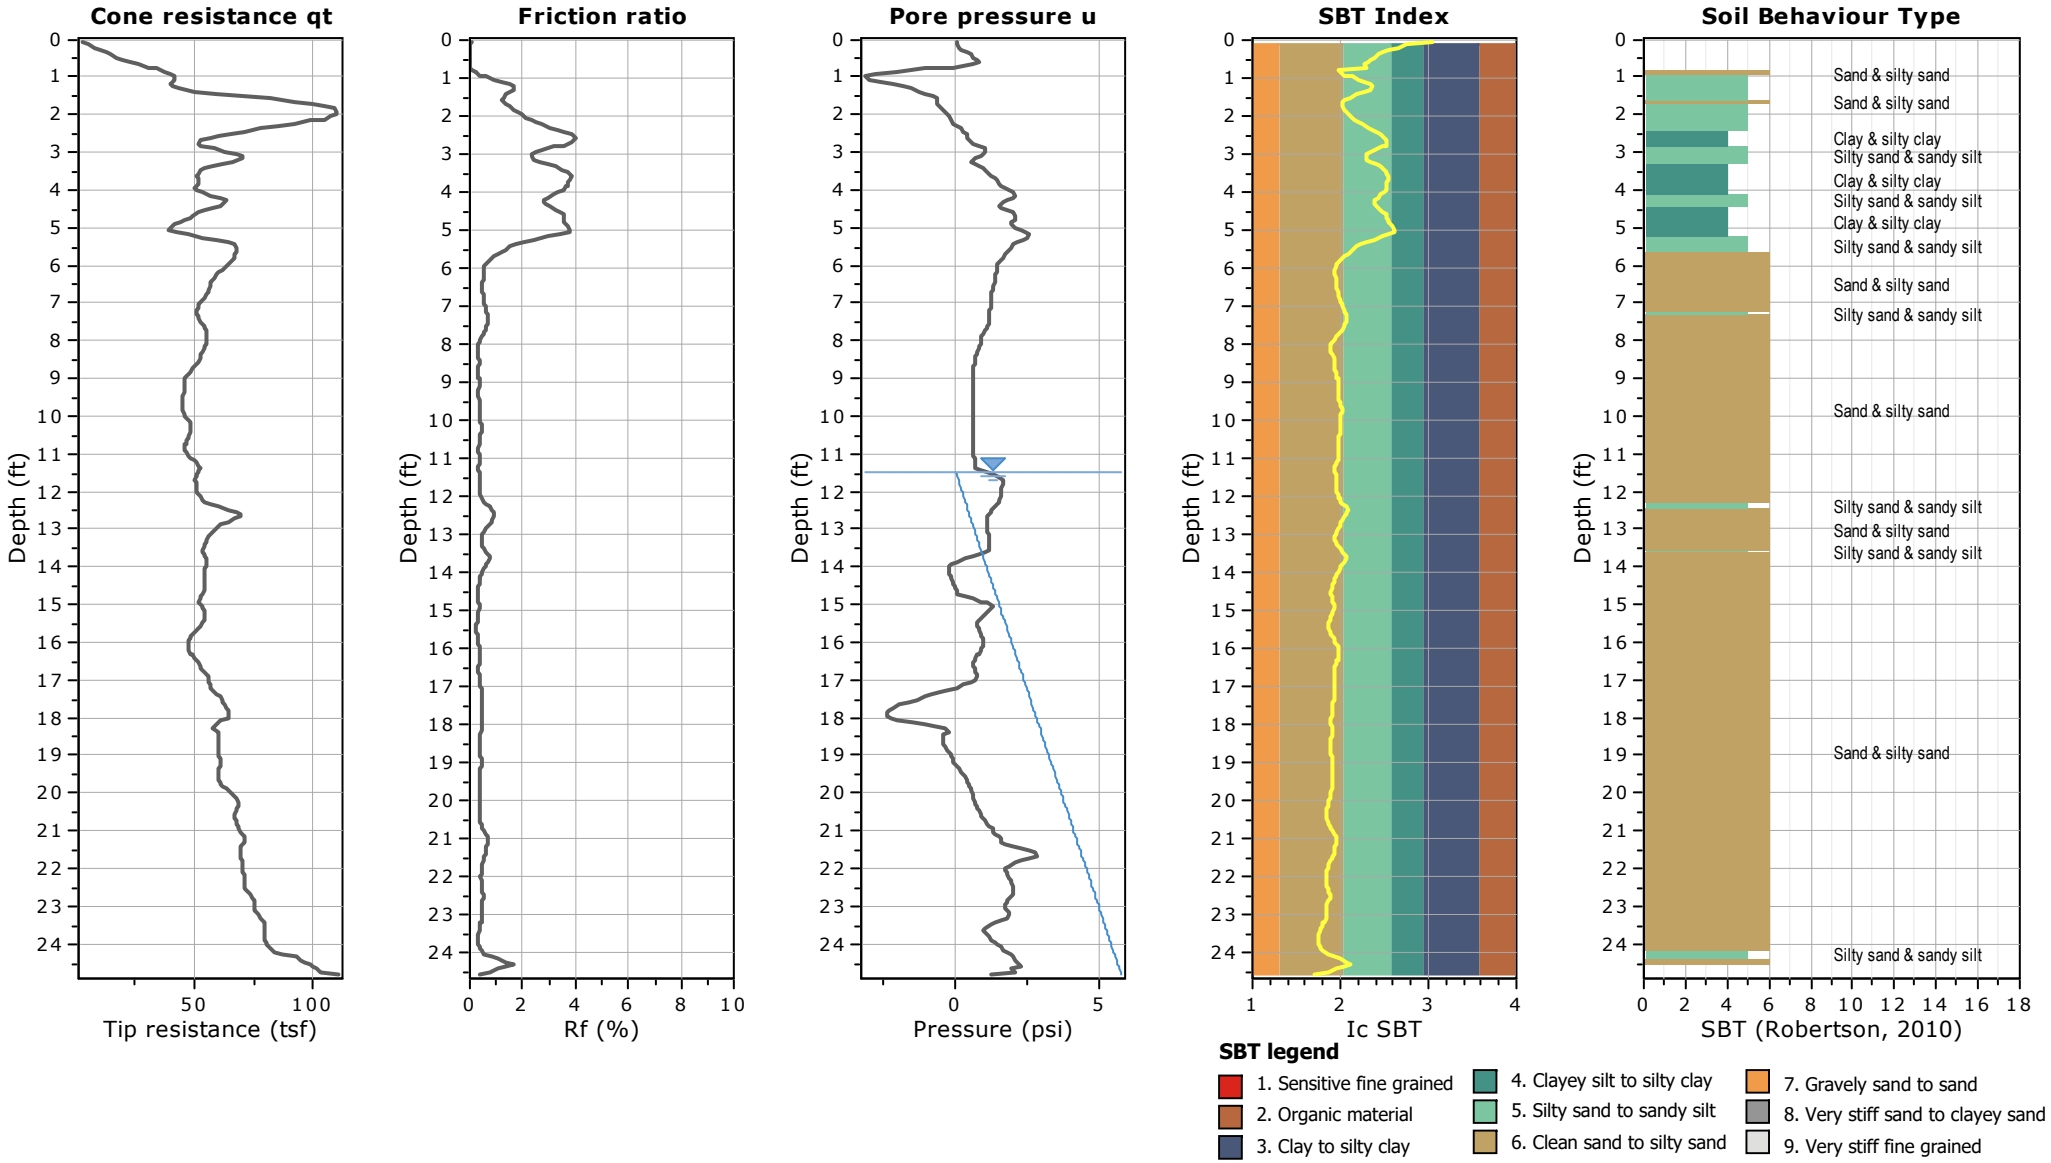



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 7
Total depth: 24.82 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

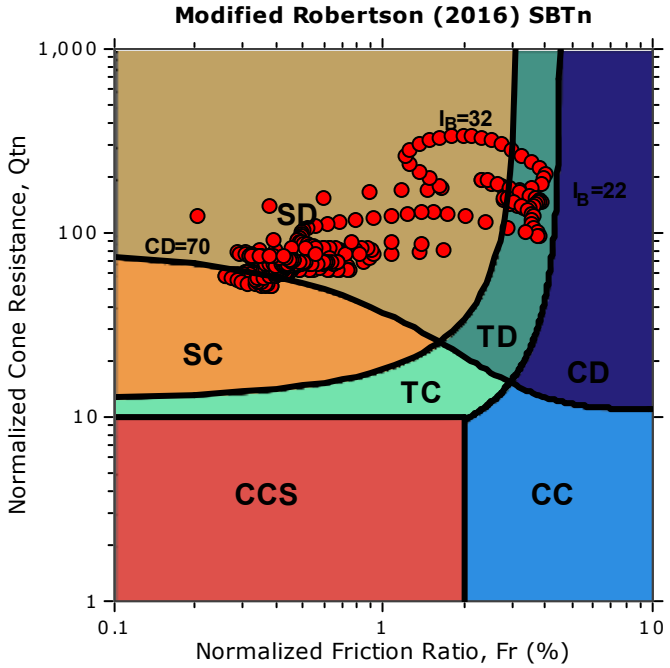

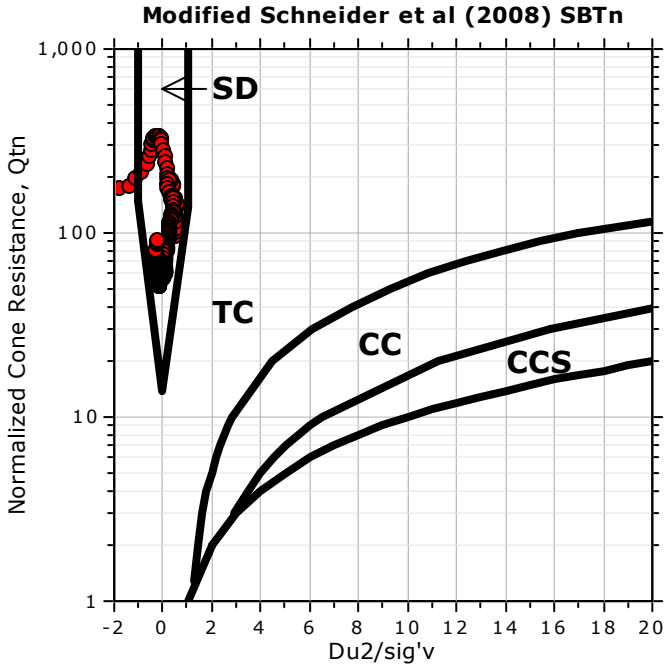

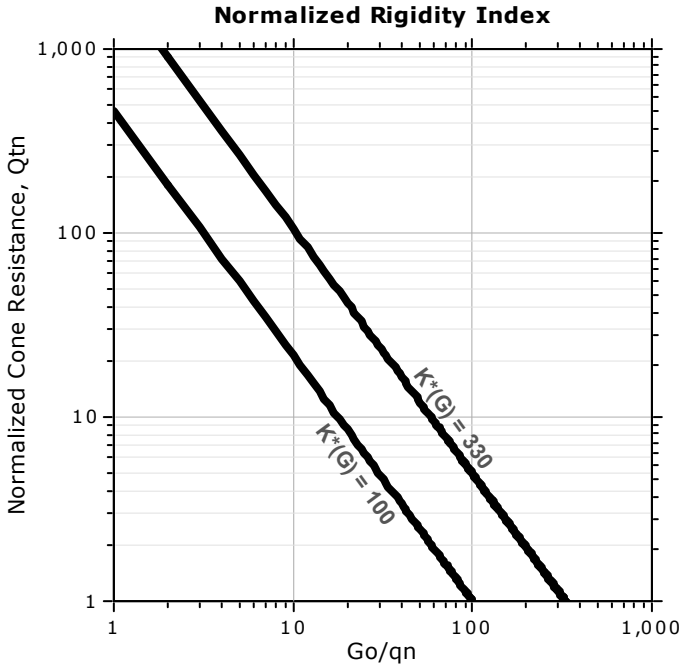


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 7
Total depth: 24.82 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

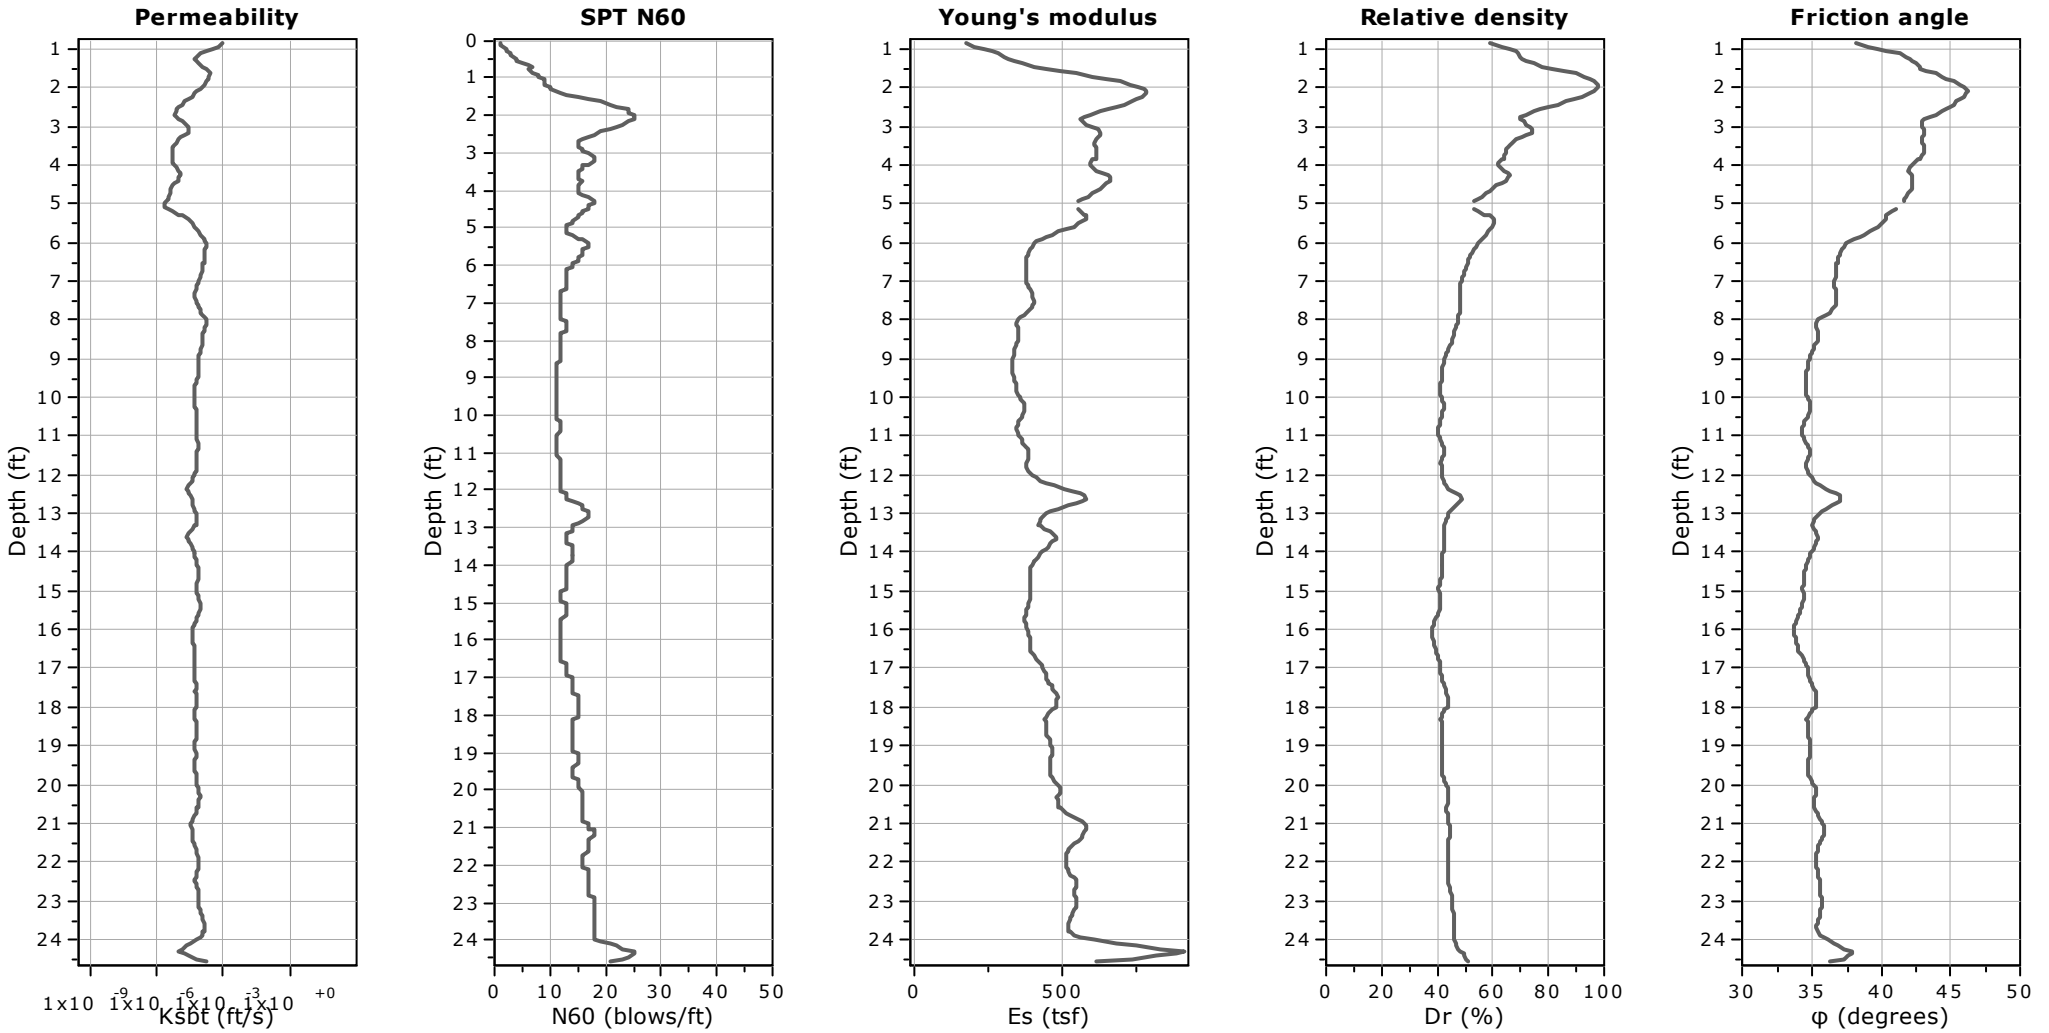


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 7
Total depth: 24.82 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

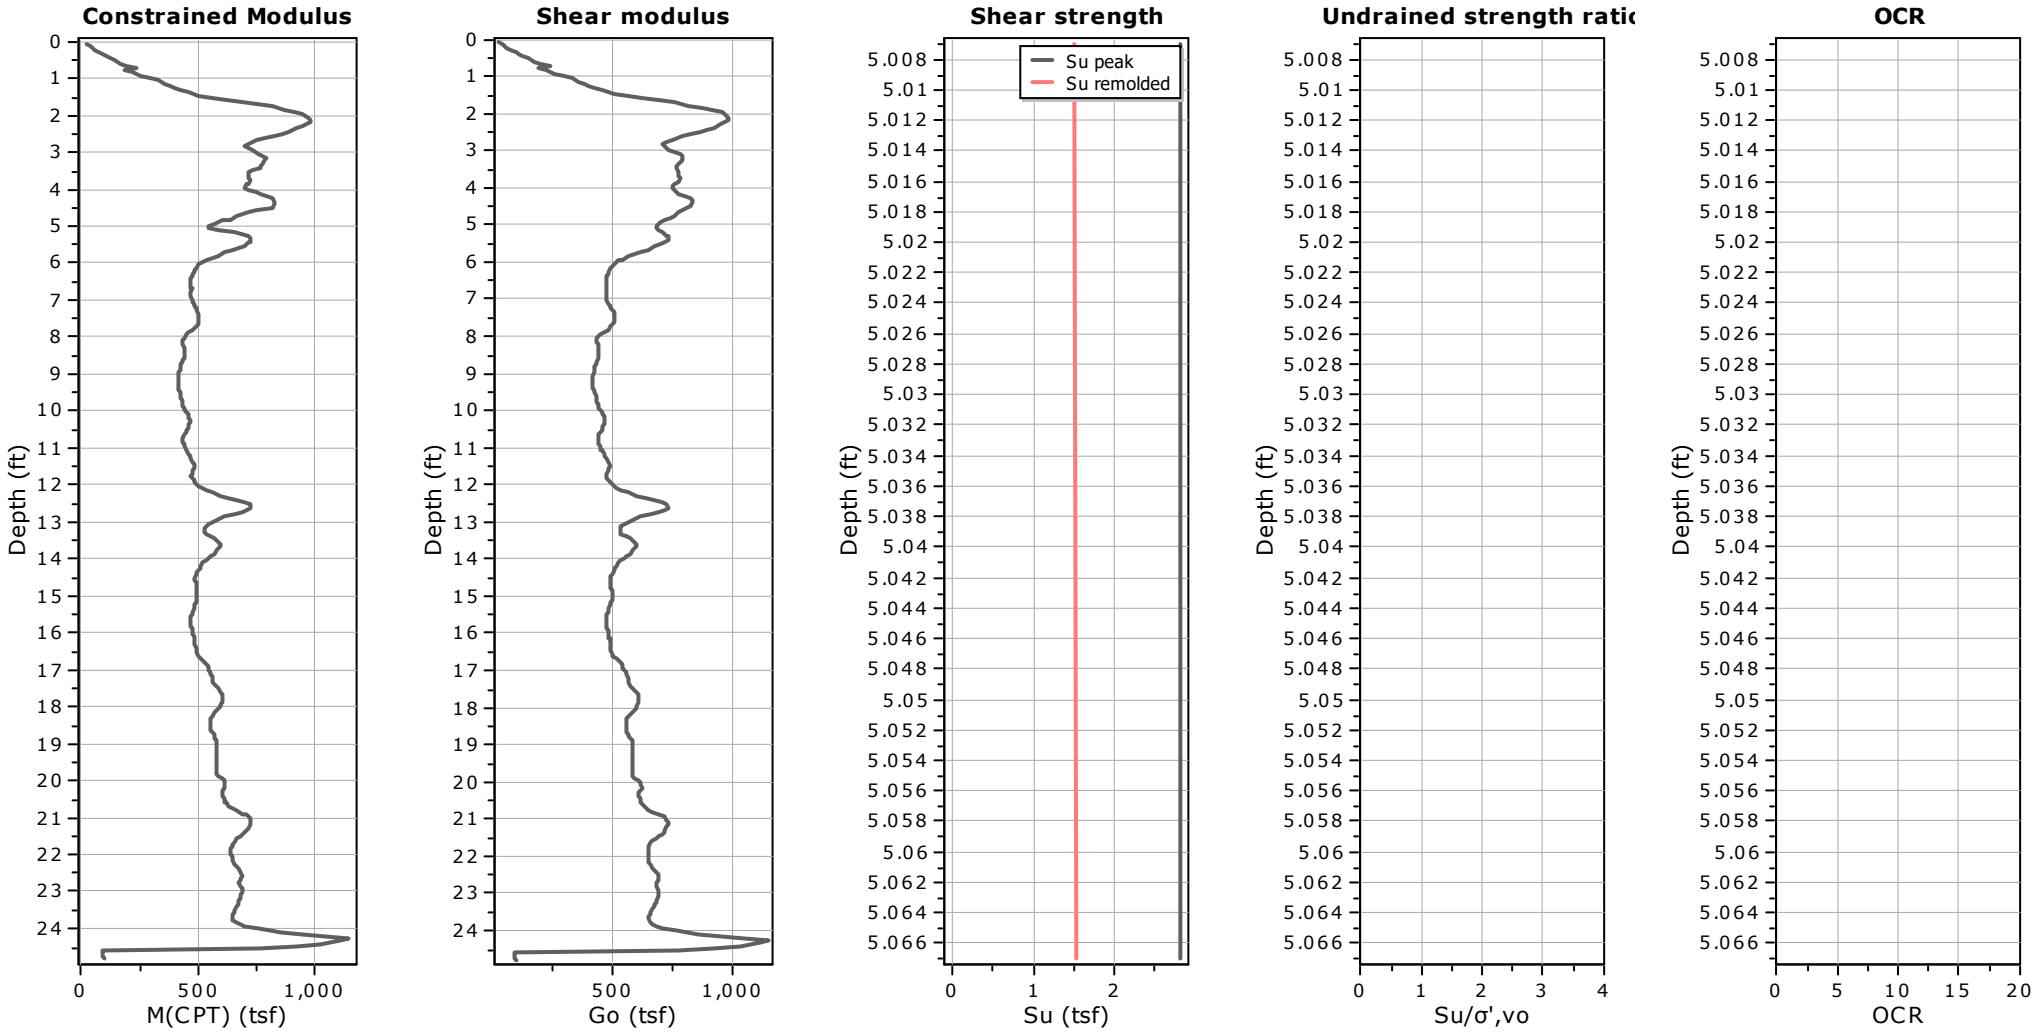


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 7
Total depth: 24.82 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

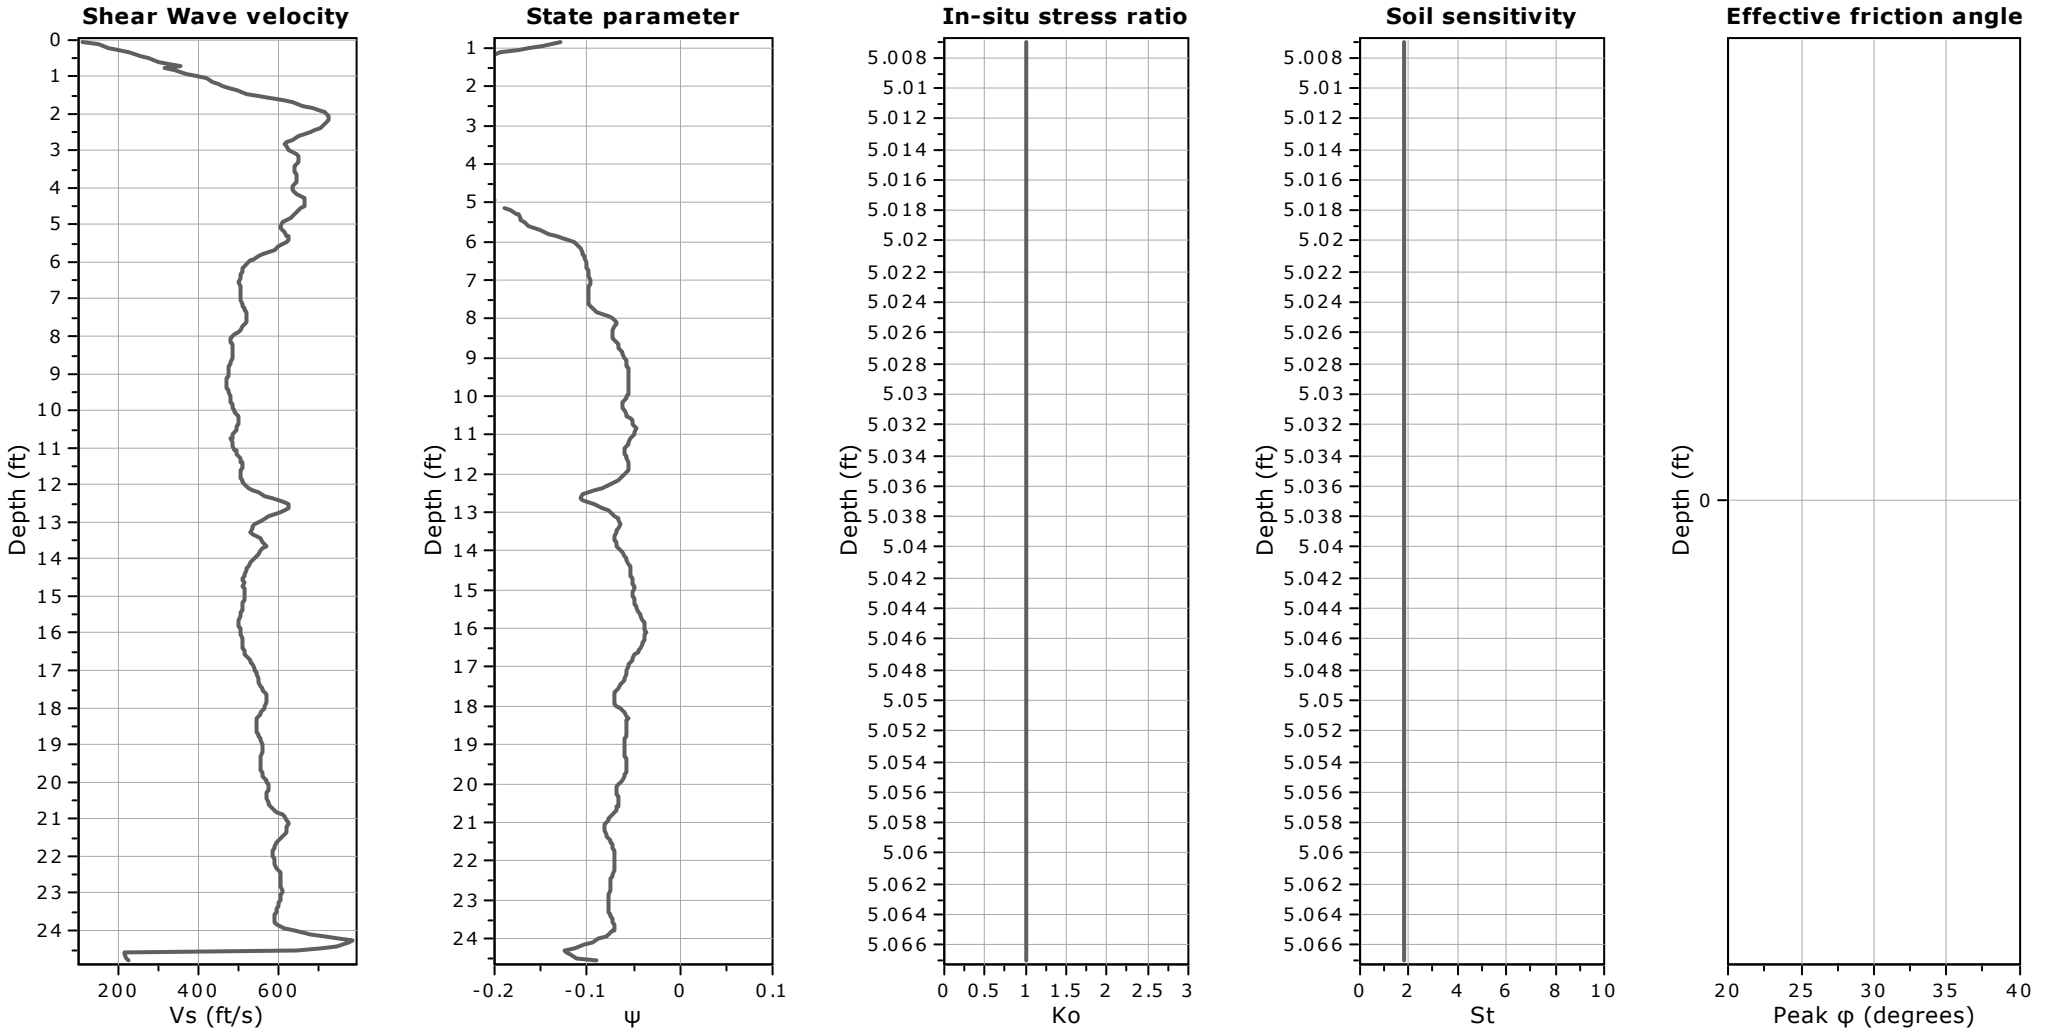

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 8
Total depth: 24.54 ft, Date: 4/20/2022
Surface Elevation: 84.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

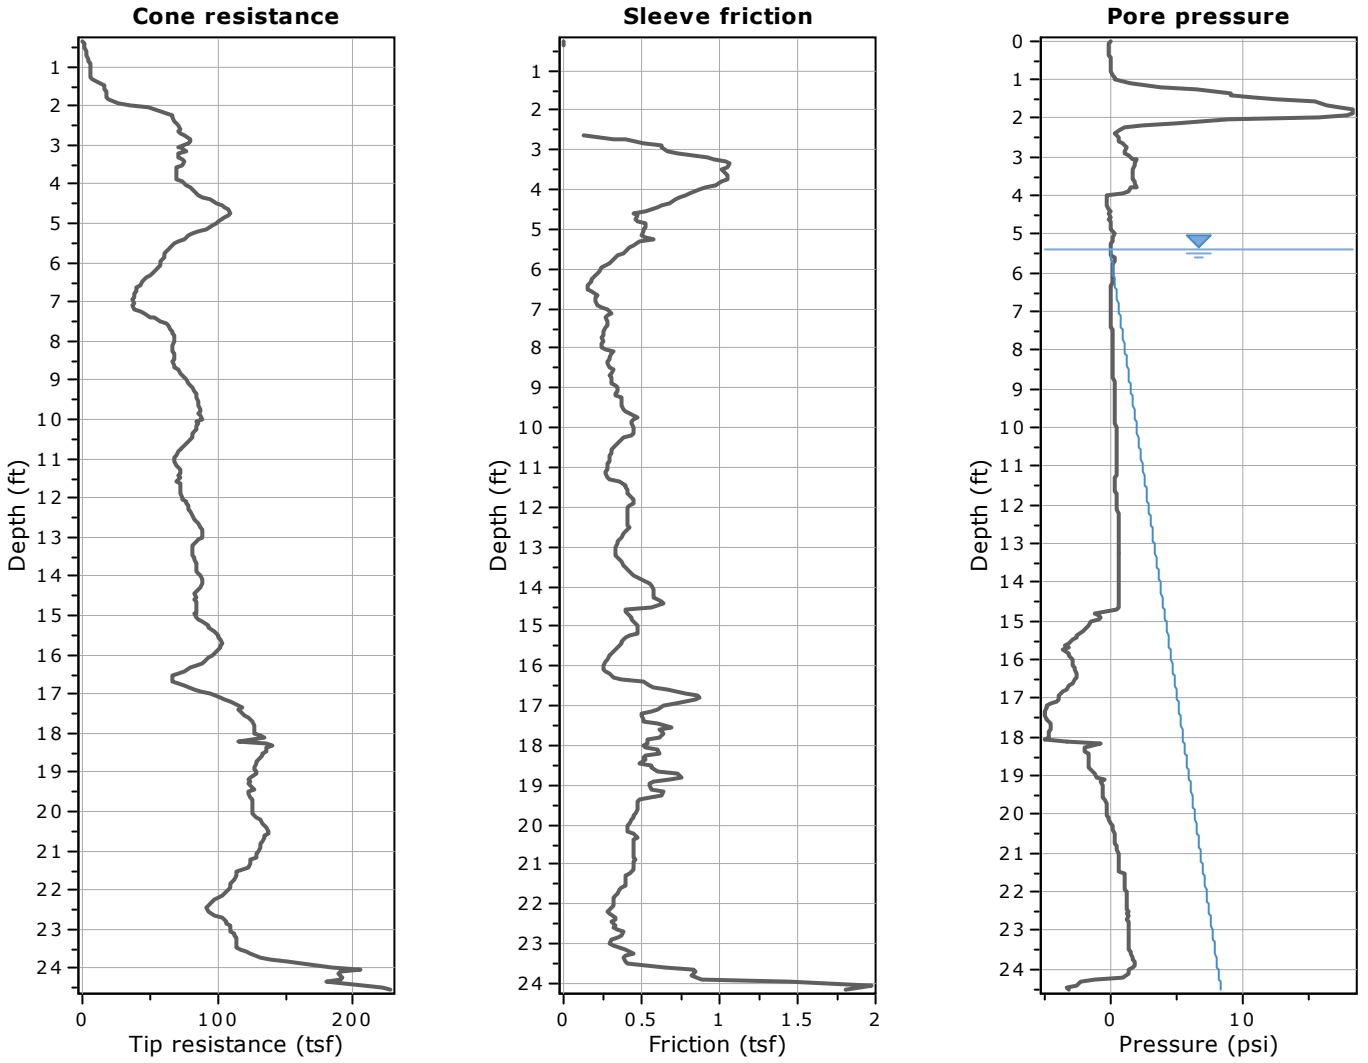


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

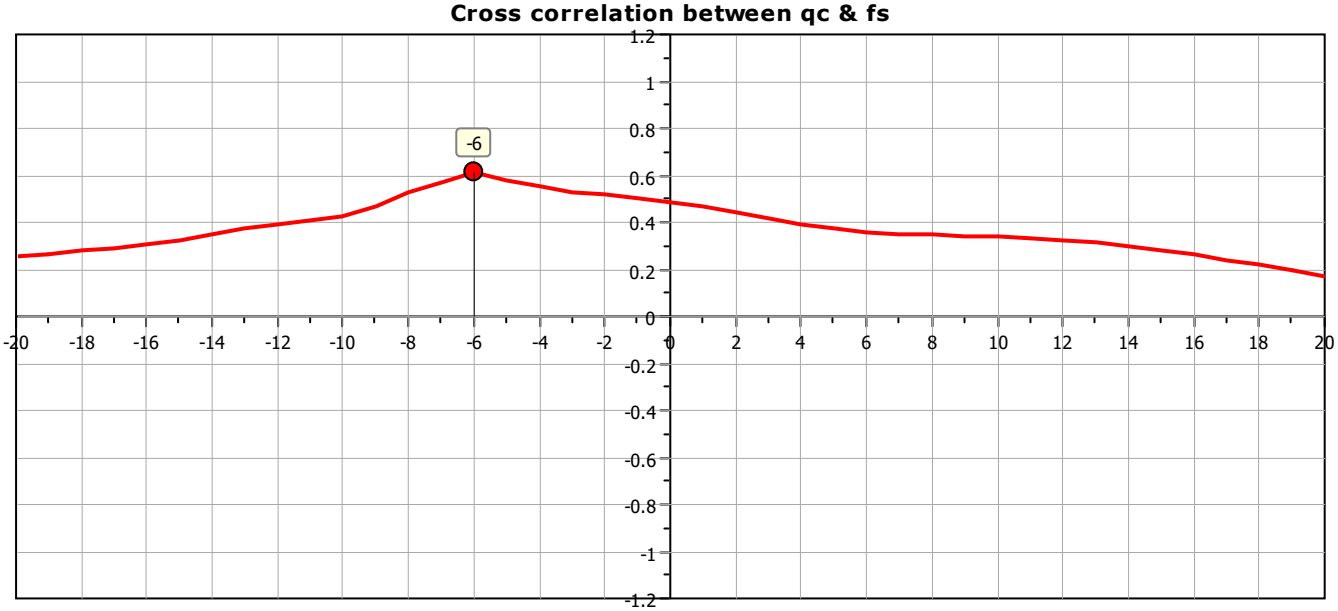

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 8
Total depth: 24.54 ft, Date: 4/20/2022
Surface Elevation: 84.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

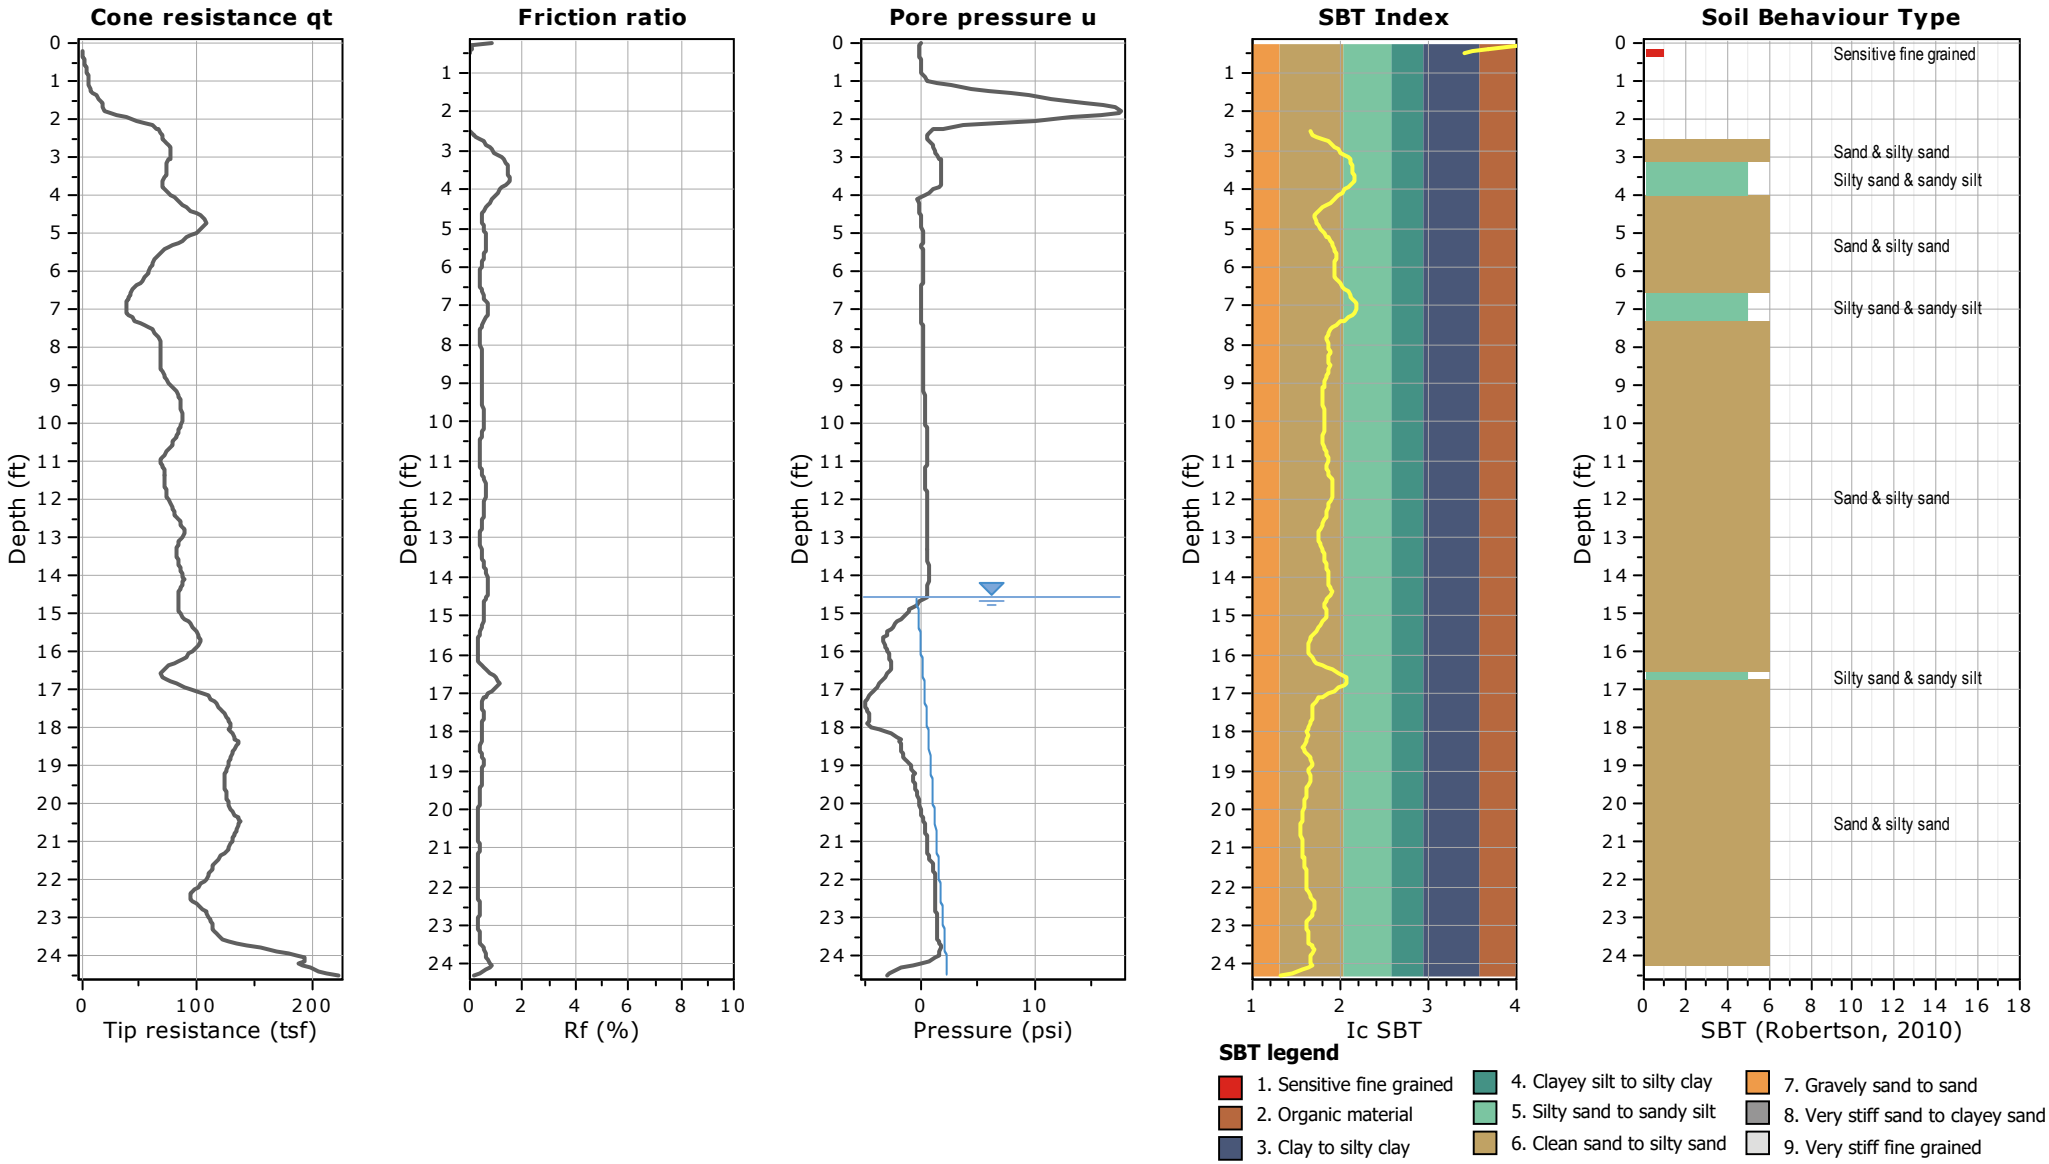



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 8
Total depth: 24.54 ft, Date: 4/20/2022
Surface Elevation: 84.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

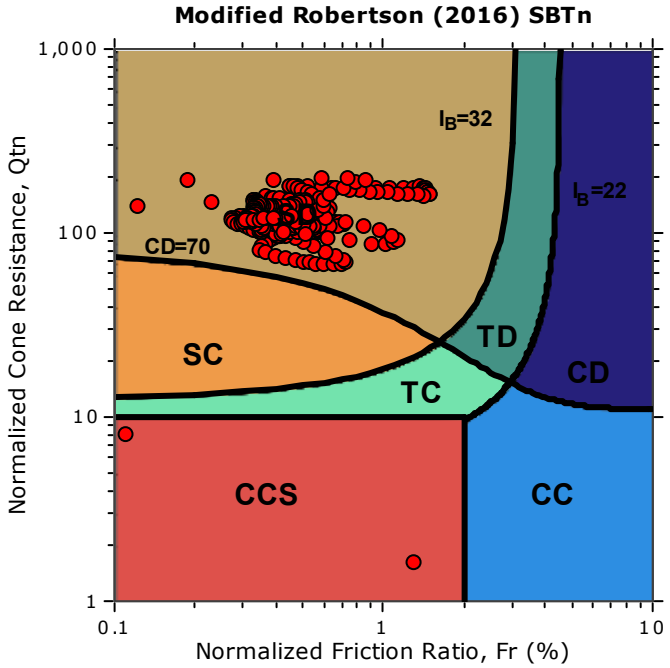

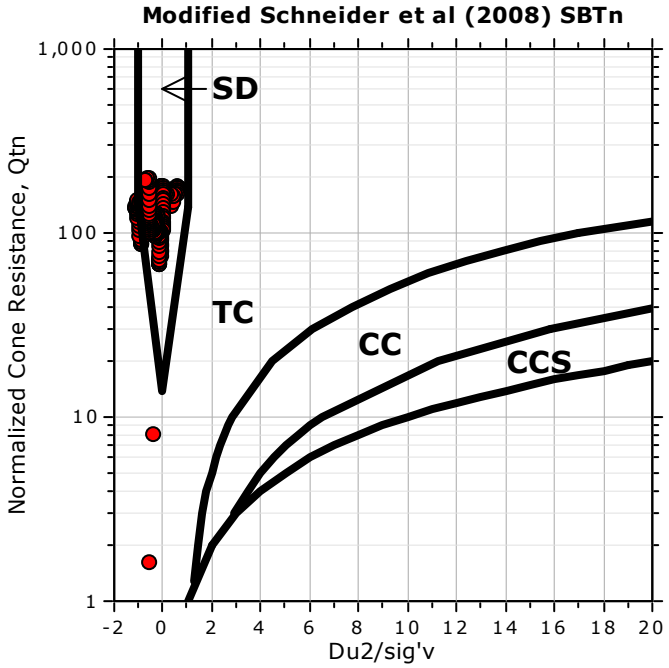

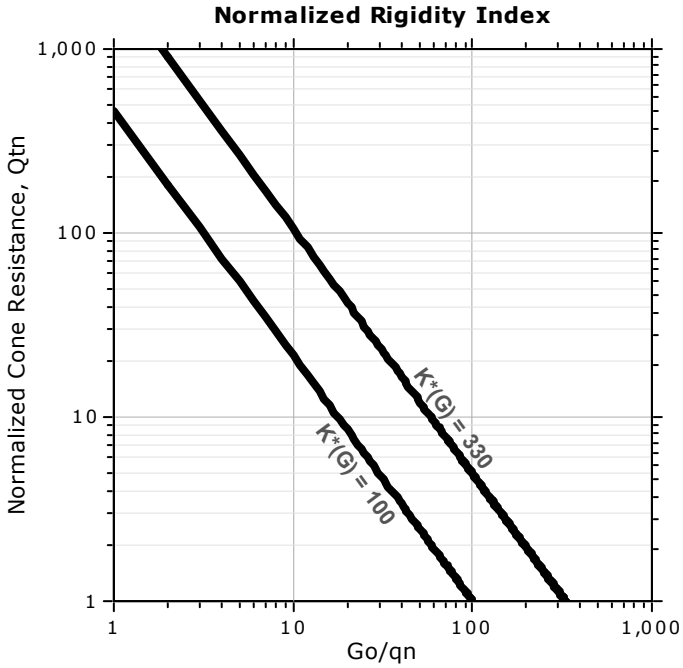


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 8
Total depth: 24.54 ft, Date: 4/20/2022
Surface Elevation: 84.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

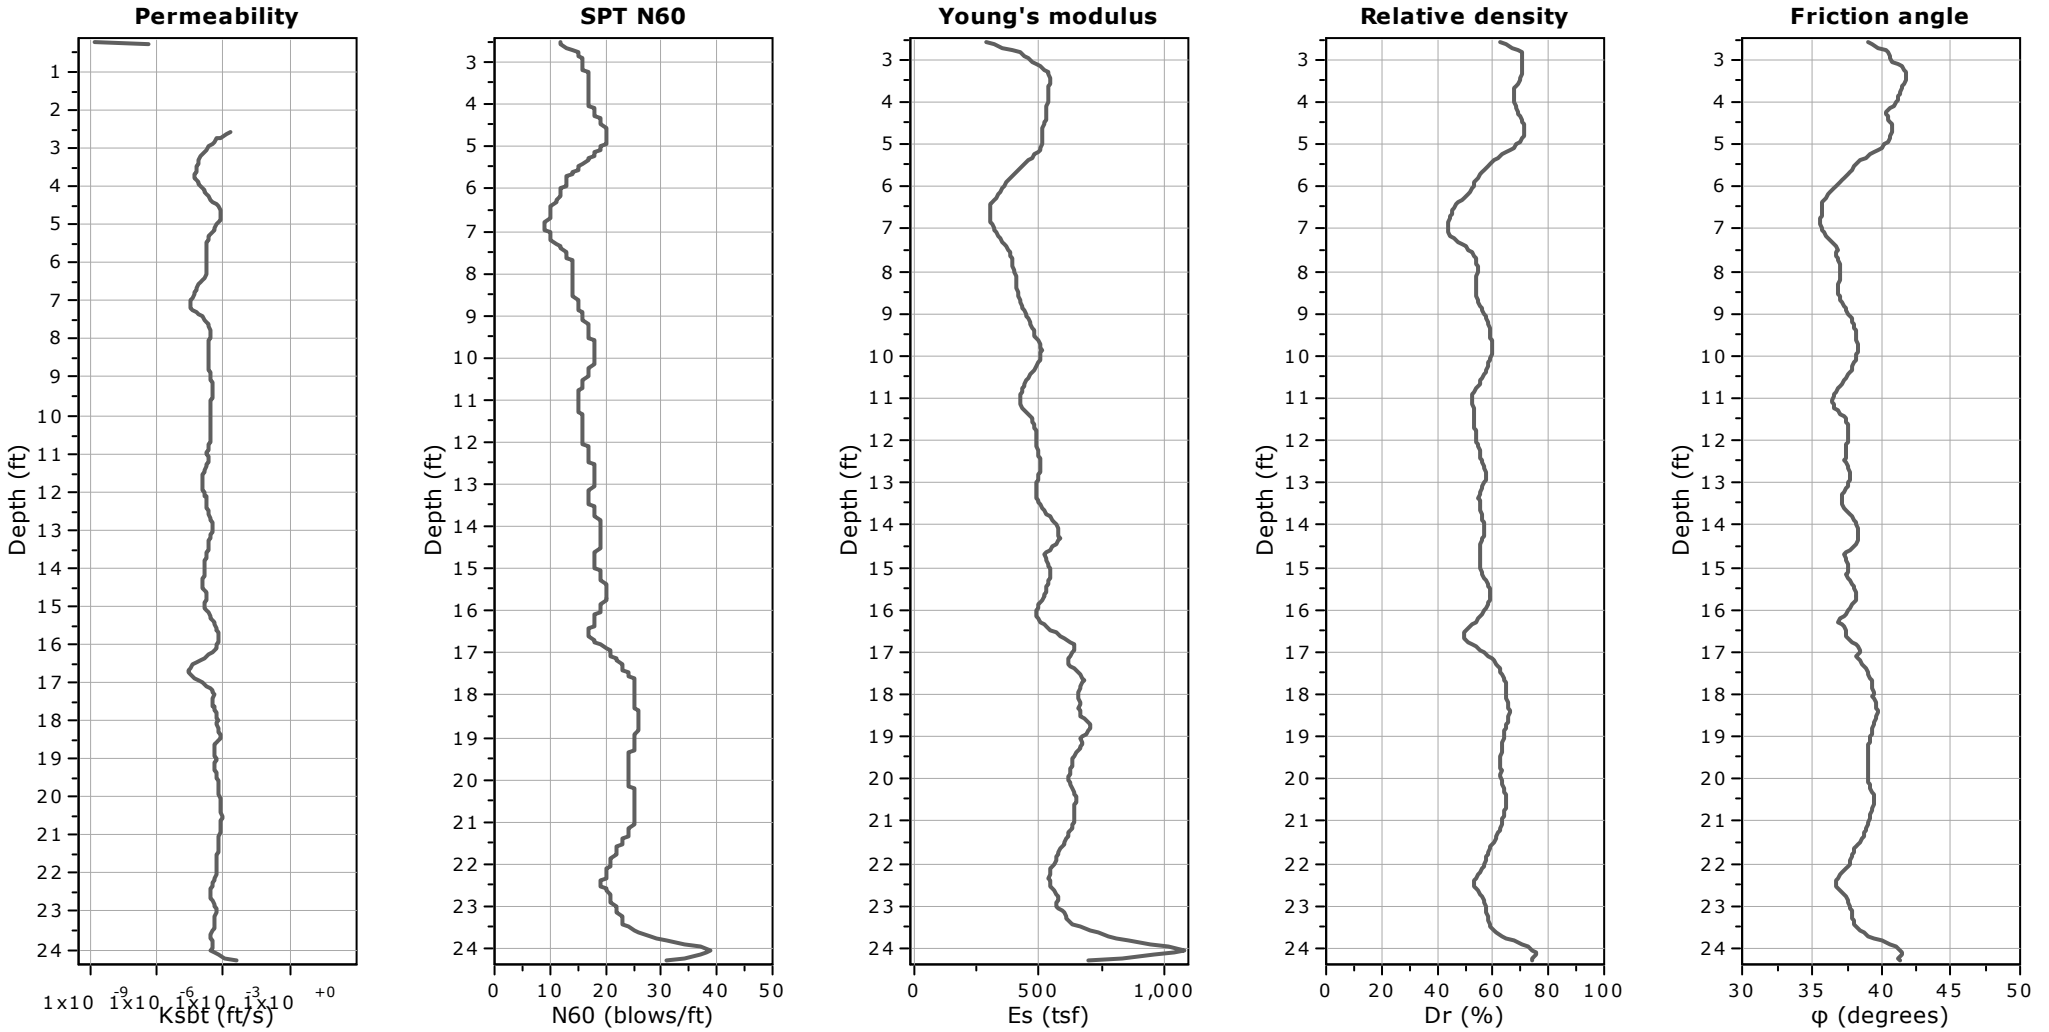


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 8
Total depth: 24.54 ft, Date: 4/20/2022
Surface Elevation: 84.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

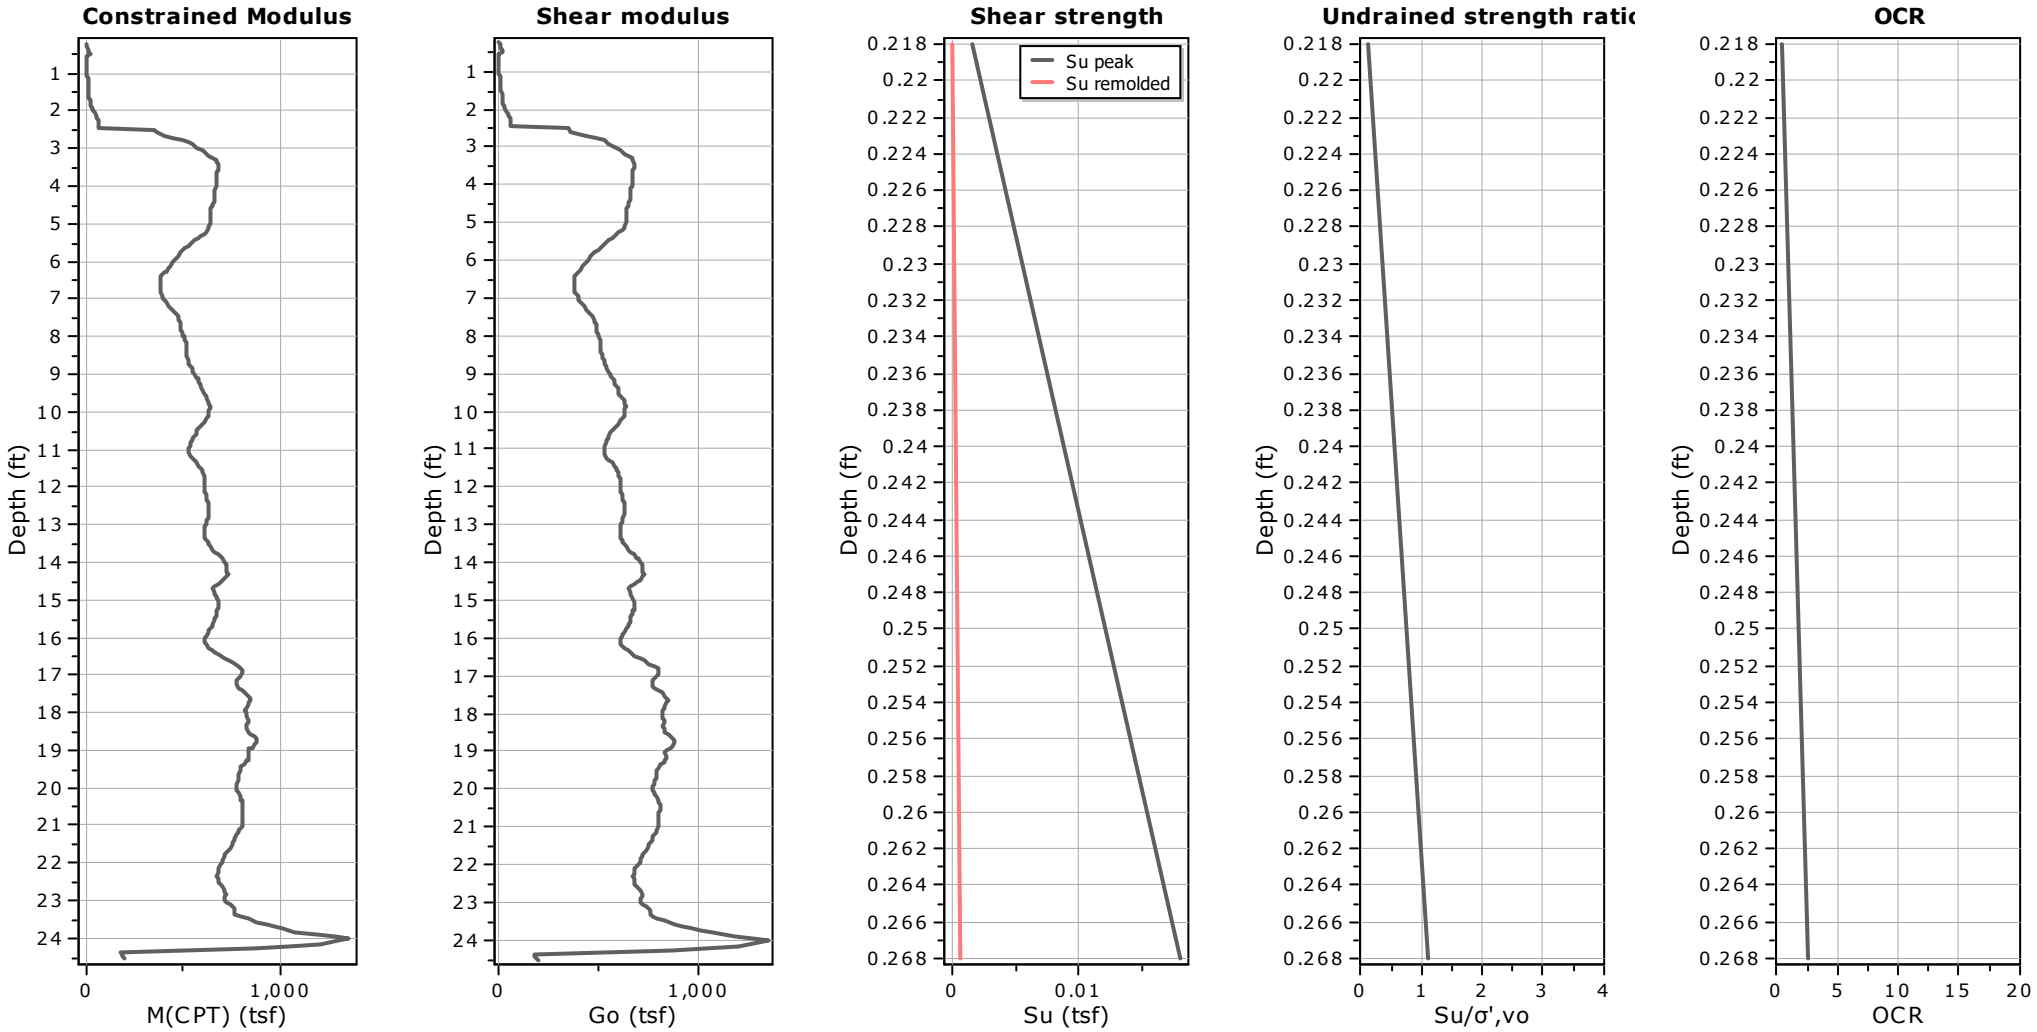


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 8
Total depth: 24.54 ft, Date: 4/20/2022
Surface Elevation: 84.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

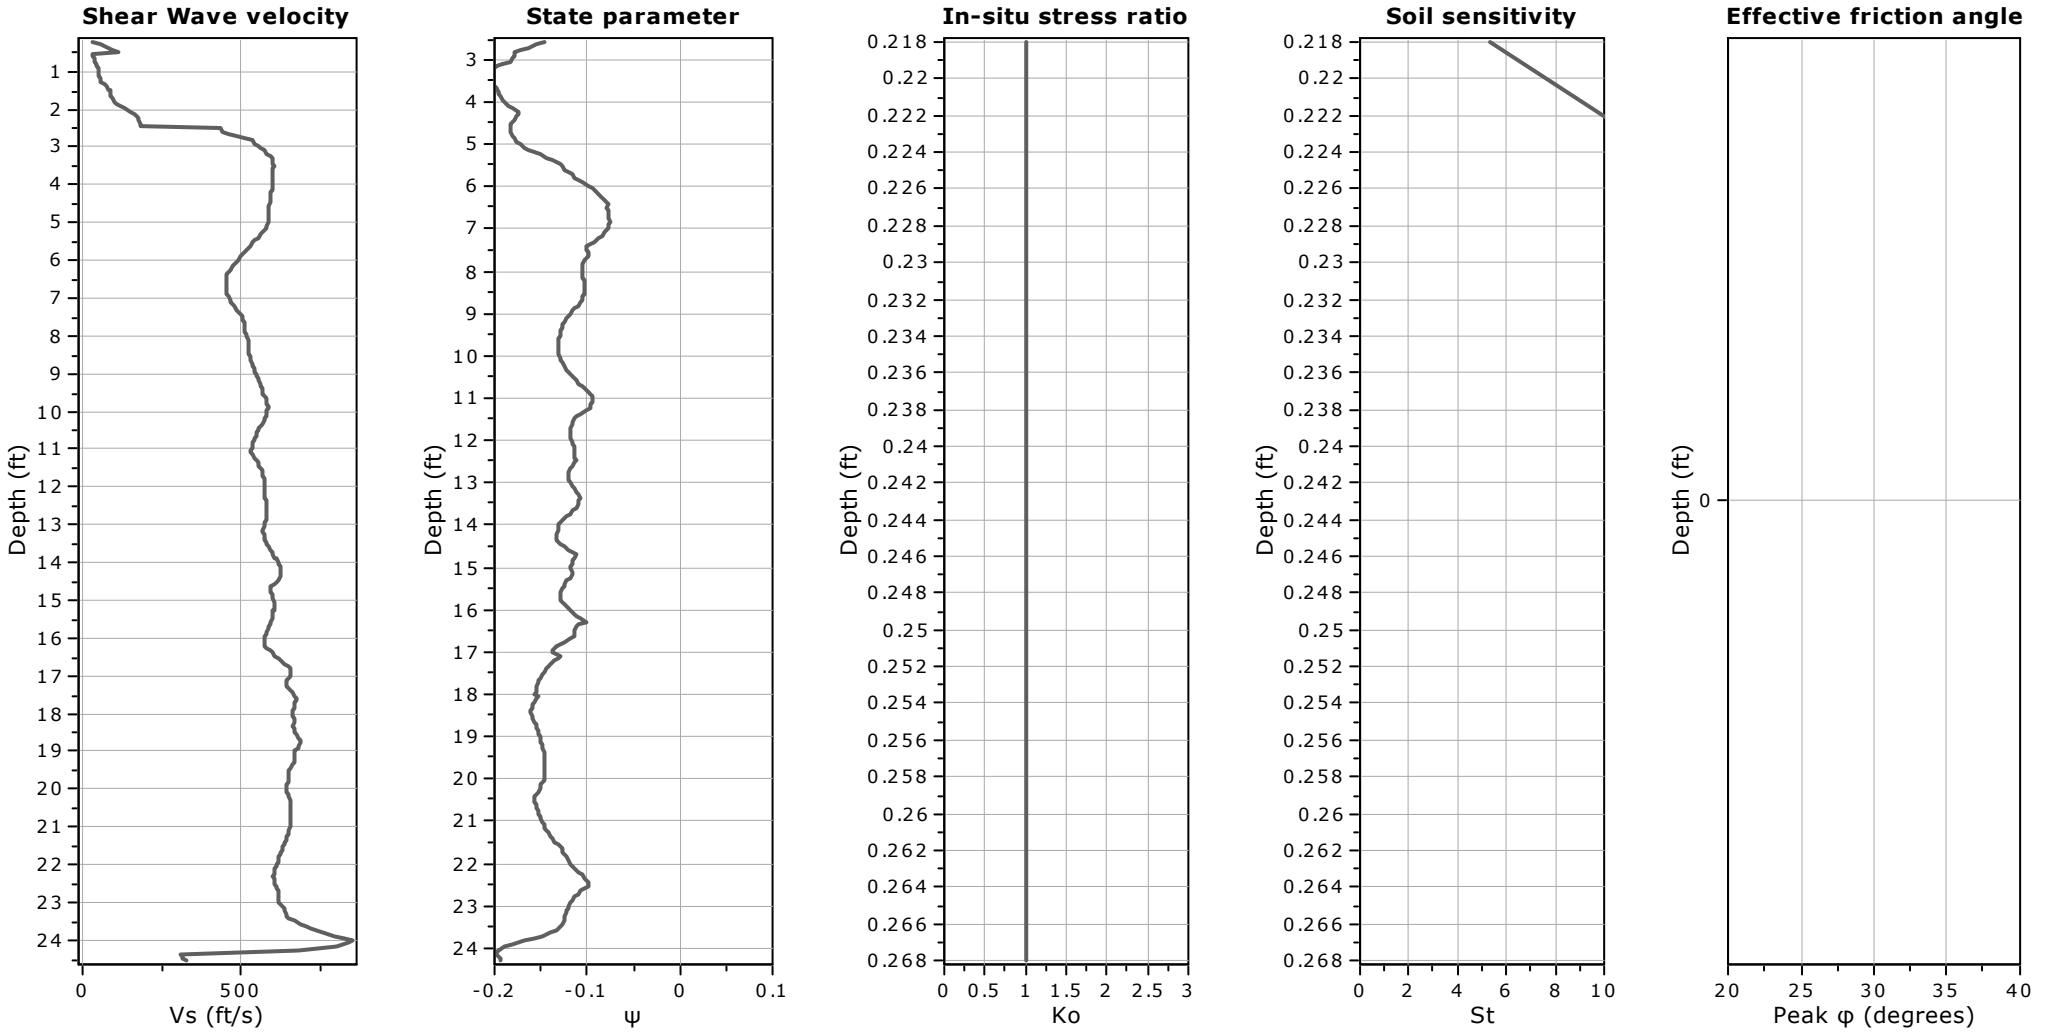

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data


GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 9
Total depth: 26.19 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

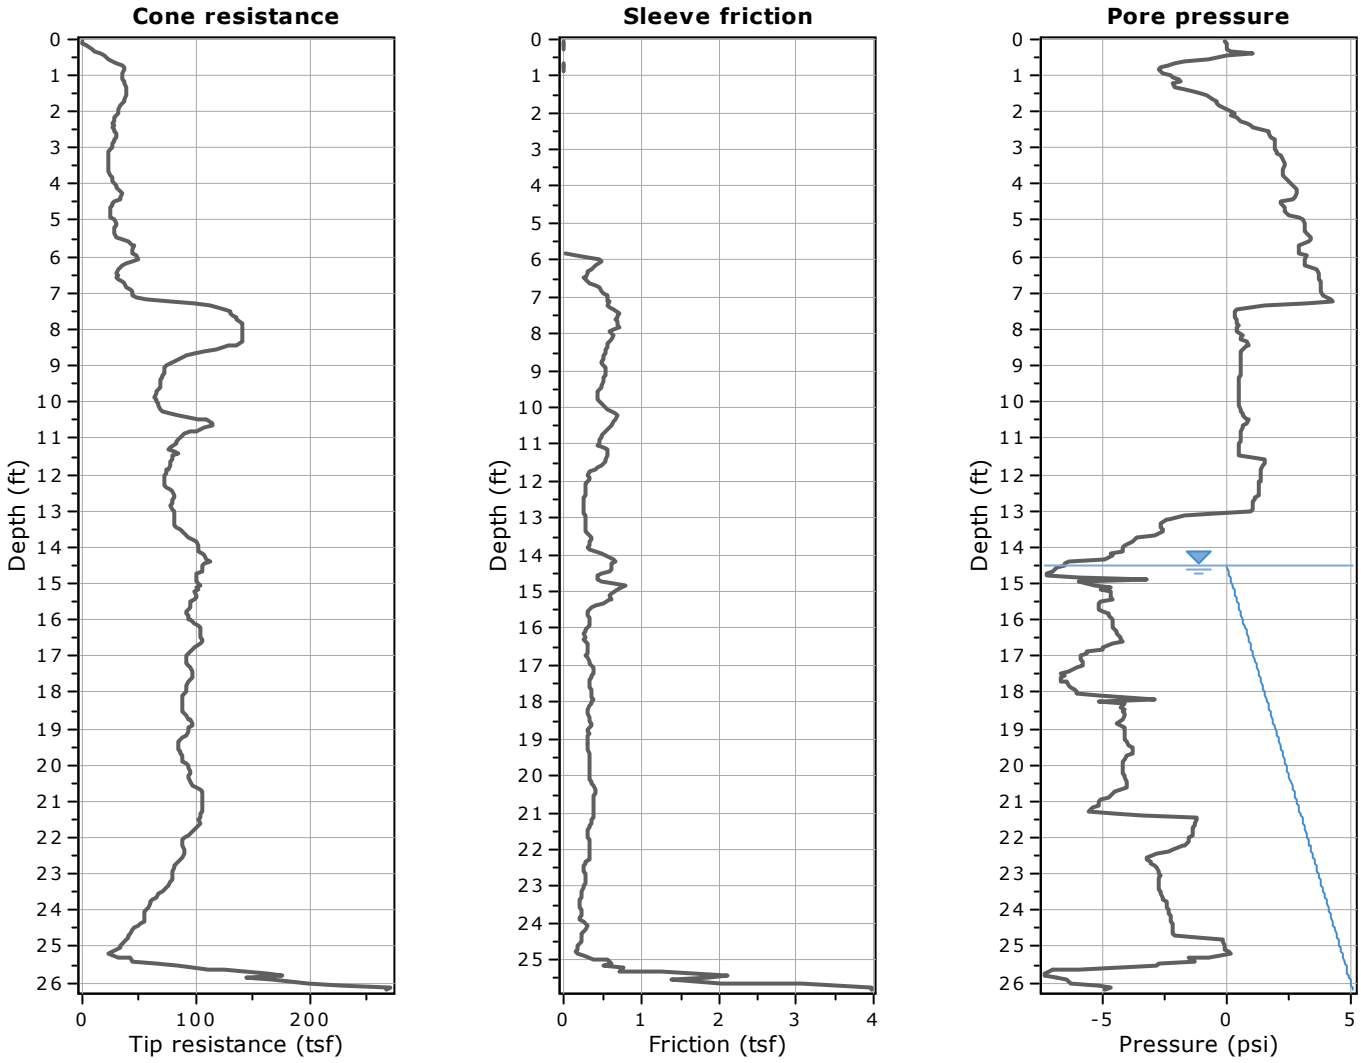


The plot below presents the cross correlation coeficient between the raw qc and fs values (as measured on the field). X axes presents the lag distance (one lag is the distance between two sucessive CPT measurements).

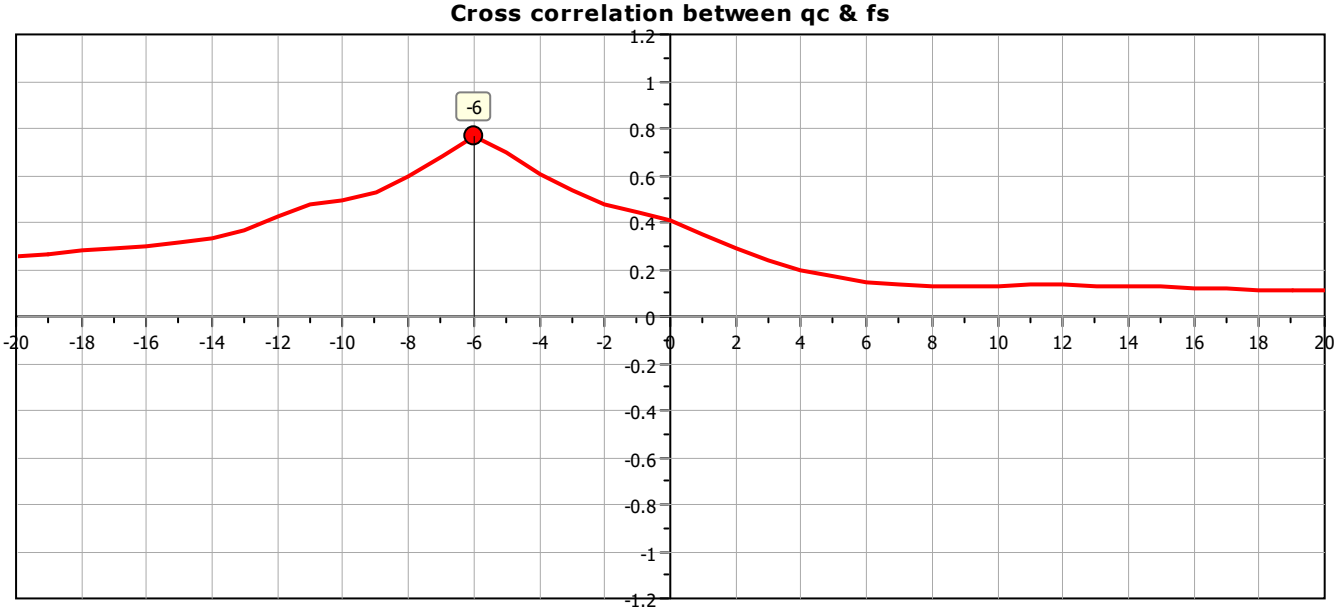

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 9
Total depth: 26.19 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

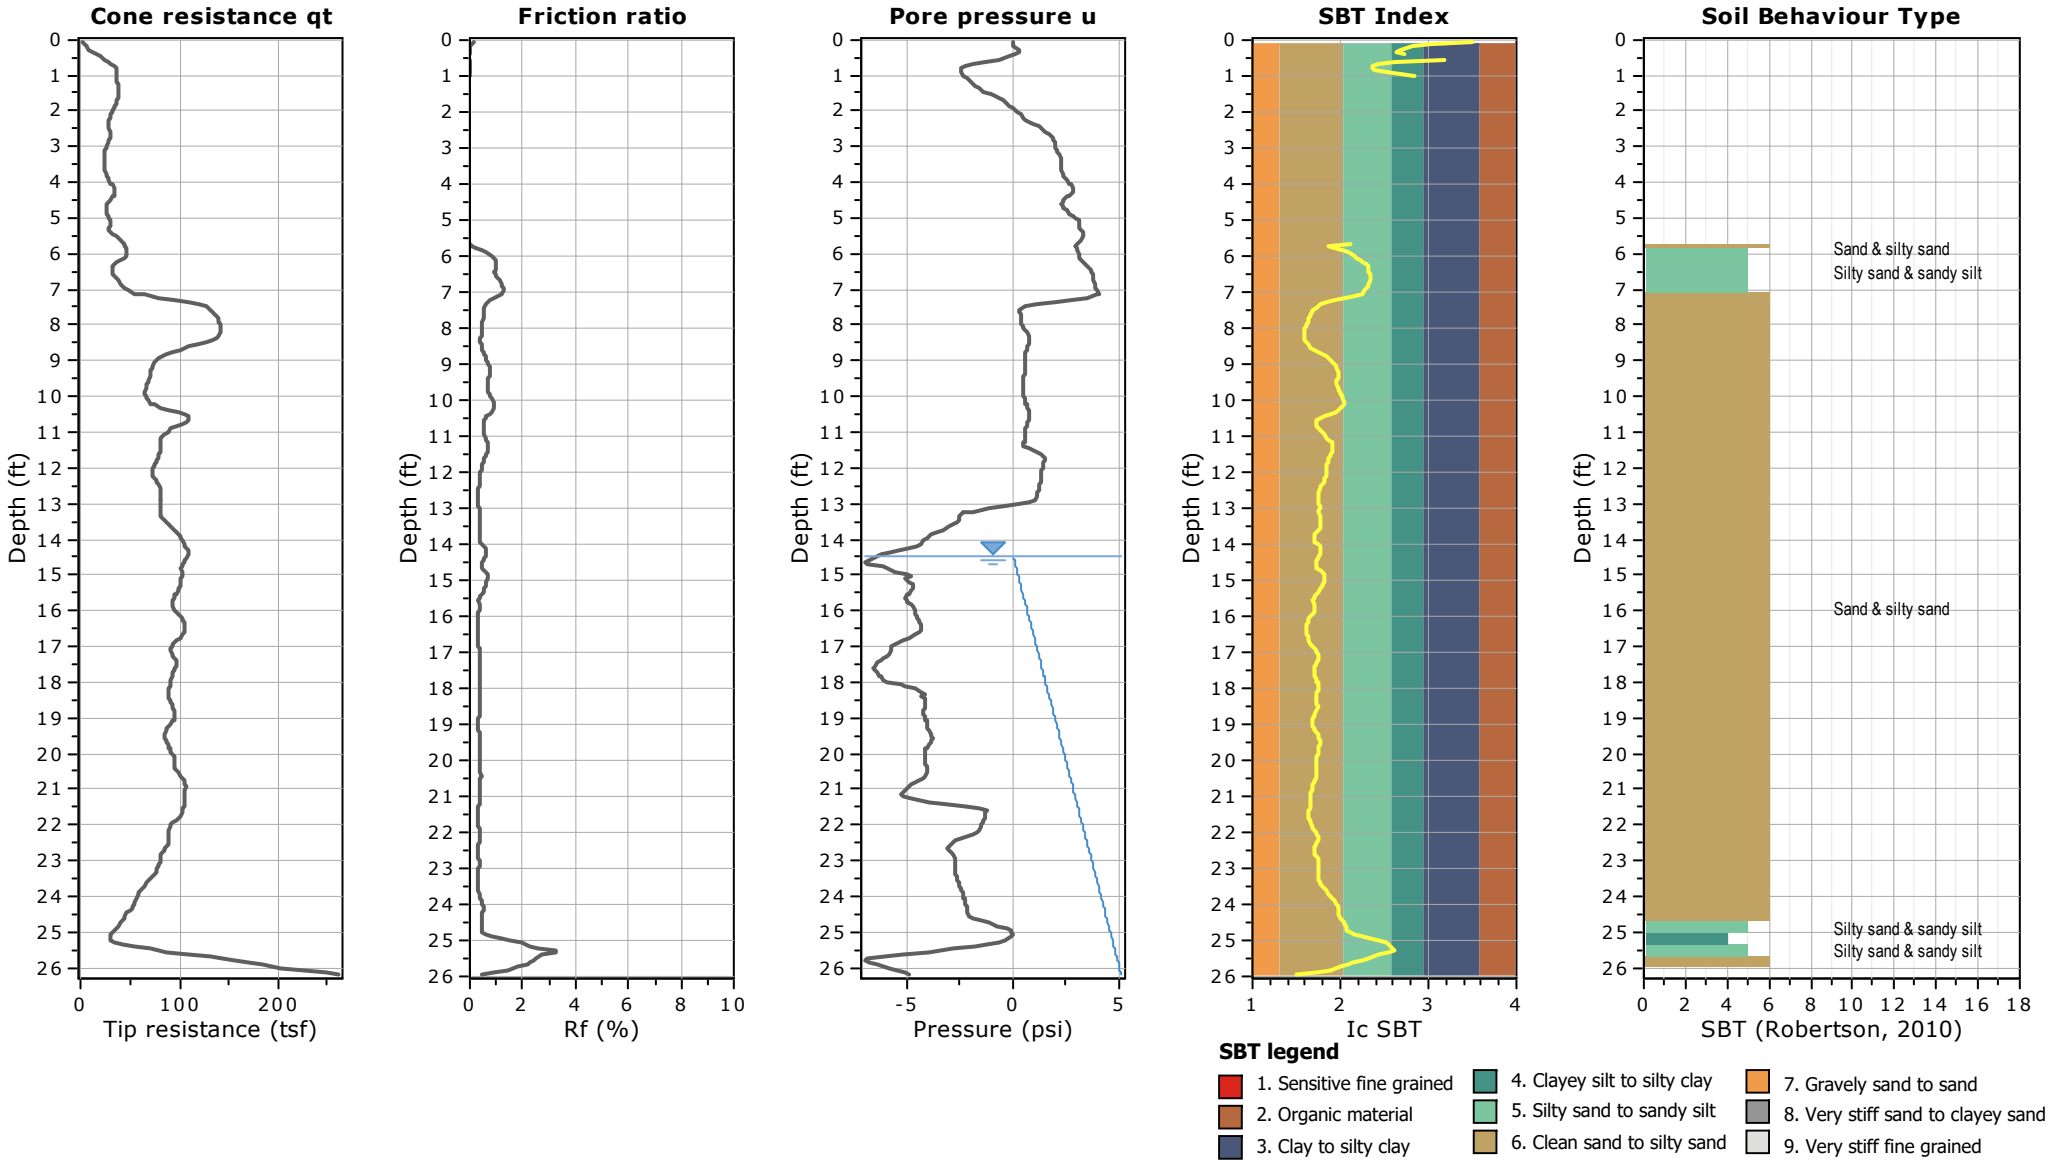



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100


CPT: 9
Total depth: 26.19 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

Updated SBTn plots

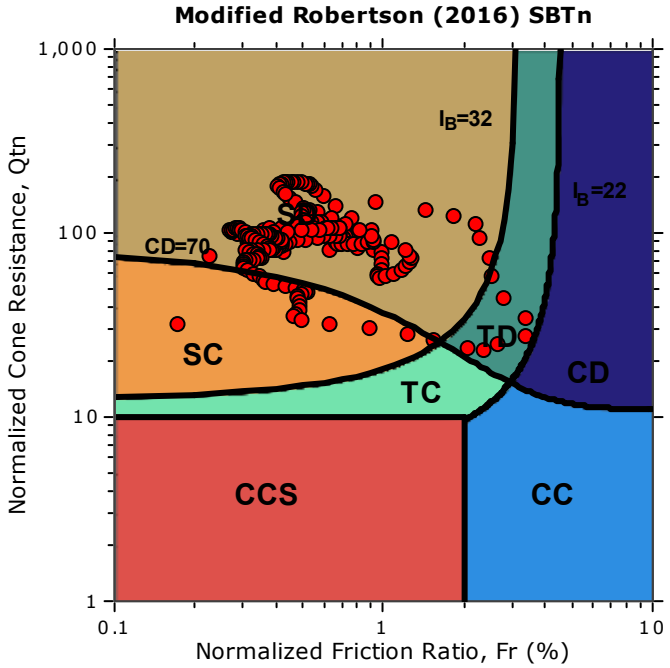

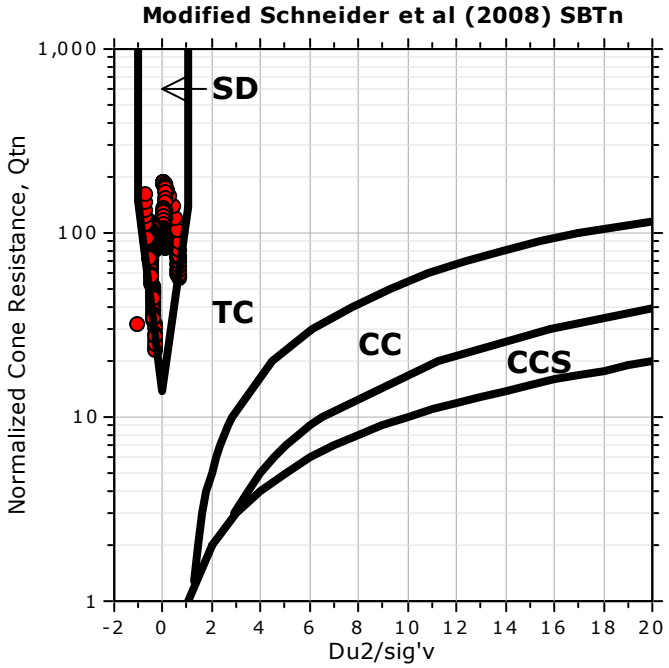

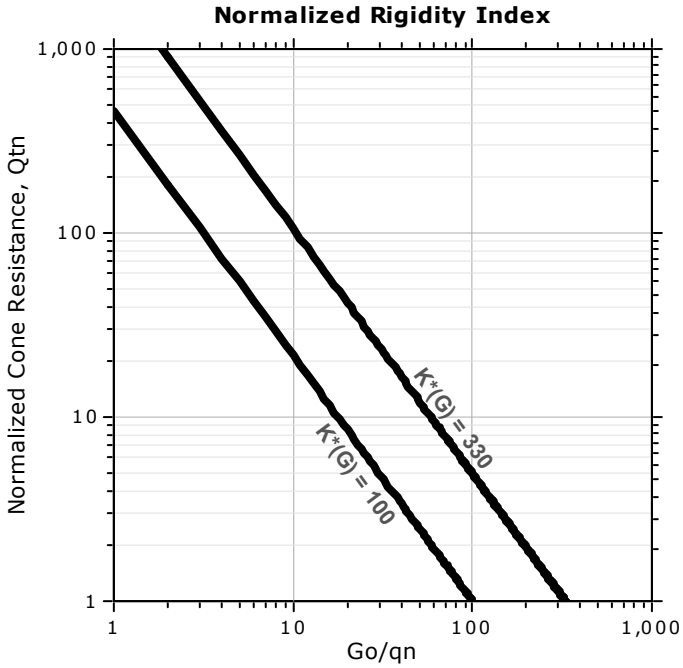


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 9
Total depth: 26.19 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

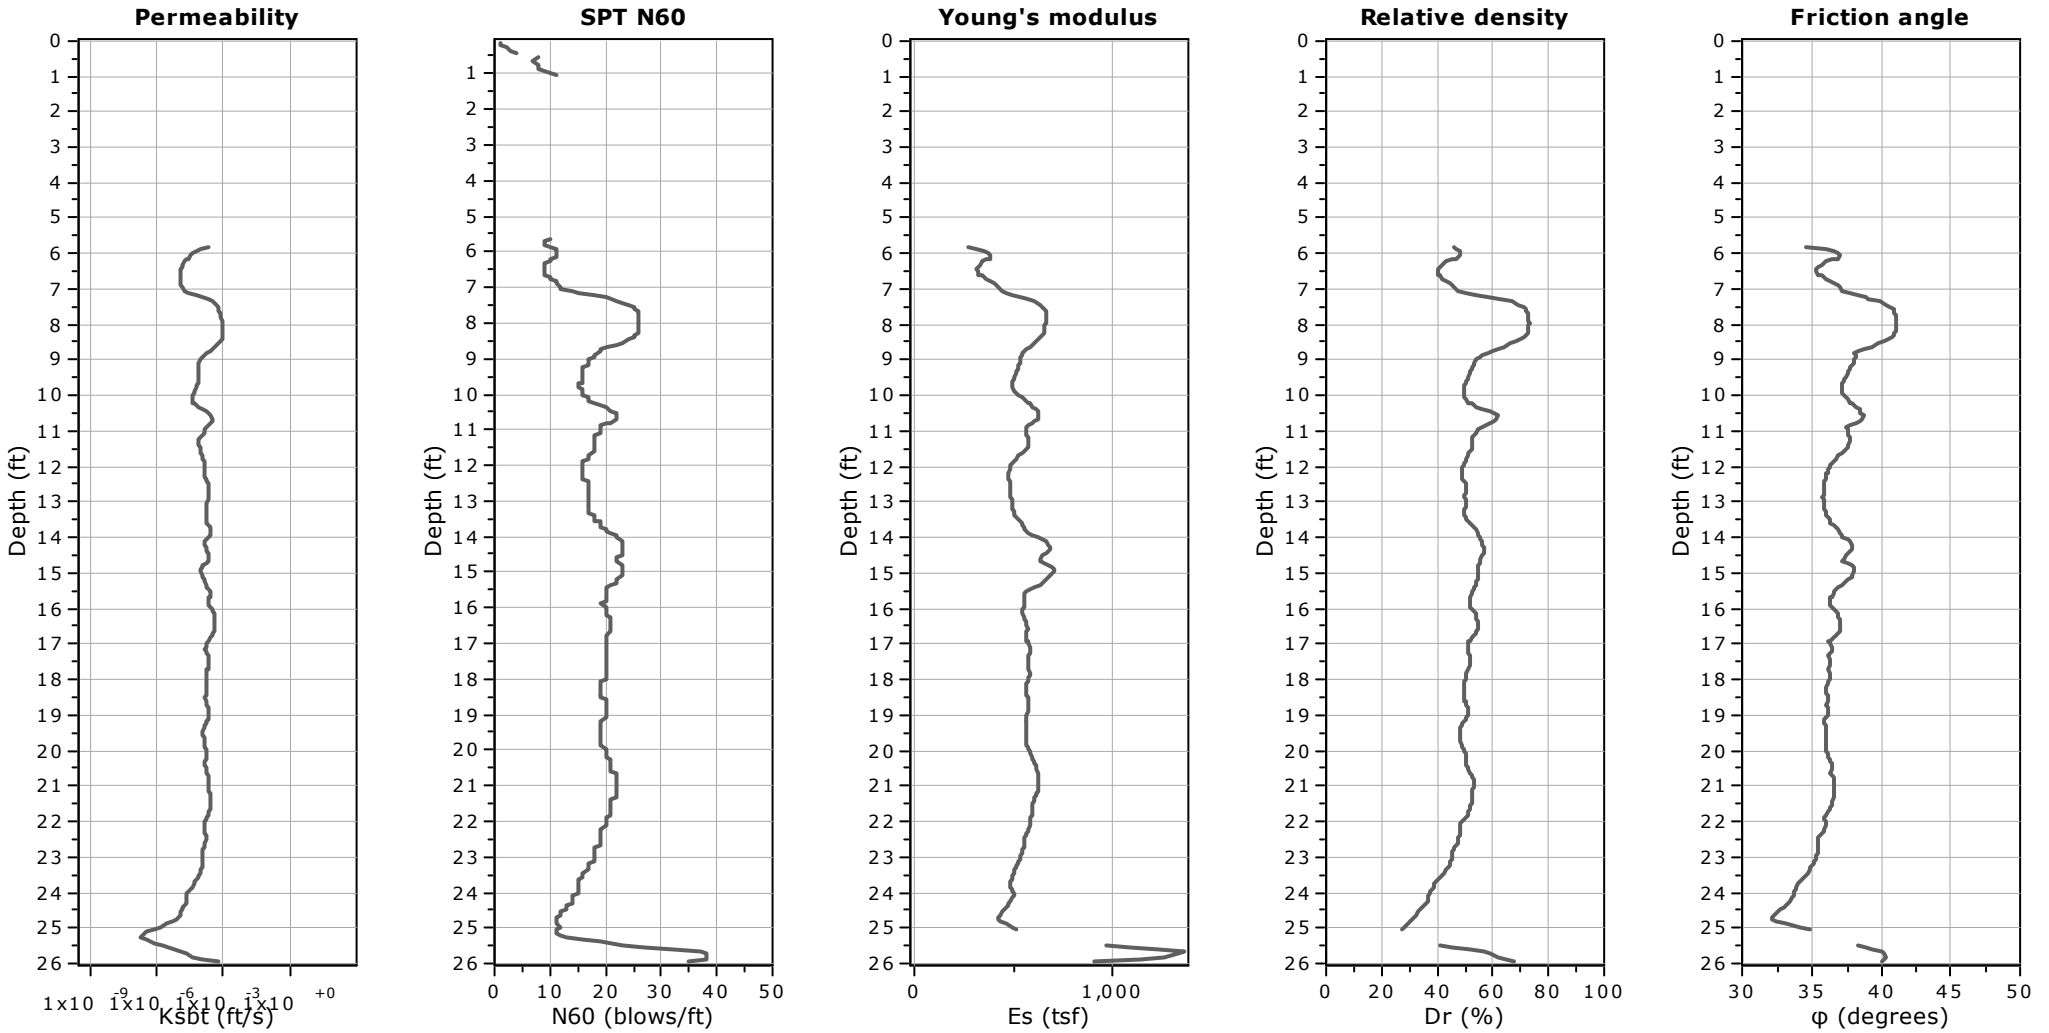


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 9
Total depth: 26.19 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

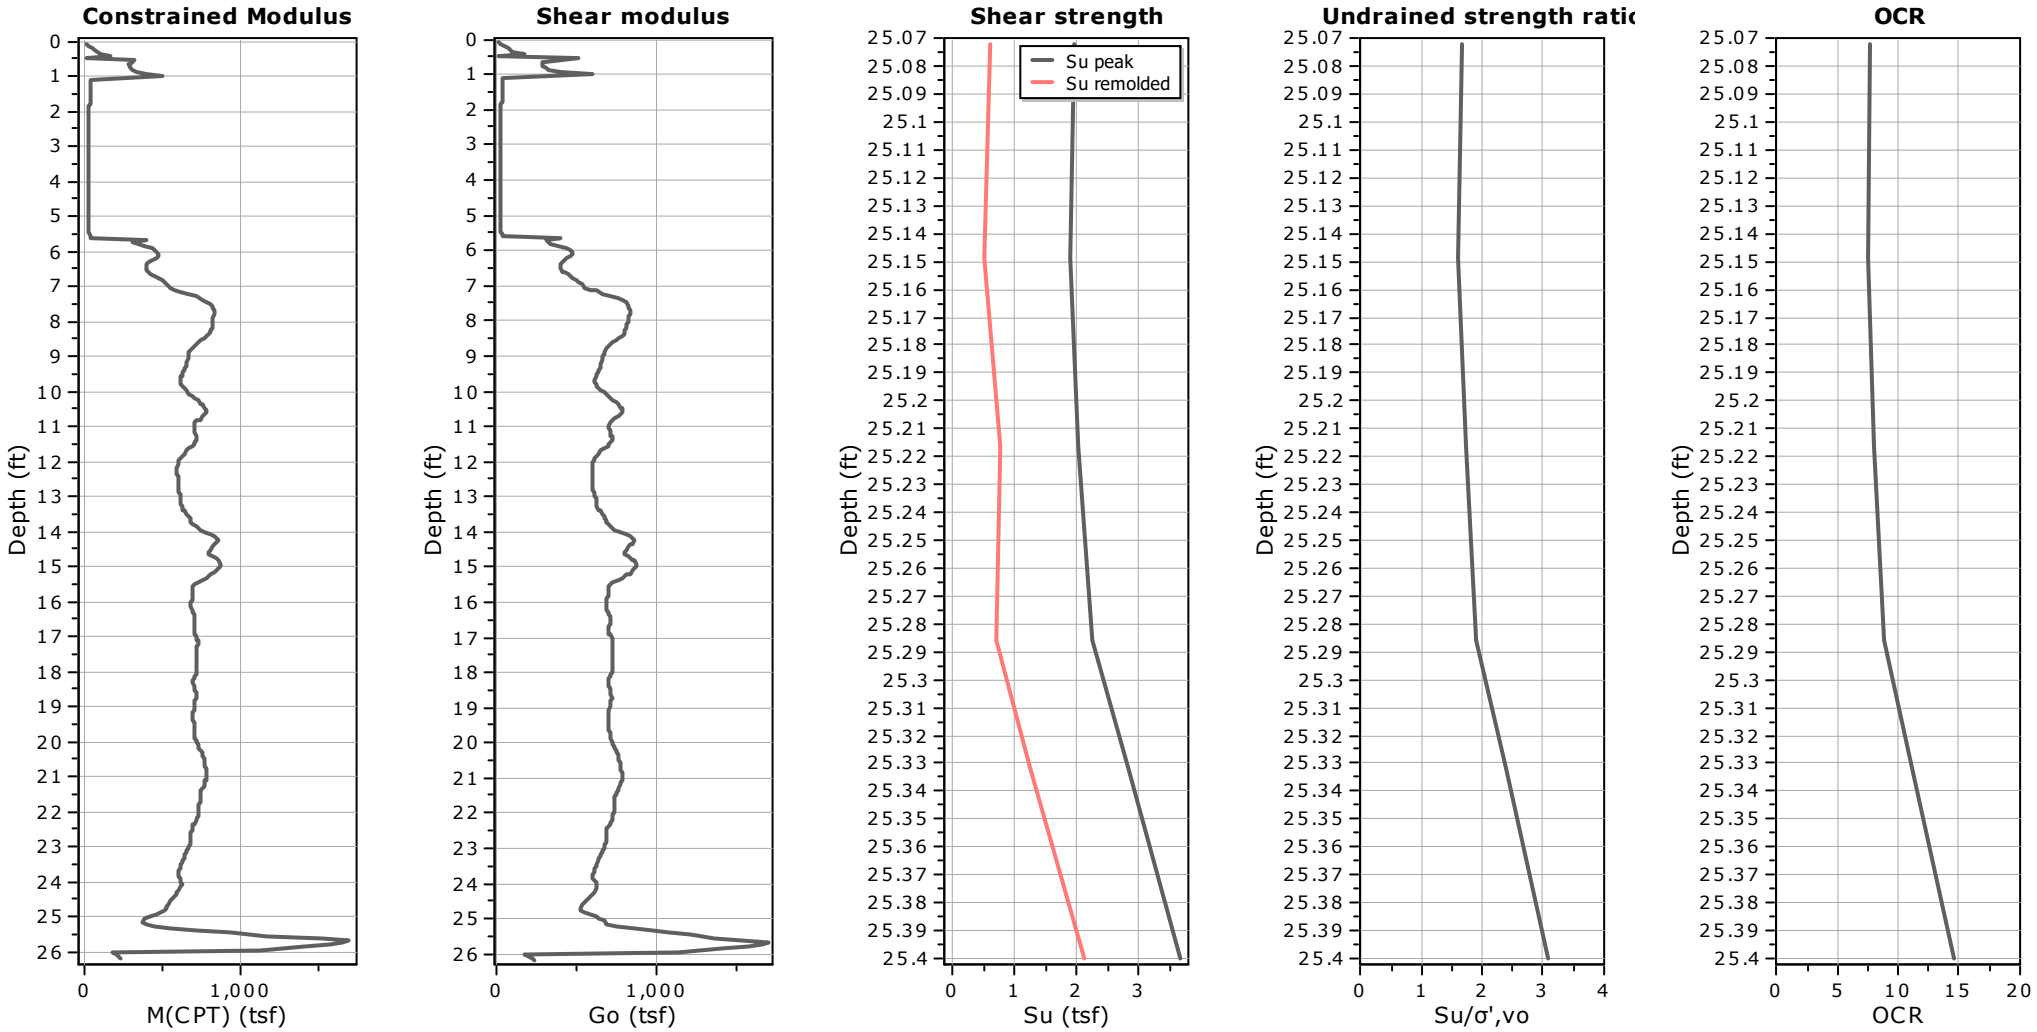


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle Suite 36
New Castle DE 19720
302 326 2100

CPT: 9
Total depth: 26.19 ft, Date: 4/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **Hodgson Vo-Tech New Campus**
Location: **New Castle County, Delaware**

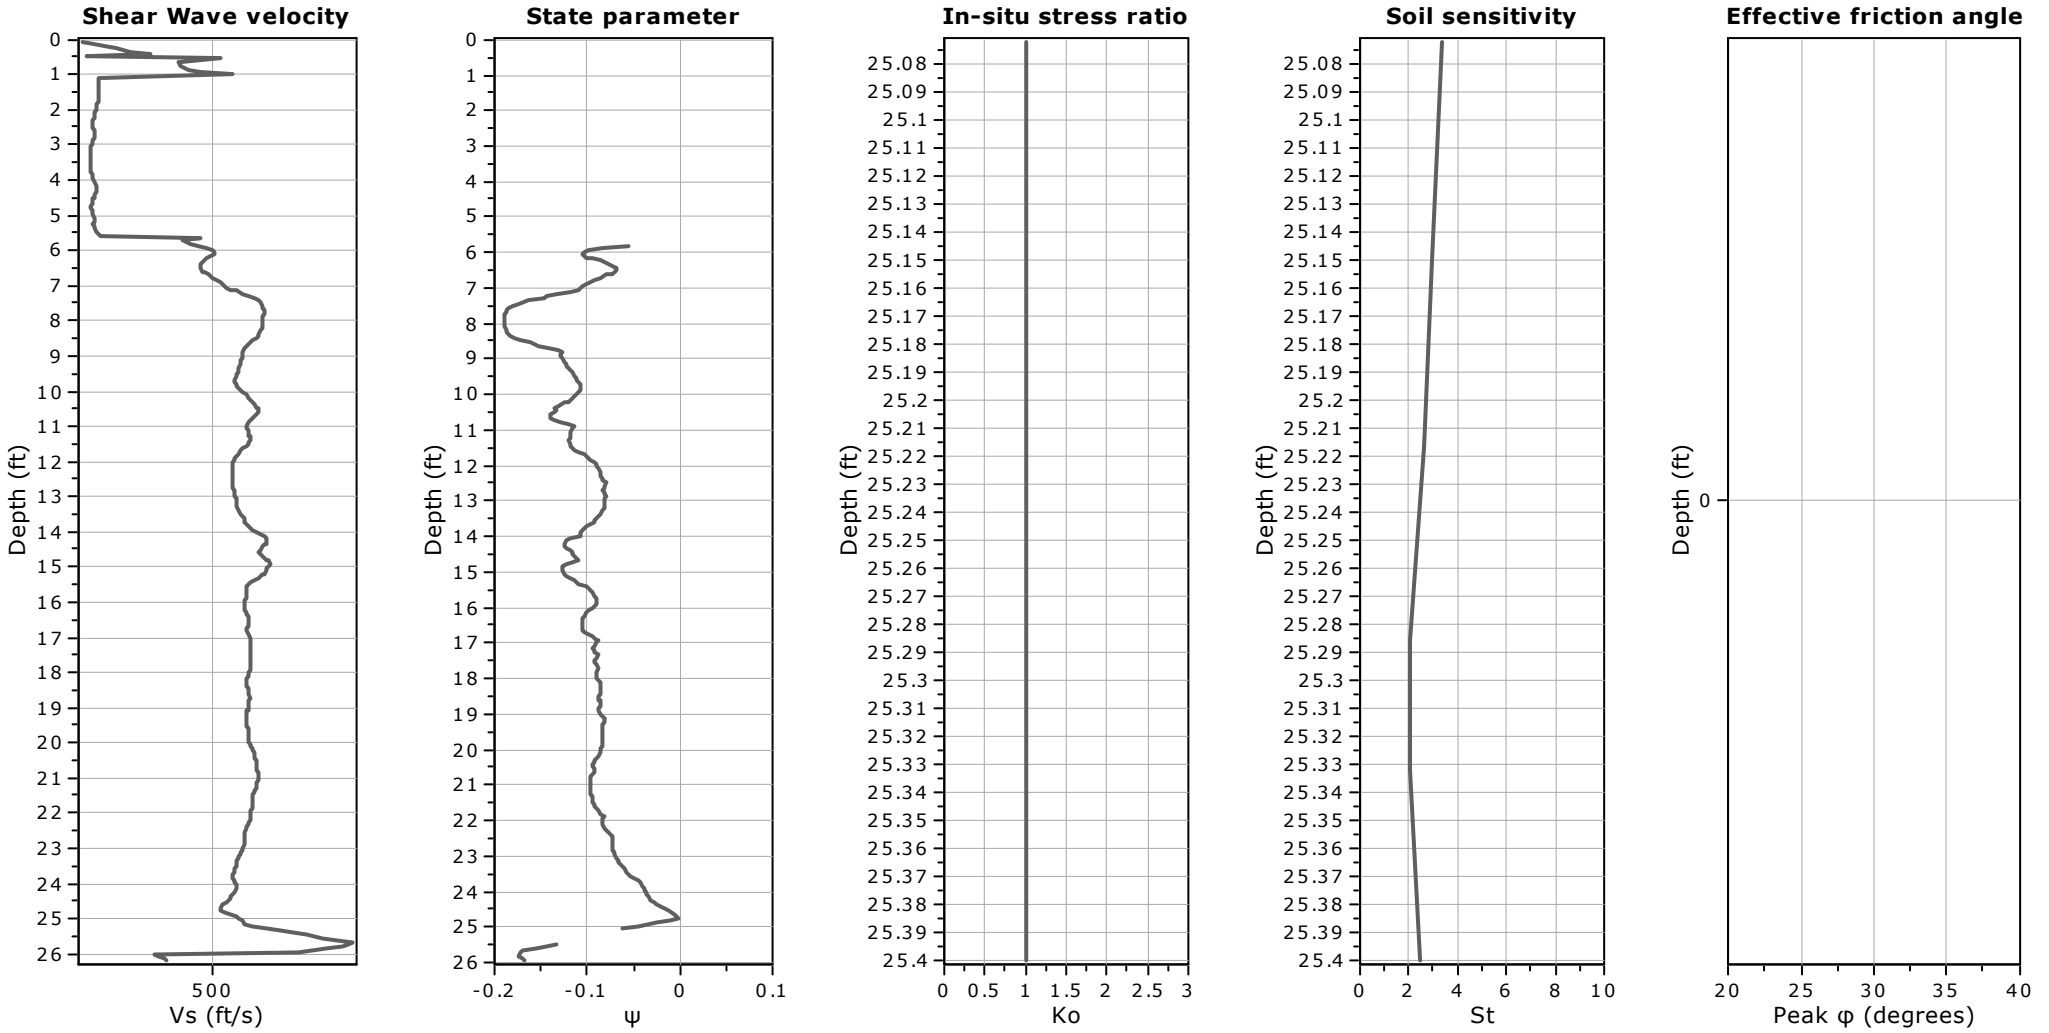

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-10
Total depth: 12.22 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

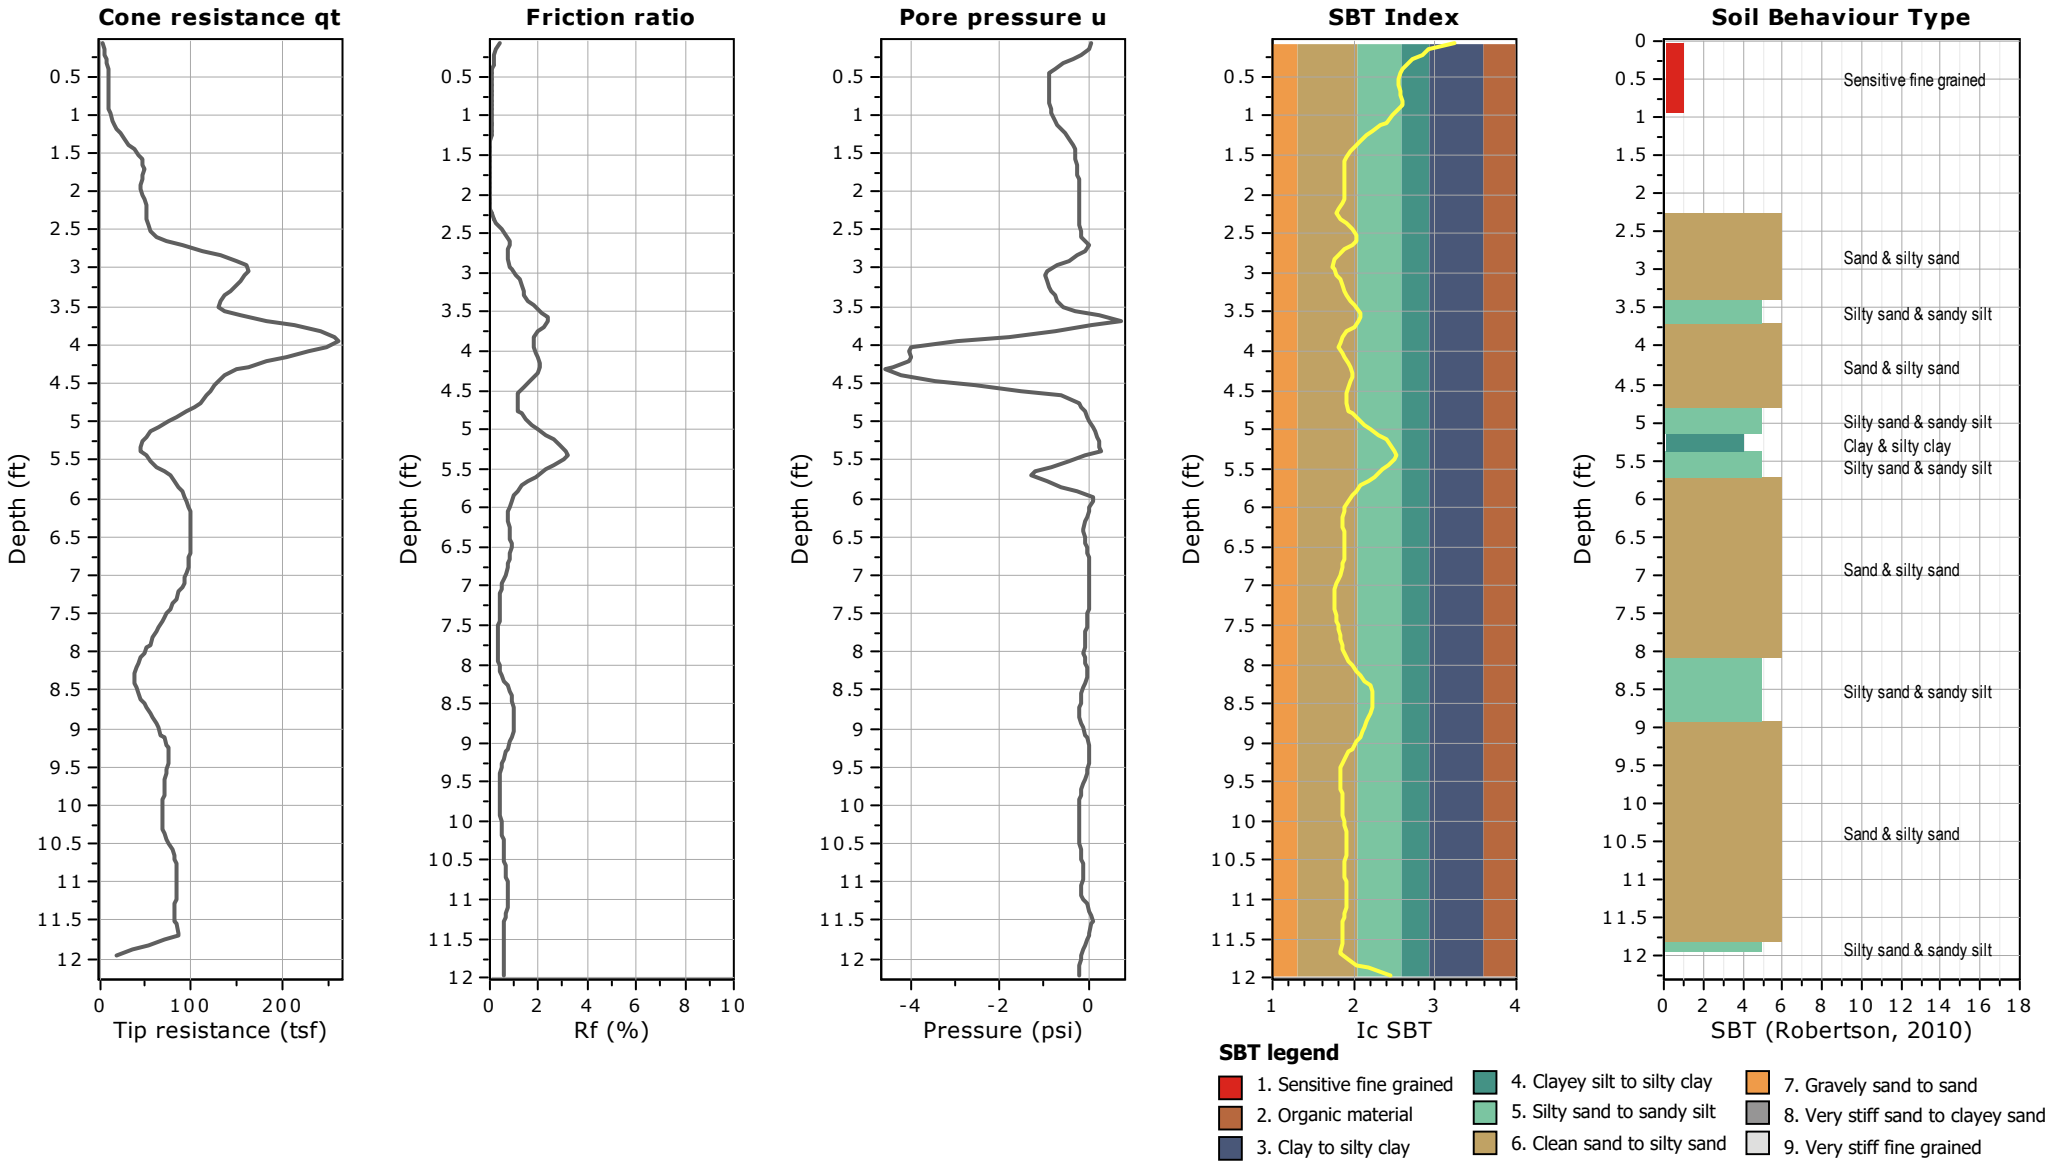



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-10
Total depth: 12.22 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

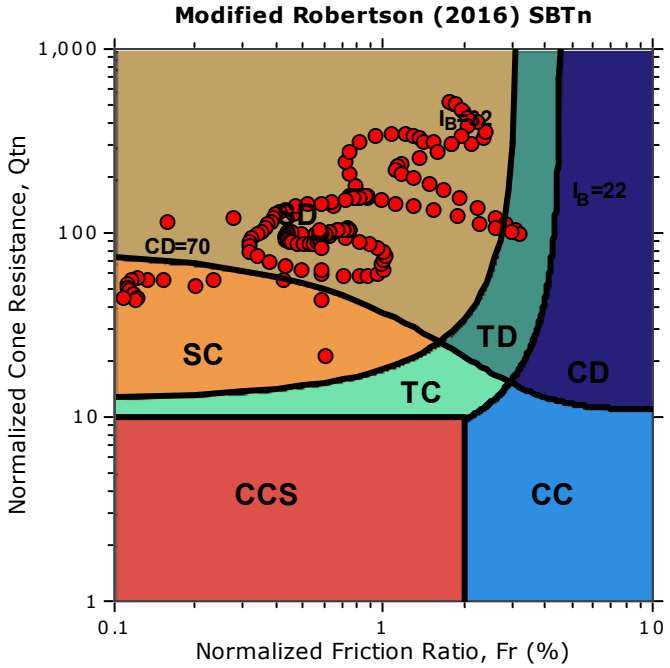

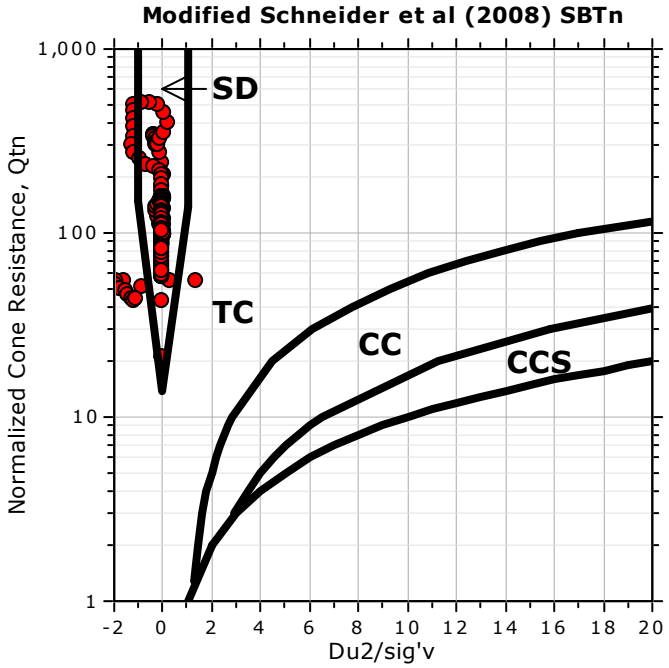

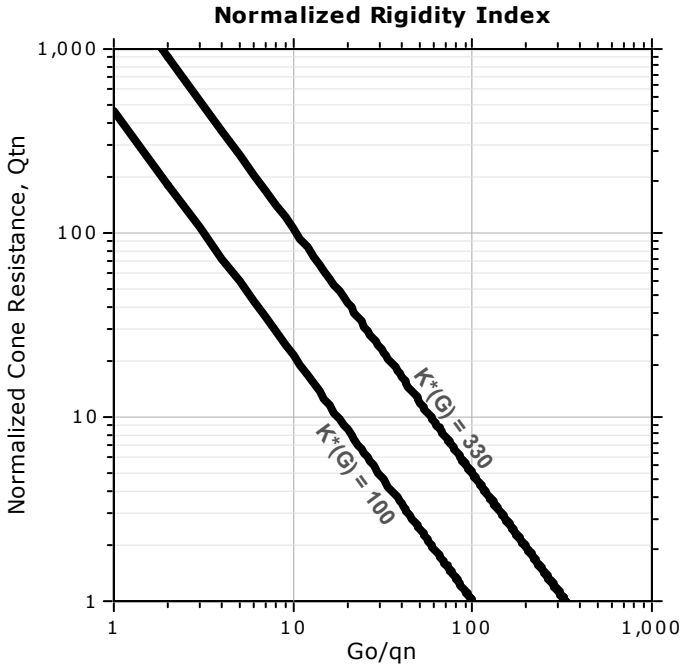


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-10
Total depth: 12.22 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

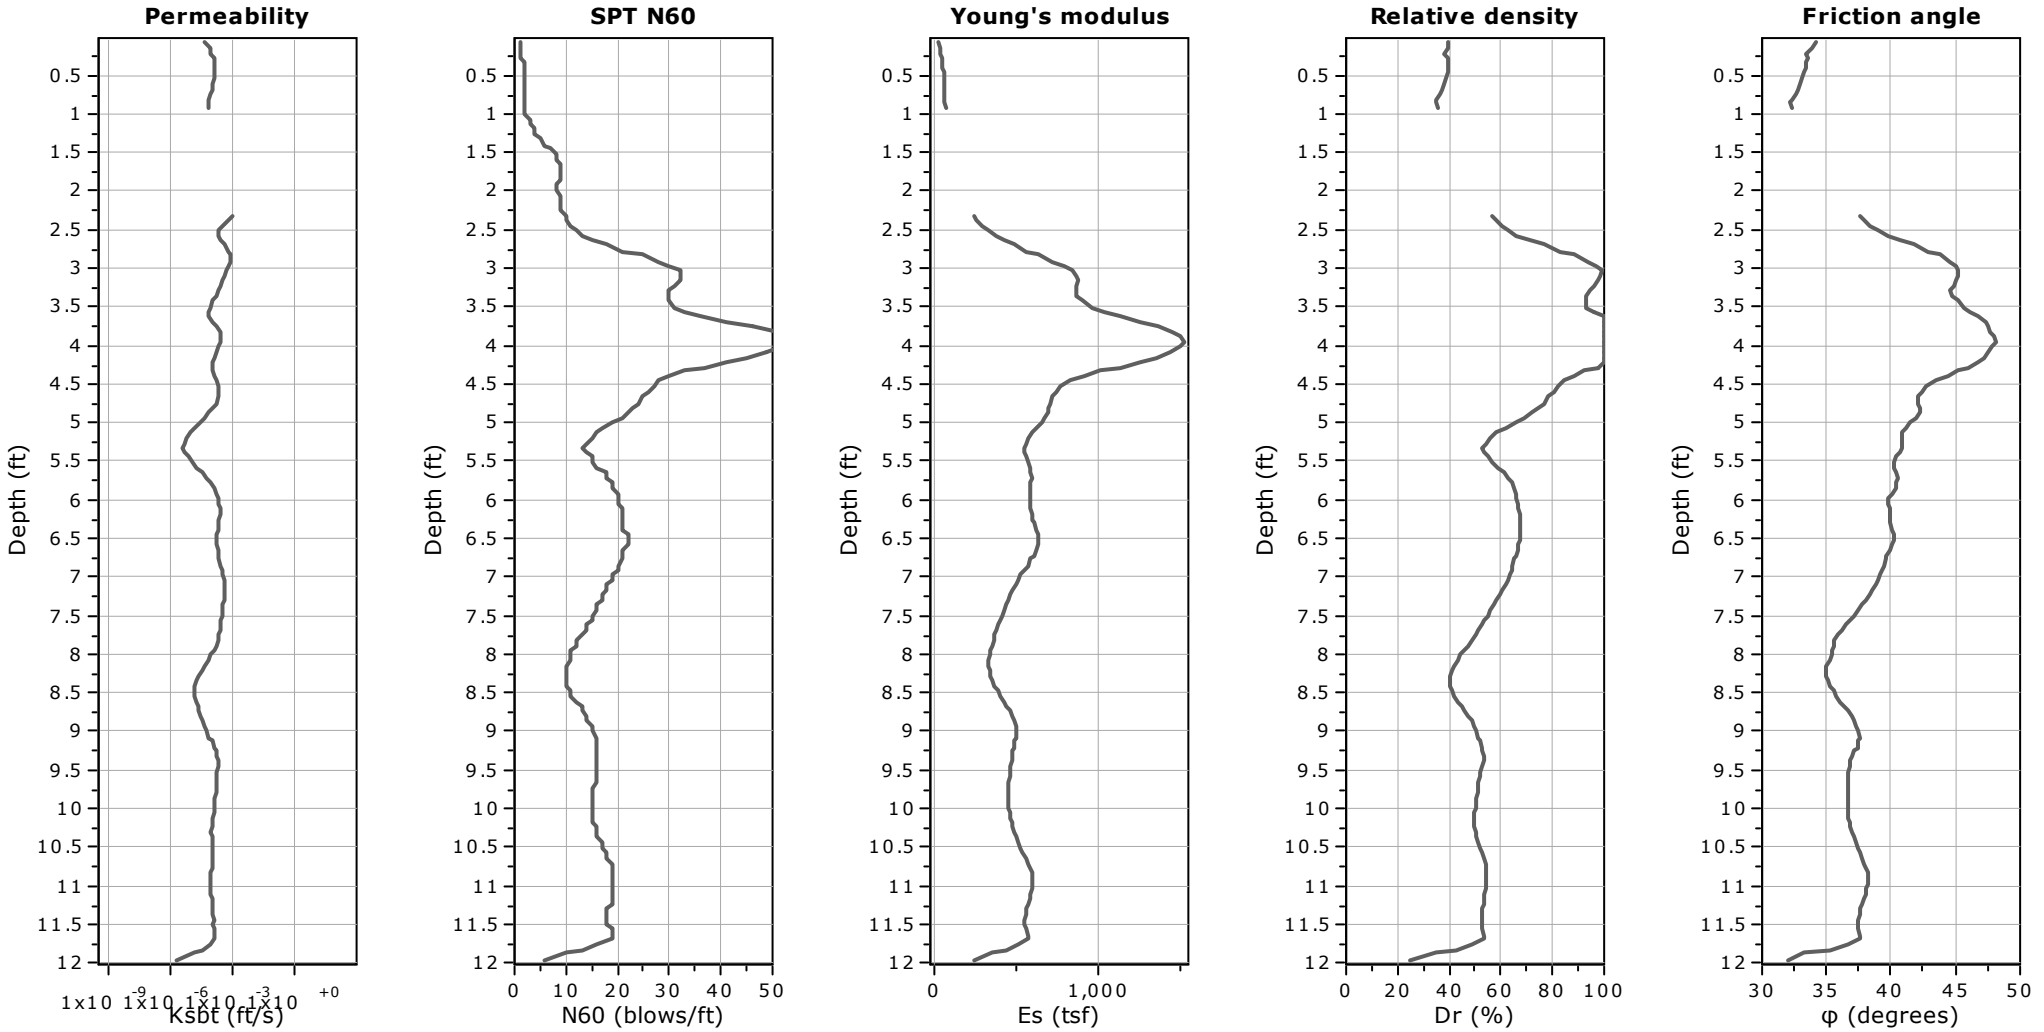


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-10
Total depth: 12.22 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

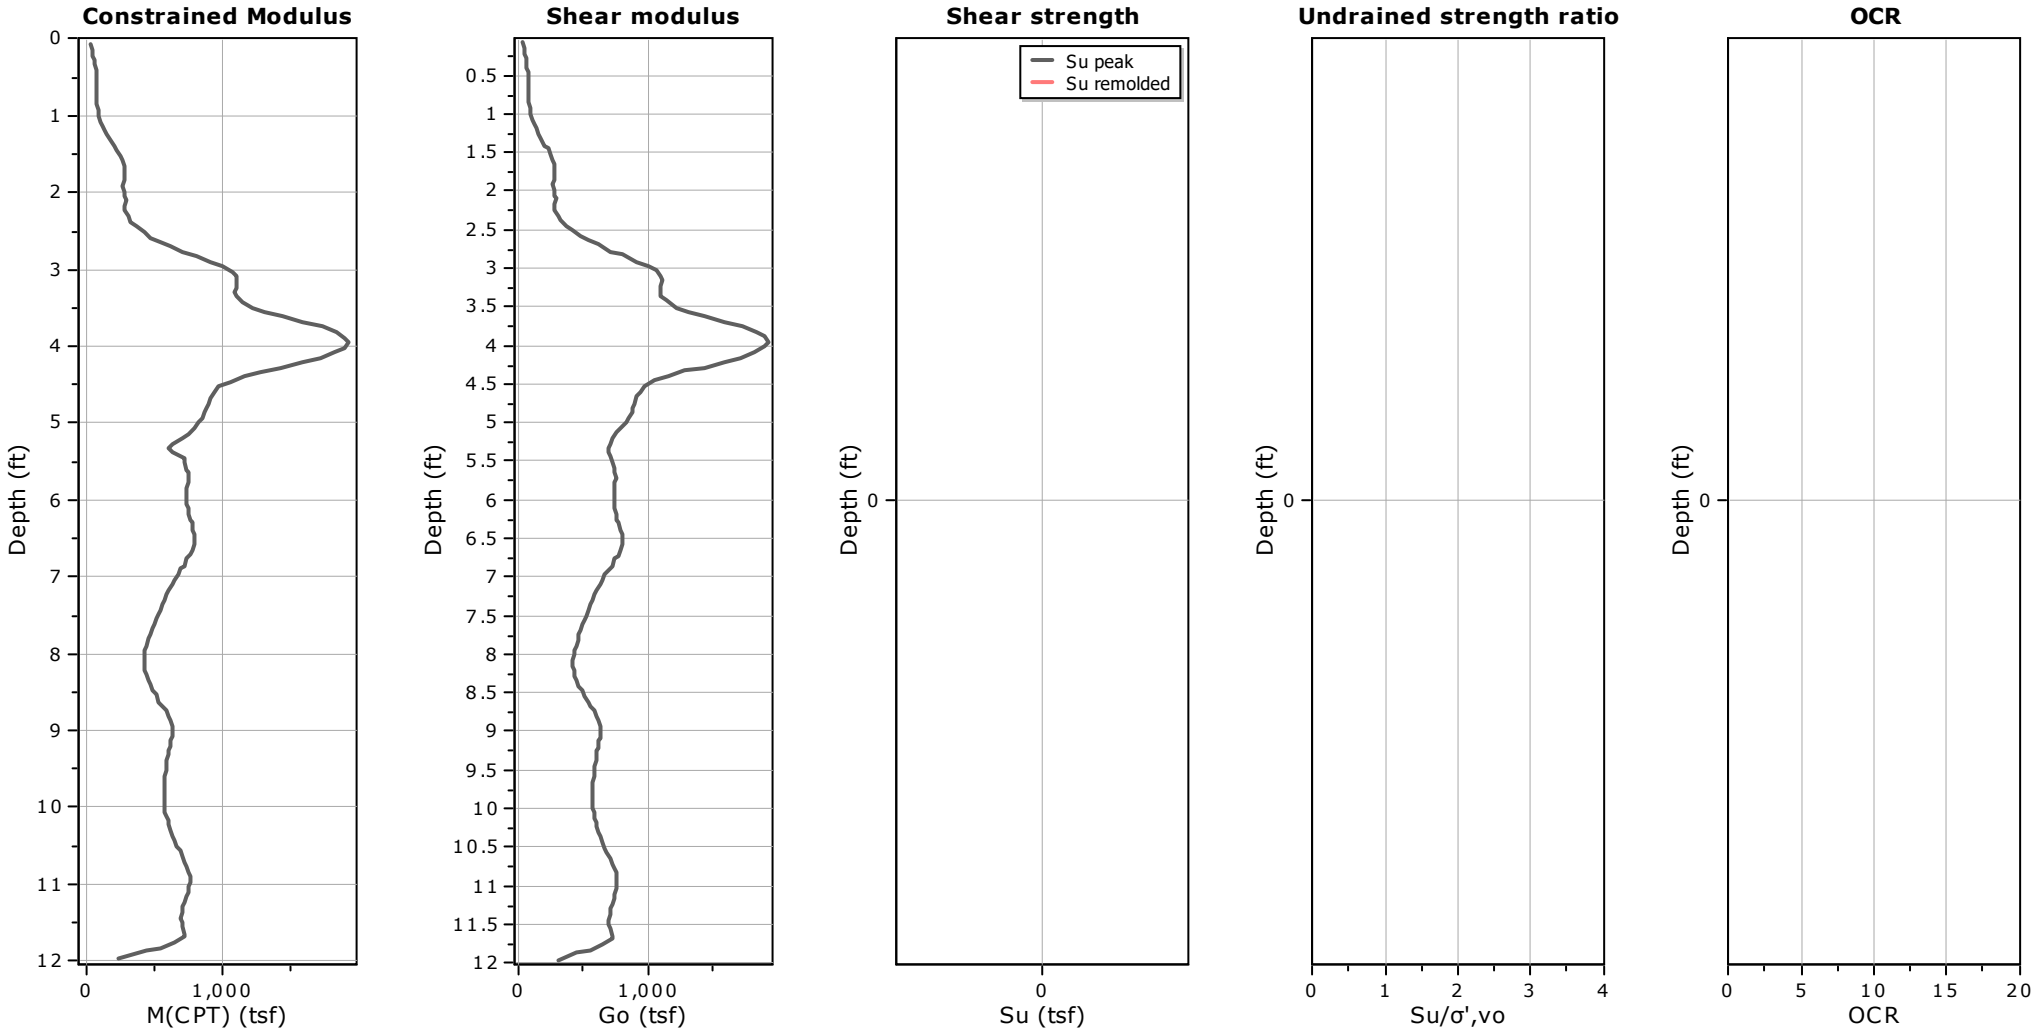

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-10
Total depth: 12.22 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

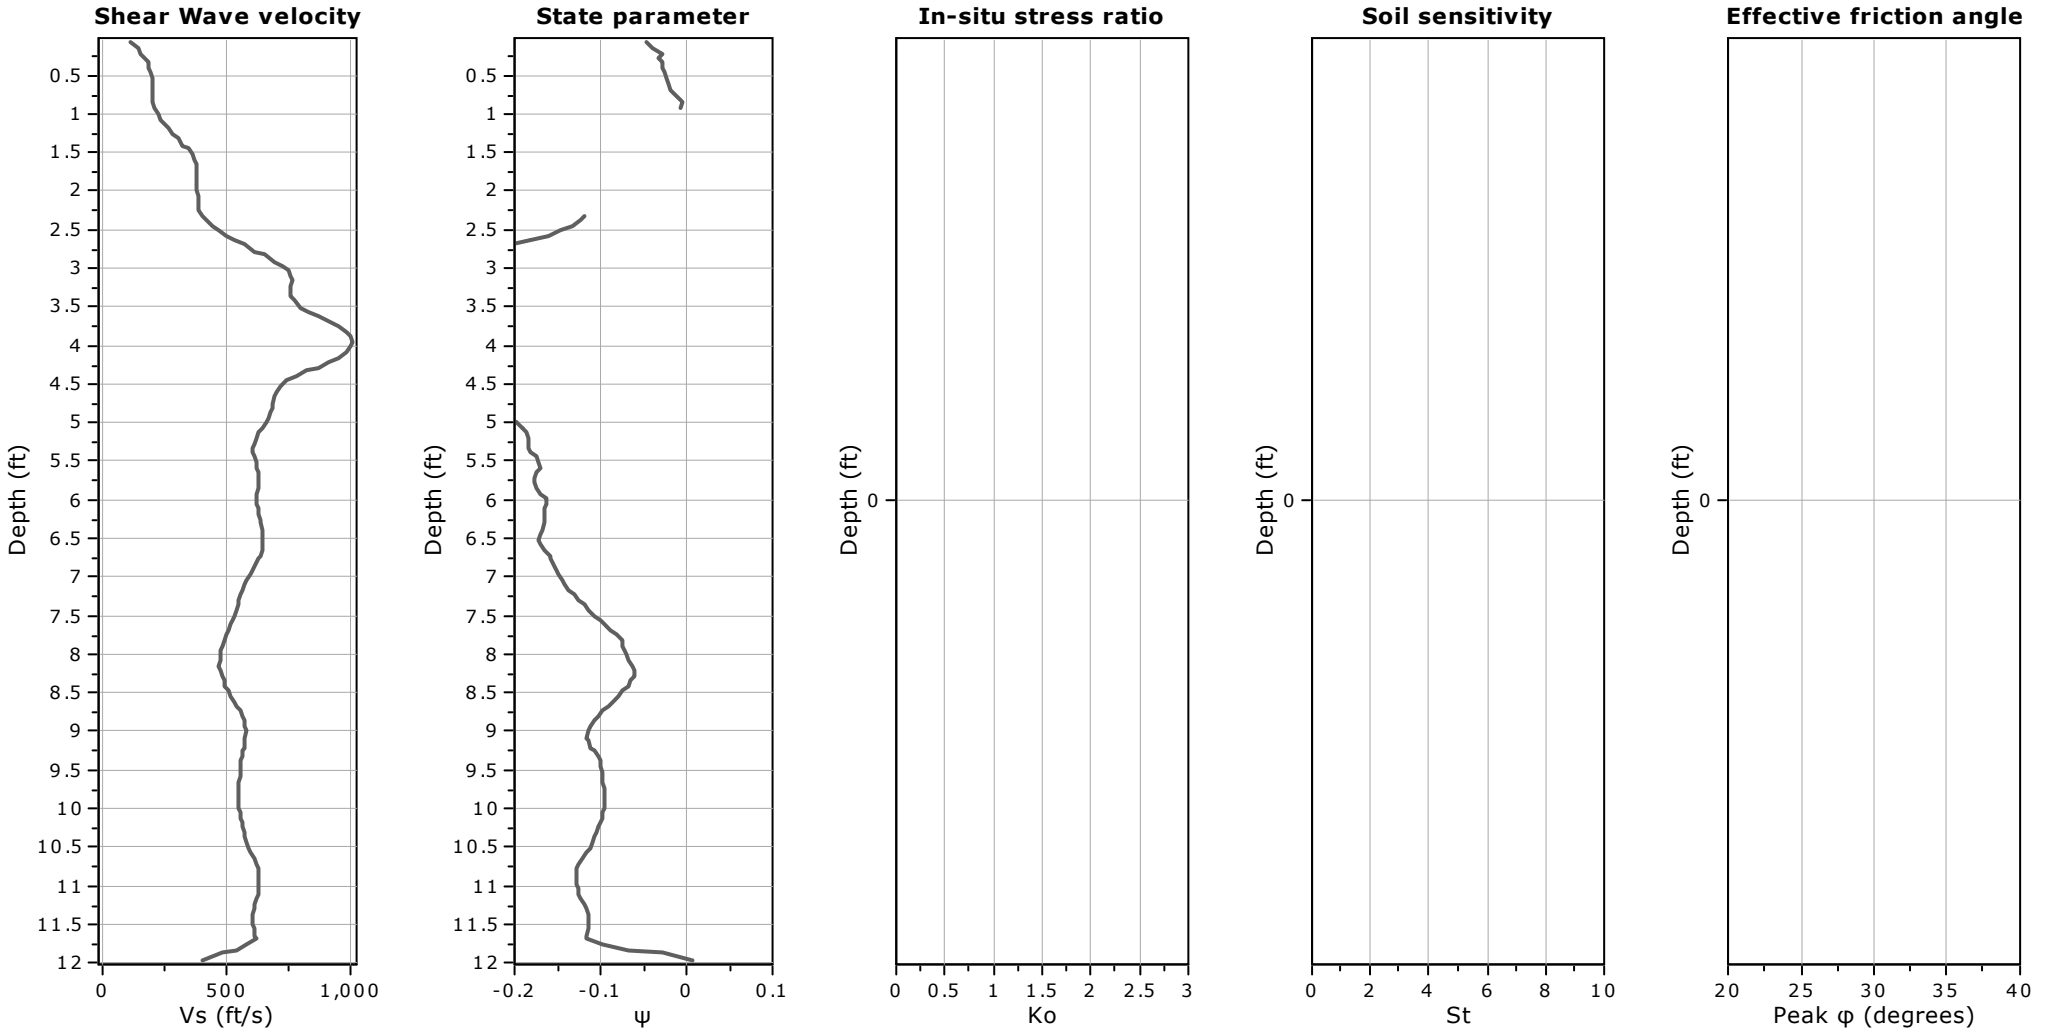

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-11
Total depth: 35.78 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

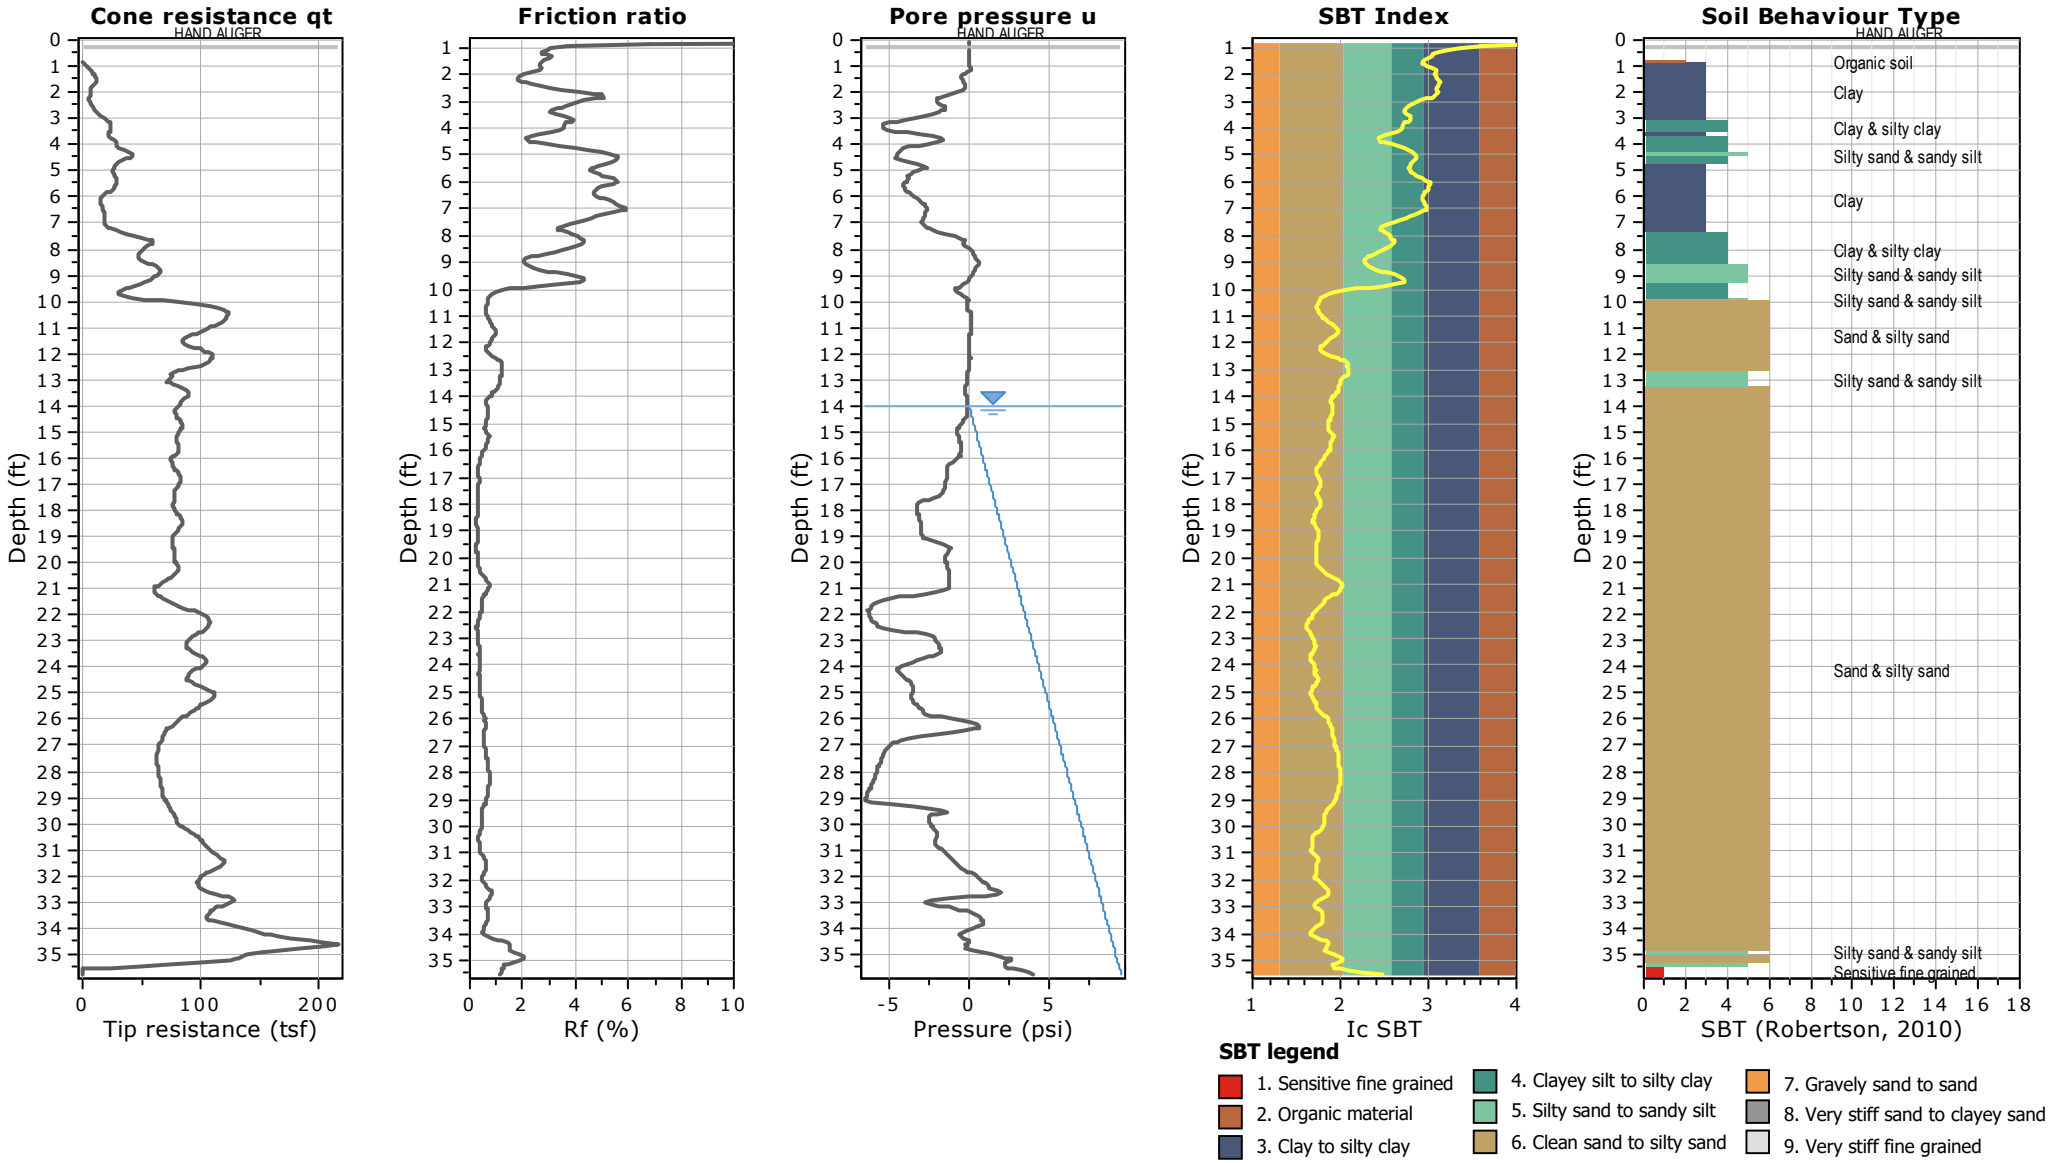



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-11
Total depth: 35.78 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

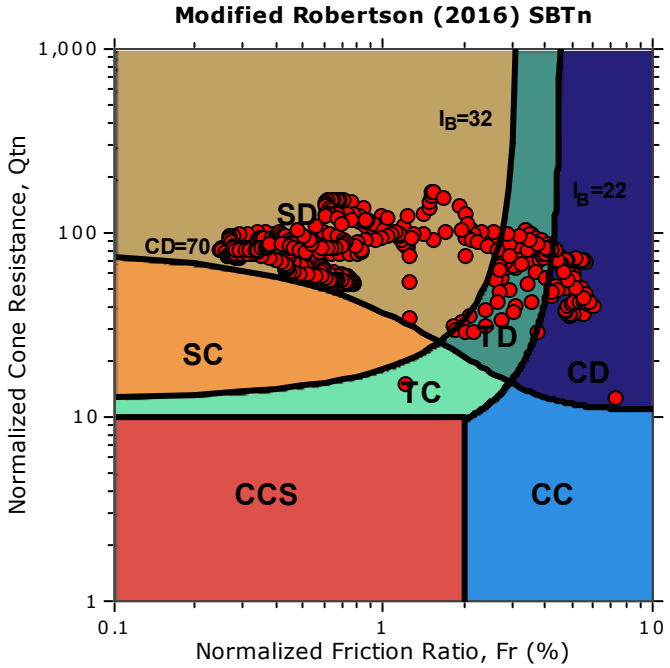

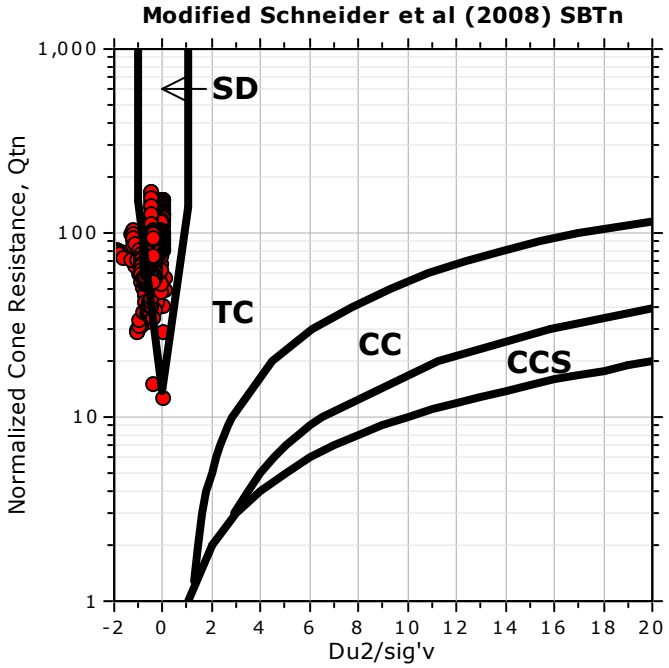

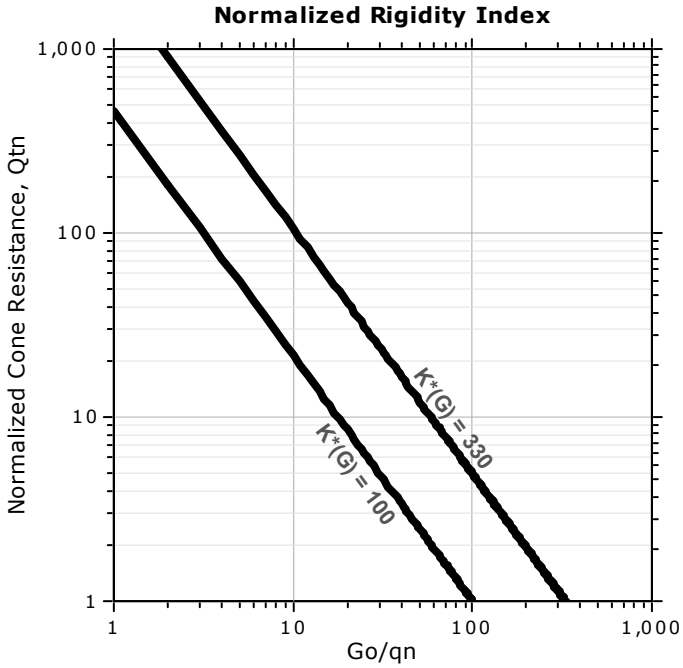


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-11
Total depth: 35.78 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

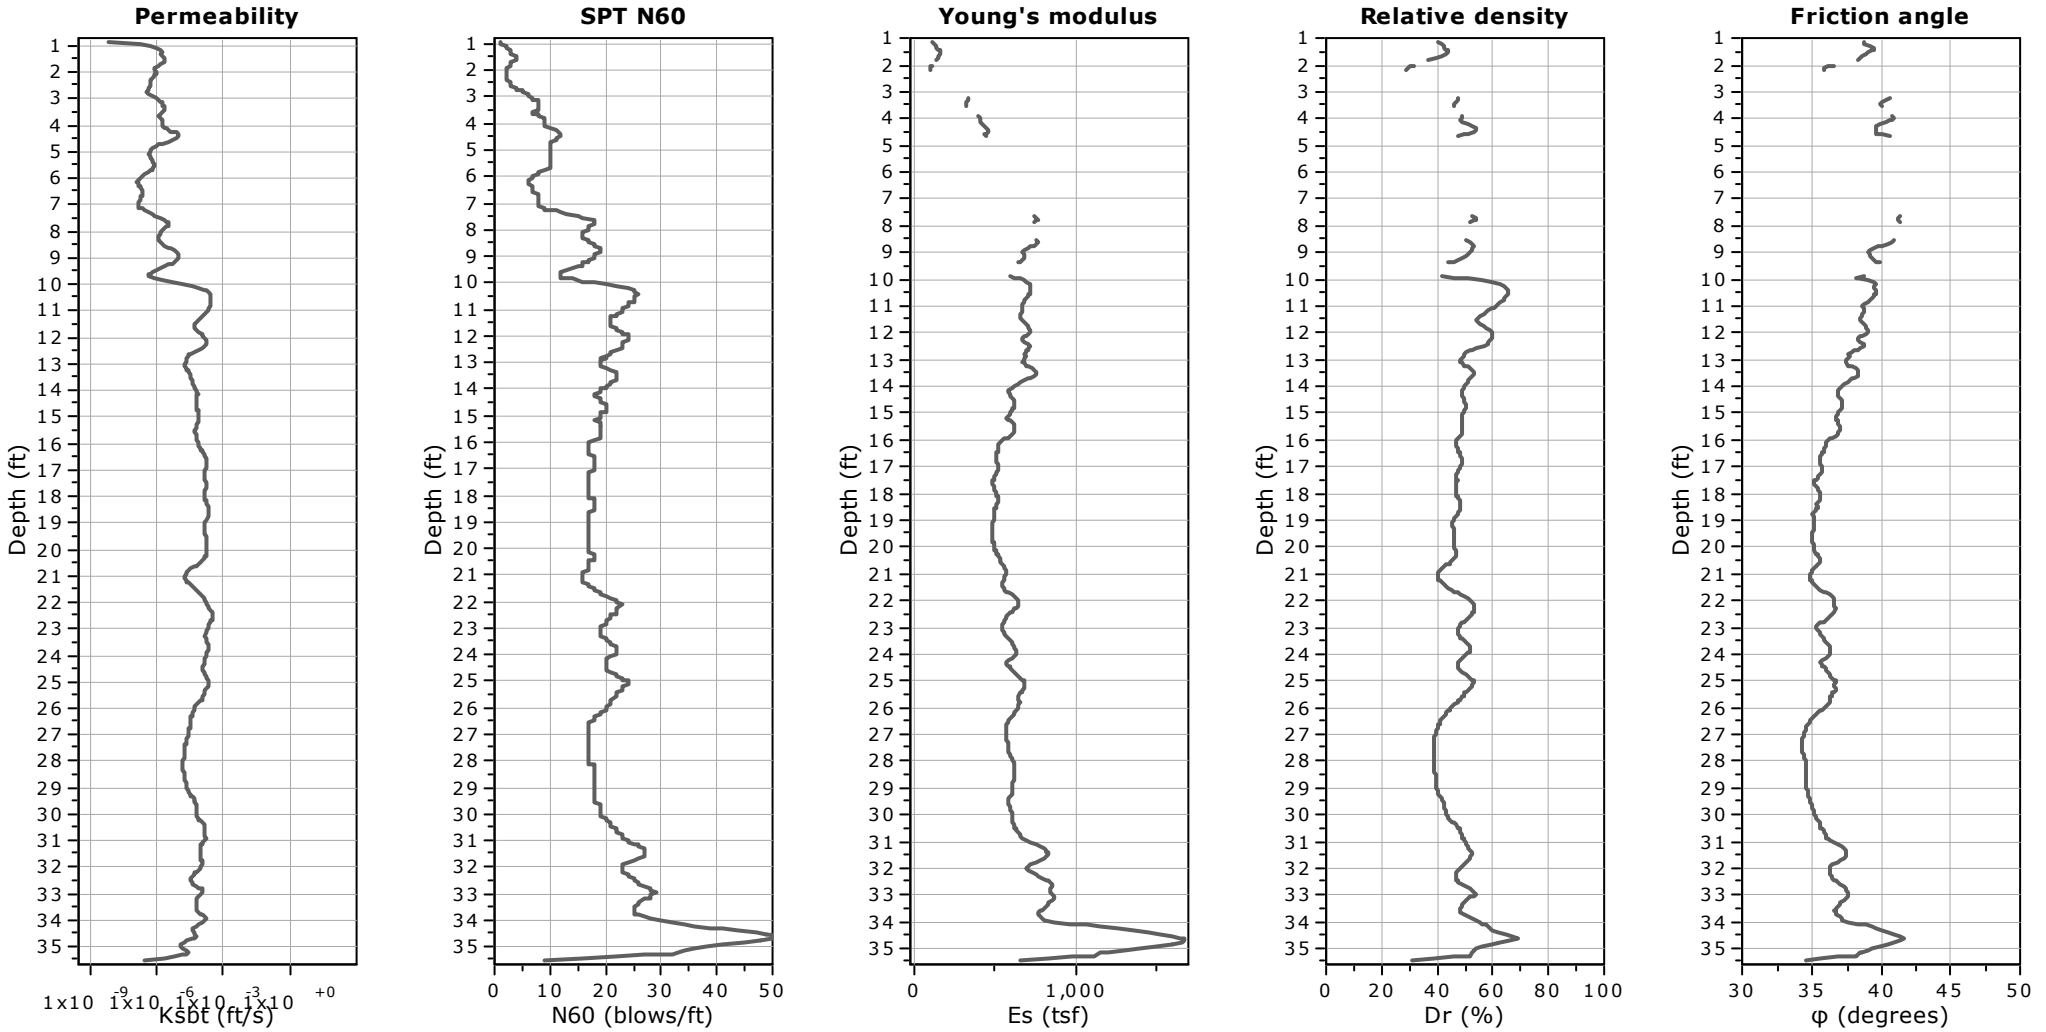


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-11
Total depth: 35.78 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

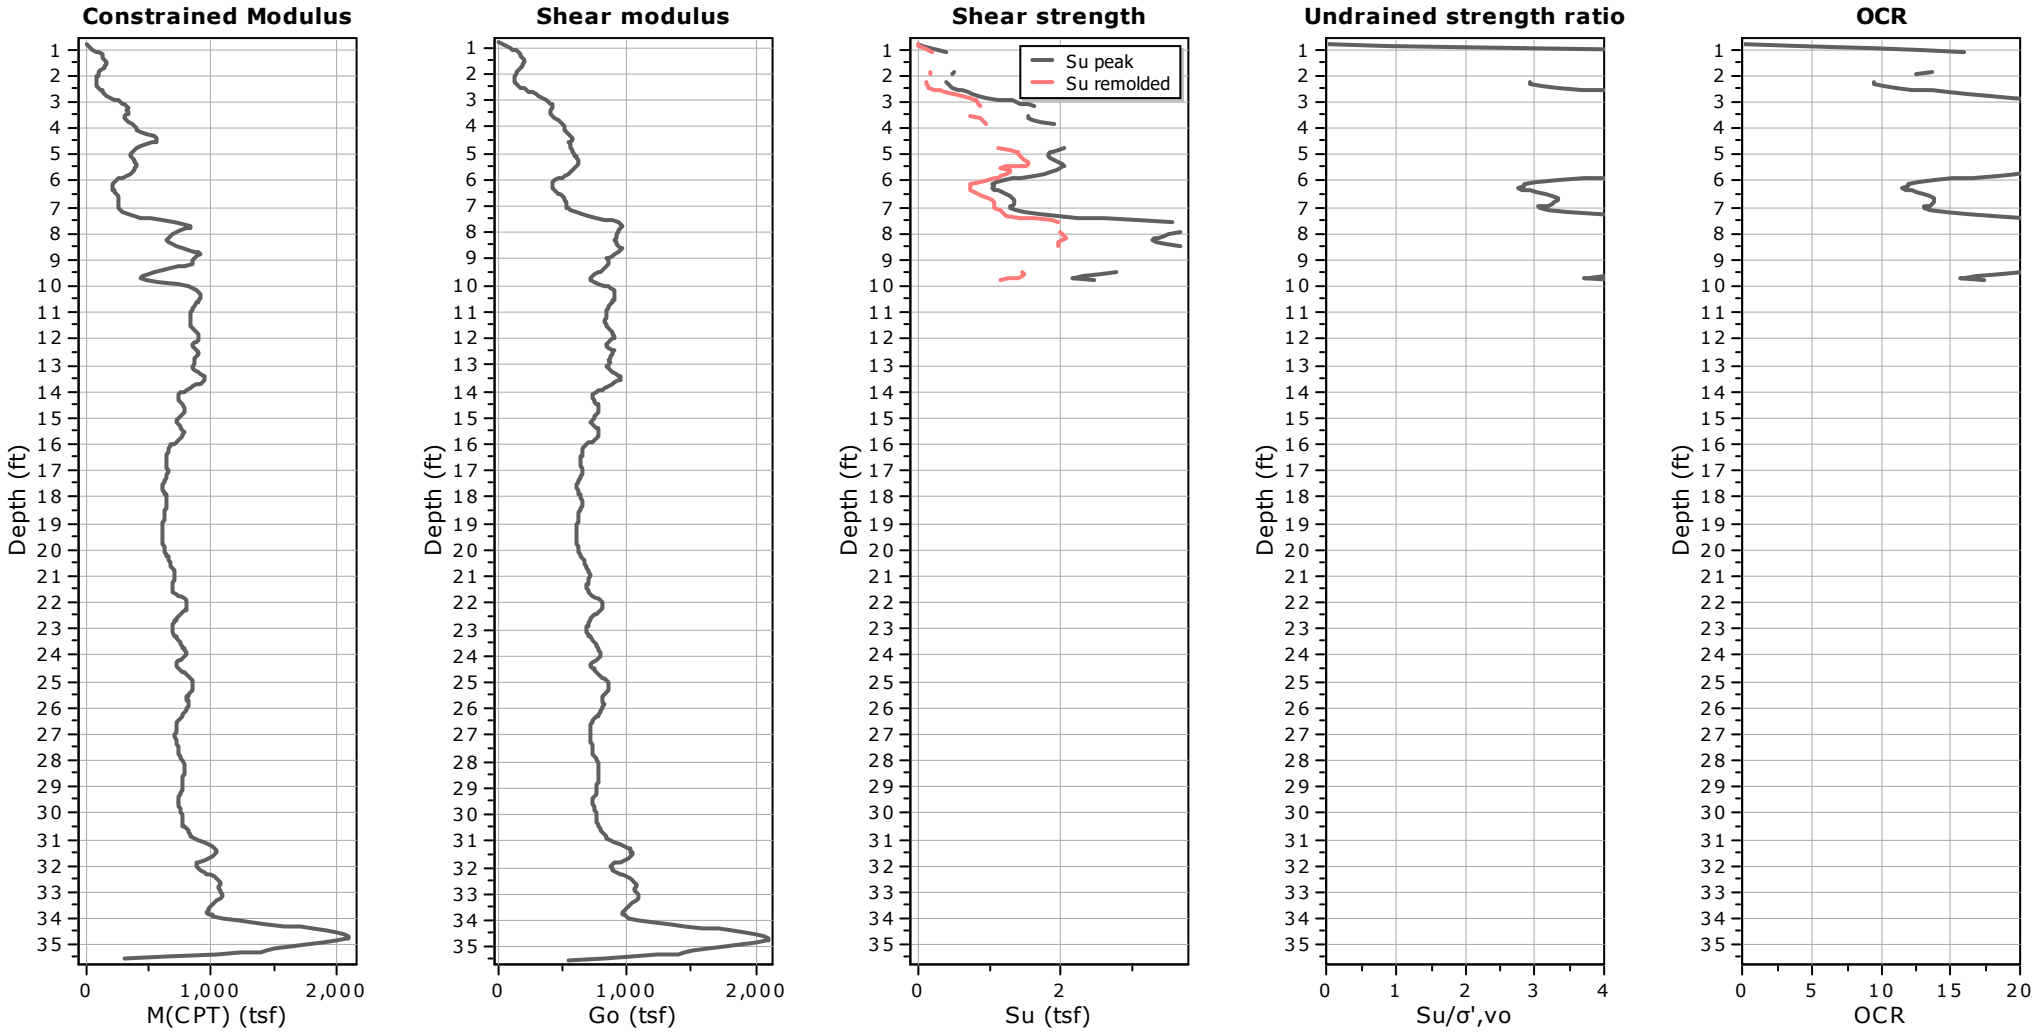

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-11
Total depth: 35.78 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

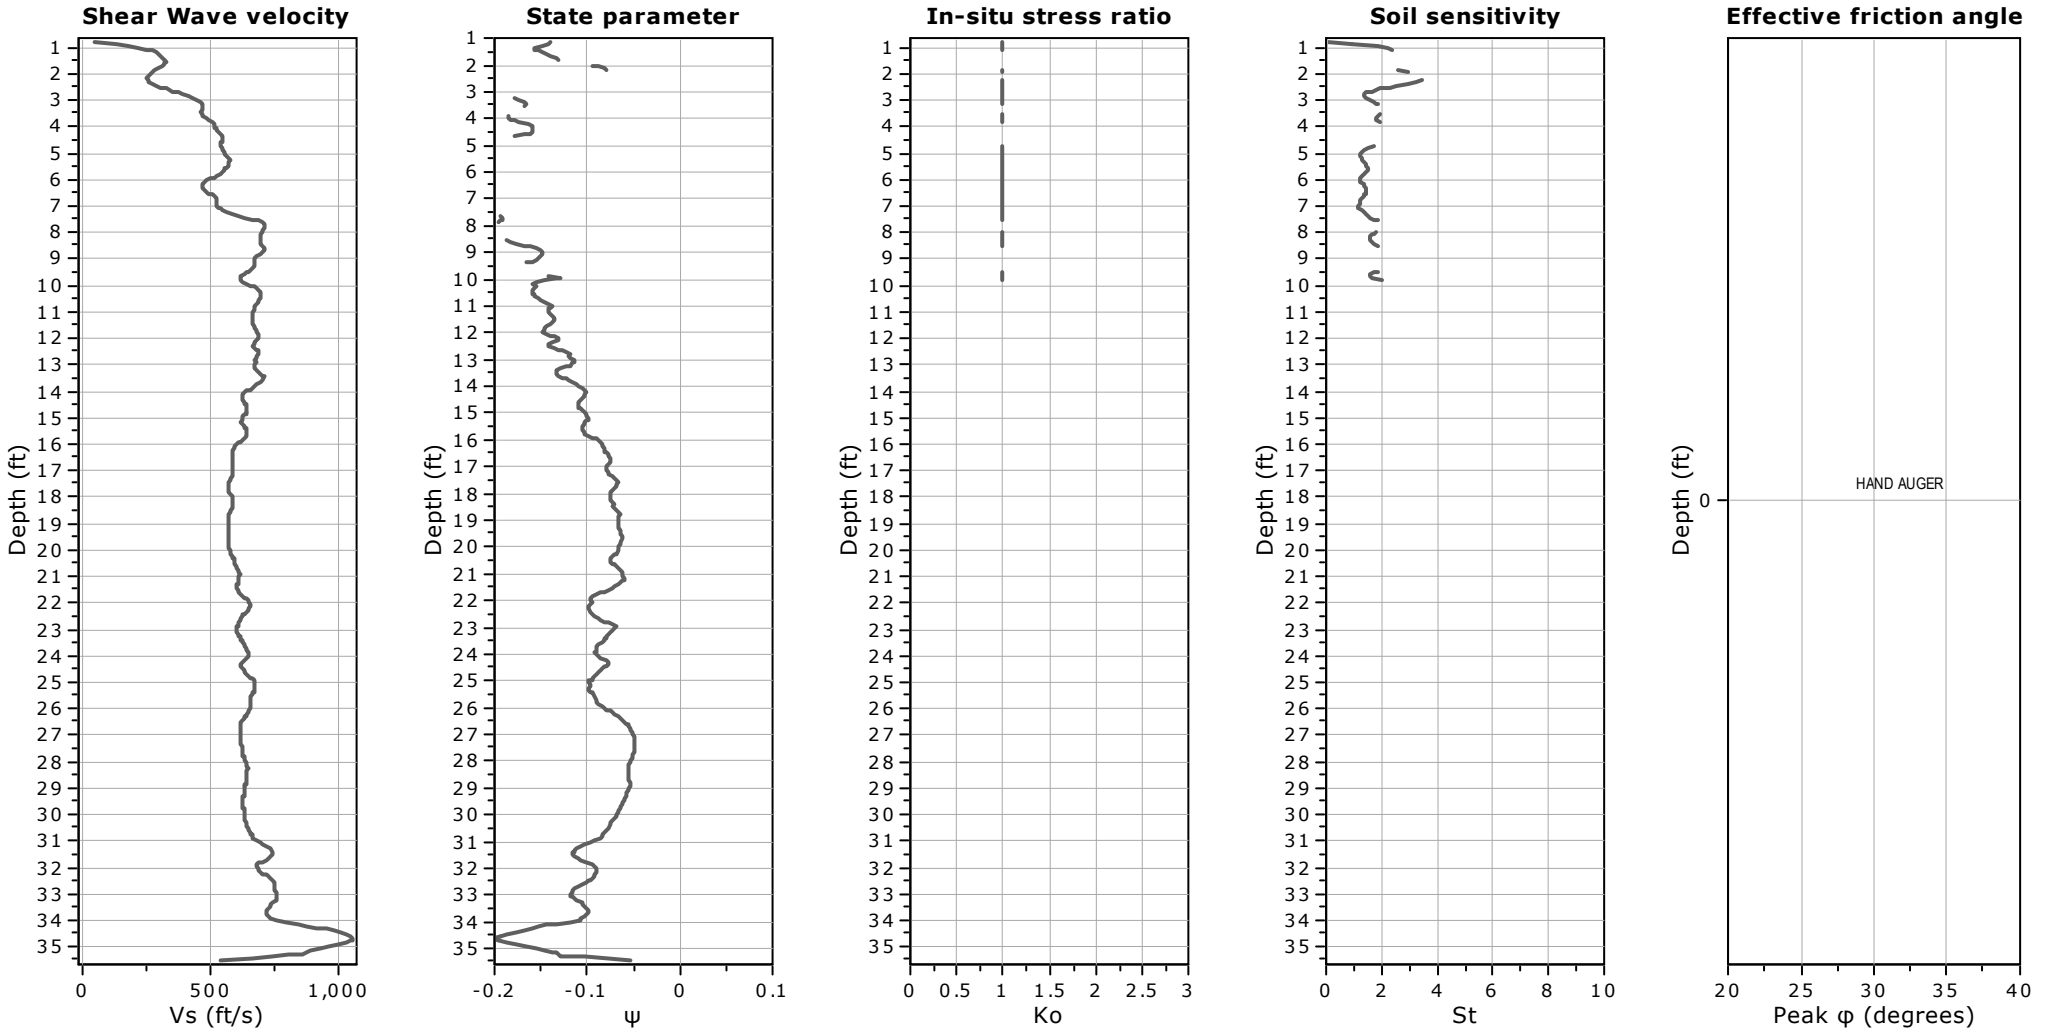

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-12
Total depth: 32.30 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

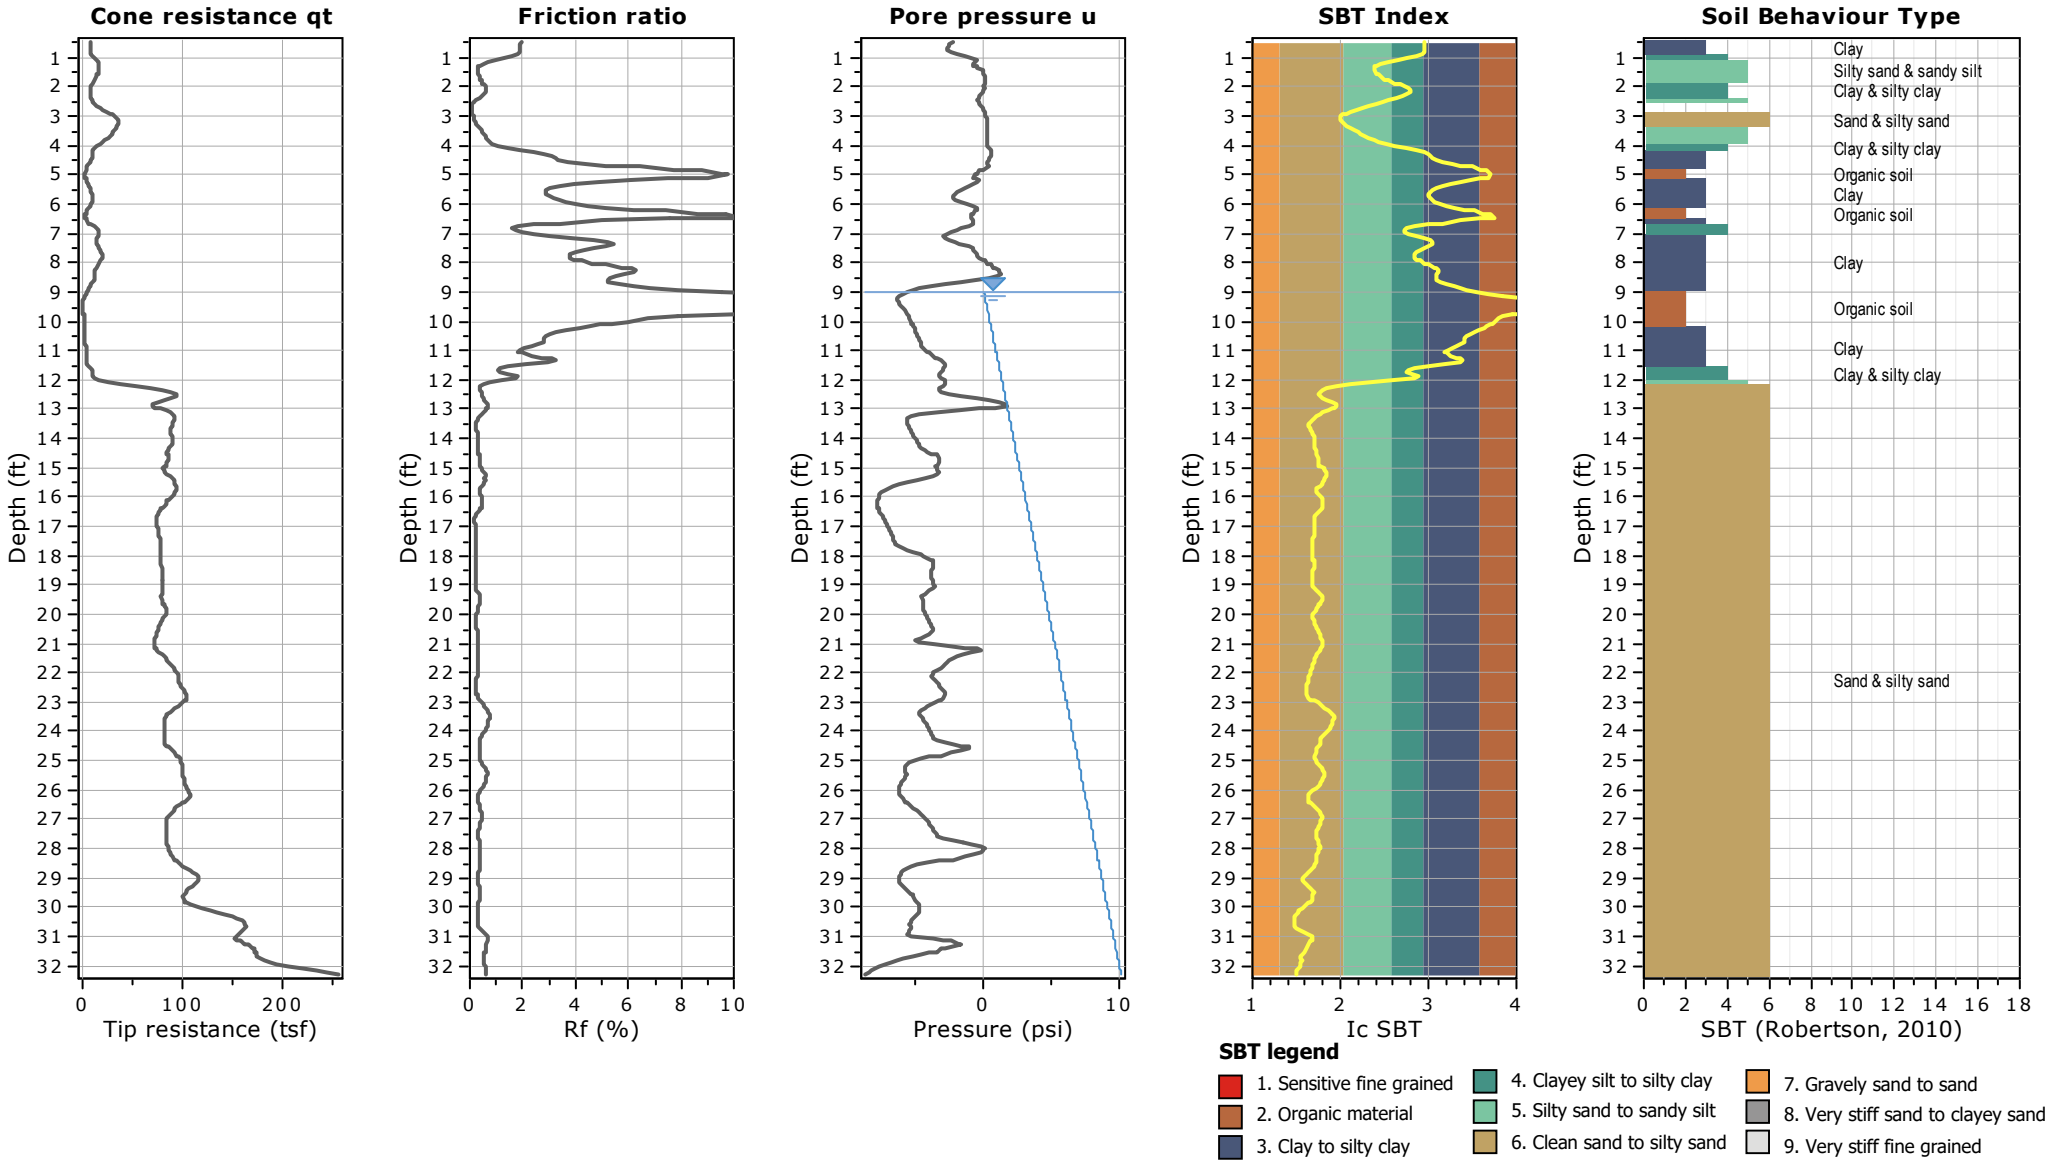



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-12
Total depth: 32.30 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

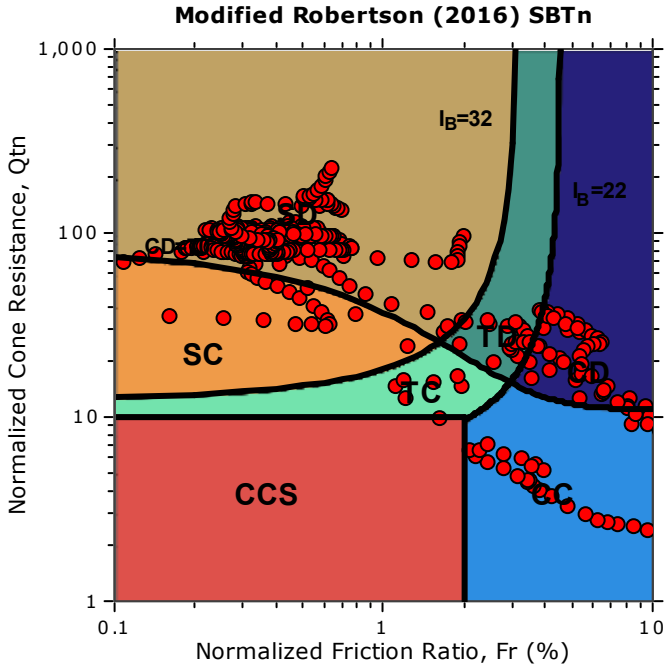

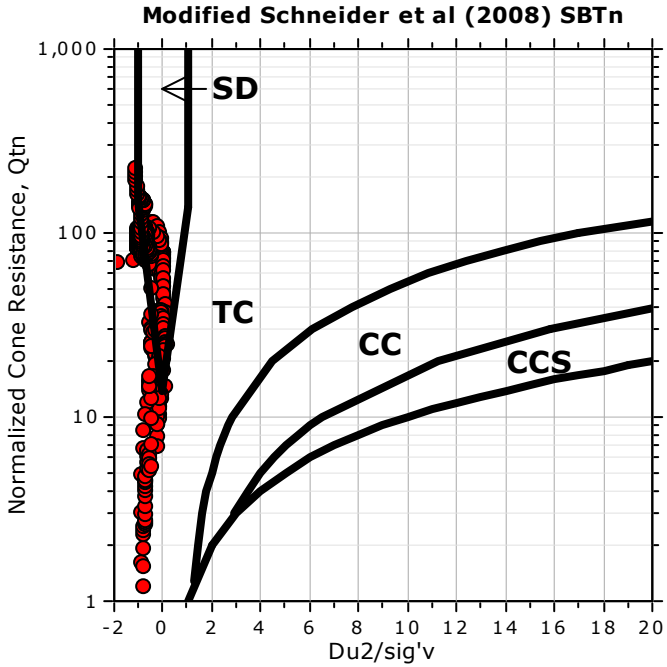

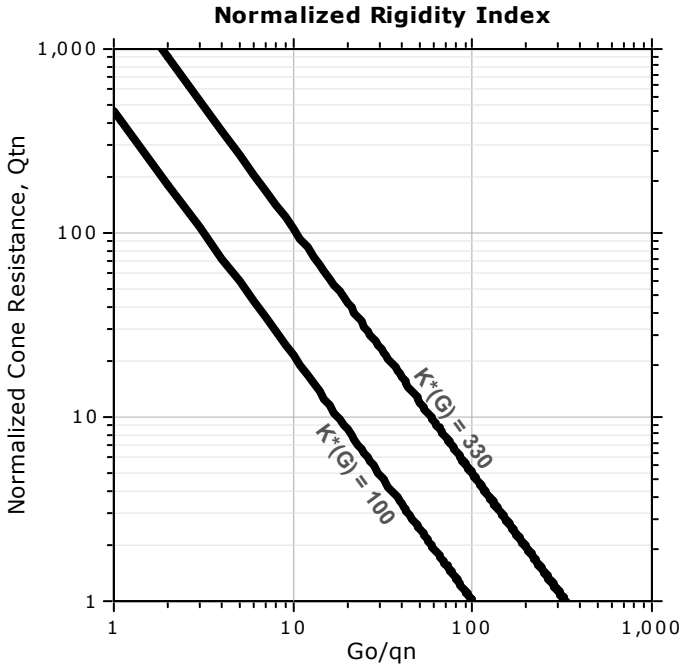


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-12
Total depth: 32.30 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

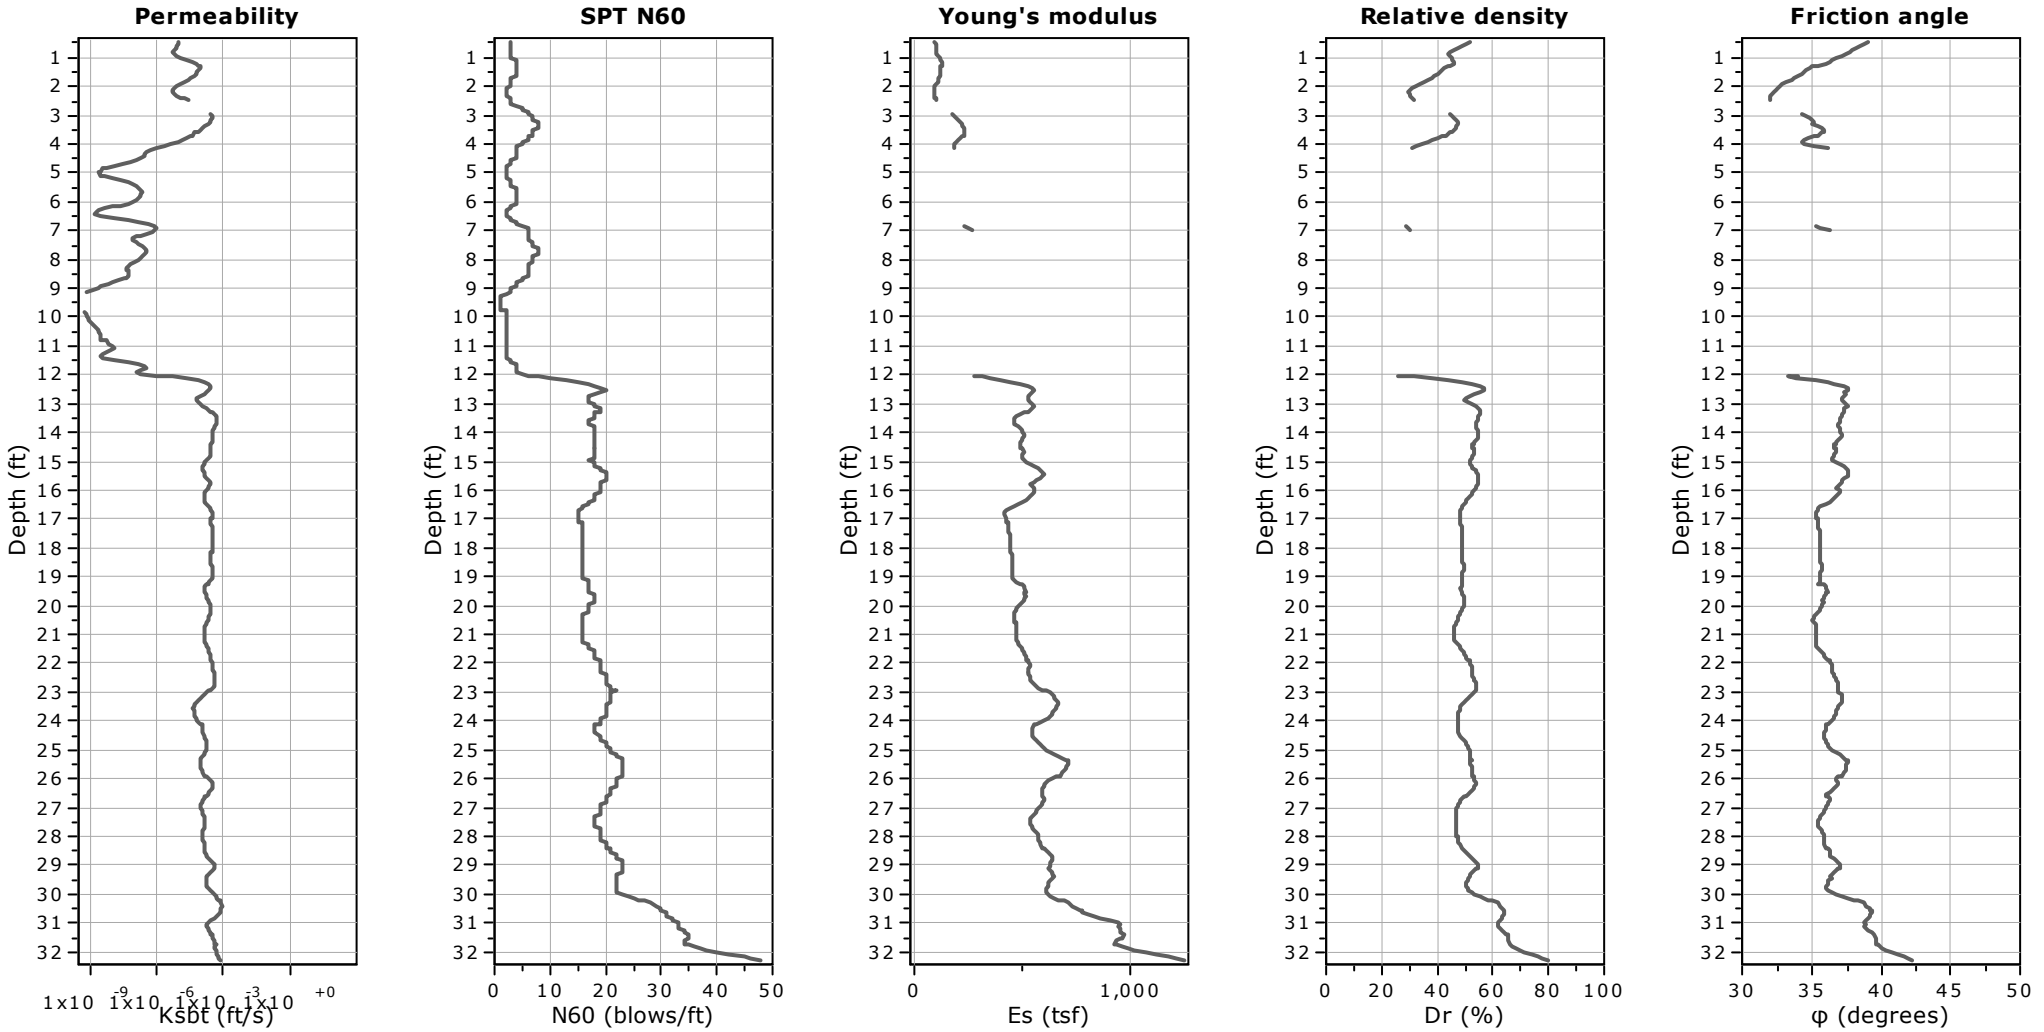


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-12
Total depth: 32.30 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

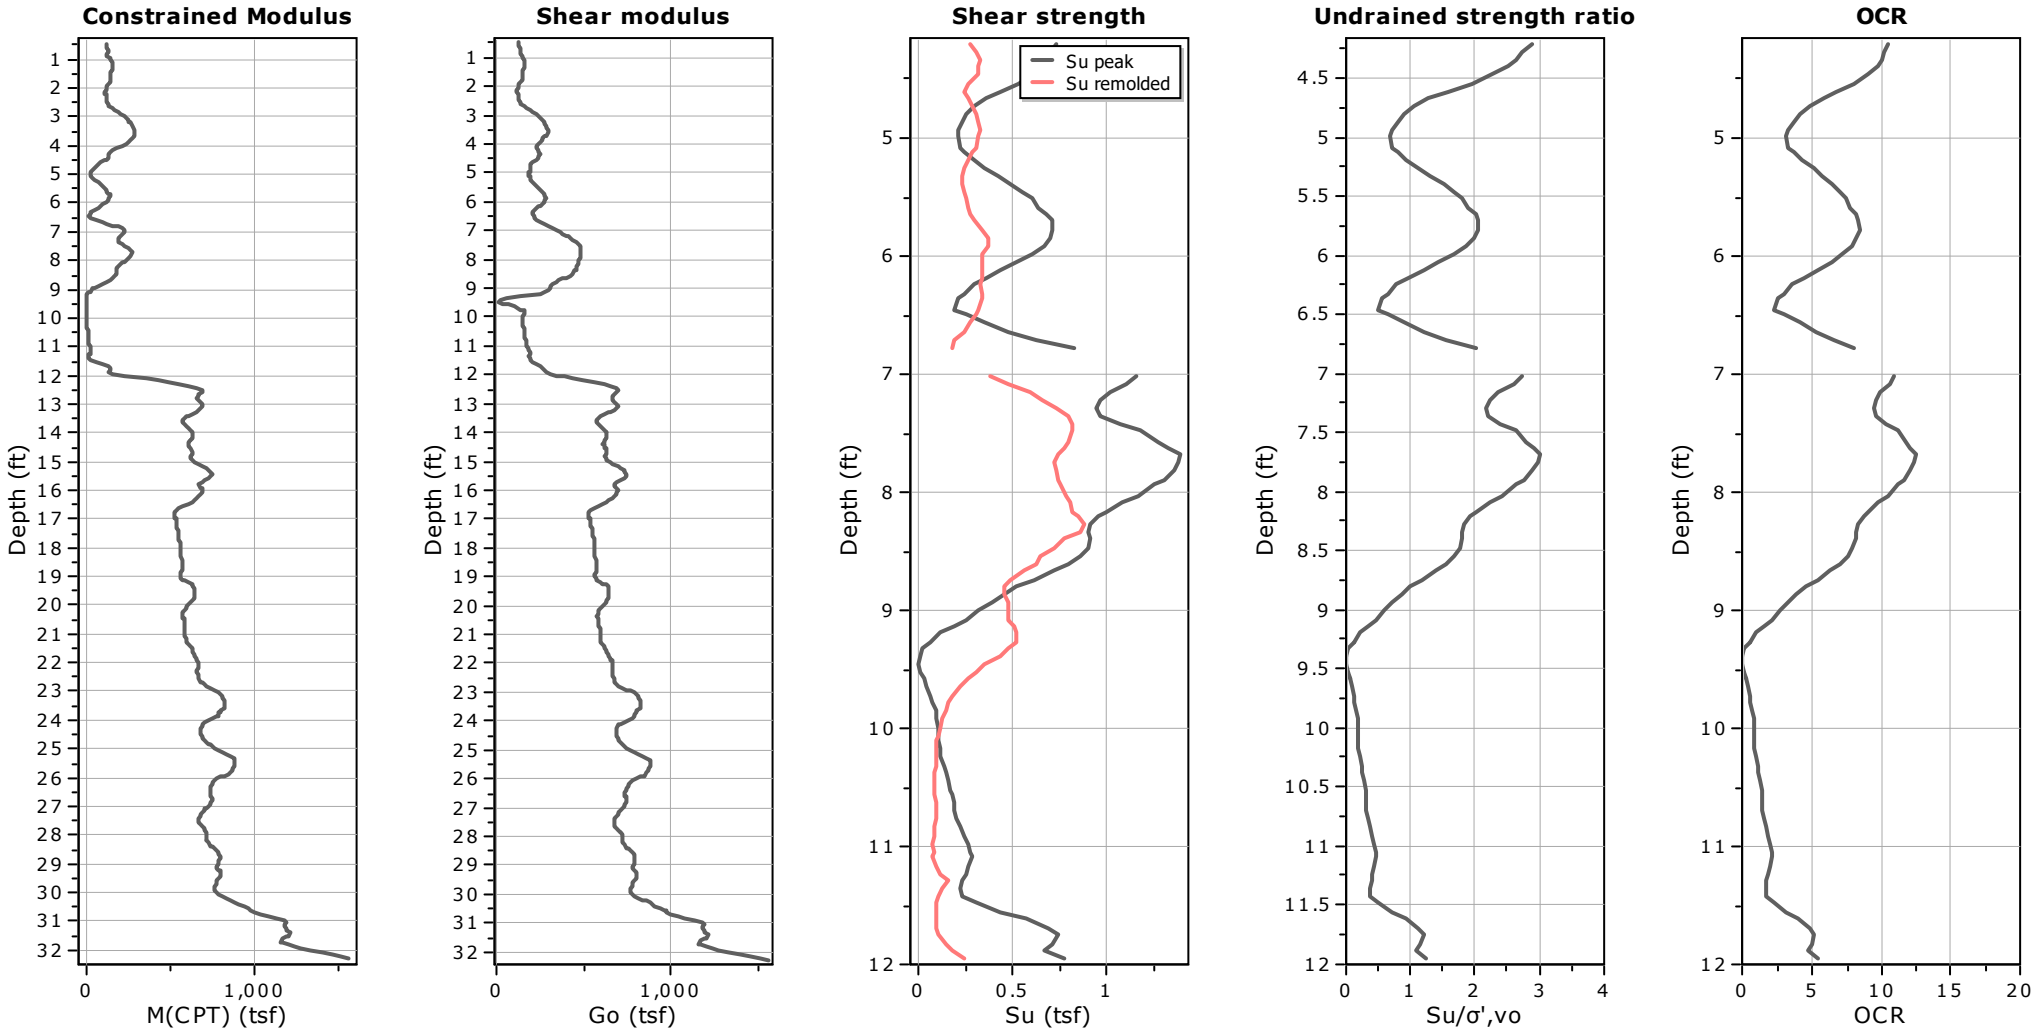

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-12
Total depth: 32.30 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

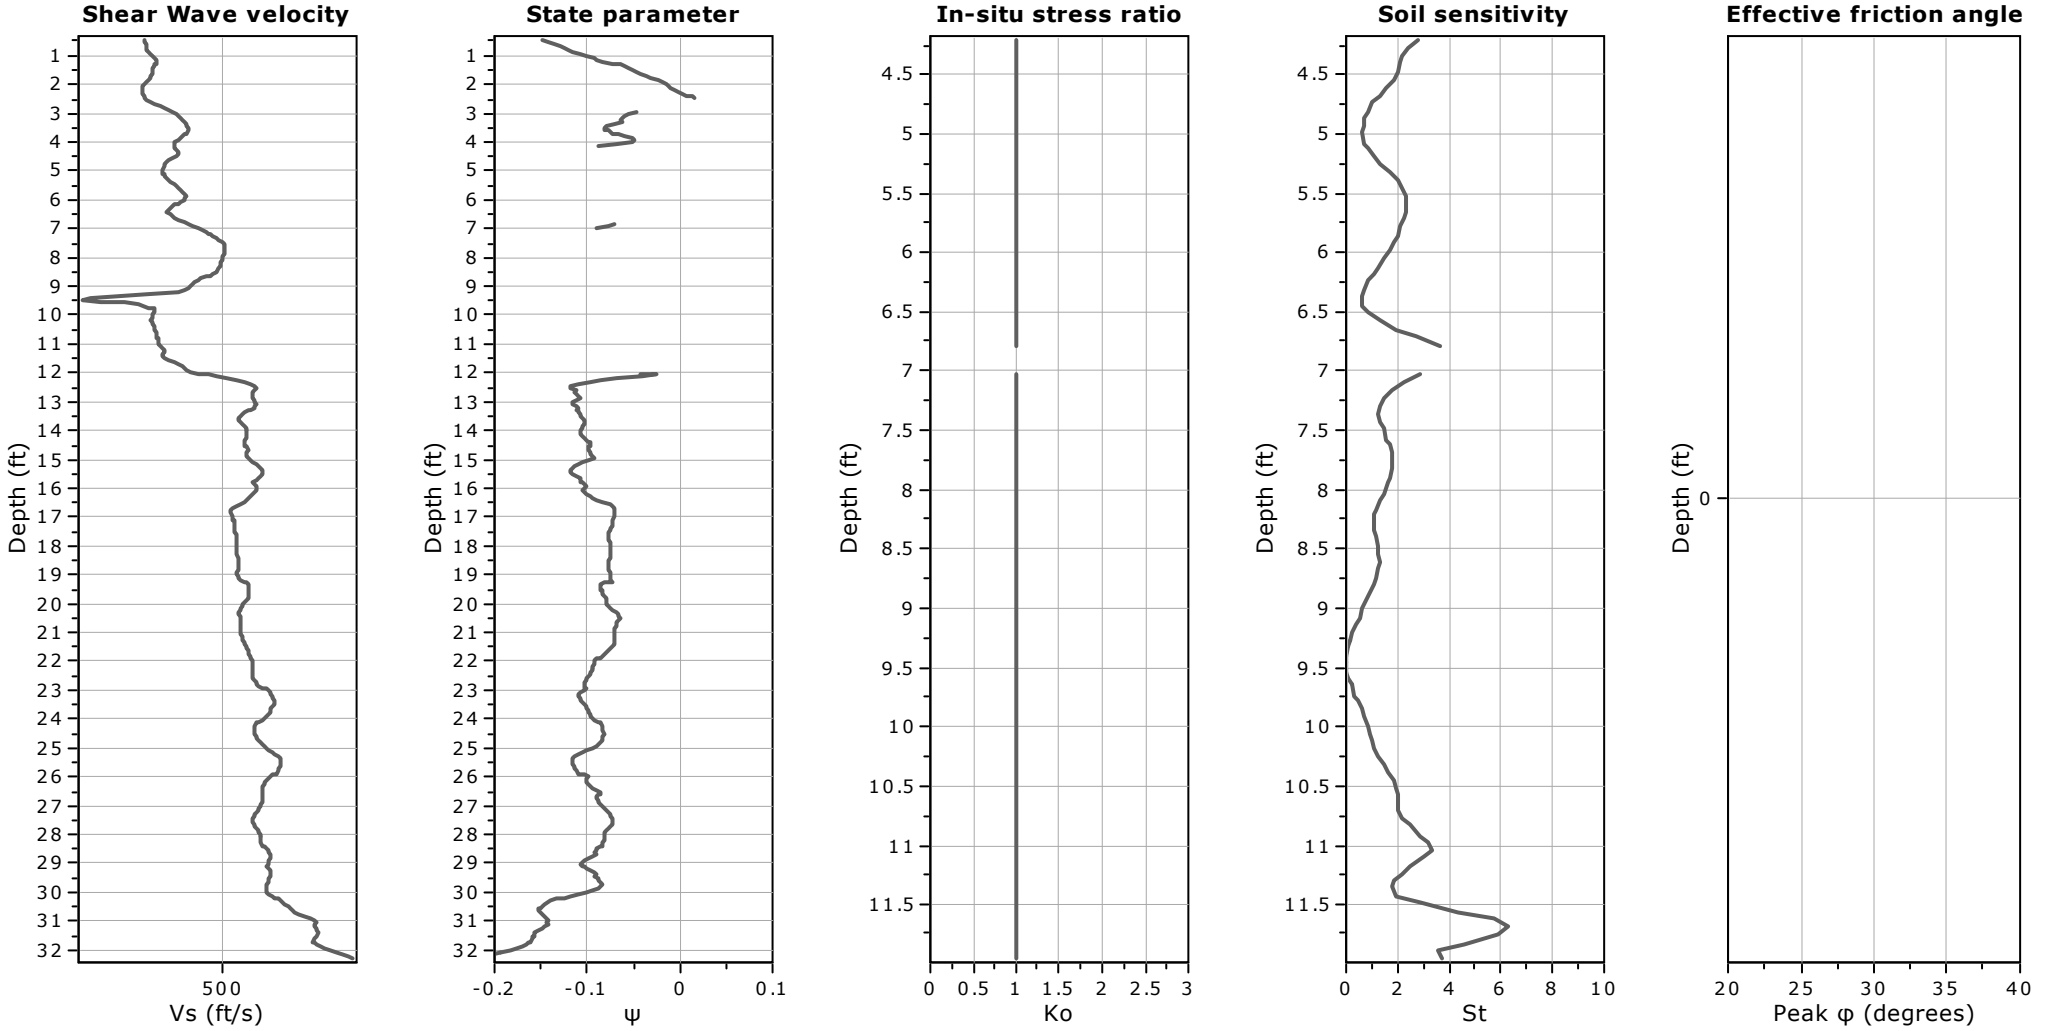

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-13
Total depth: 34.85 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

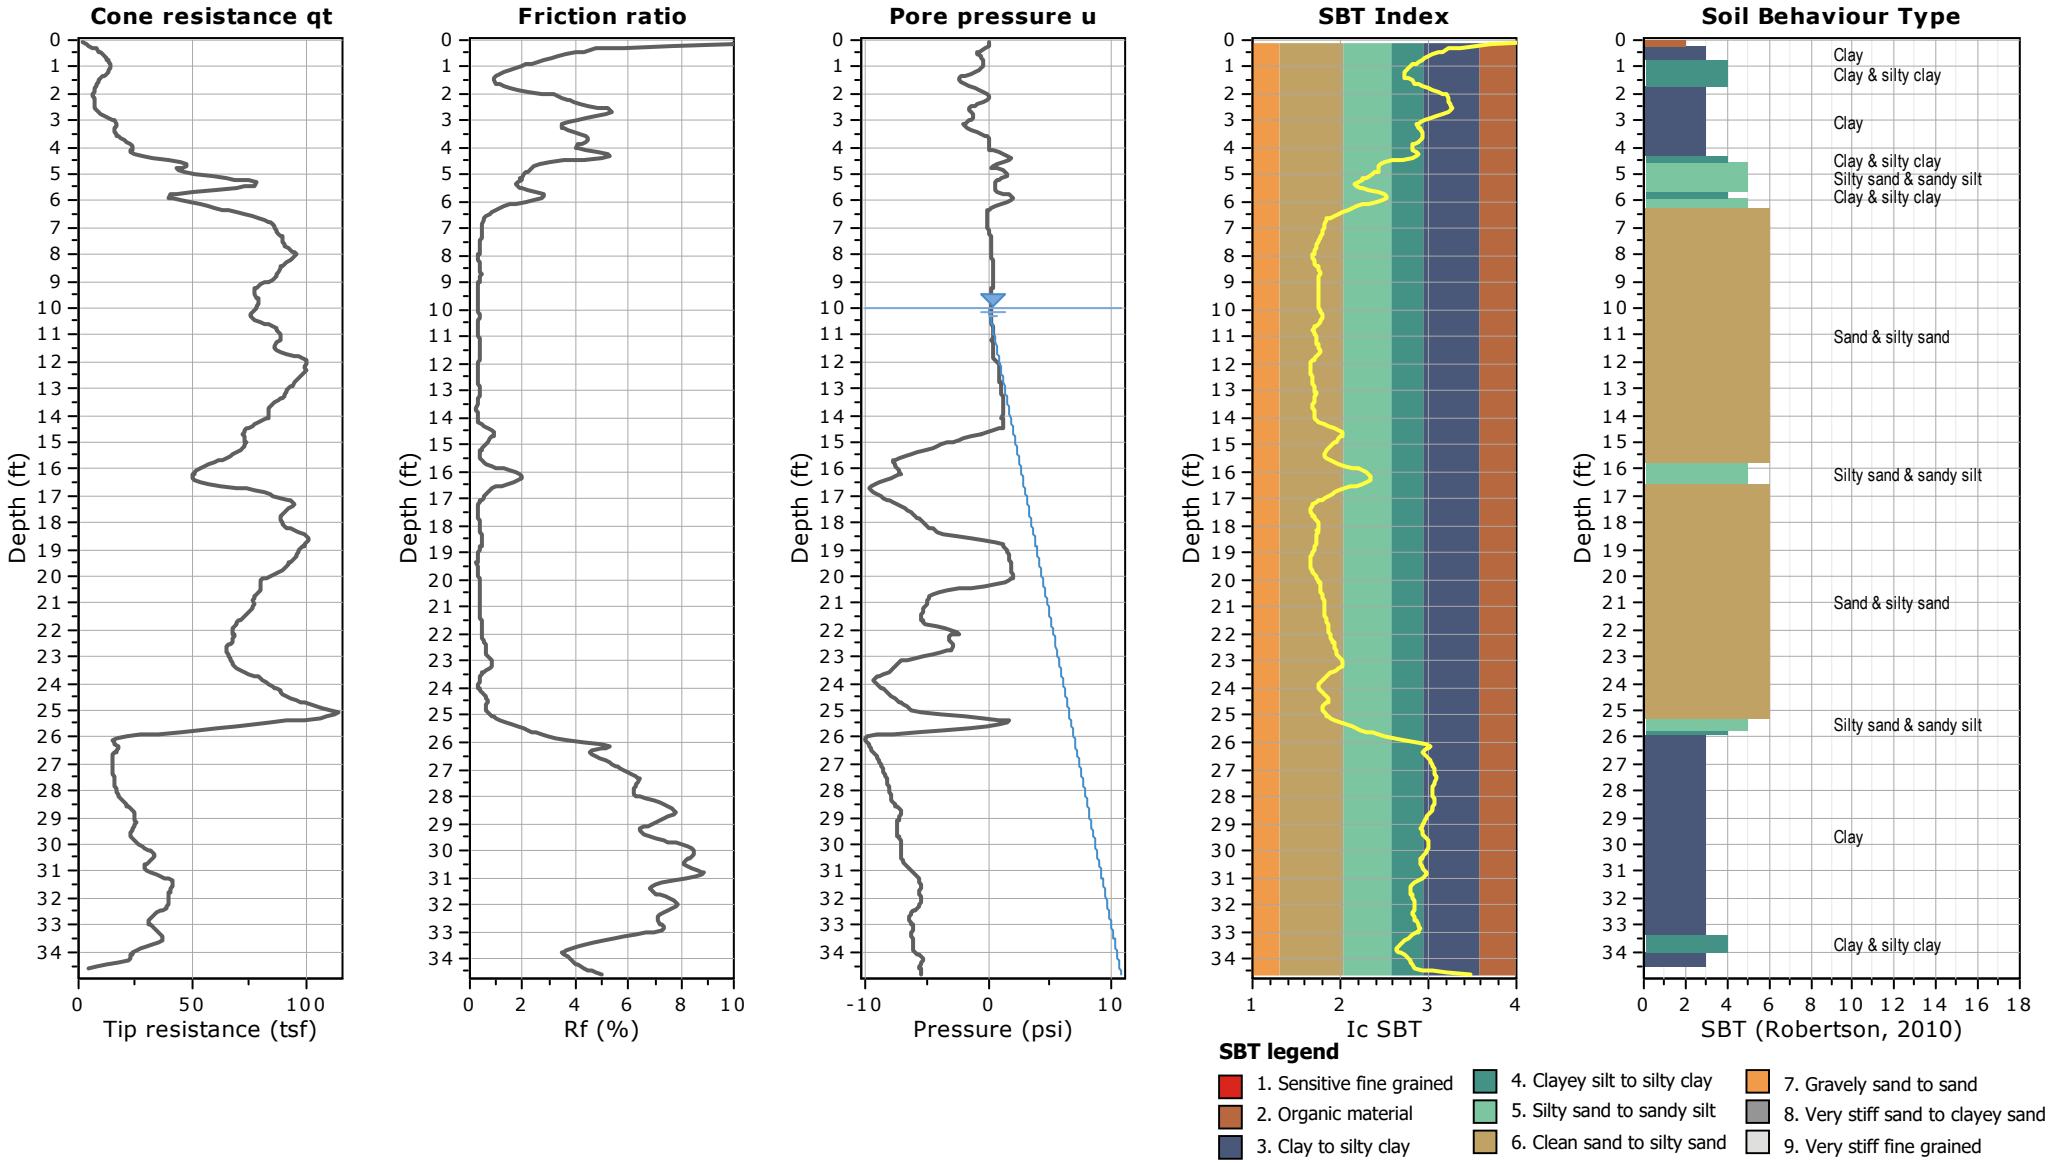



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

CPT: CPT-13
Total depth: 34.85 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Updated SBTn plots

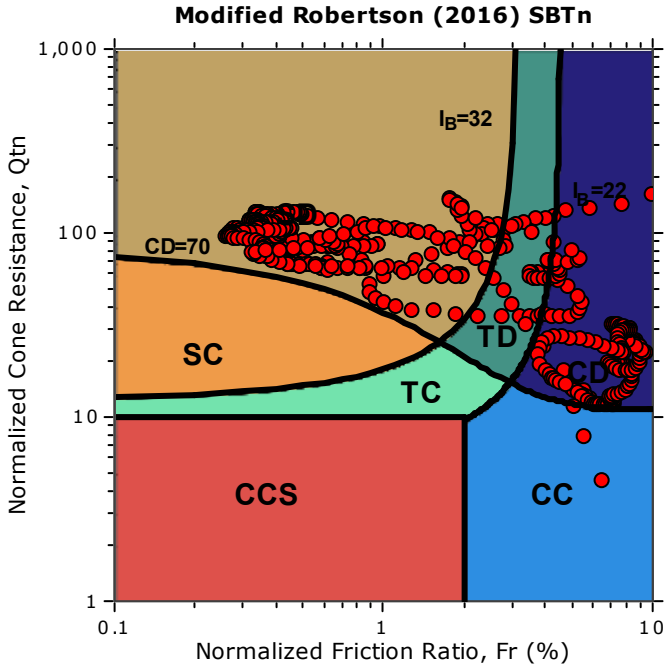

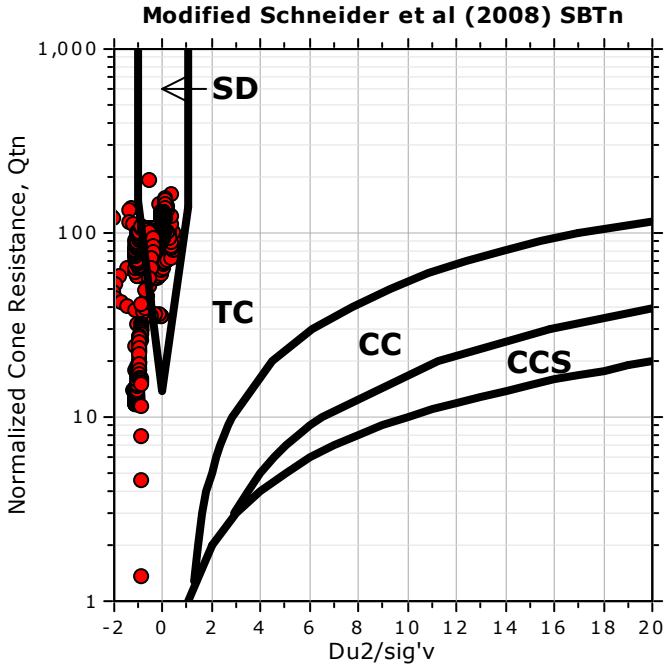

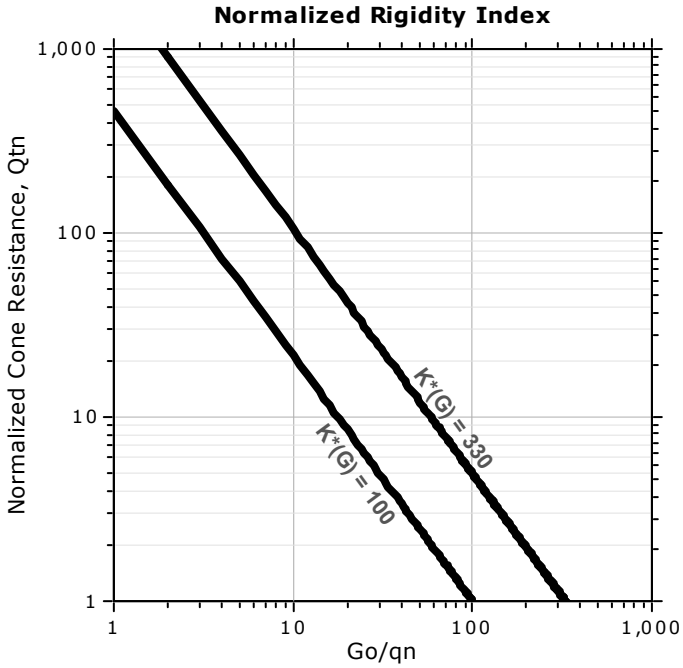


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-13
Total depth: 34.85 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

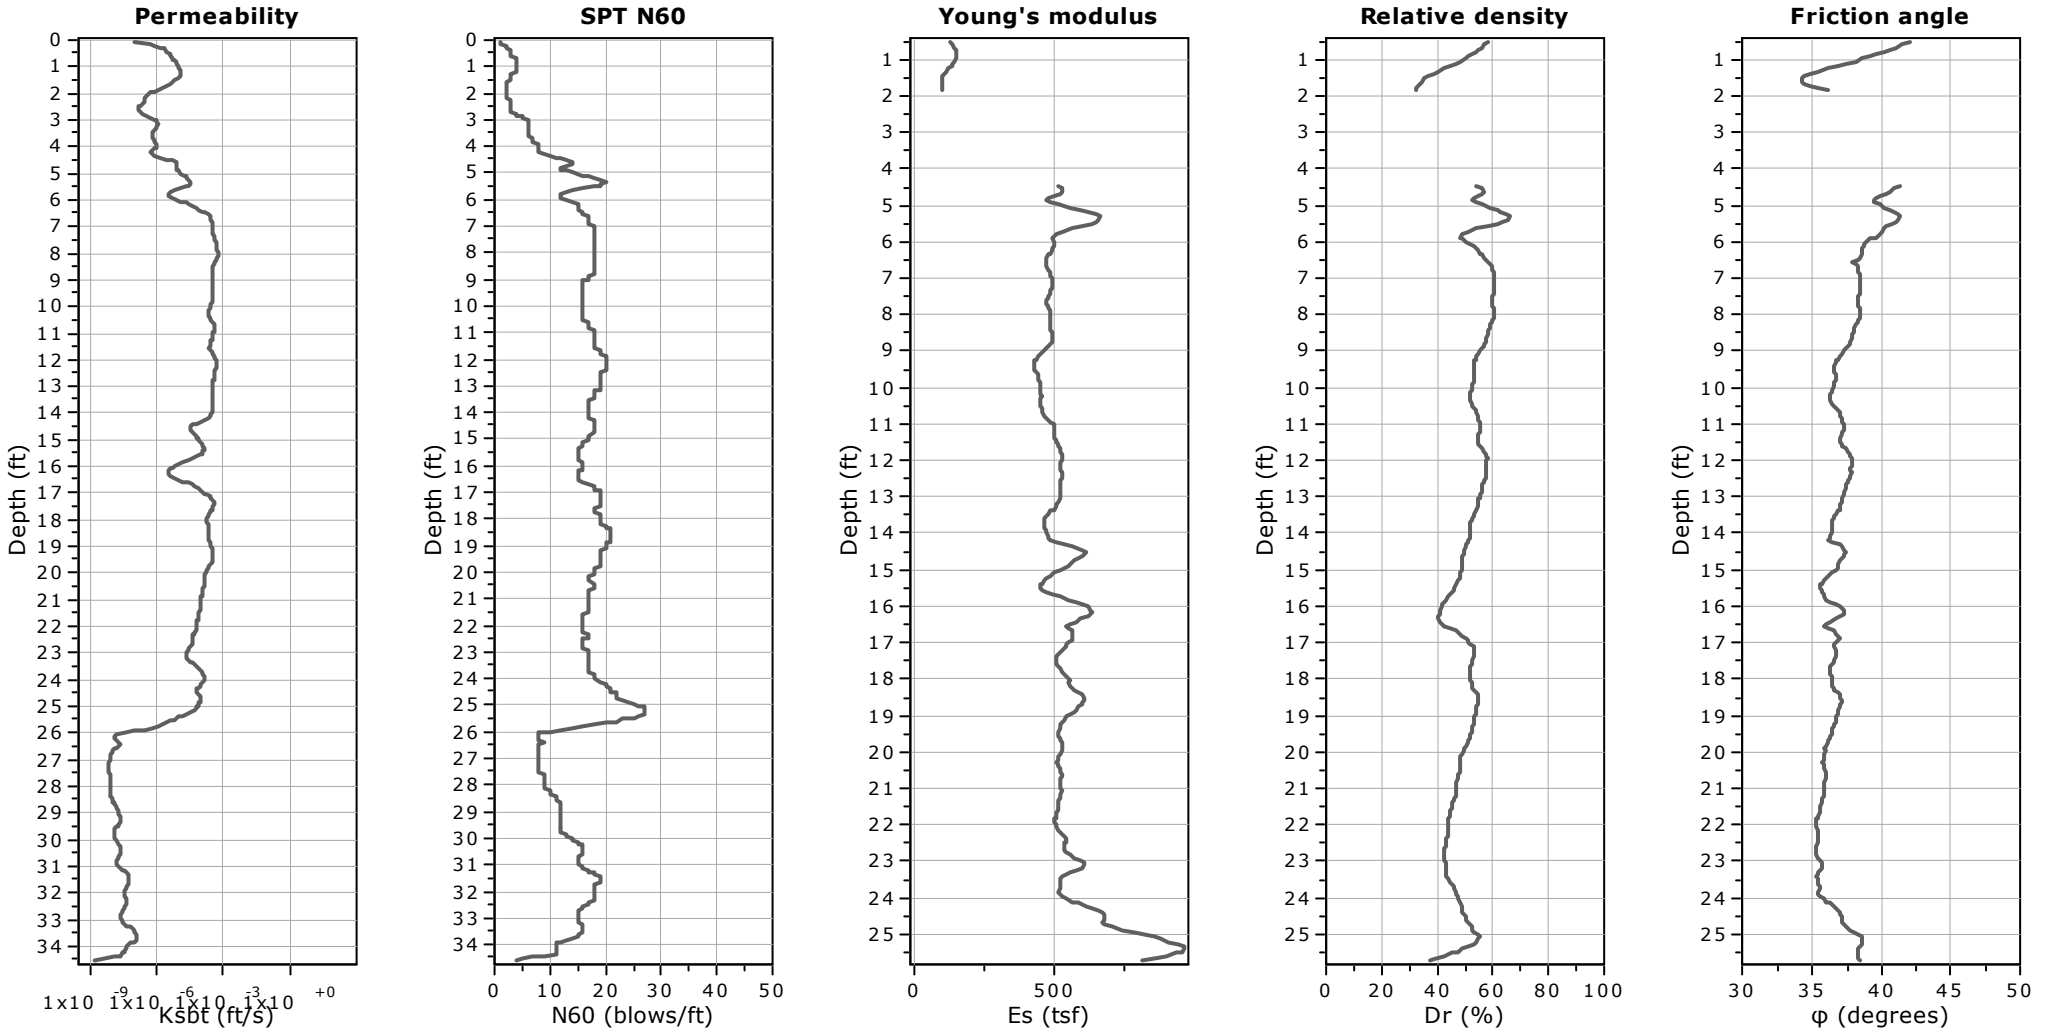


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-13
Total depth: 34.85 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

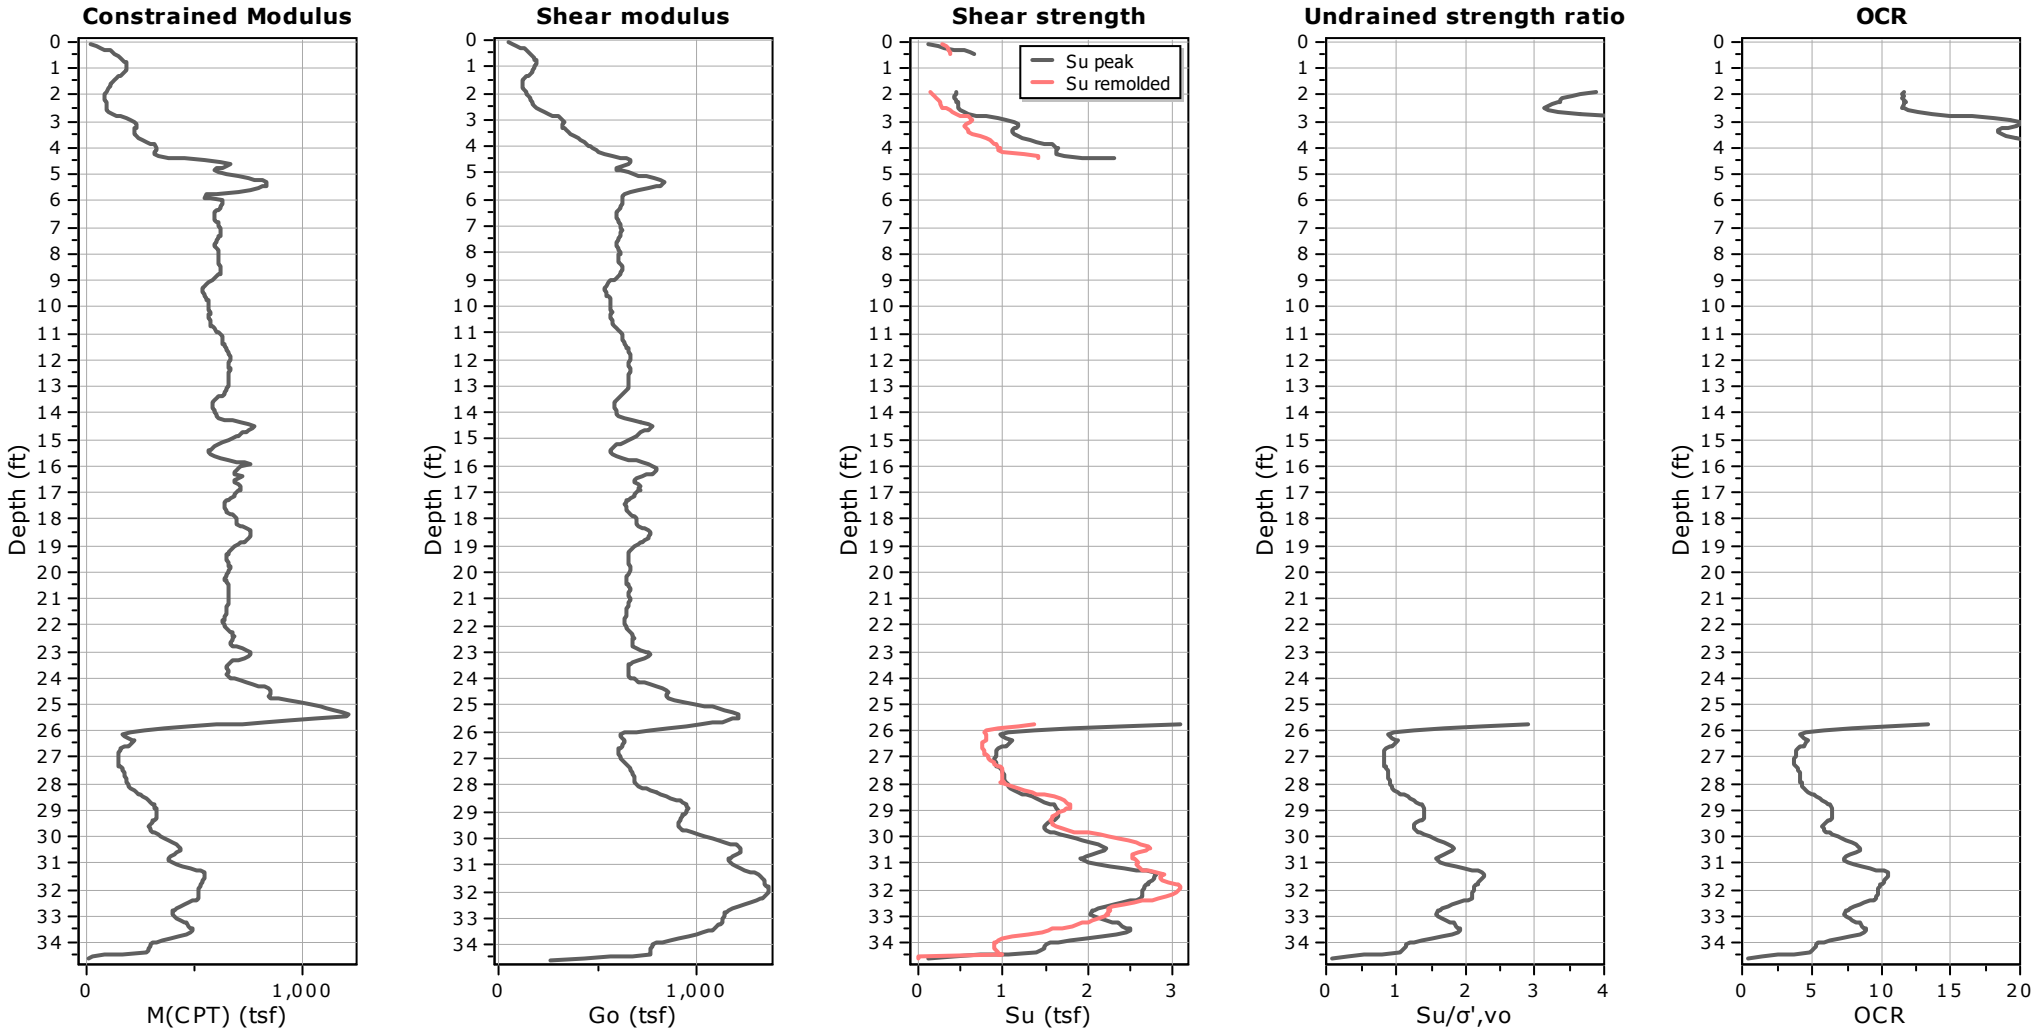

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-13
Total depth: 34.85 ft, Date: 12/20/2022
Surface Elevation: 81.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

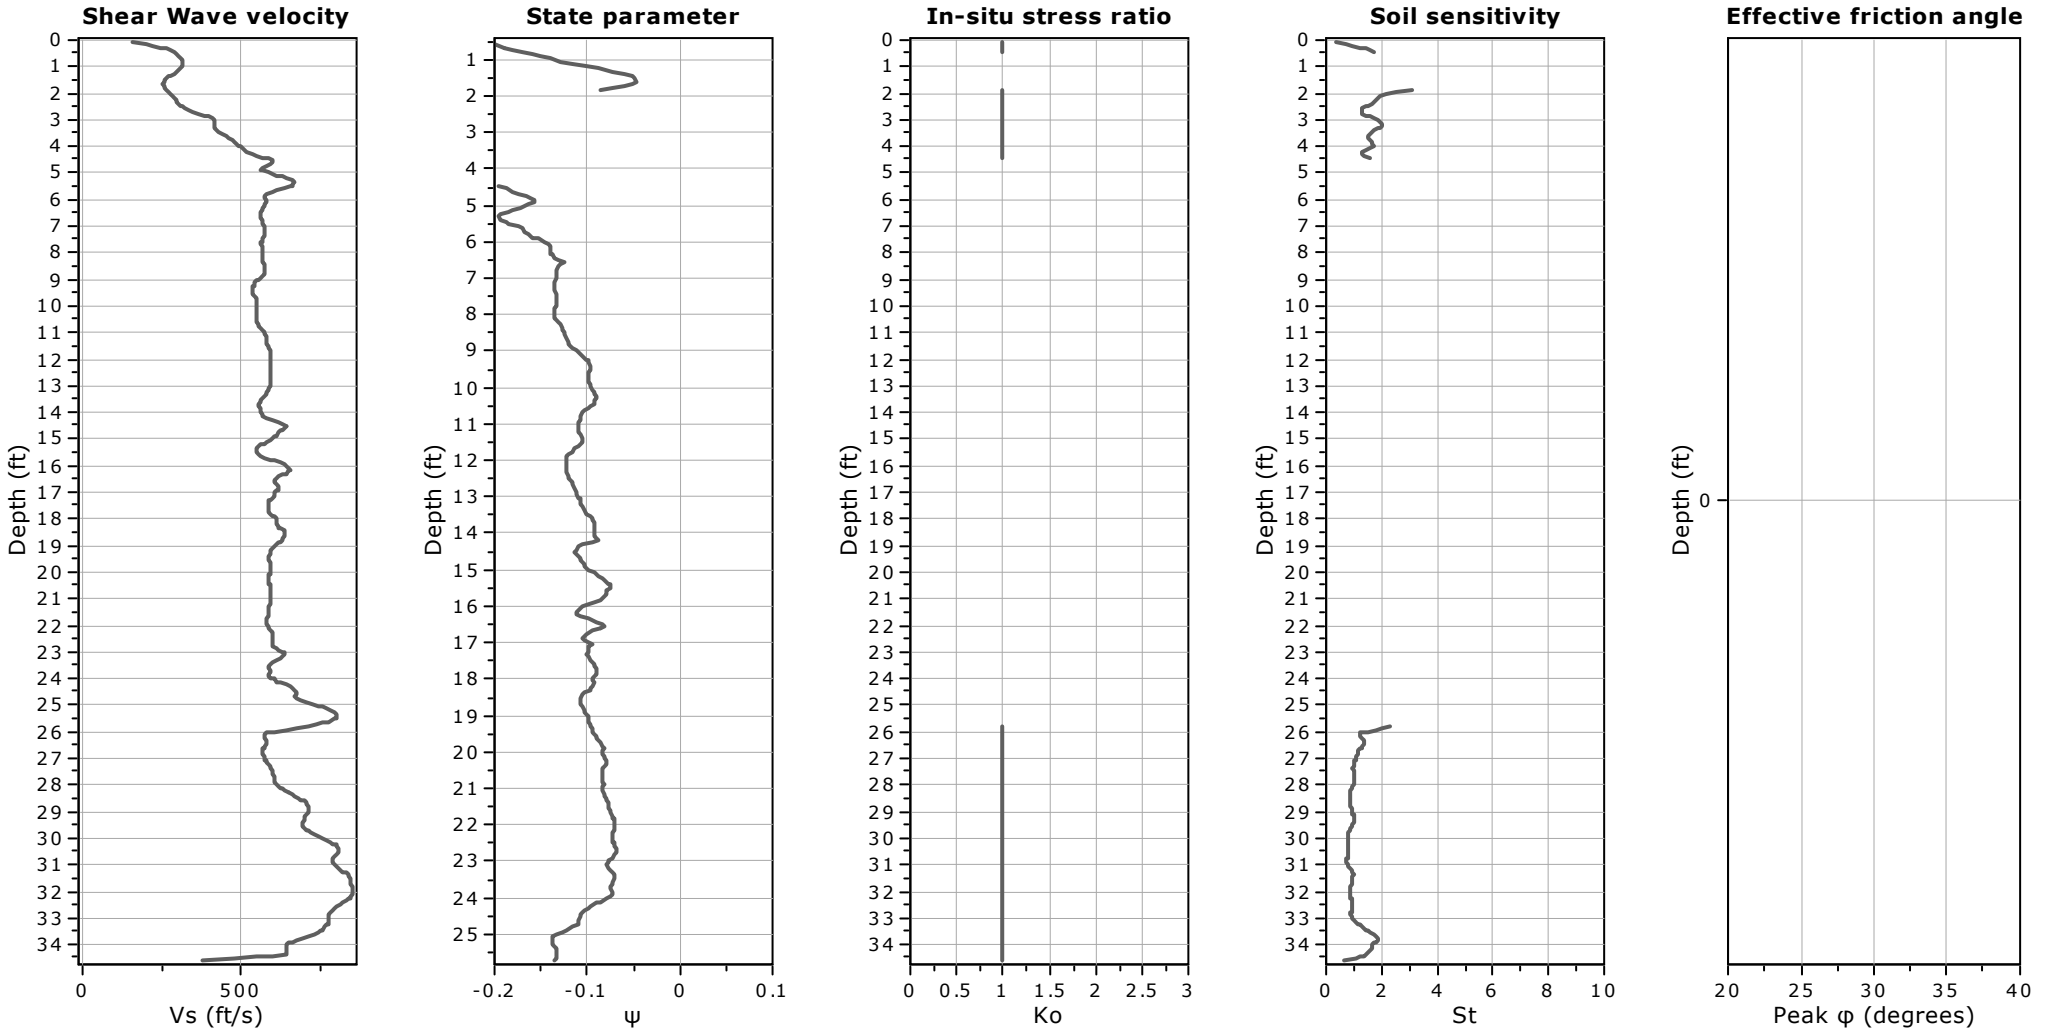


Calculation parameters

Soil Sensitivity factor, N_S: 7.00
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-14
Total depth: 30.58 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

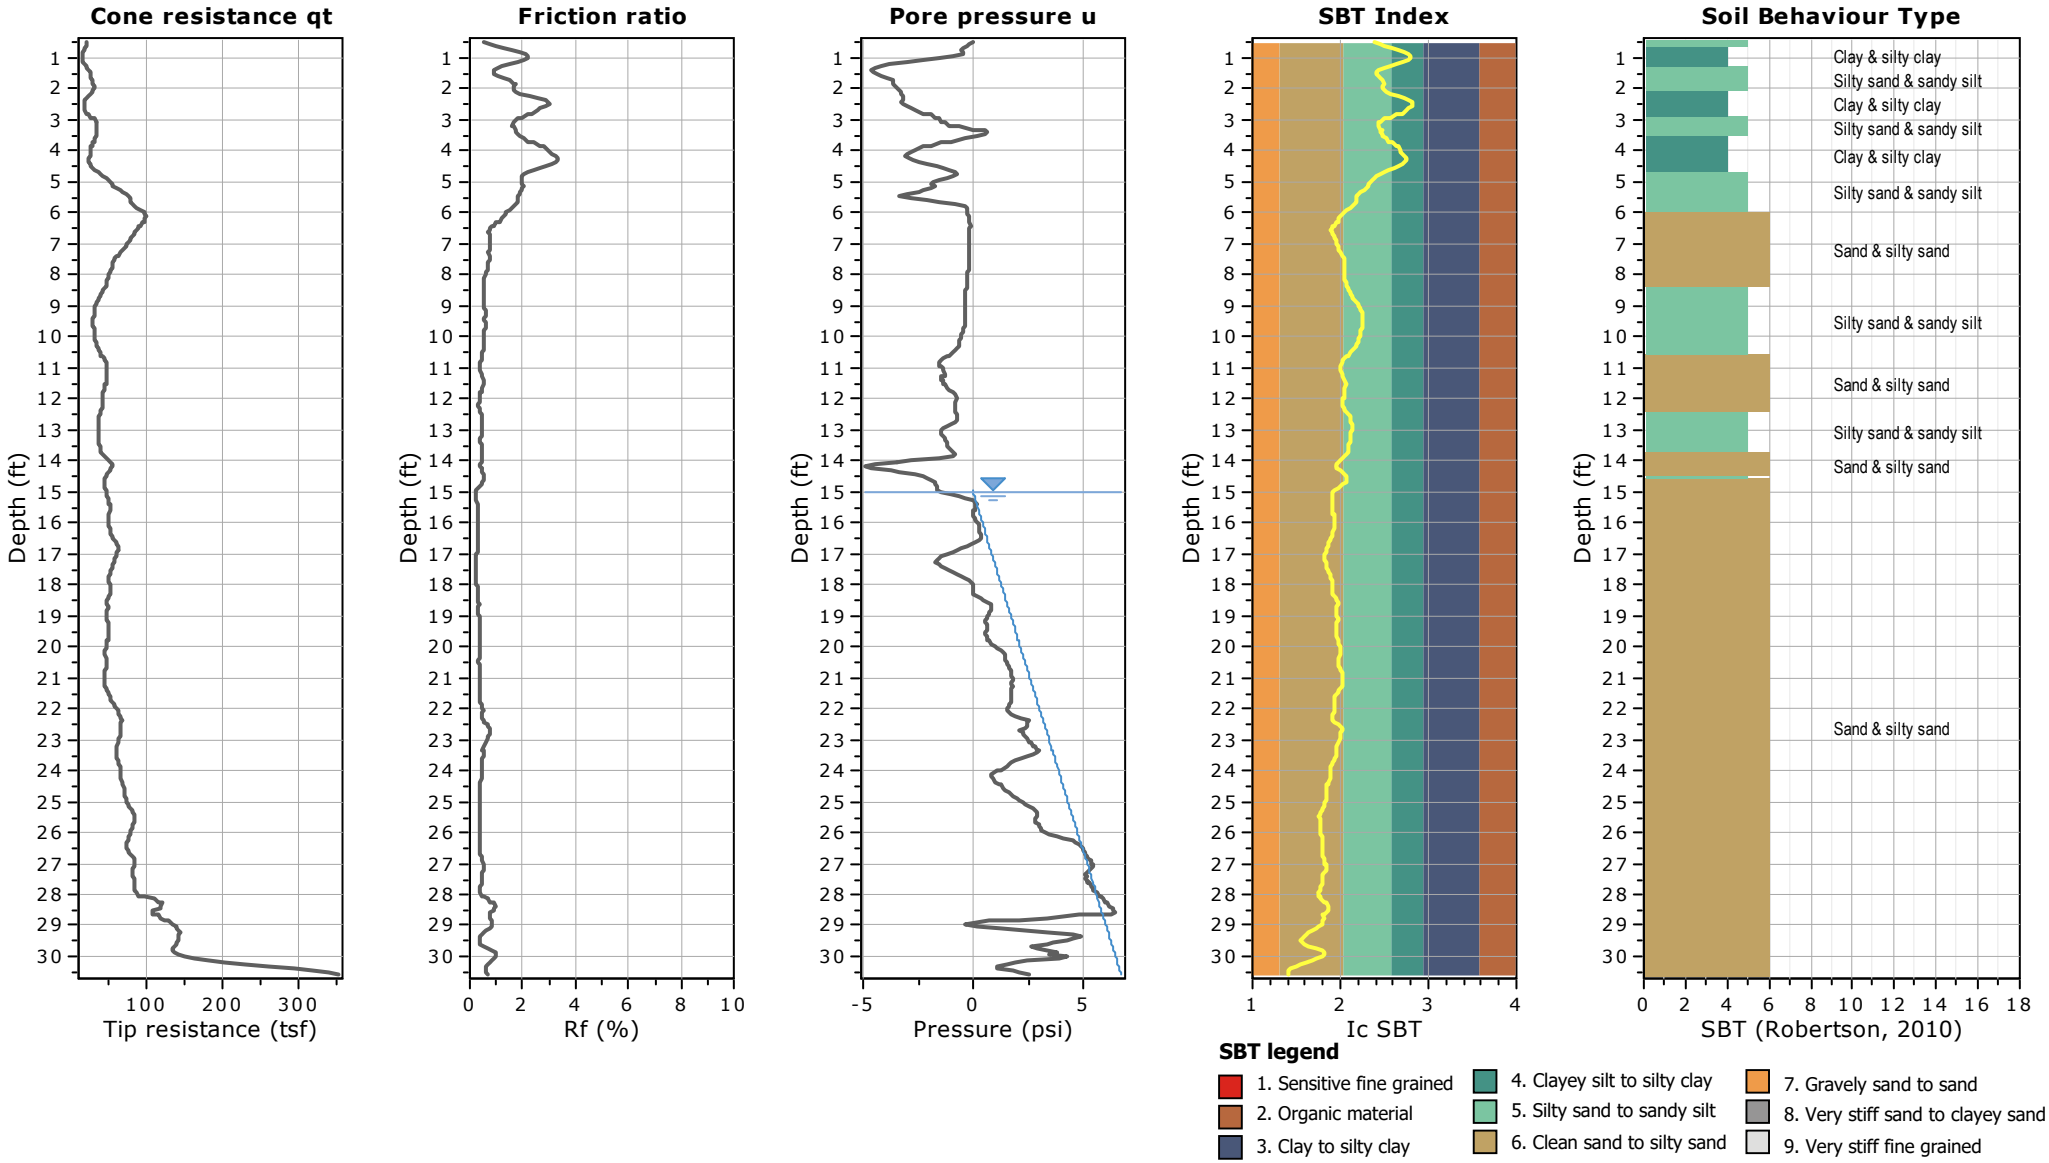



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-14
Total depth: 30.58 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

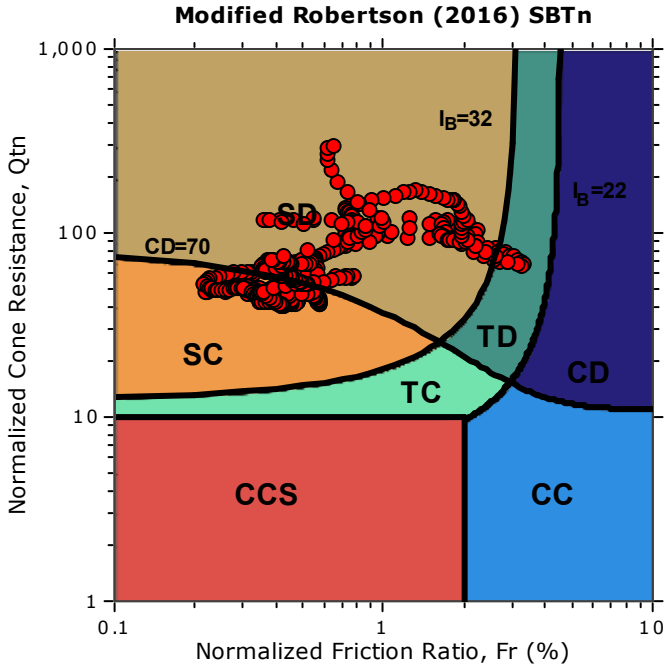

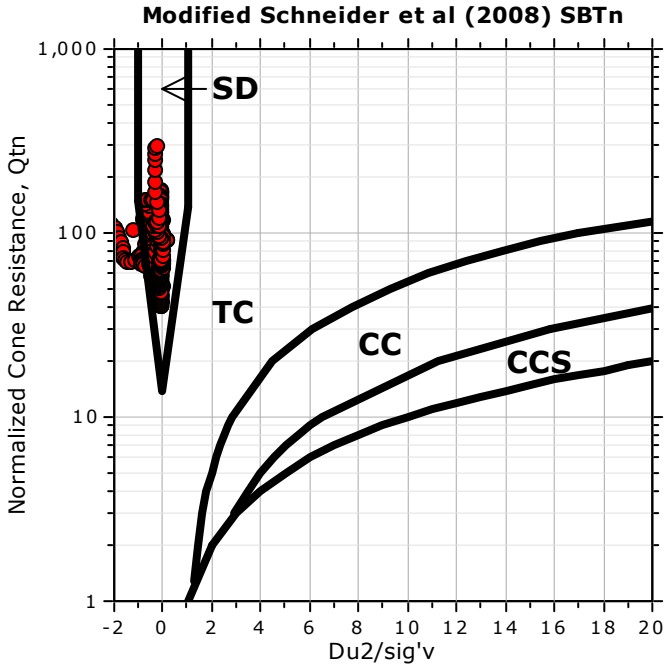

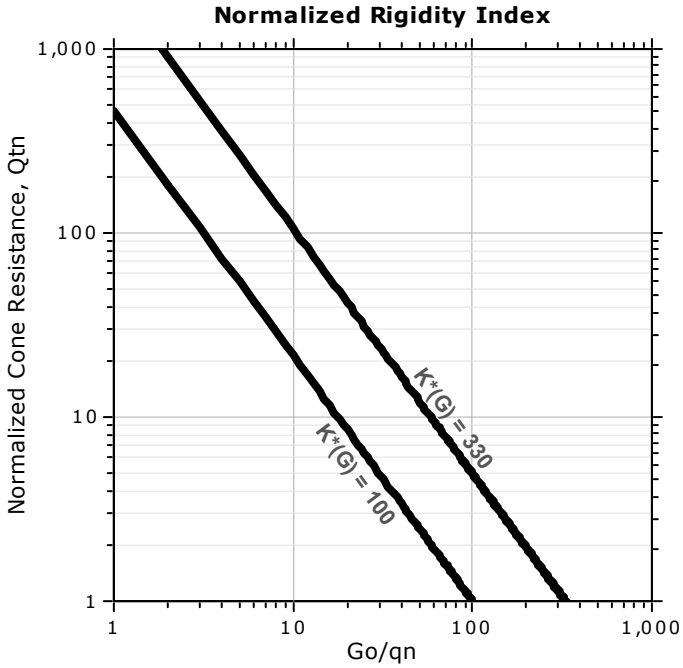


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-14
Total depth: 30.58 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

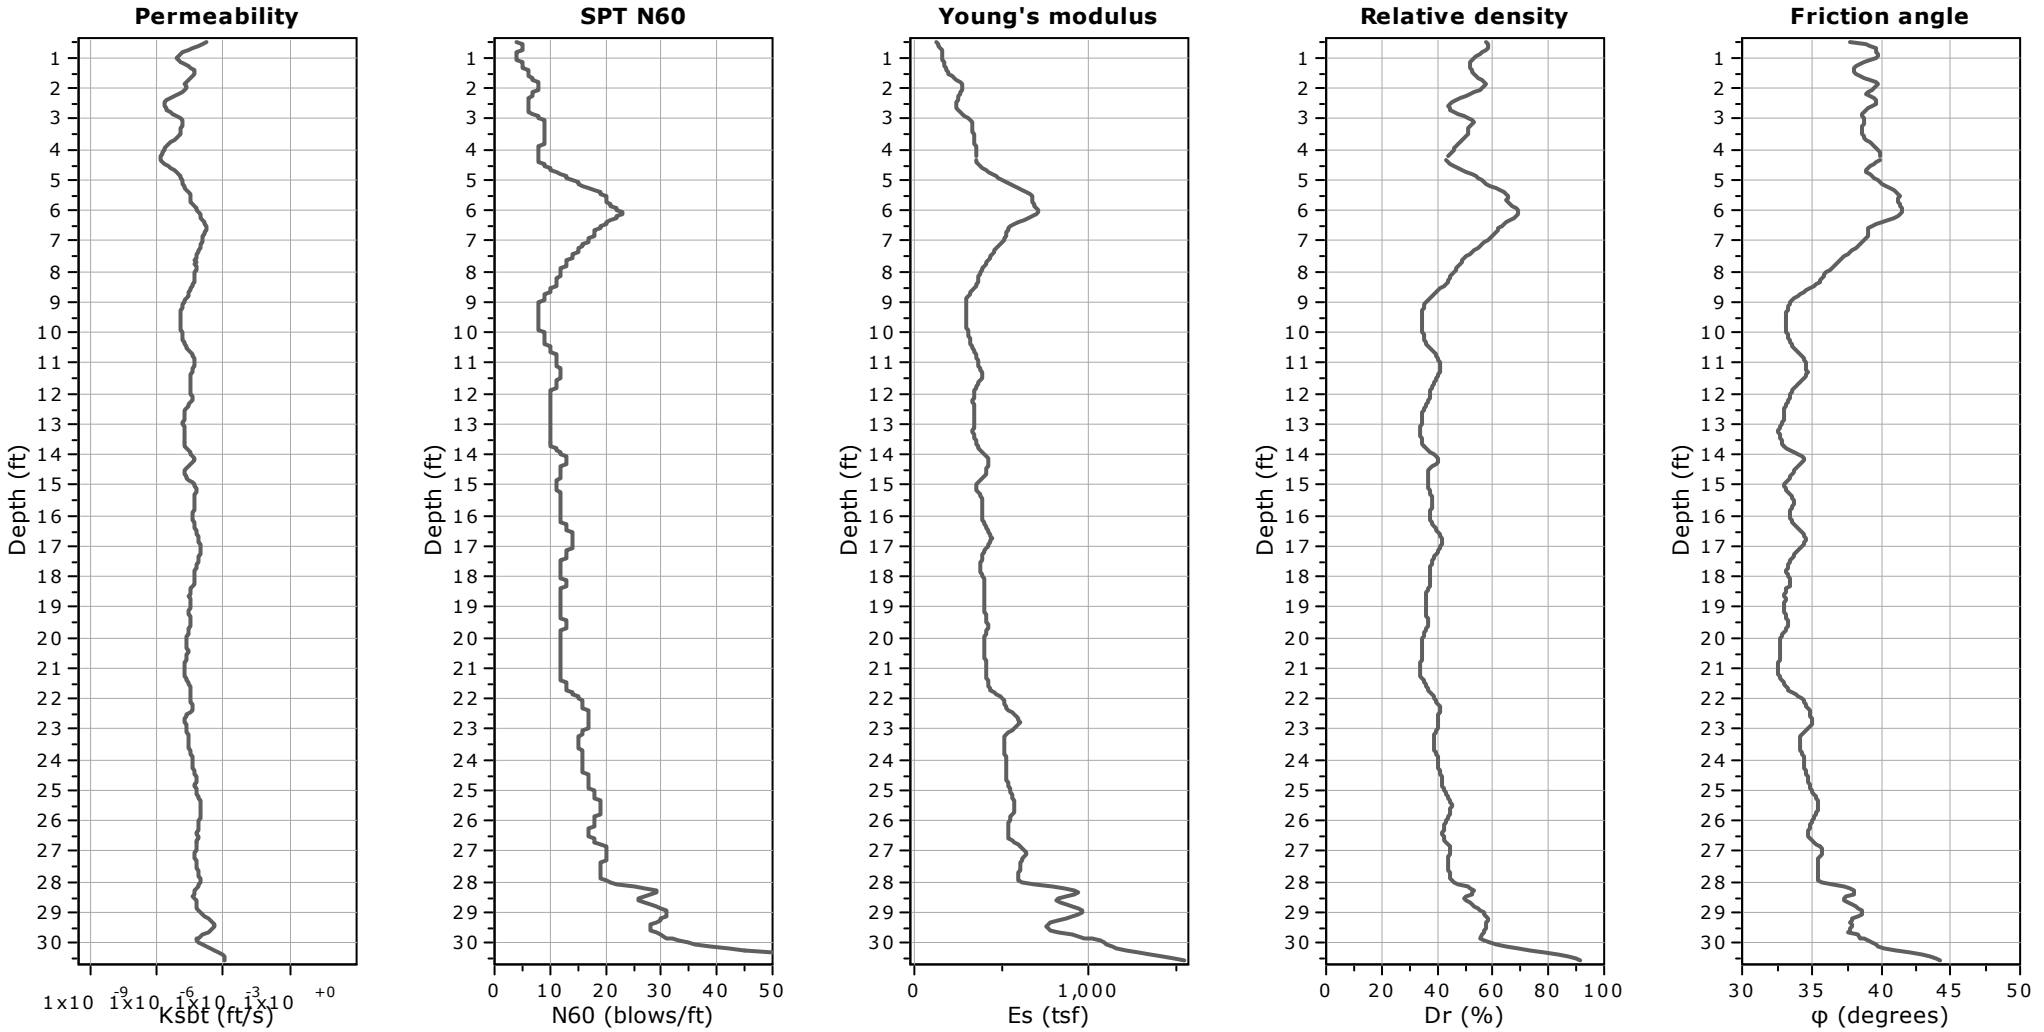


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-14
Total depth: 30.58 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

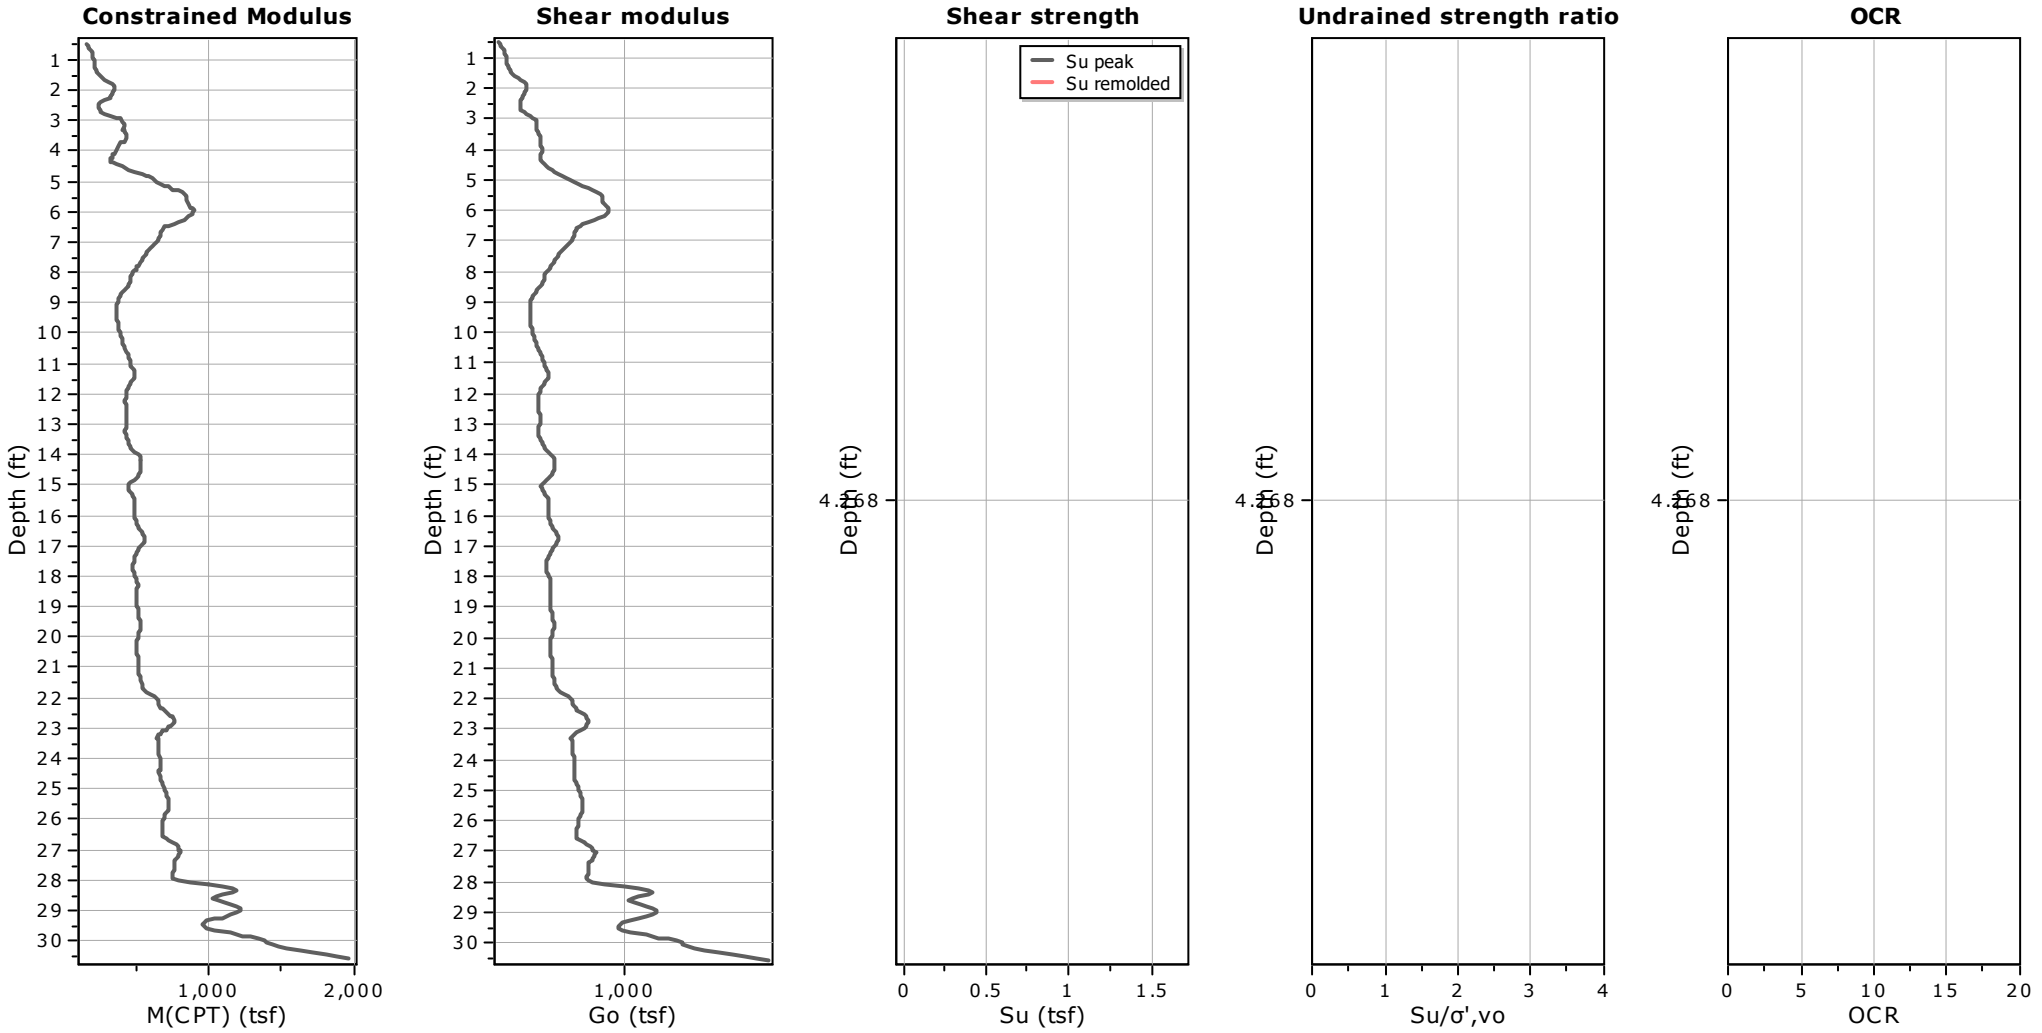

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-14
Total depth: 30.58 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

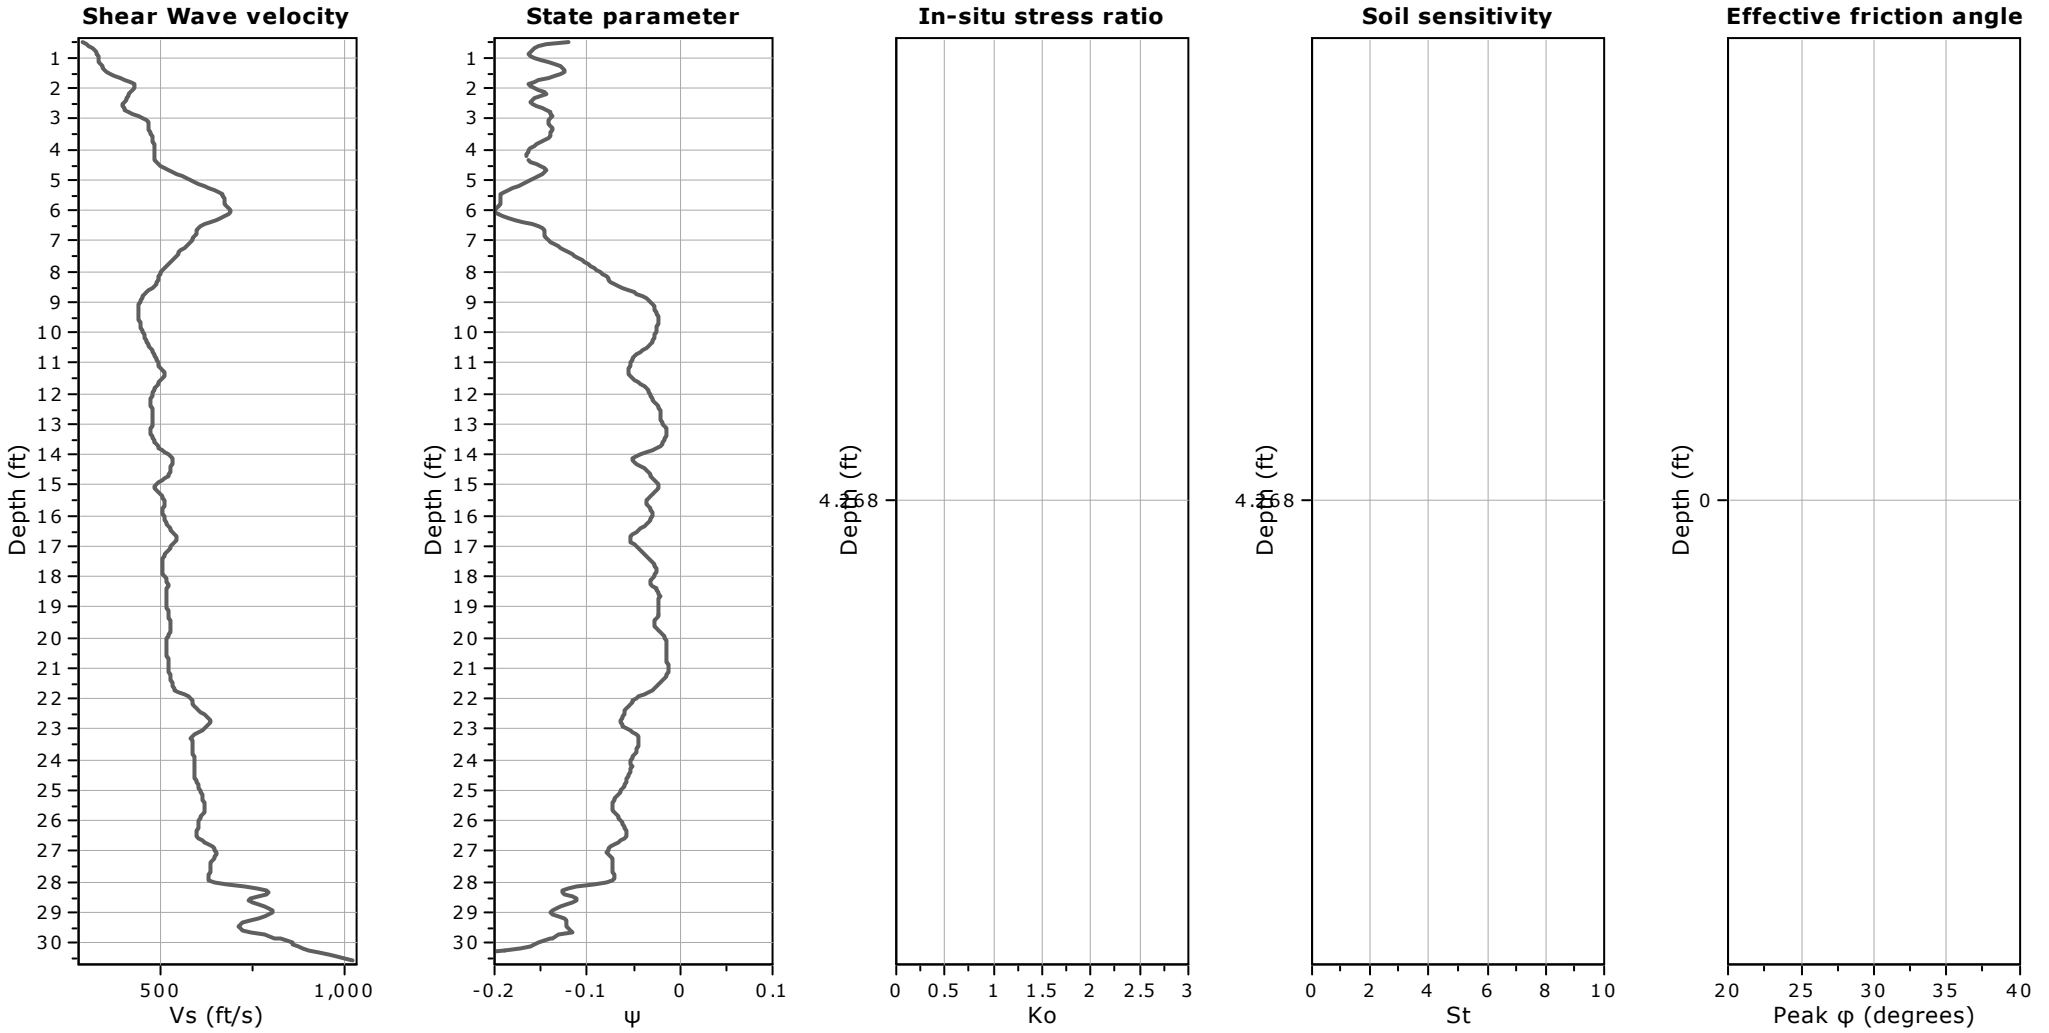

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-15
Total depth: 32.51 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

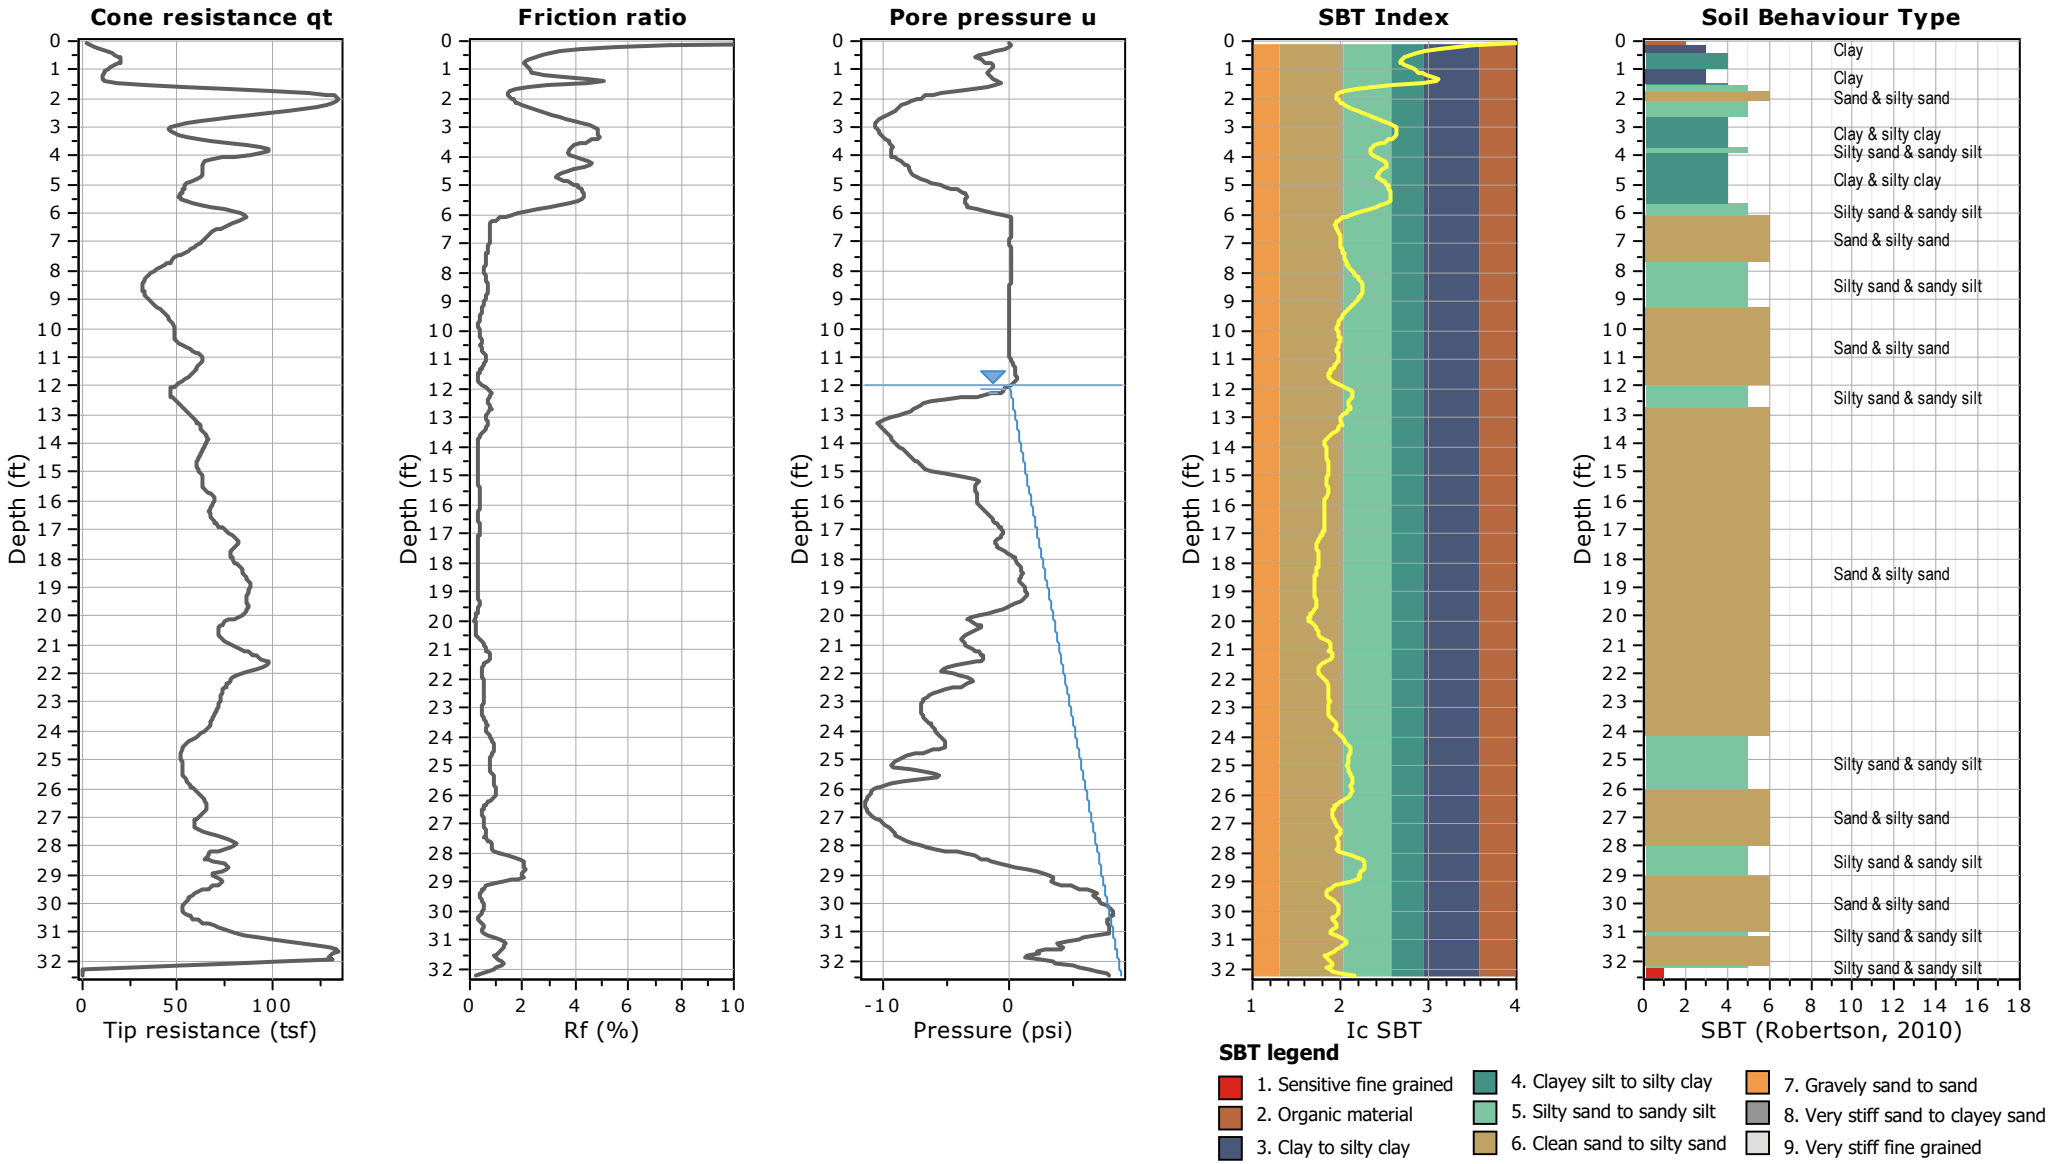



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

CPT: CPT-15
Total depth: 32.51 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Updated SBTn plots

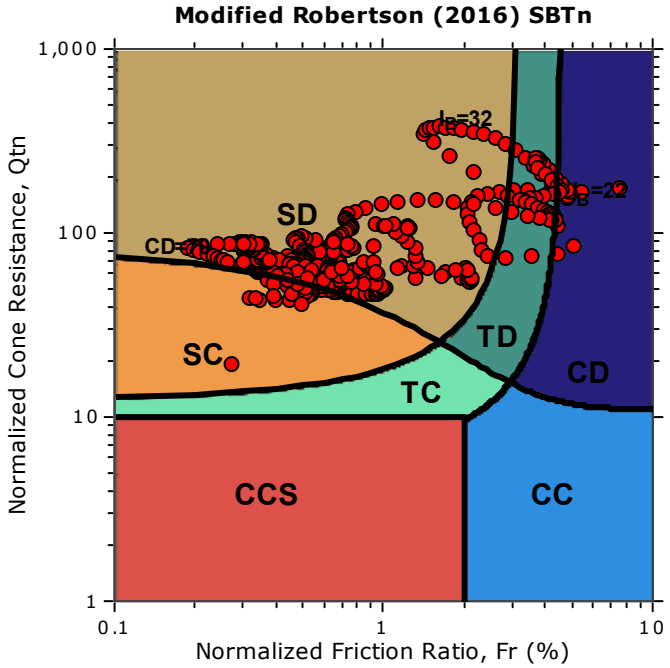

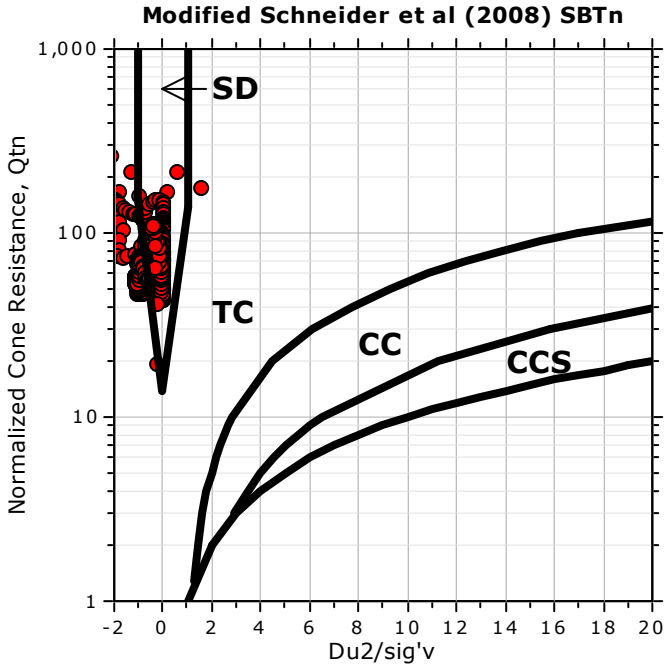

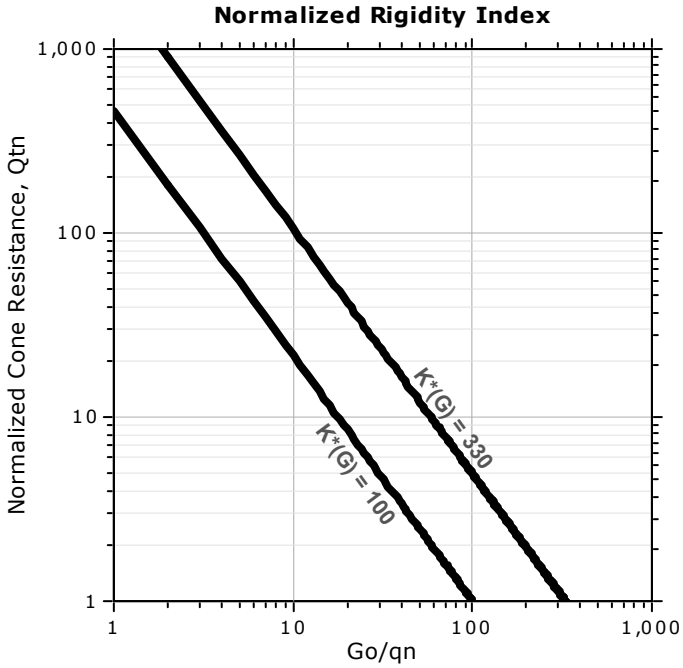


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-15
Total depth: 32.51 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

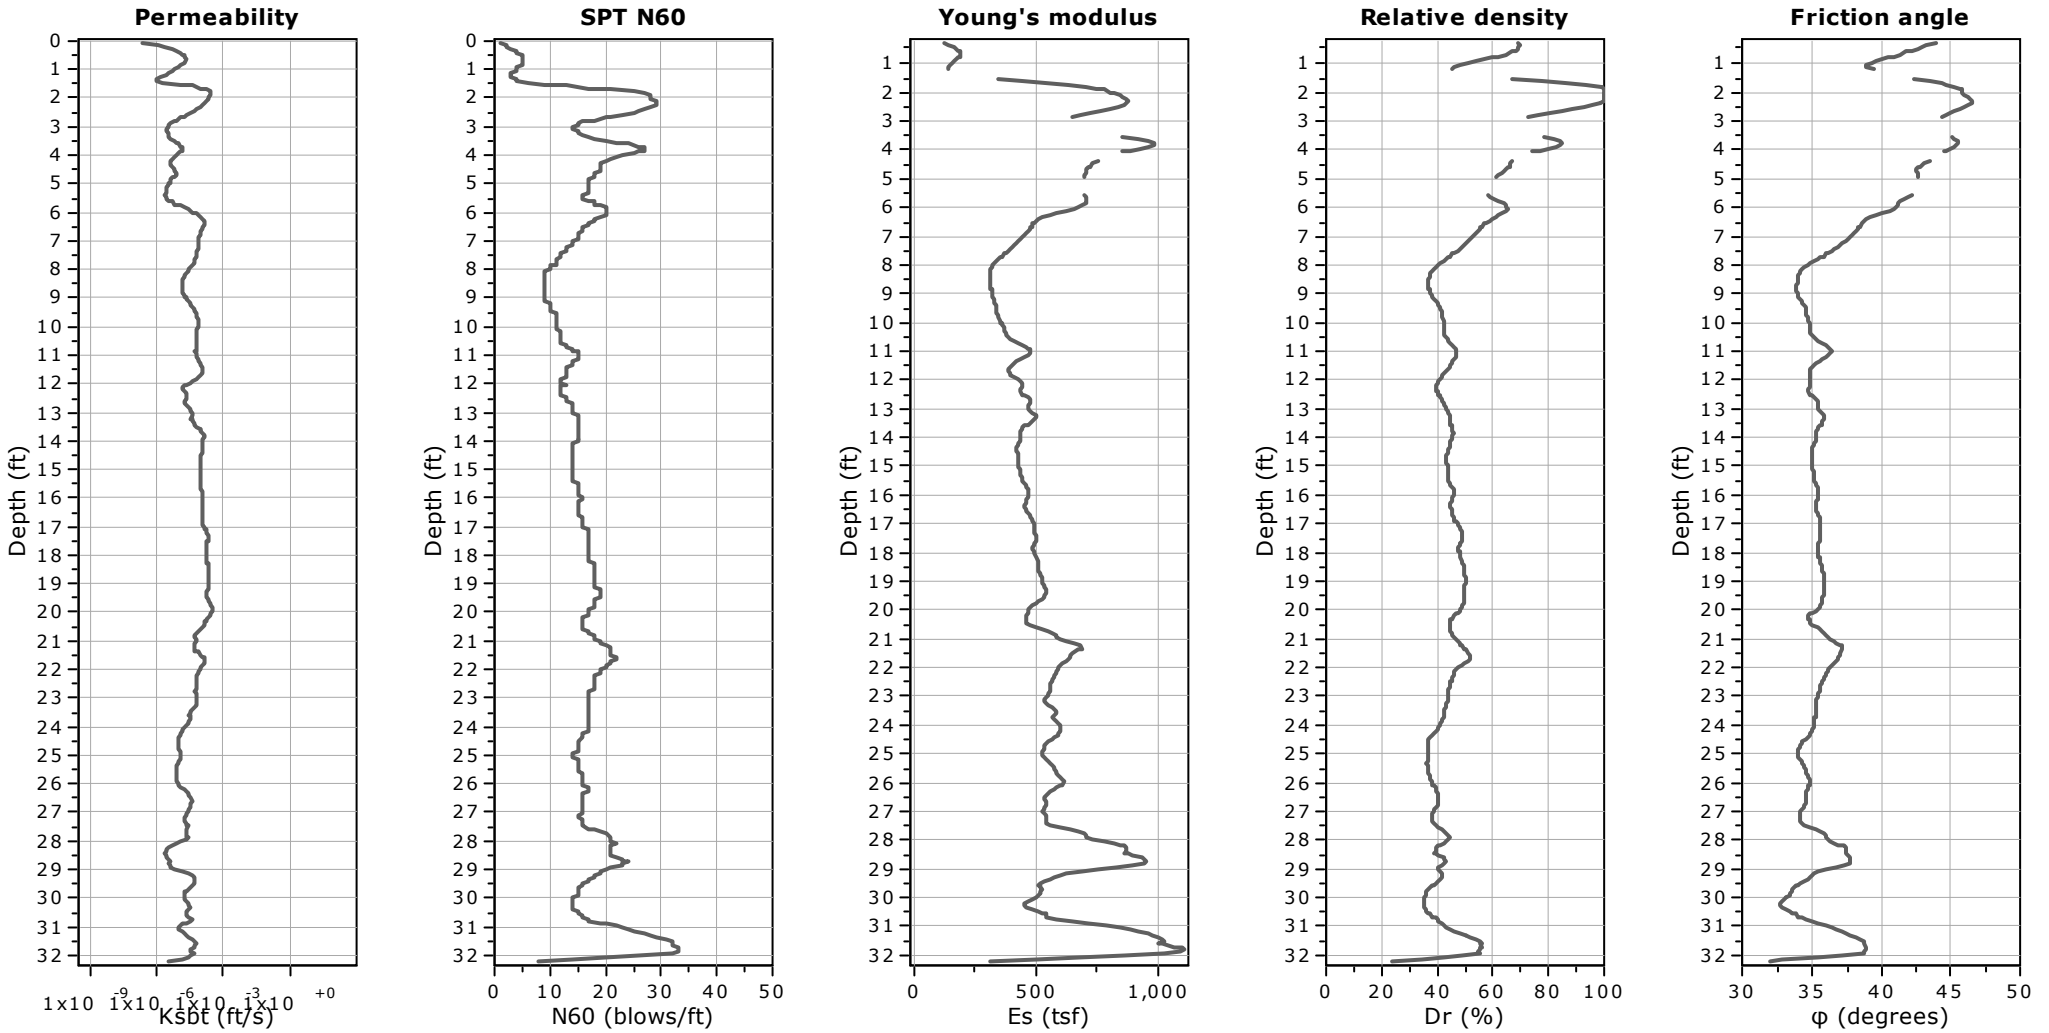


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-15
Total depth: 32.51 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

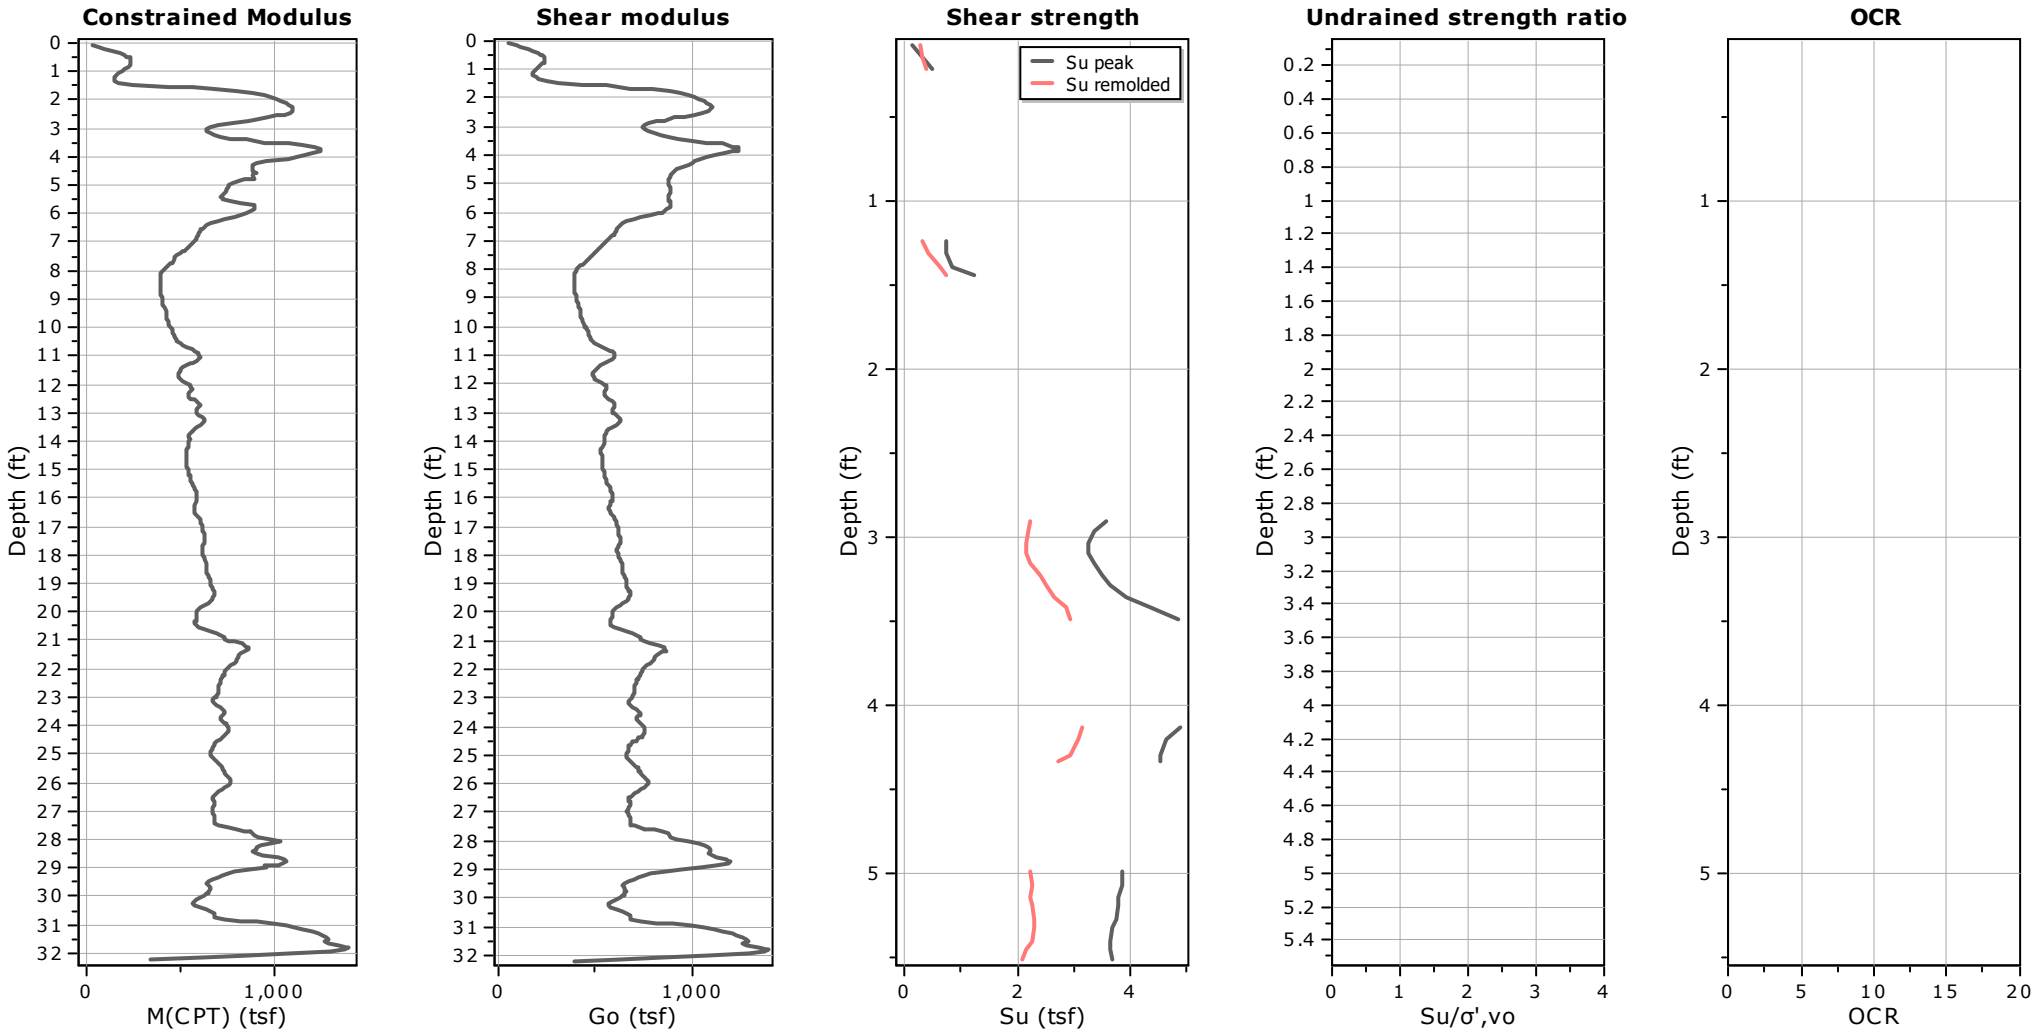

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-15
Total depth: 32.51 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

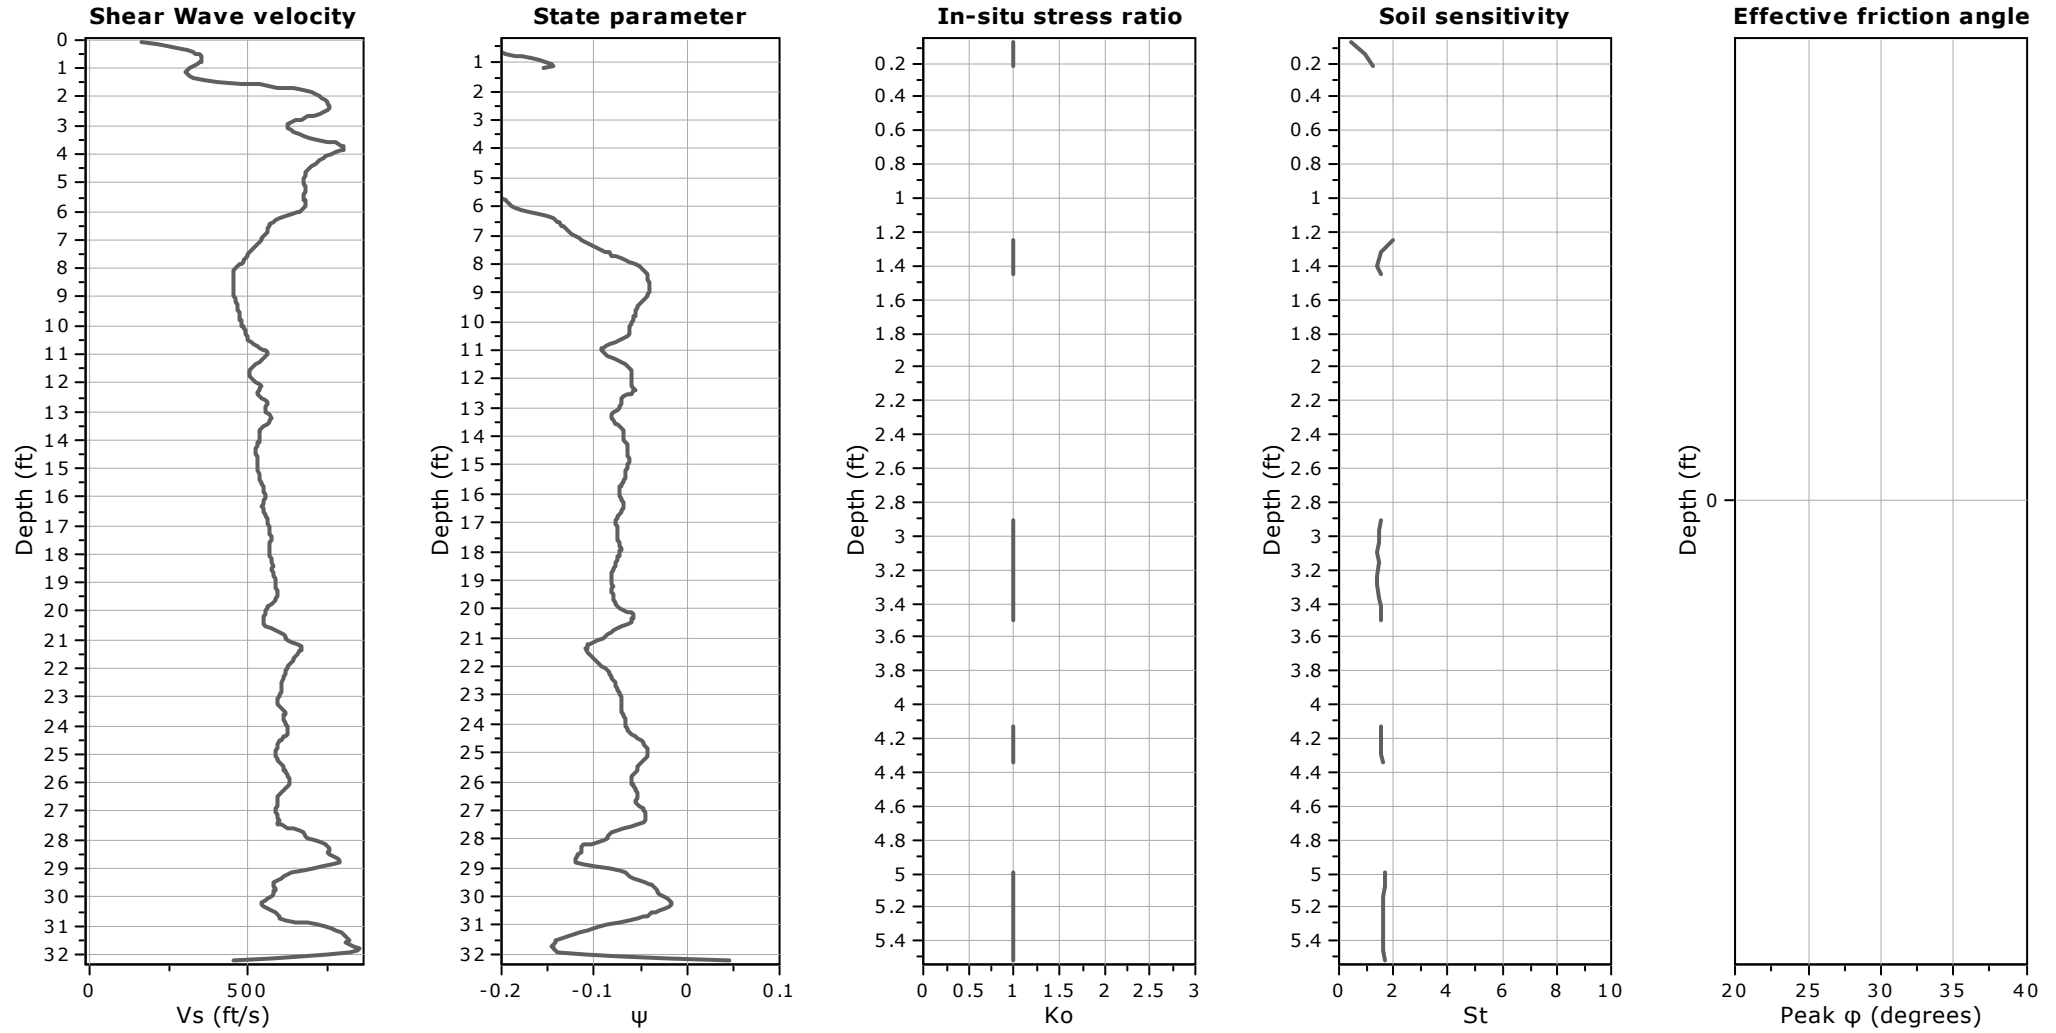


Calculation parameters

Soil Sensitivity factor, N_S: 7.00
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-16
Total depth: 32.03 ft, Date: 12/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

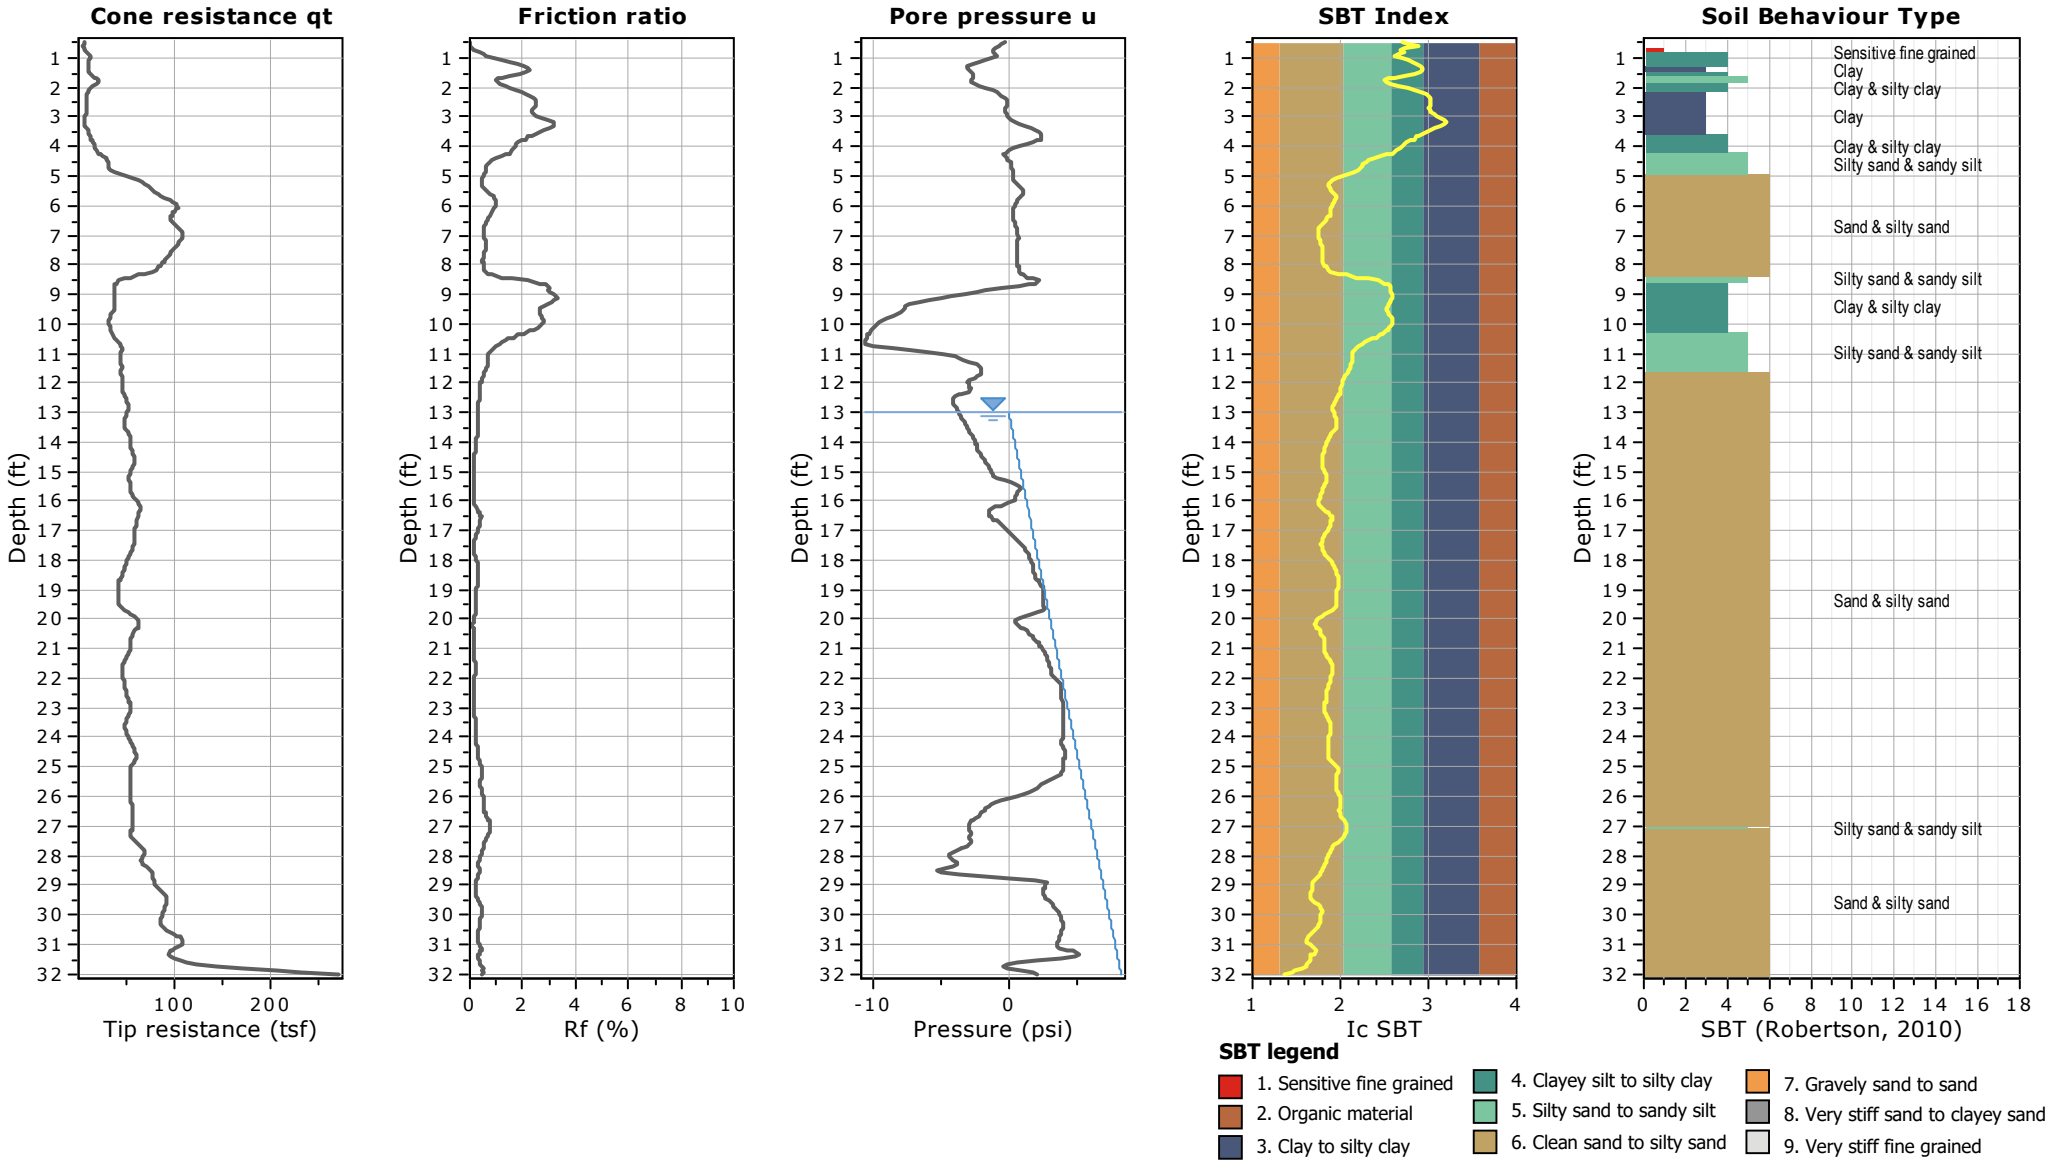



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-16
Total depth: 32.03 ft, Date: 12/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

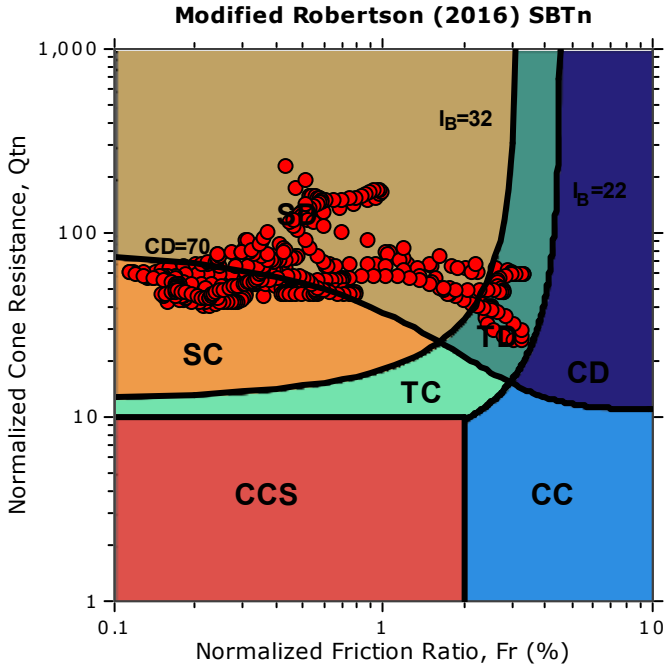

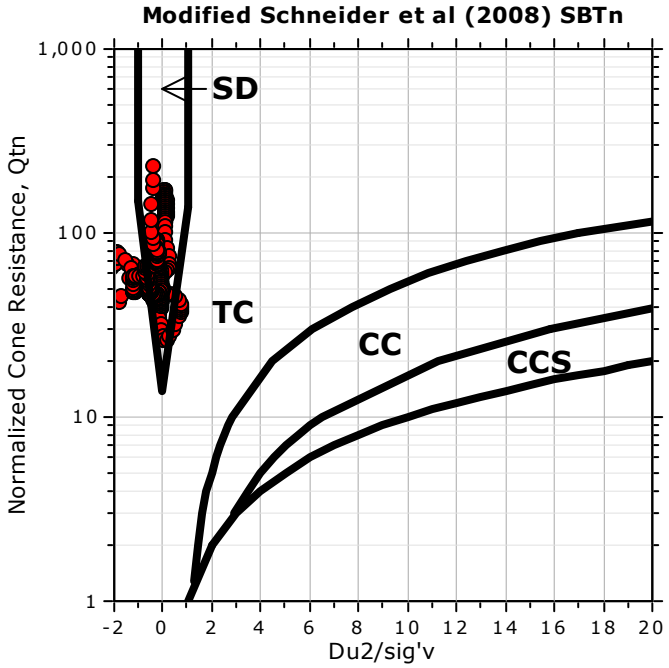

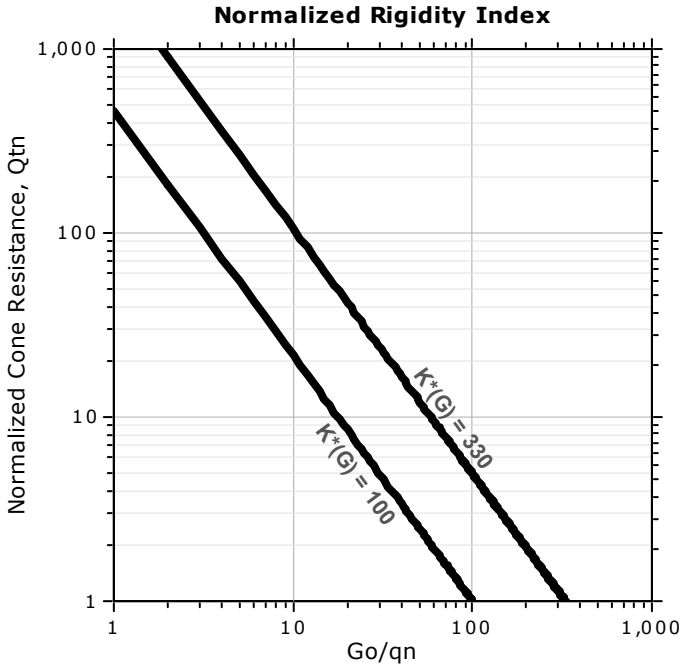


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-16
Total depth: 32.03 ft, Date: 12/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

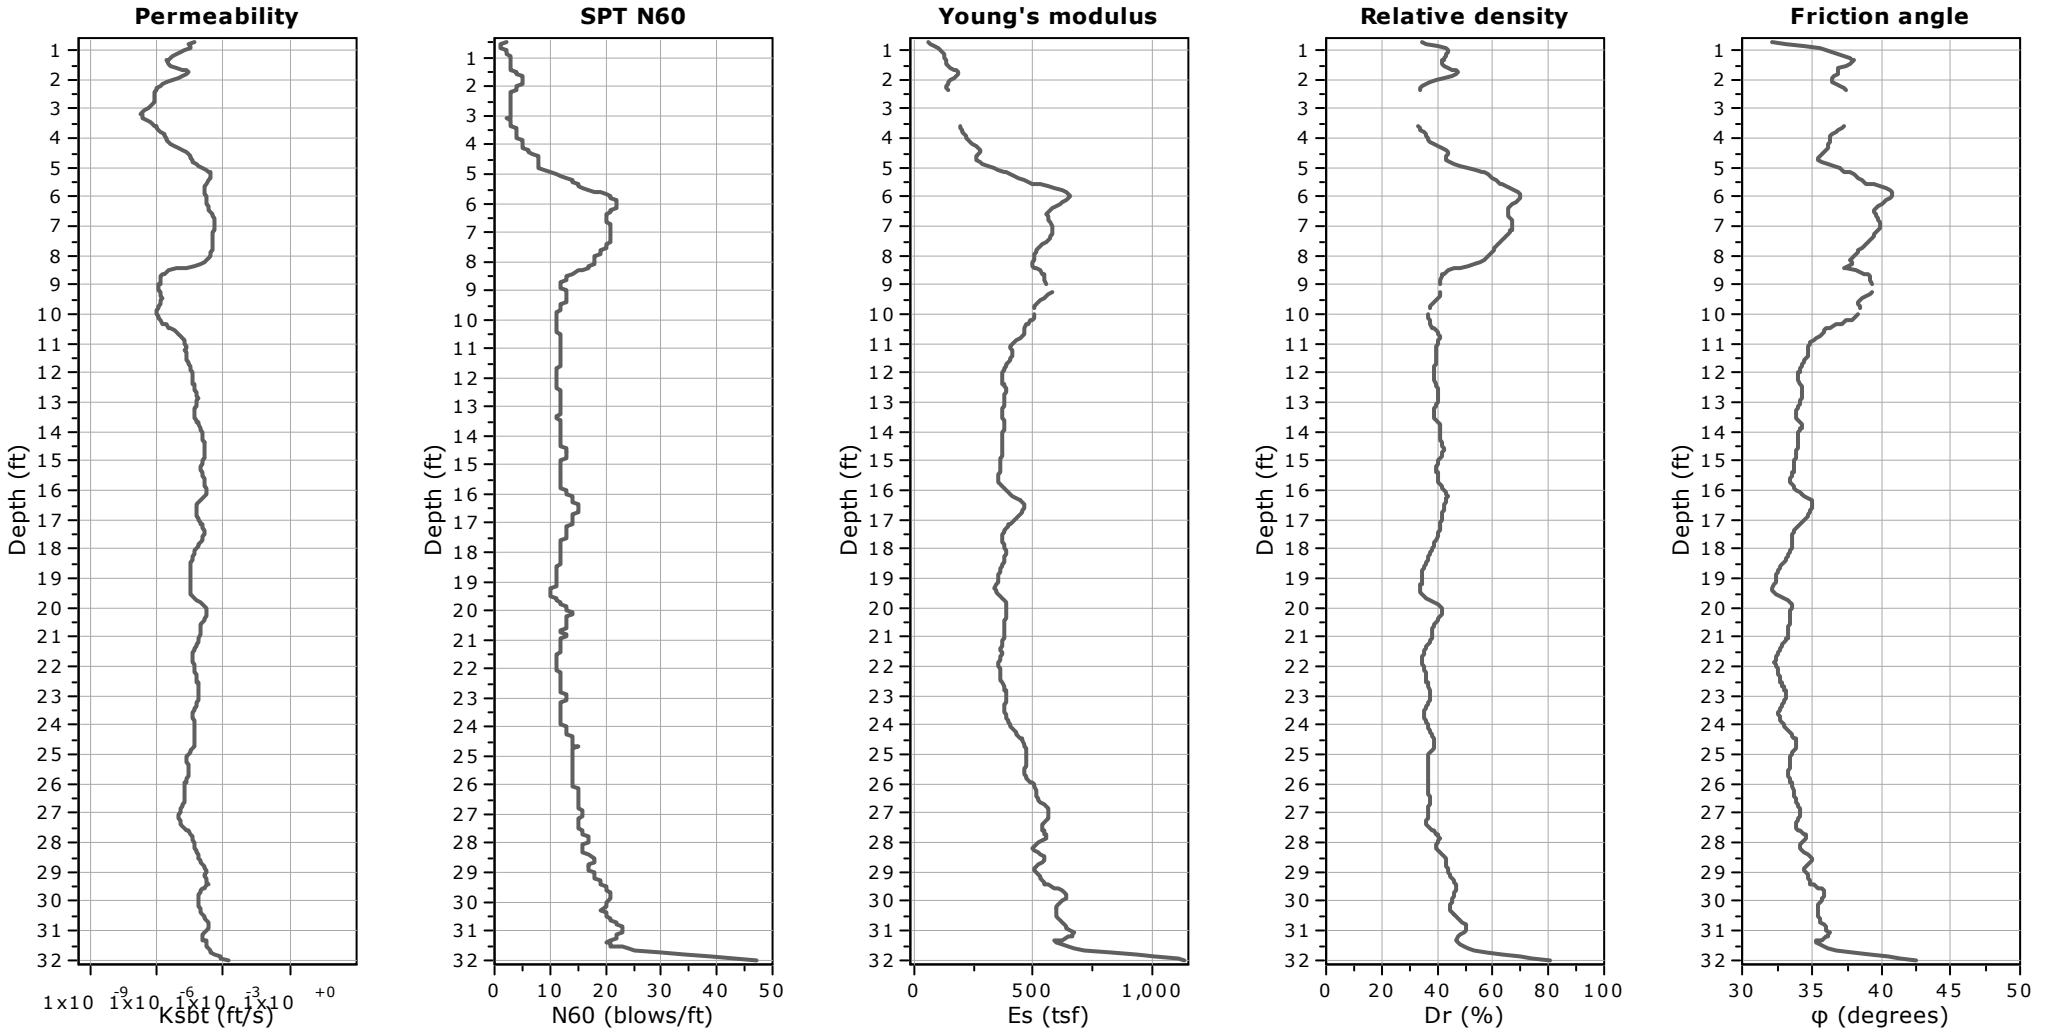


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-16
Total depth: 32.03 ft, Date: 12/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

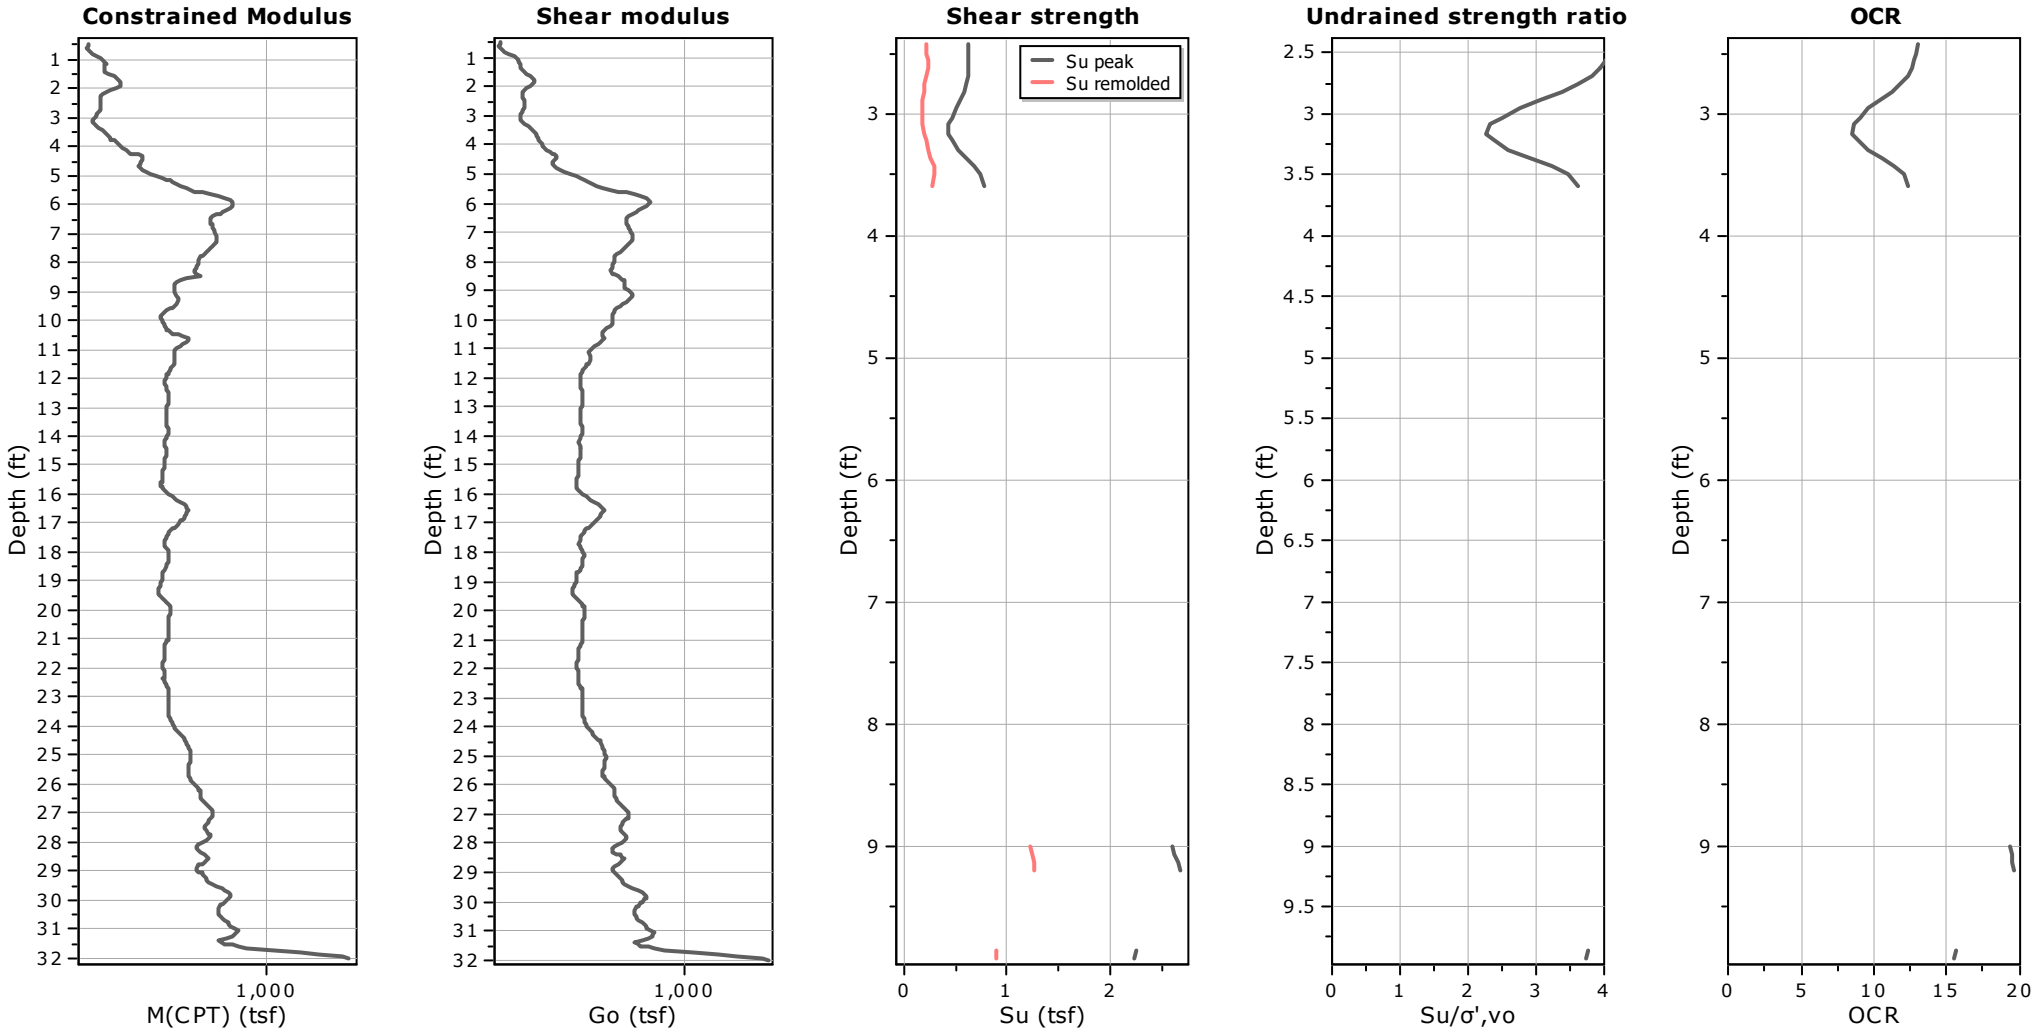

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-16
Total depth: 32.03 ft, Date: 12/20/2022
Surface Elevation: 79.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

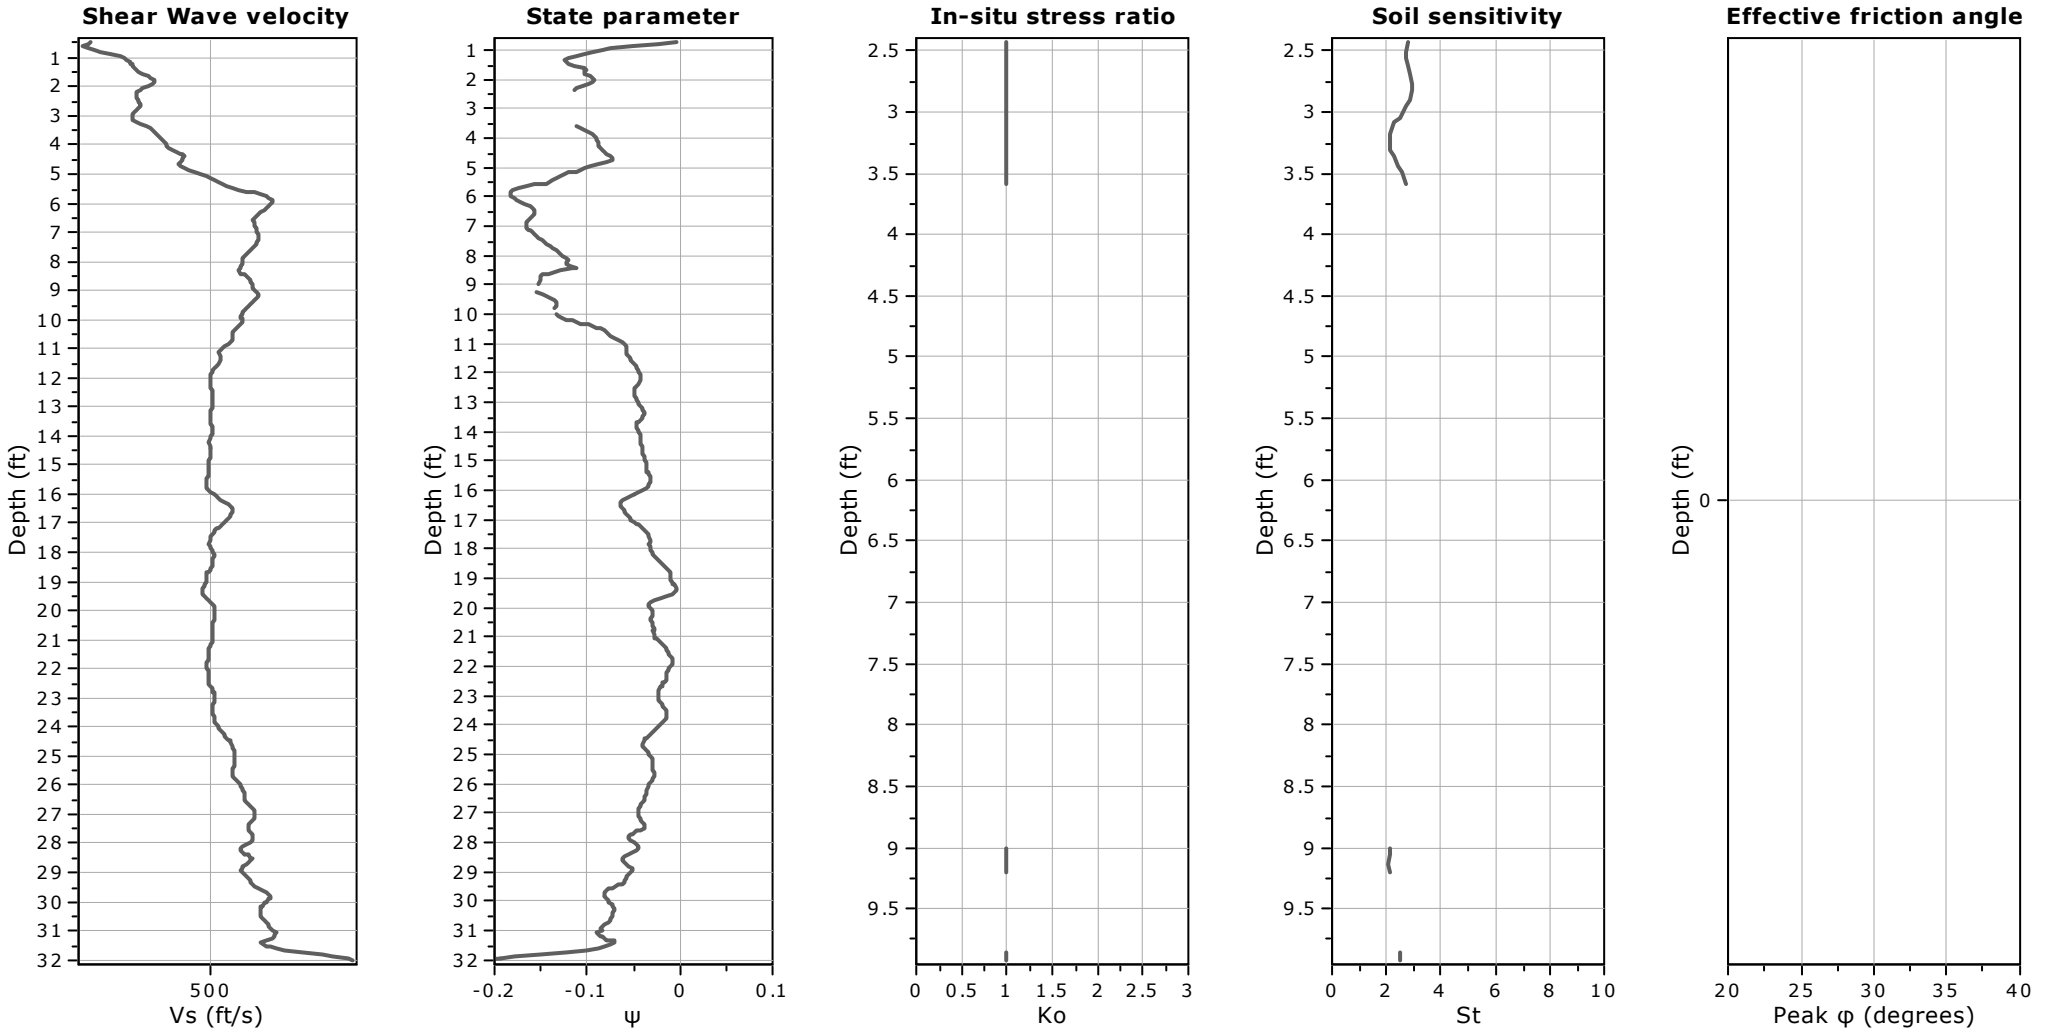


Calculation parameters

Soil Sensitivity factor, N_S: 7.00
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-17
Total depth: 30.98 ft, Date: 12/20/2022
Surface Elevation: 83.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

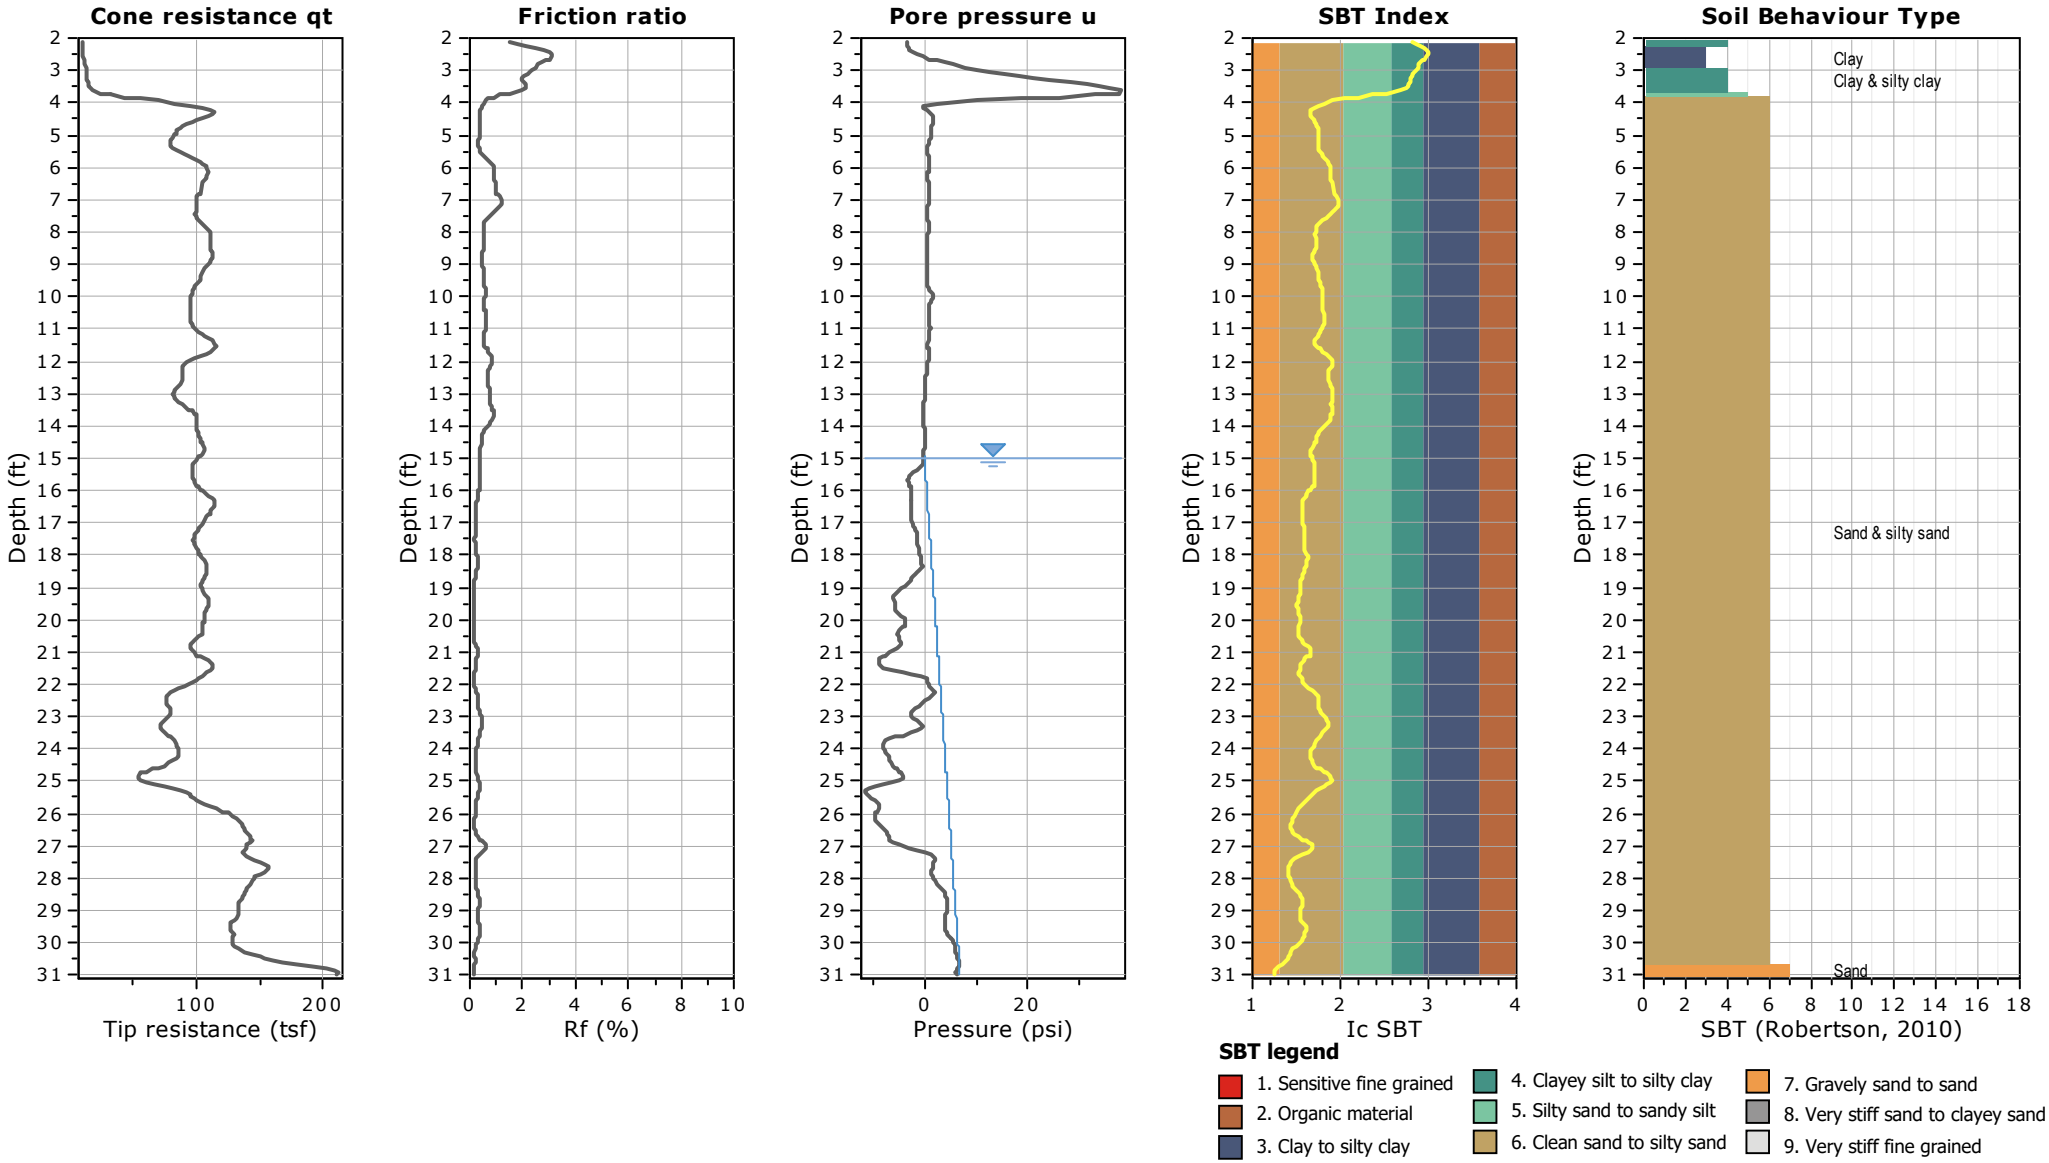



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-17
Total depth: 30.98 ft, Date: 12/20/2022
Surface Elevation: 83.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

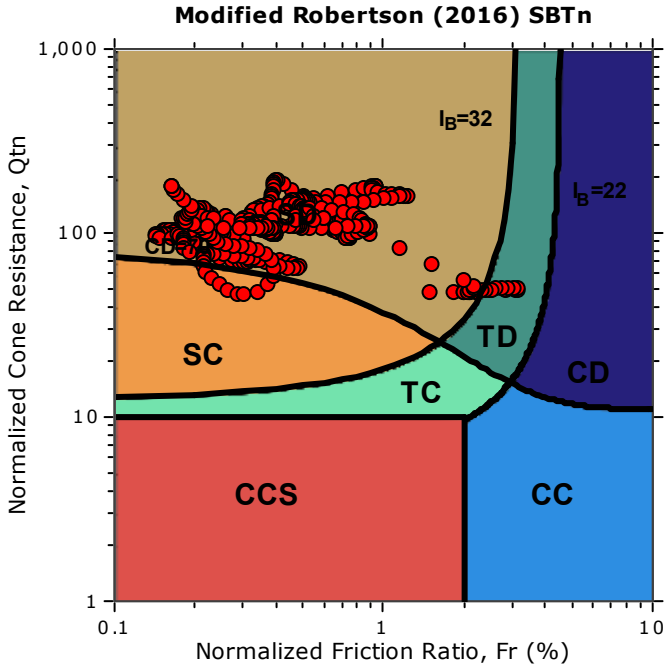

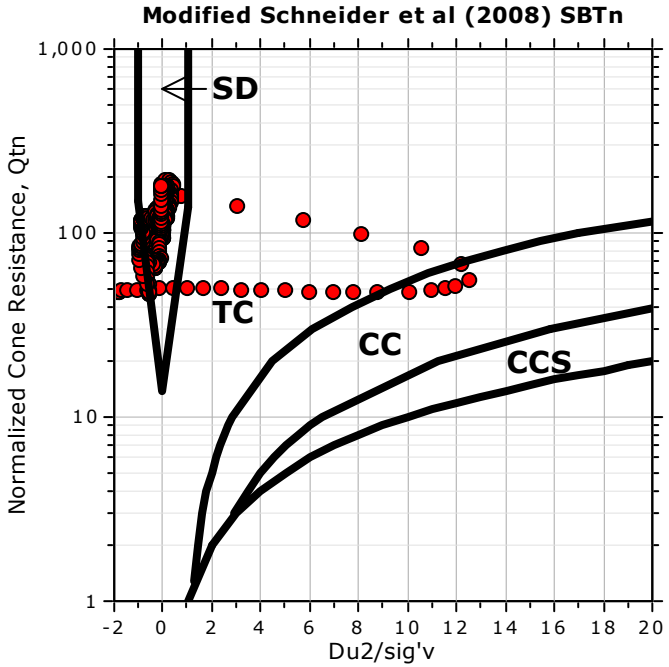

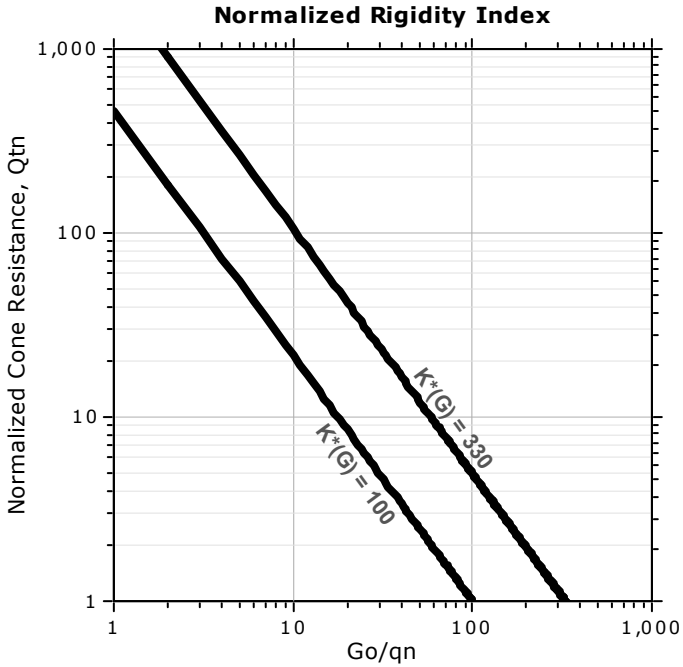


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-17
Total depth: 30.98 ft, Date: 12/20/2022
Surface Elevation: 83.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

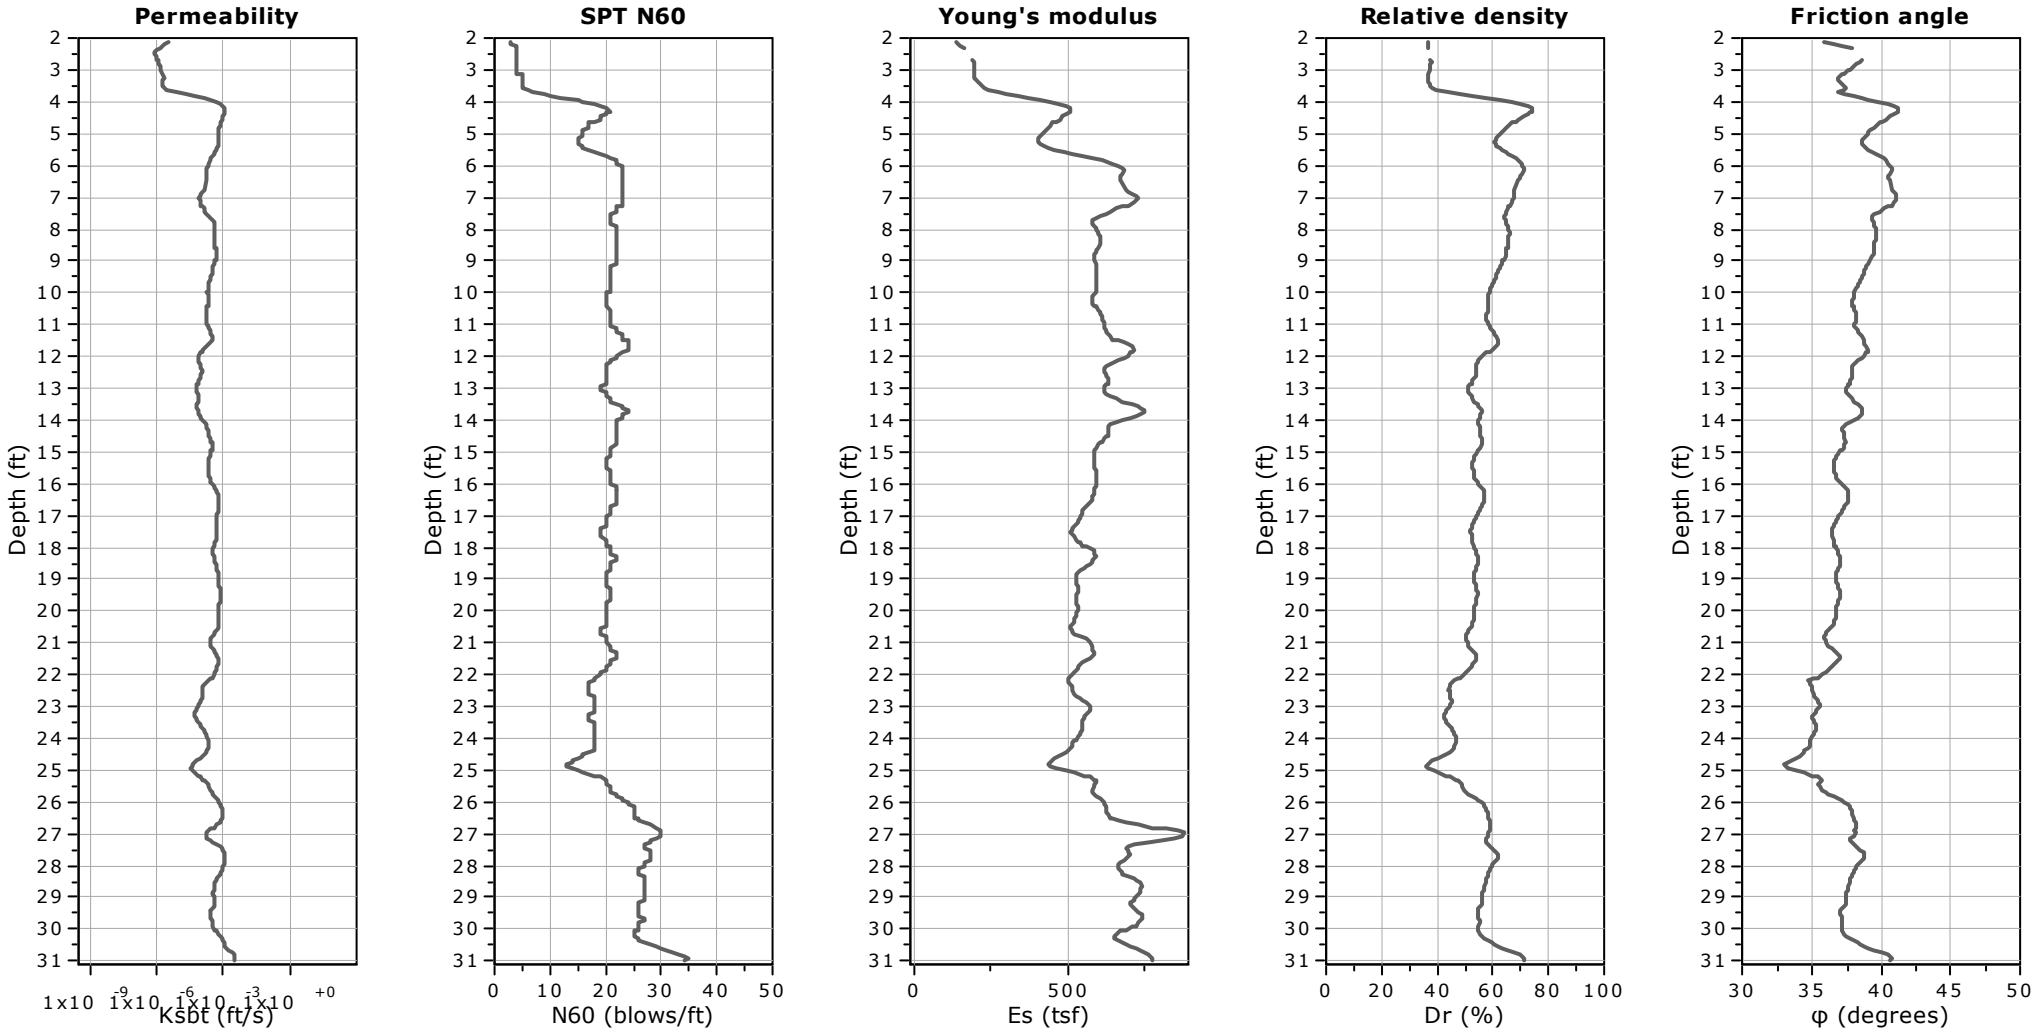


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-17
Total depth: 30.98 ft, Date: 12/20/2022
Surface Elevation: 83.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

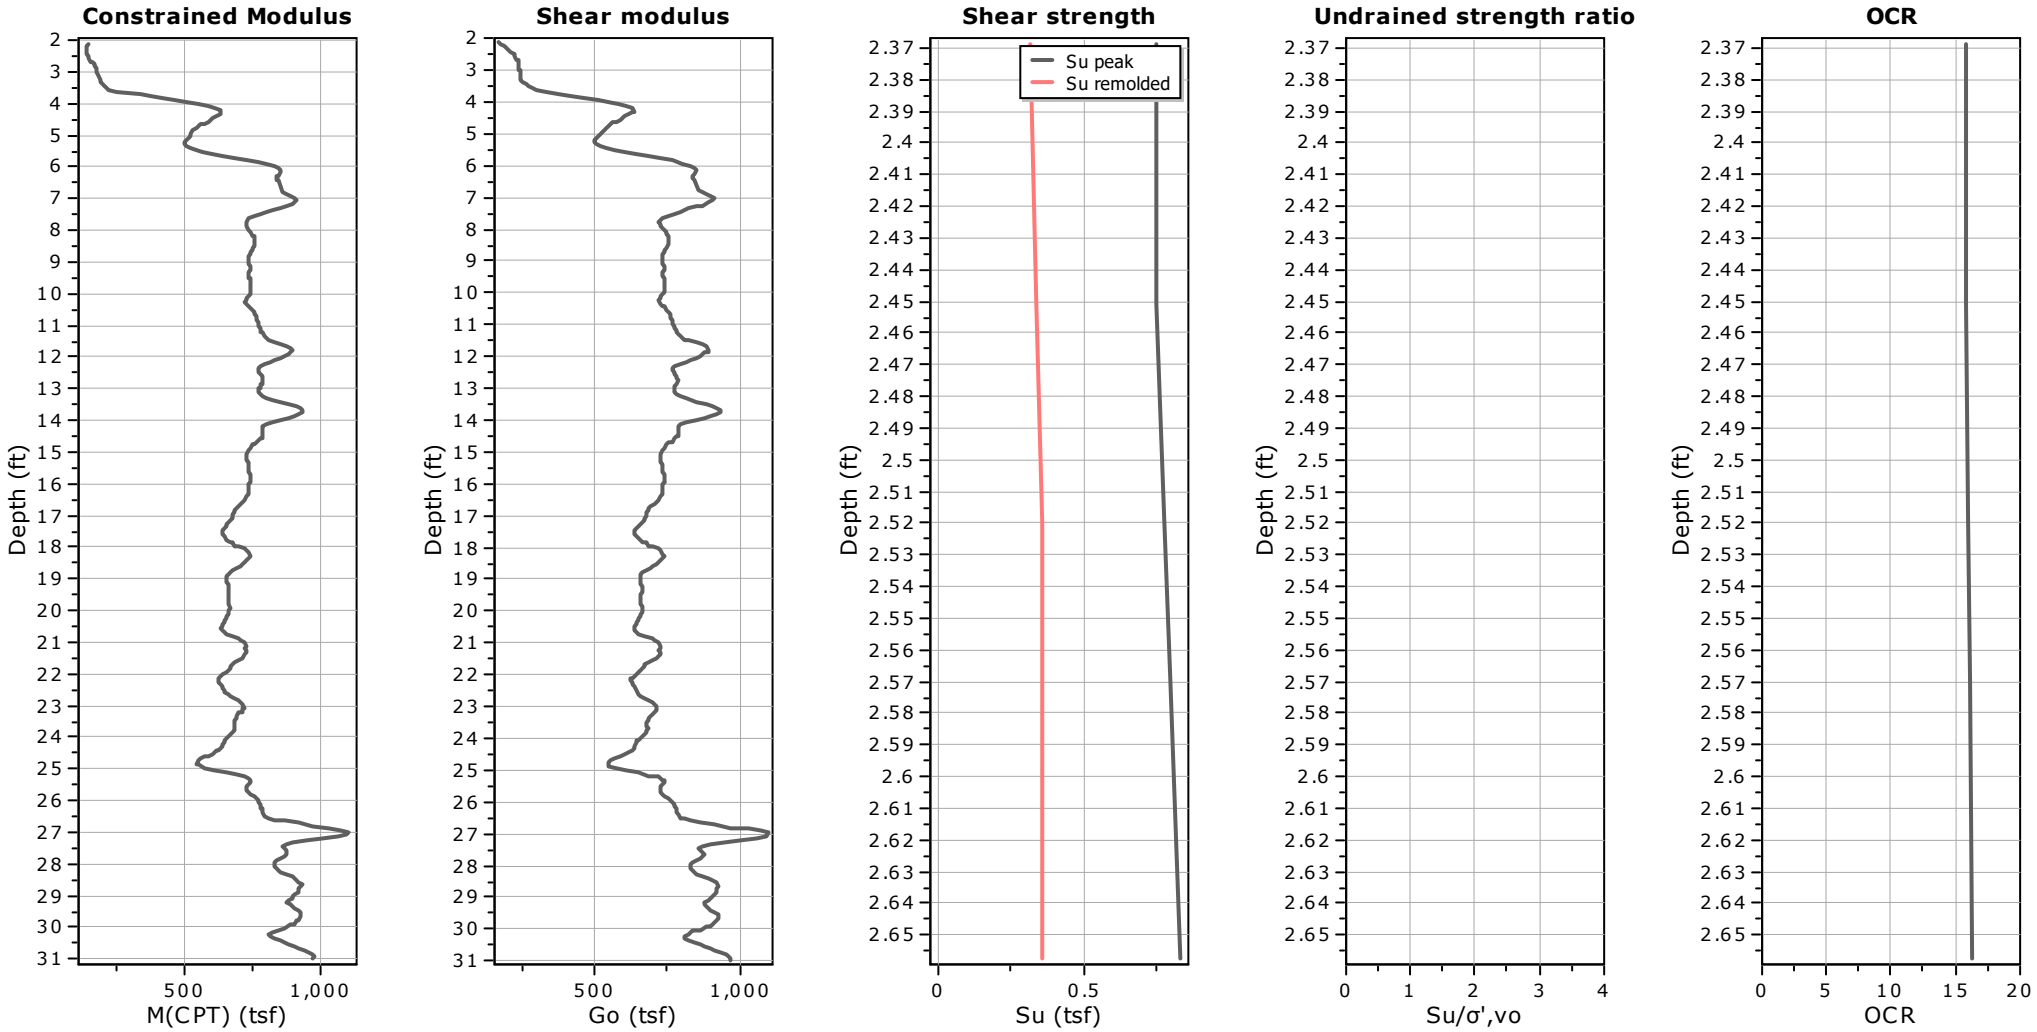


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-17
Total depth: 30.98 ft, Date: 12/20/2022
Surface Elevation: 83.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

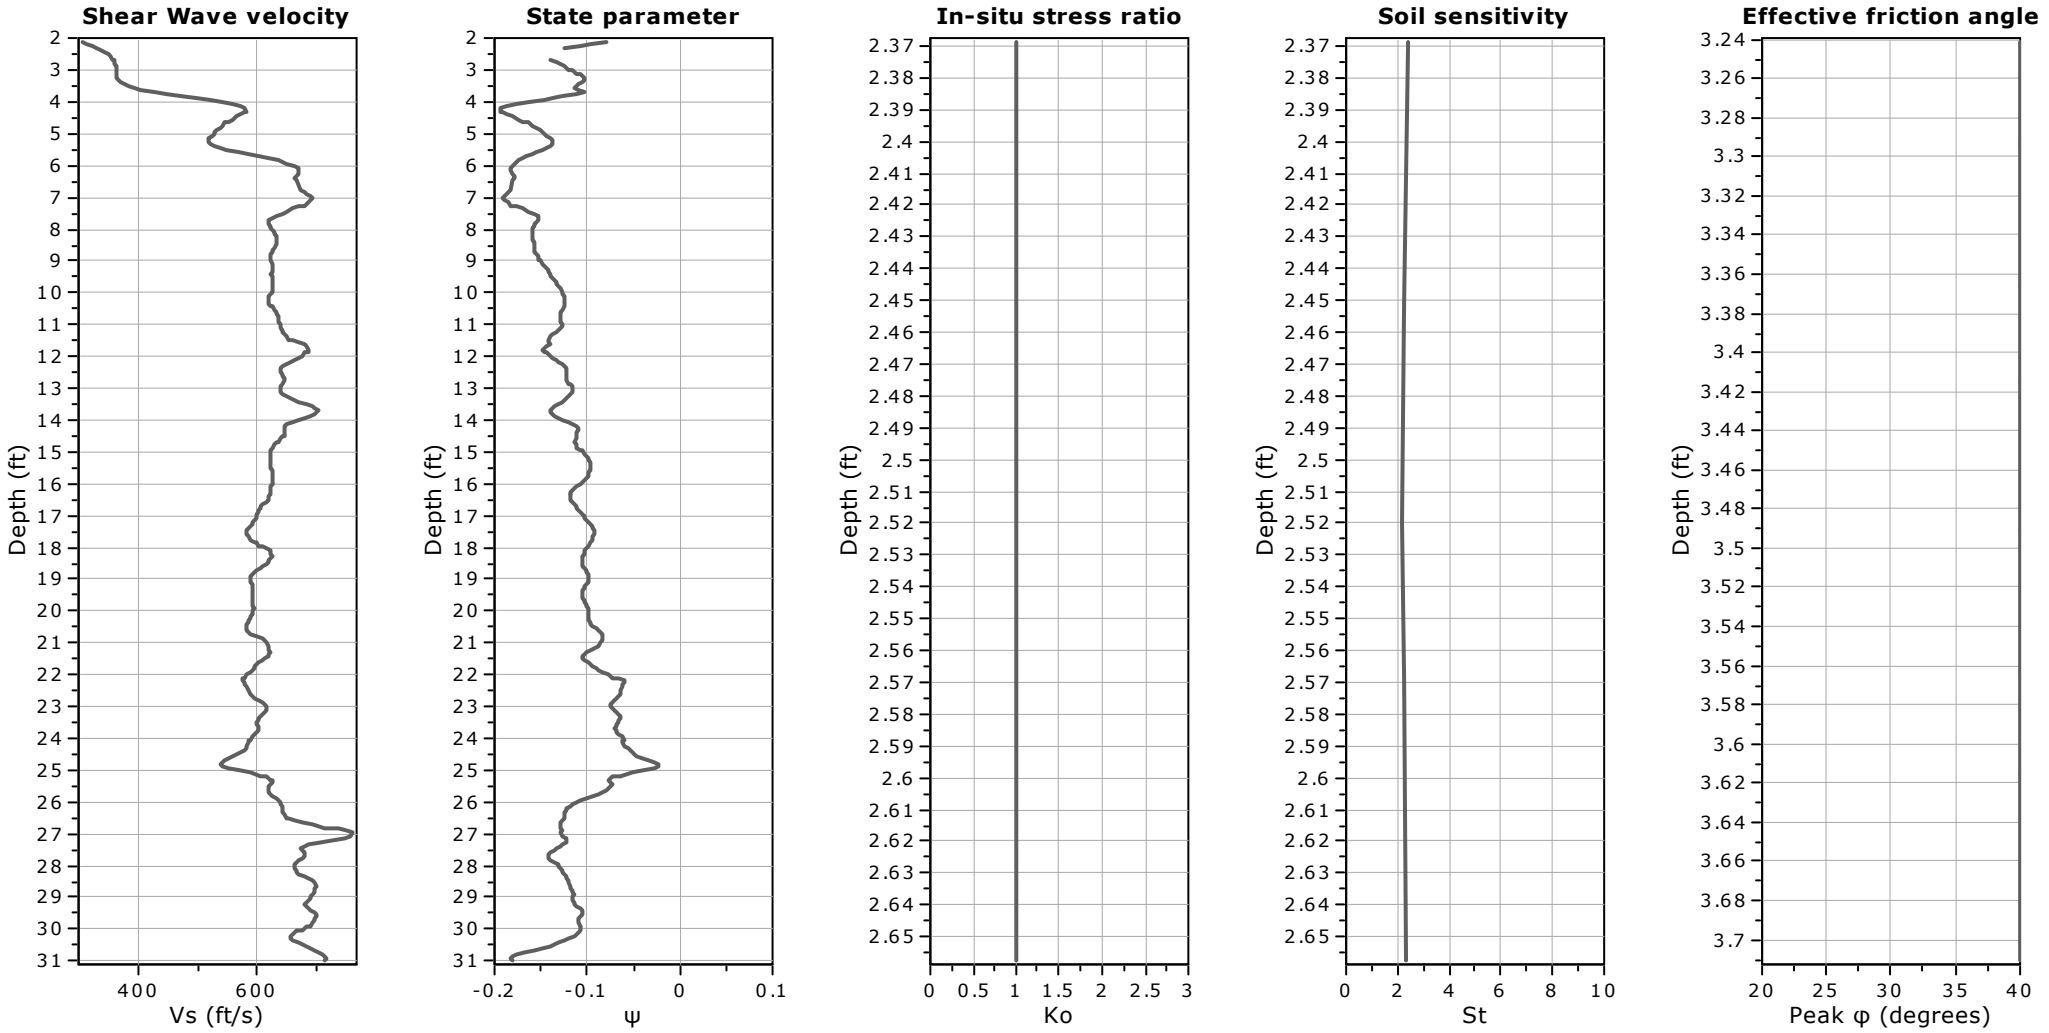


Calculation parameters

Soil Sensitivity factor, N_S: 7.00
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-18
Total depth: 30.00 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

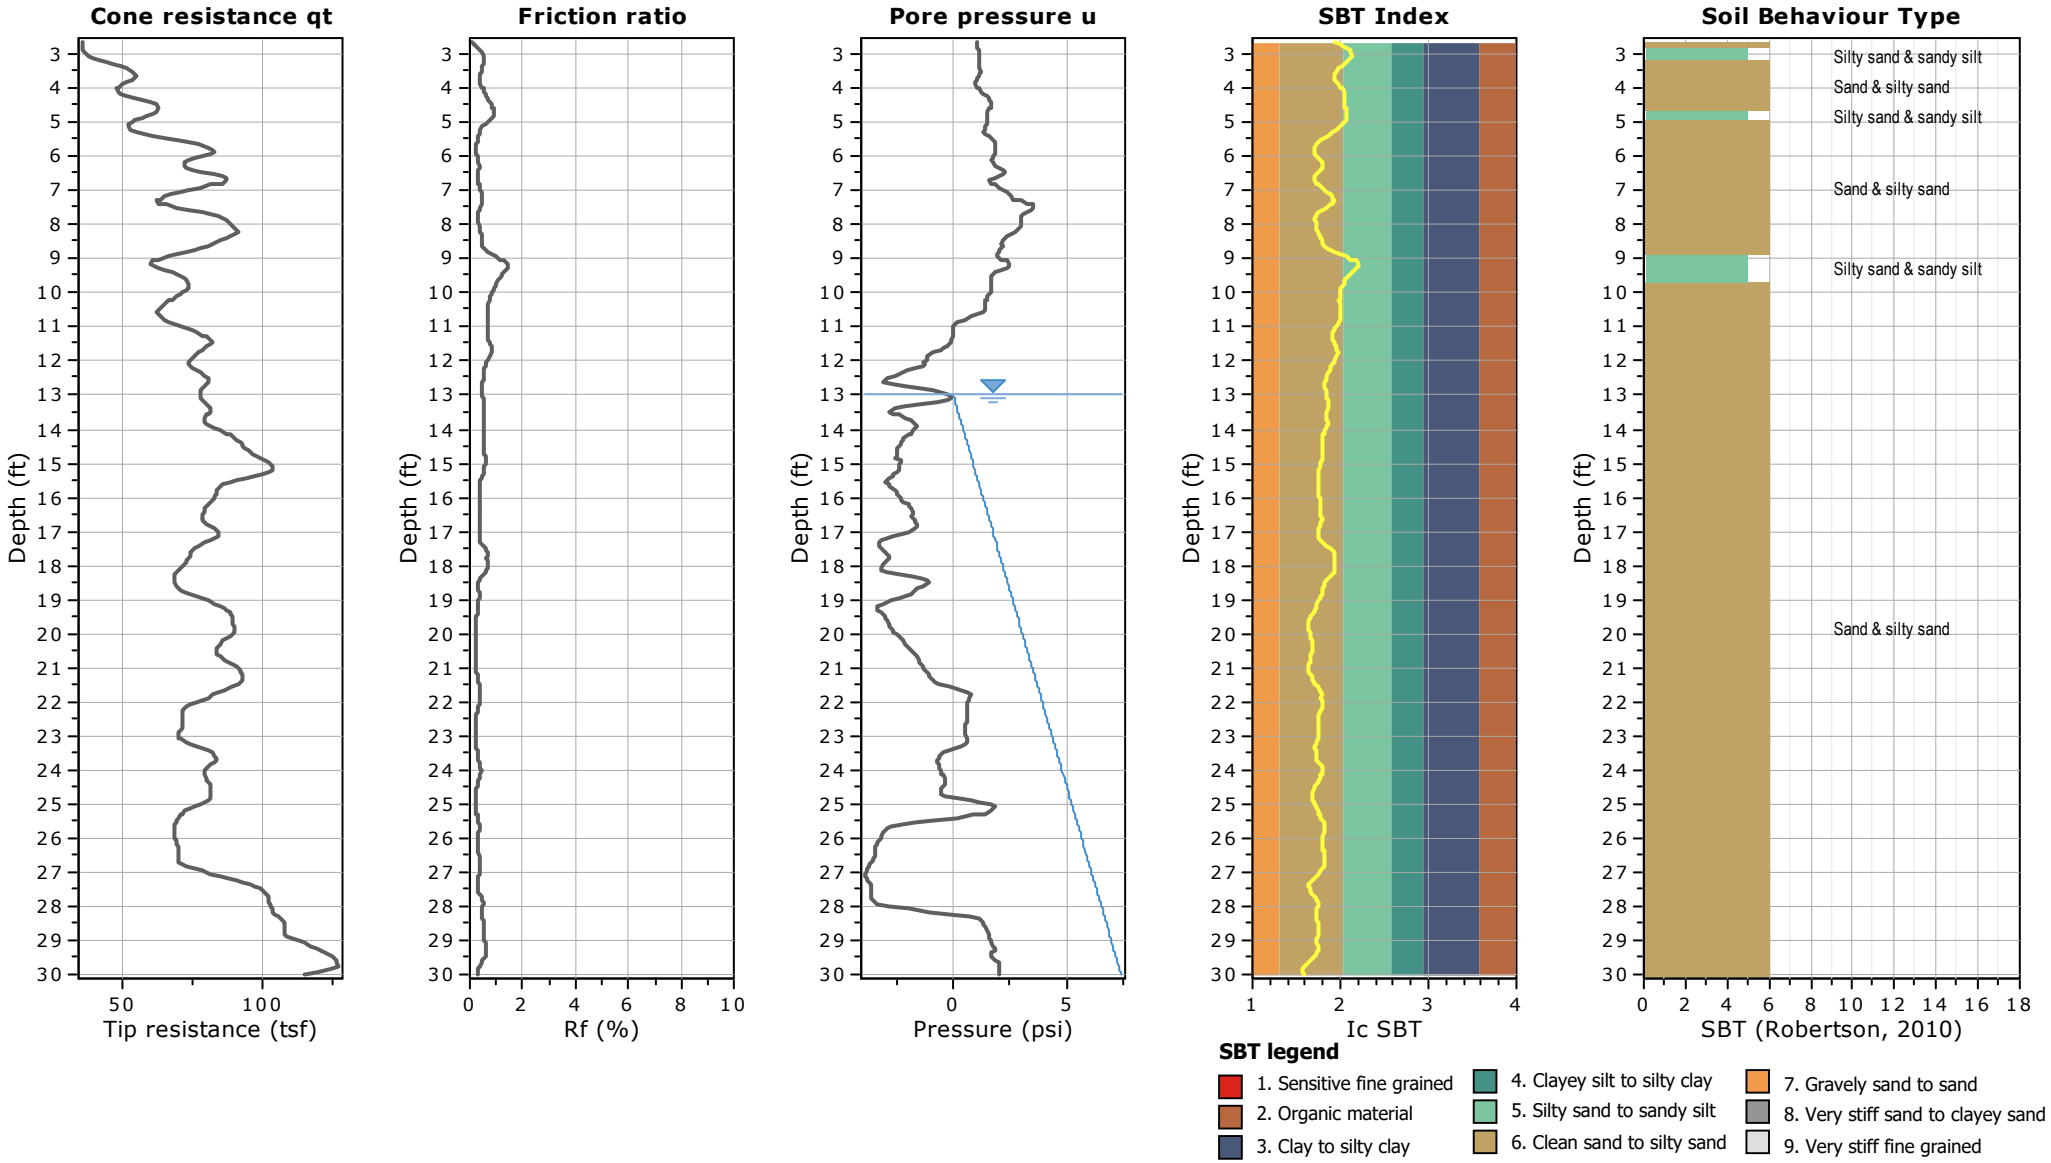



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

CPT: CPT-18
Total depth: 30.00 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Updated SBTn plots

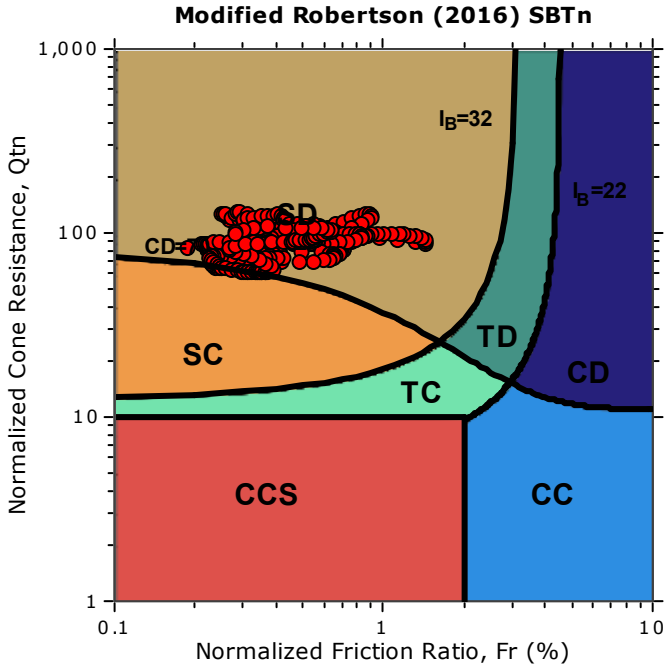

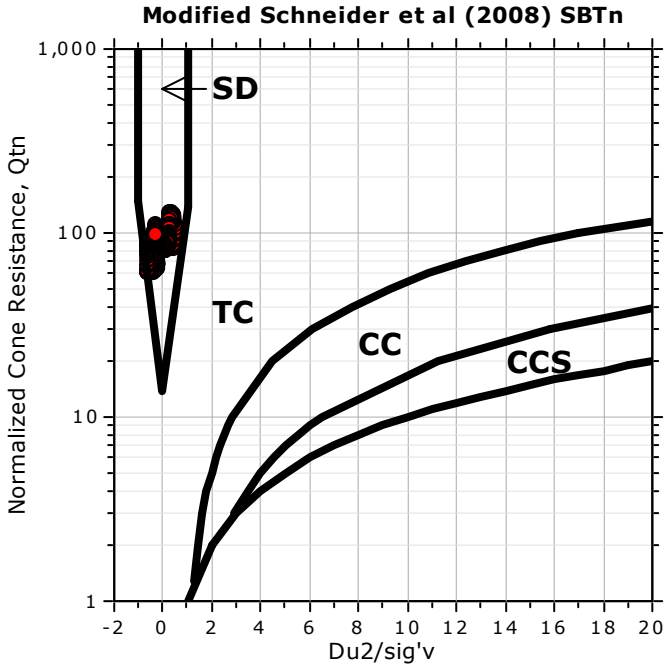

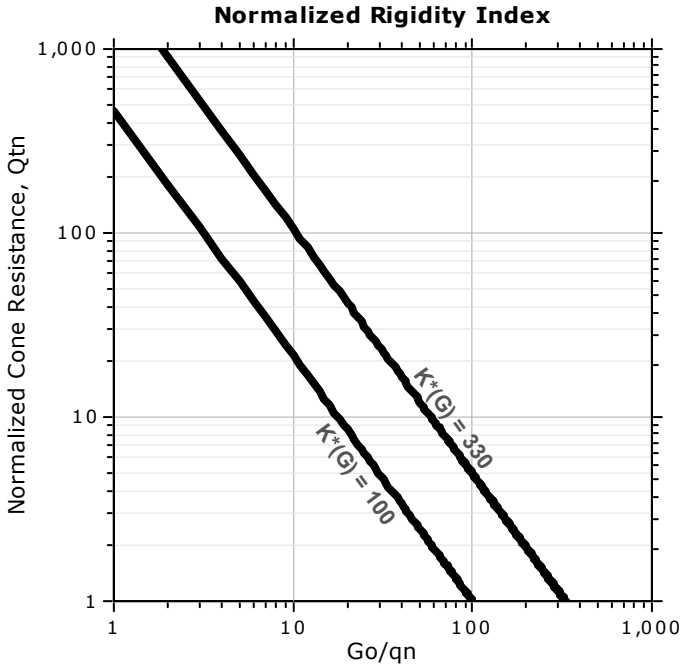


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-18
Total depth: 30.00 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

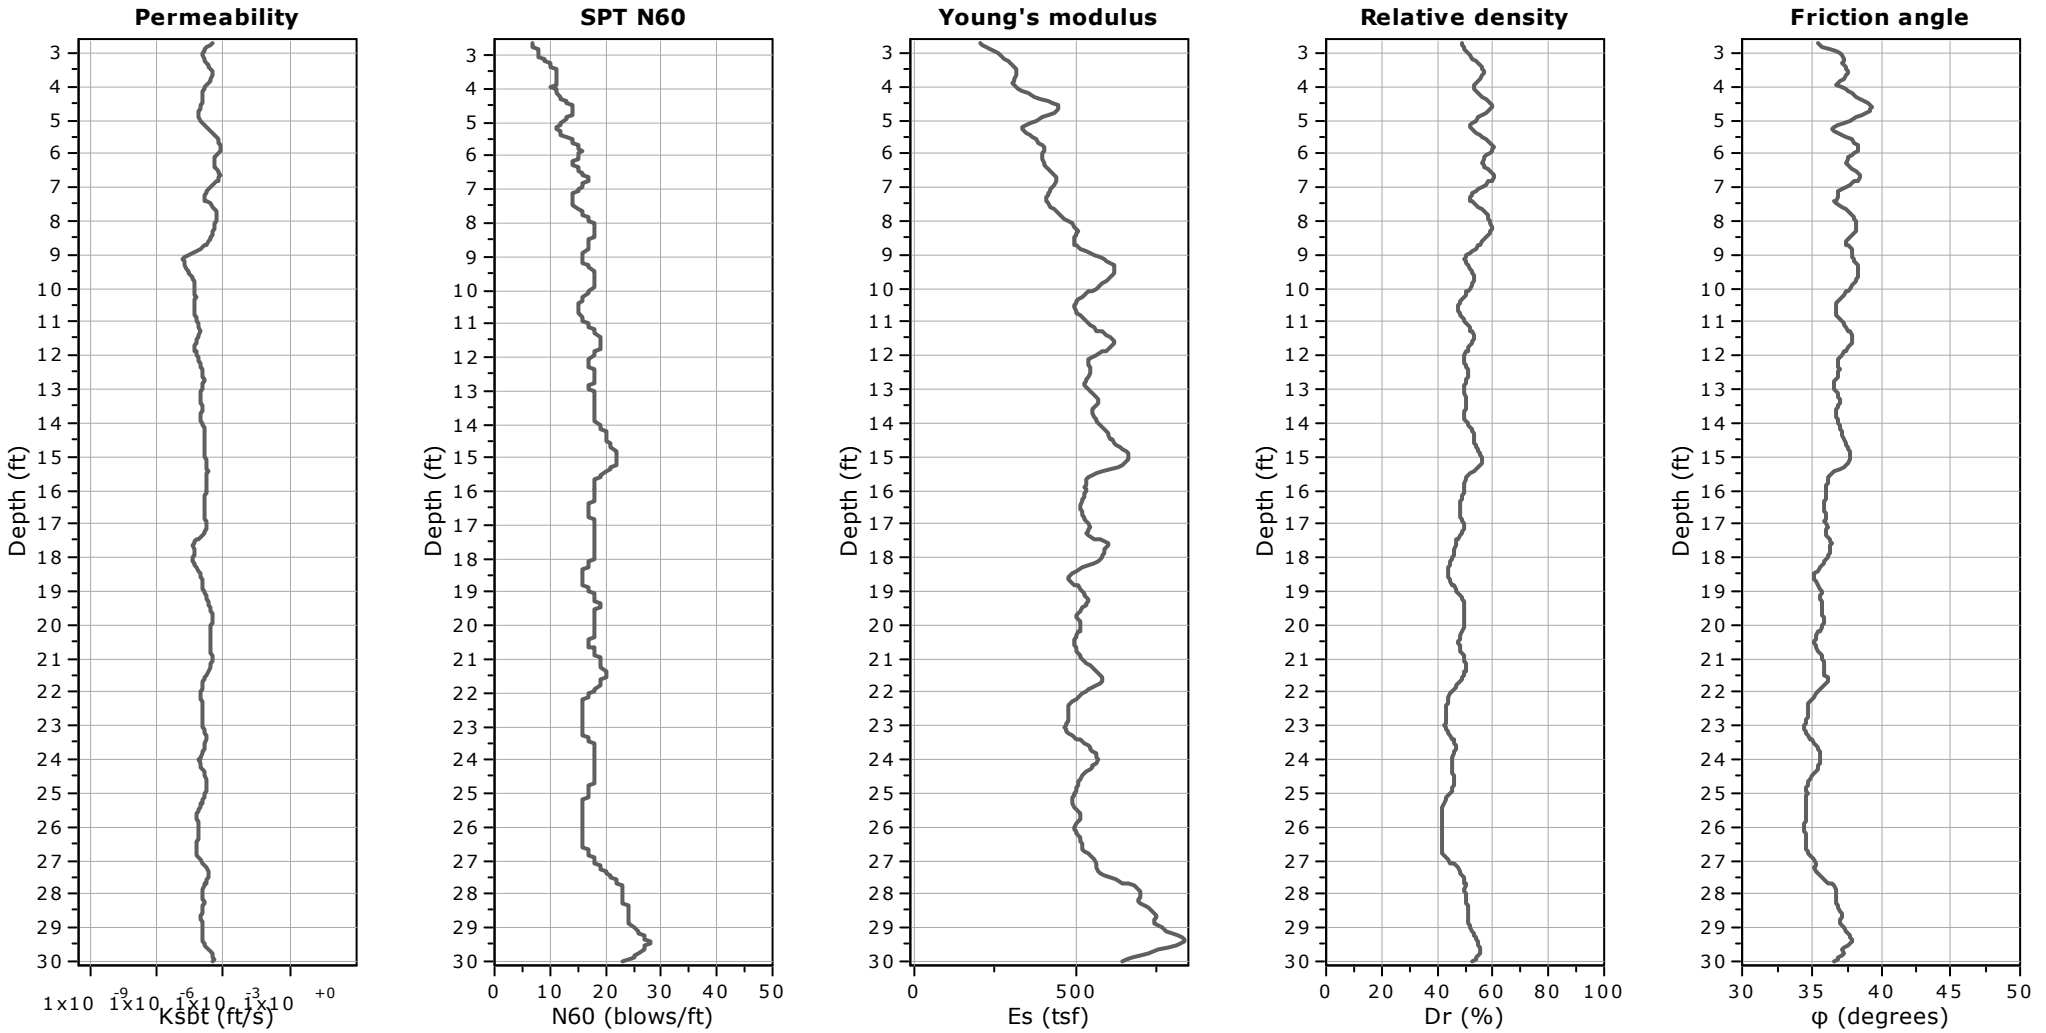


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-18
Total depth: 30.00 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

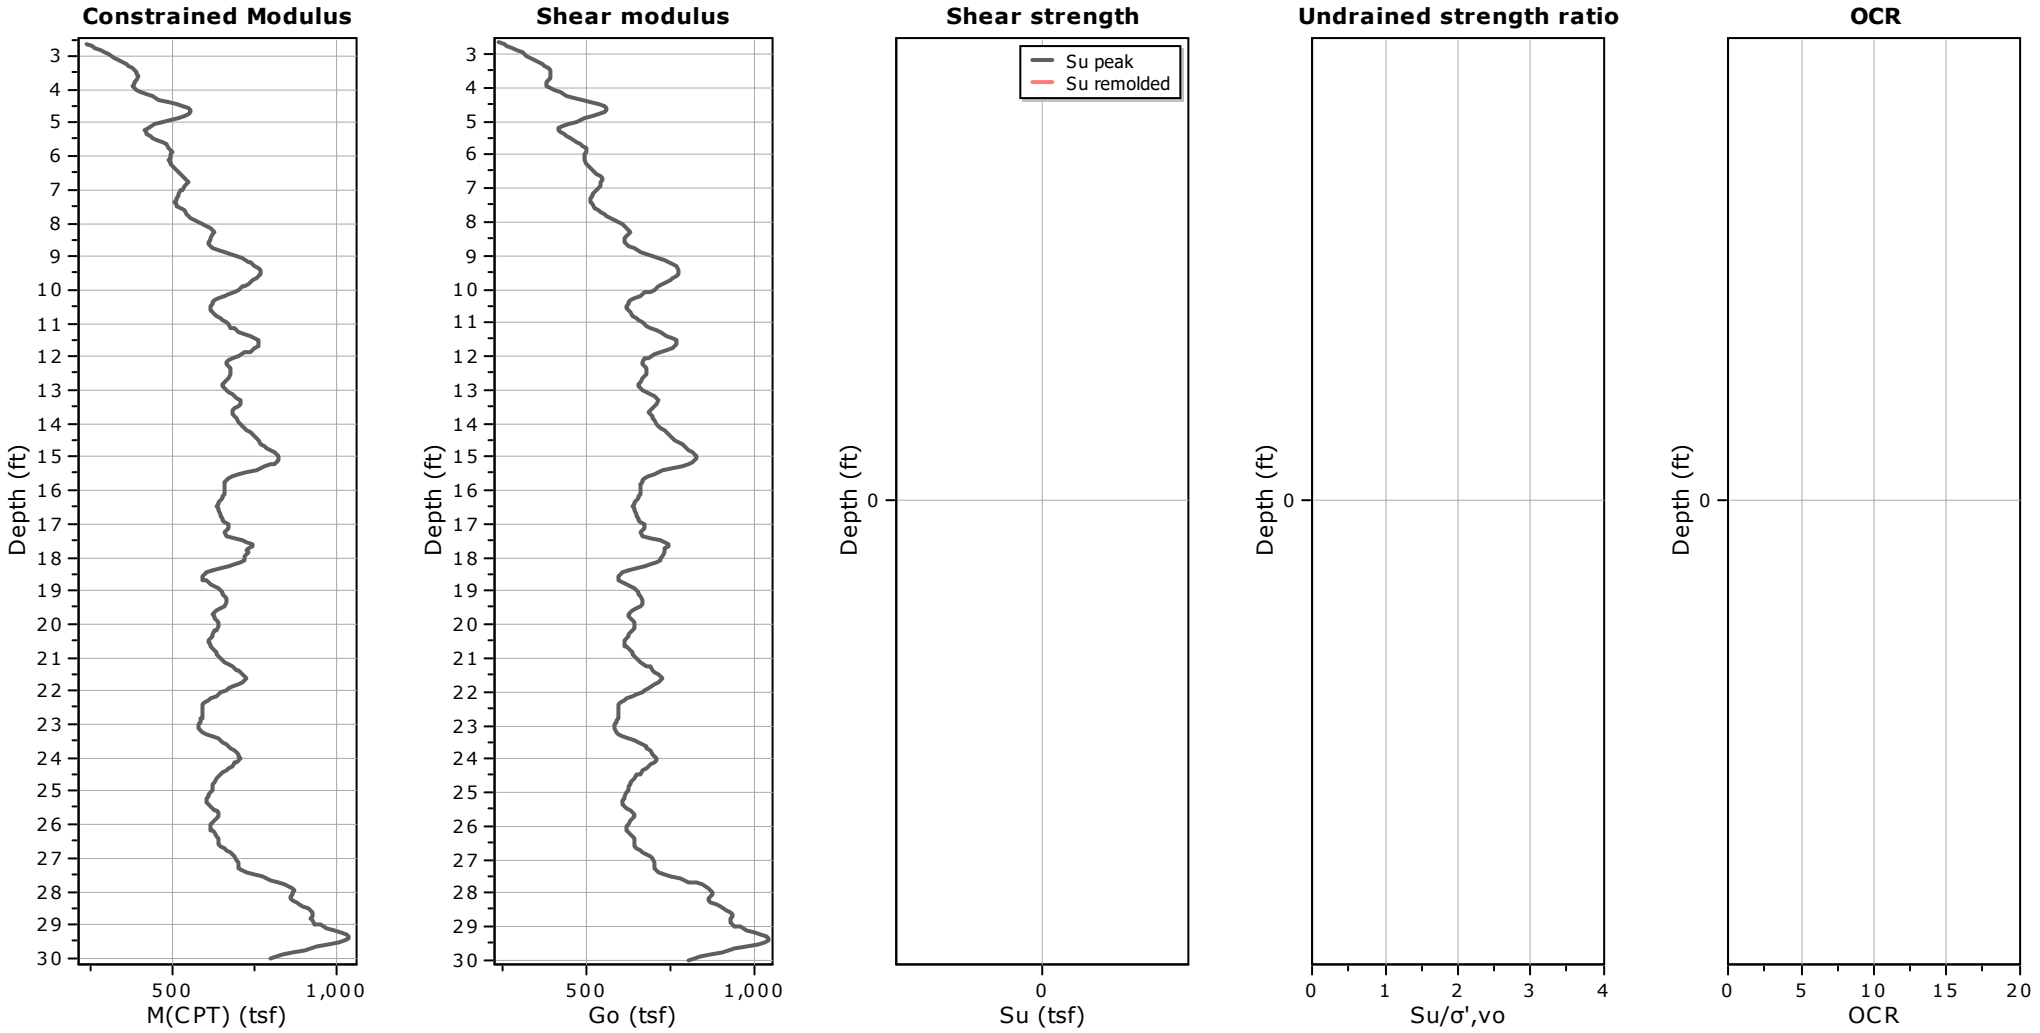


Calculation parameters

Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14
OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-18
Total depth: 30.00 ft, Date: 12/21/2022
Surface Elevation: 82.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

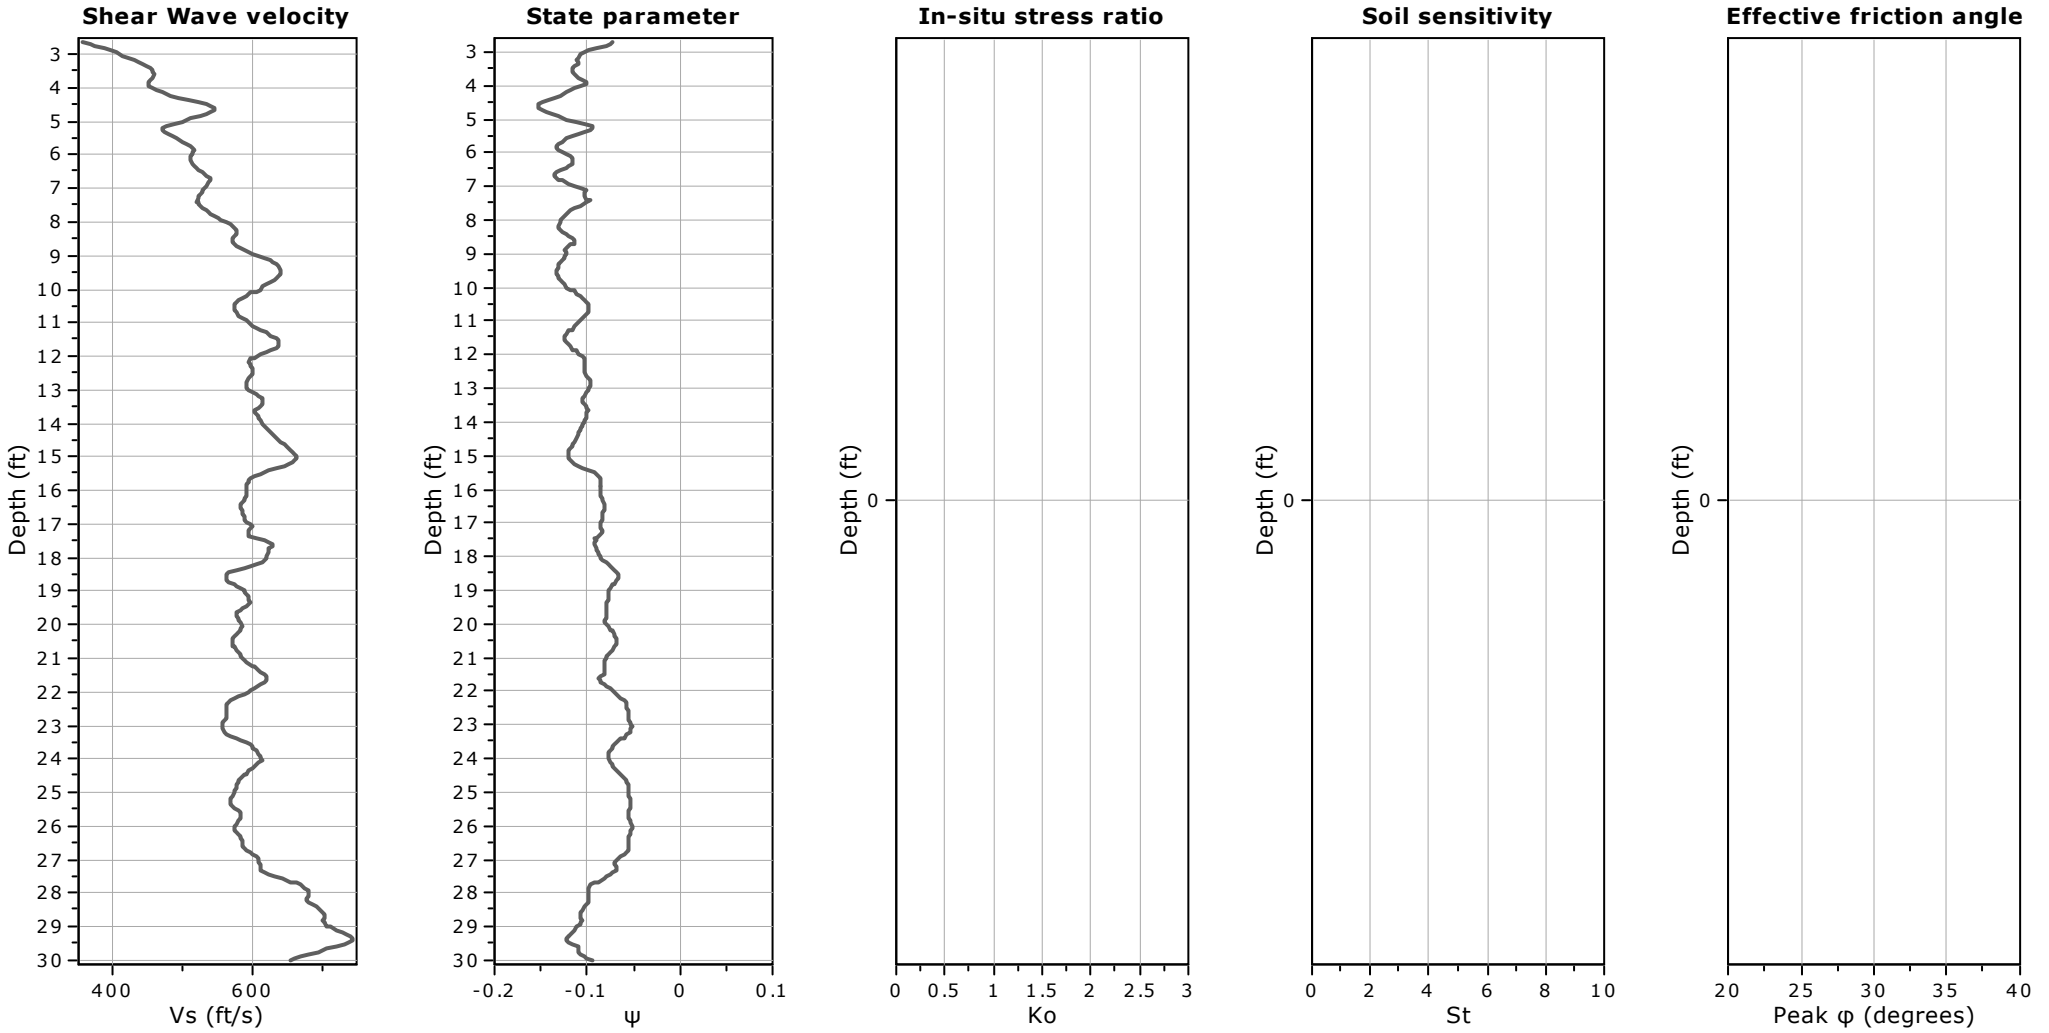

Calculation parameters


Soil Sensitivity factor, N_S: 7.00

User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-19
Total depth: 28.56 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

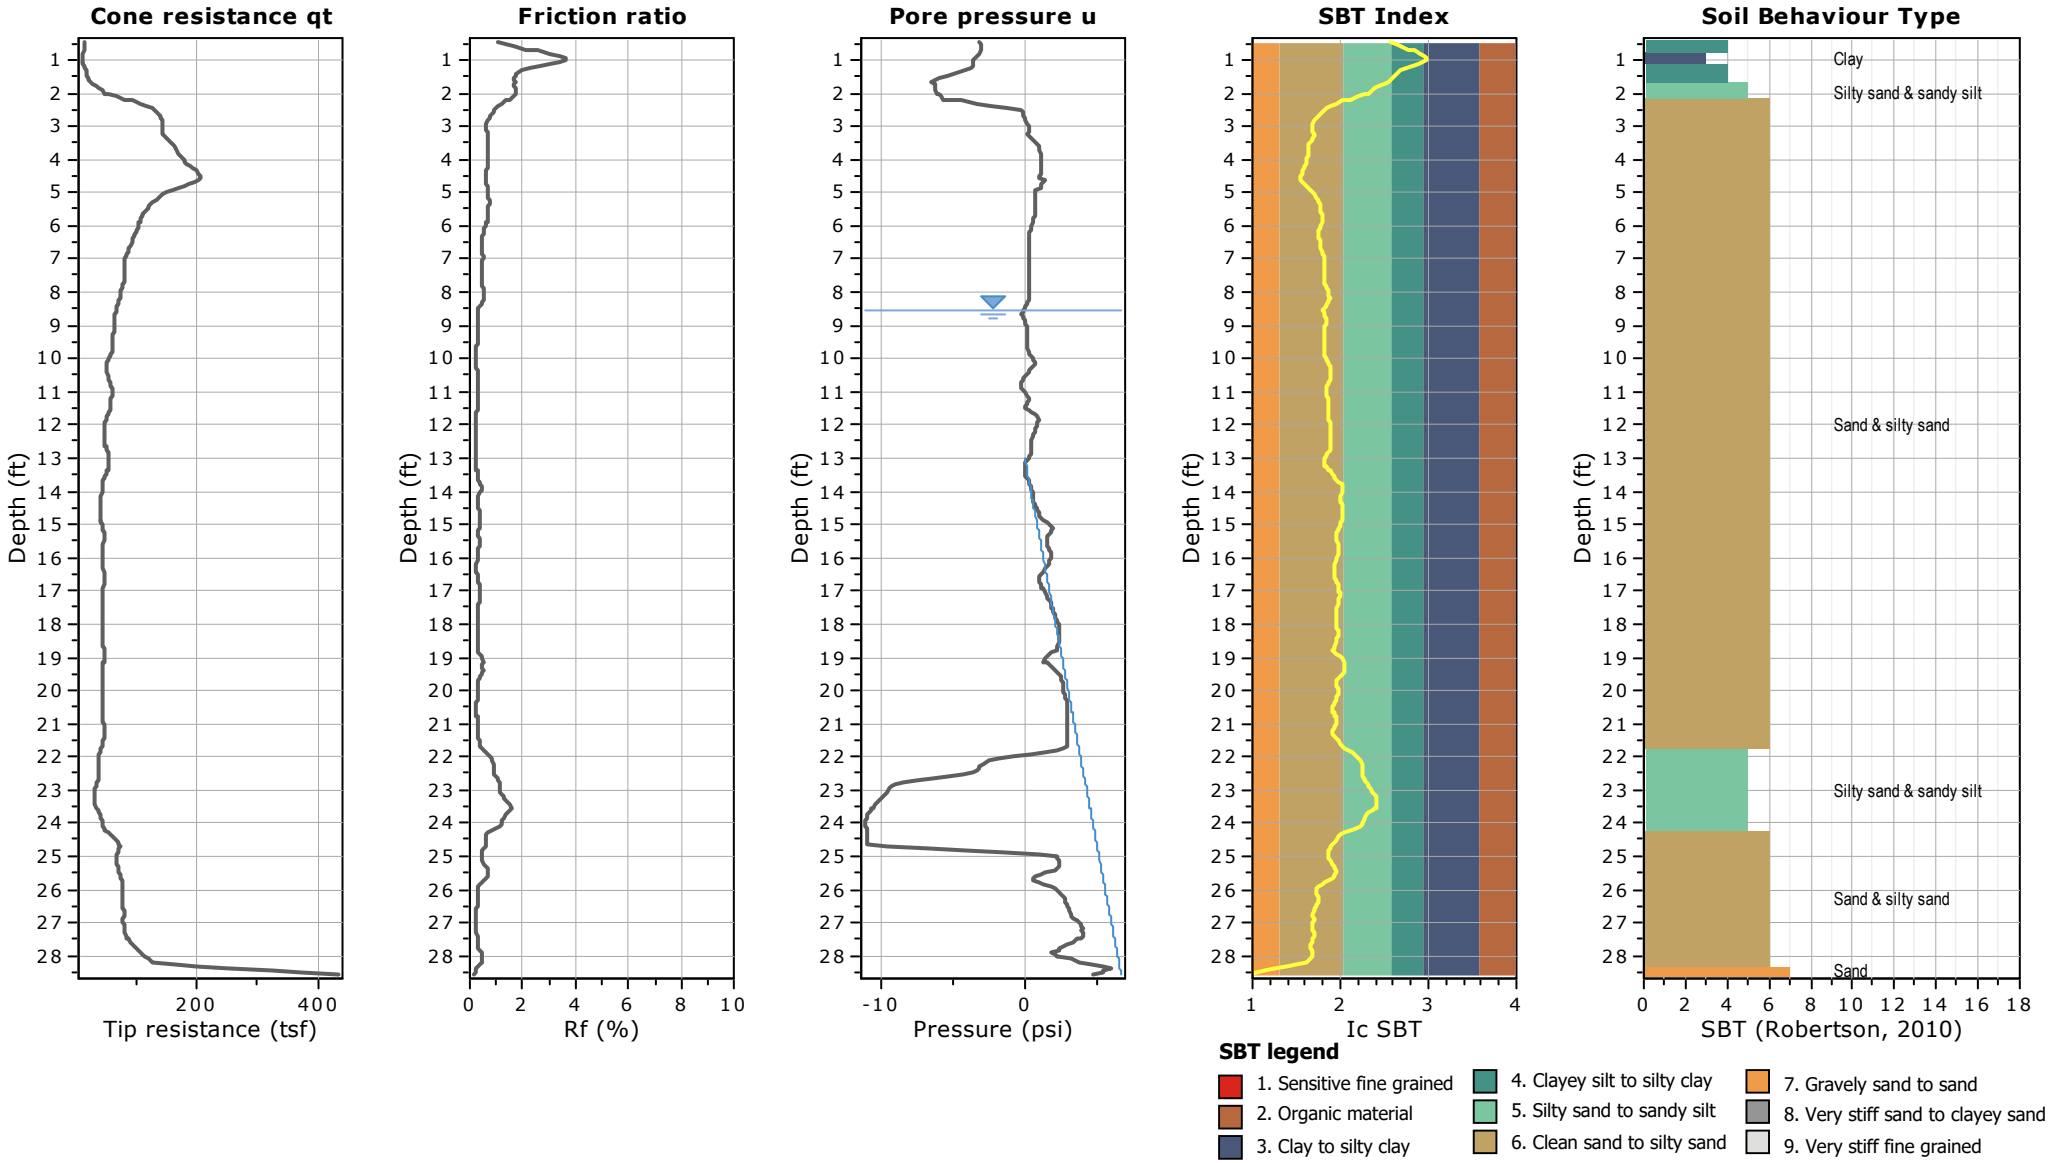



GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com


CPT: CPT-19
Total depth: 28.56 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

Updated SBTn plots

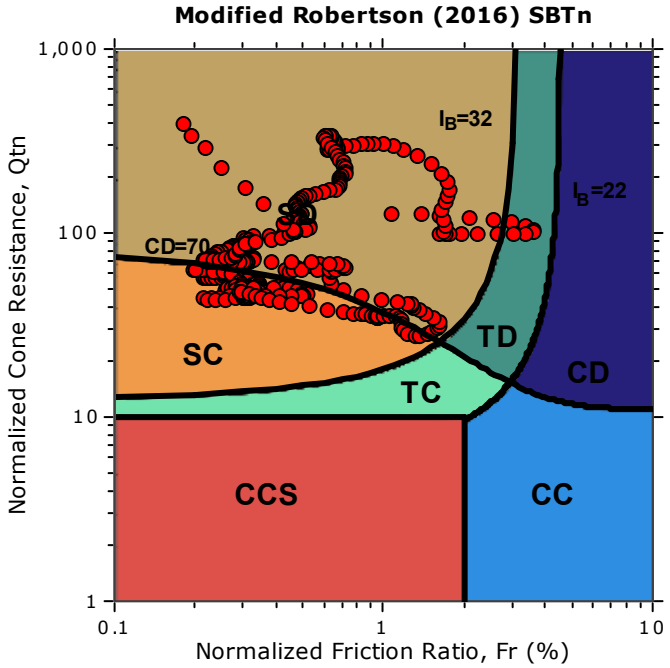

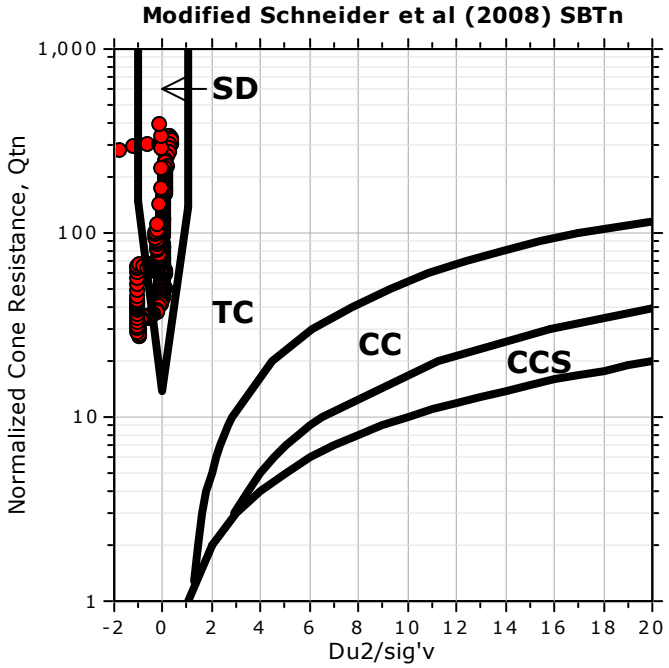

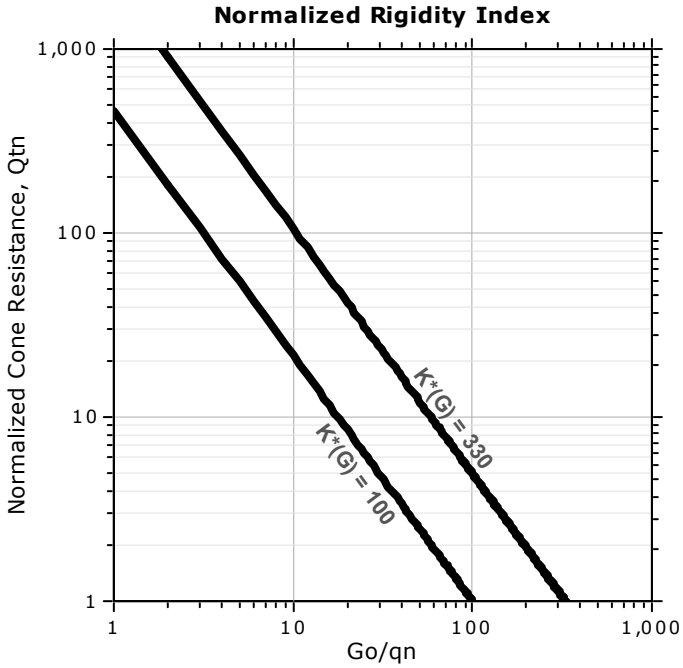


CCS: Clay-like - Contractive - Sensitive
CC: Clay-like - Contractive
CD: Clay-like - Dilative
TC: Transitional - Contractive
TD: Transitional - Dilative
SC: Sand-like - Contractive
SD: Sand-like - Dilative

K(G) > 330: Soils with significant microstructure (e.g. age/cementation)

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-19
Total depth: 28.56 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

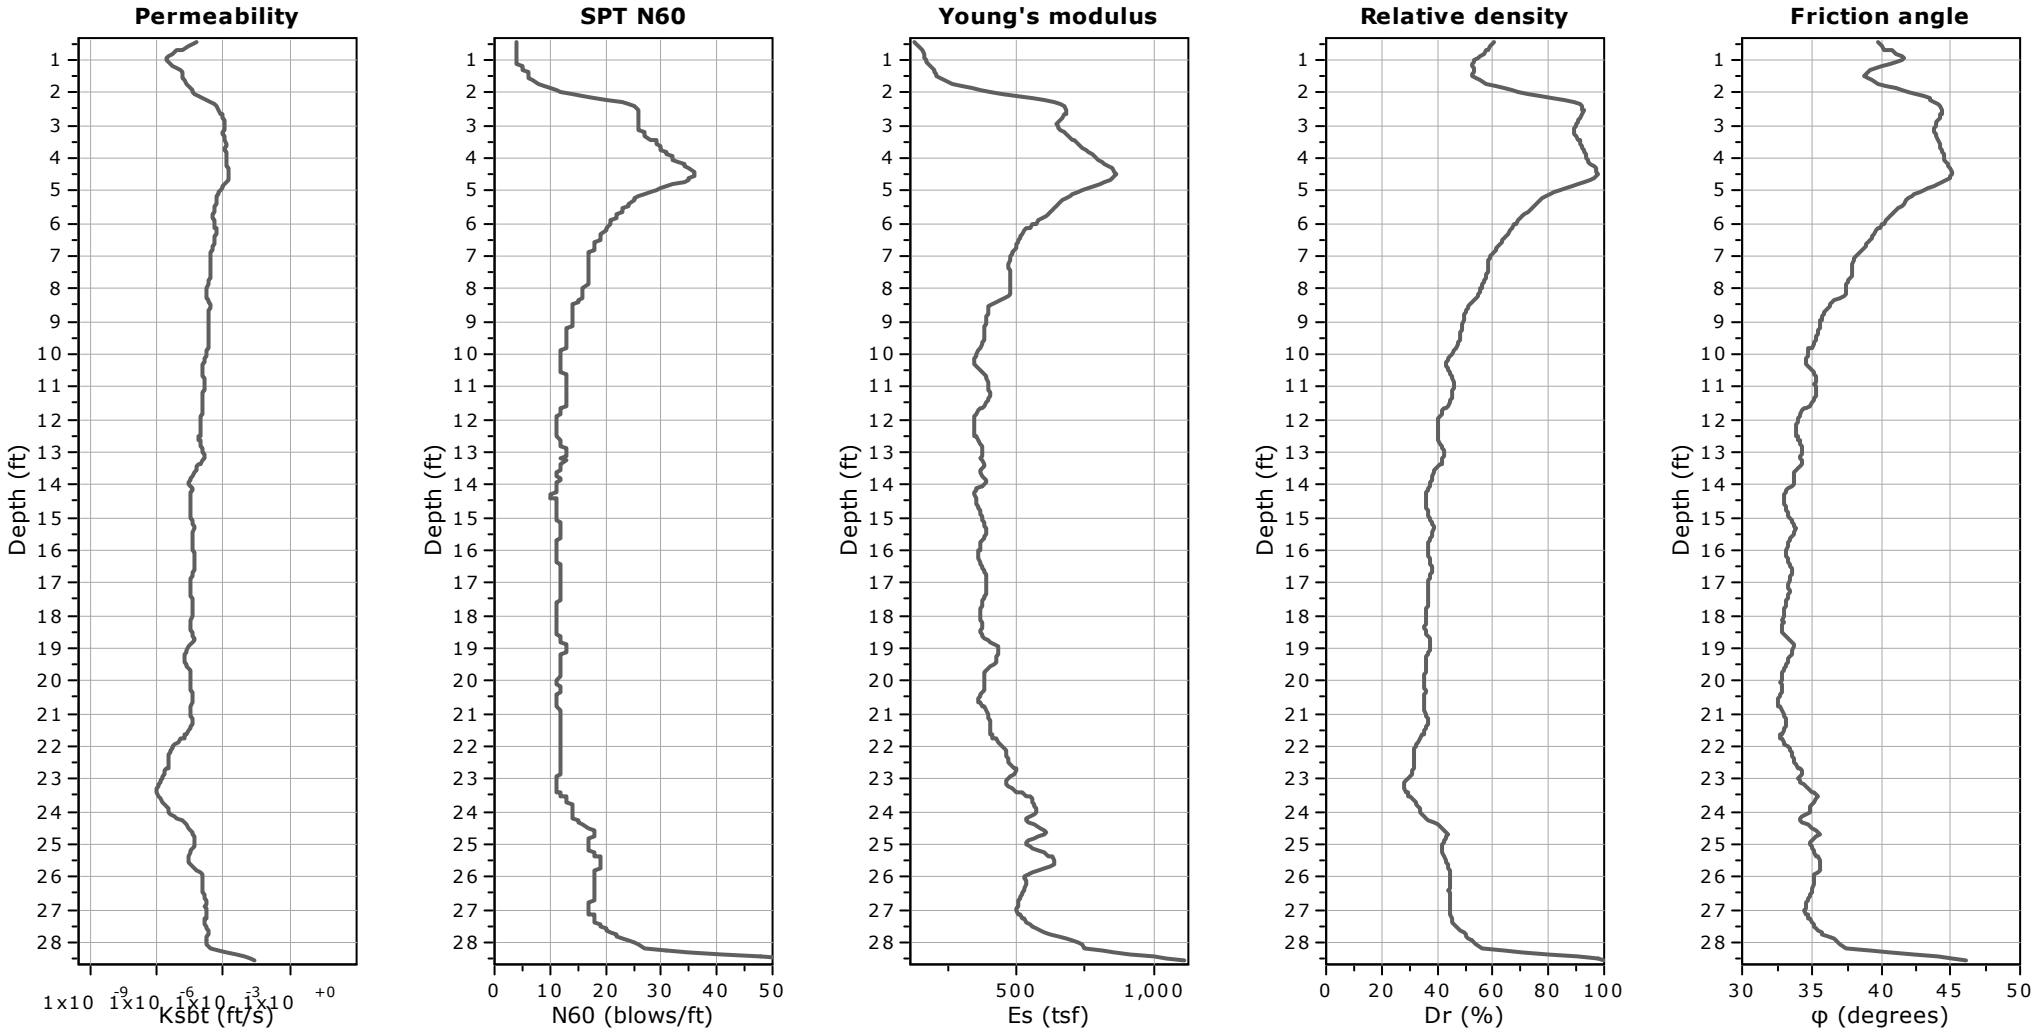


Calculation parameters

Permeability: Based on SBT_n
SPT N_{60}: Based on I_c and q_t
Young's modulus: Based on variable alpha using I_c (Robertson, 2009)
Relative density constant, C_{Dr}: 350.0
Phi: Based on Kulhawy & Mayne (1990)
User defined estimation data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-19
Total depth: 28.56 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

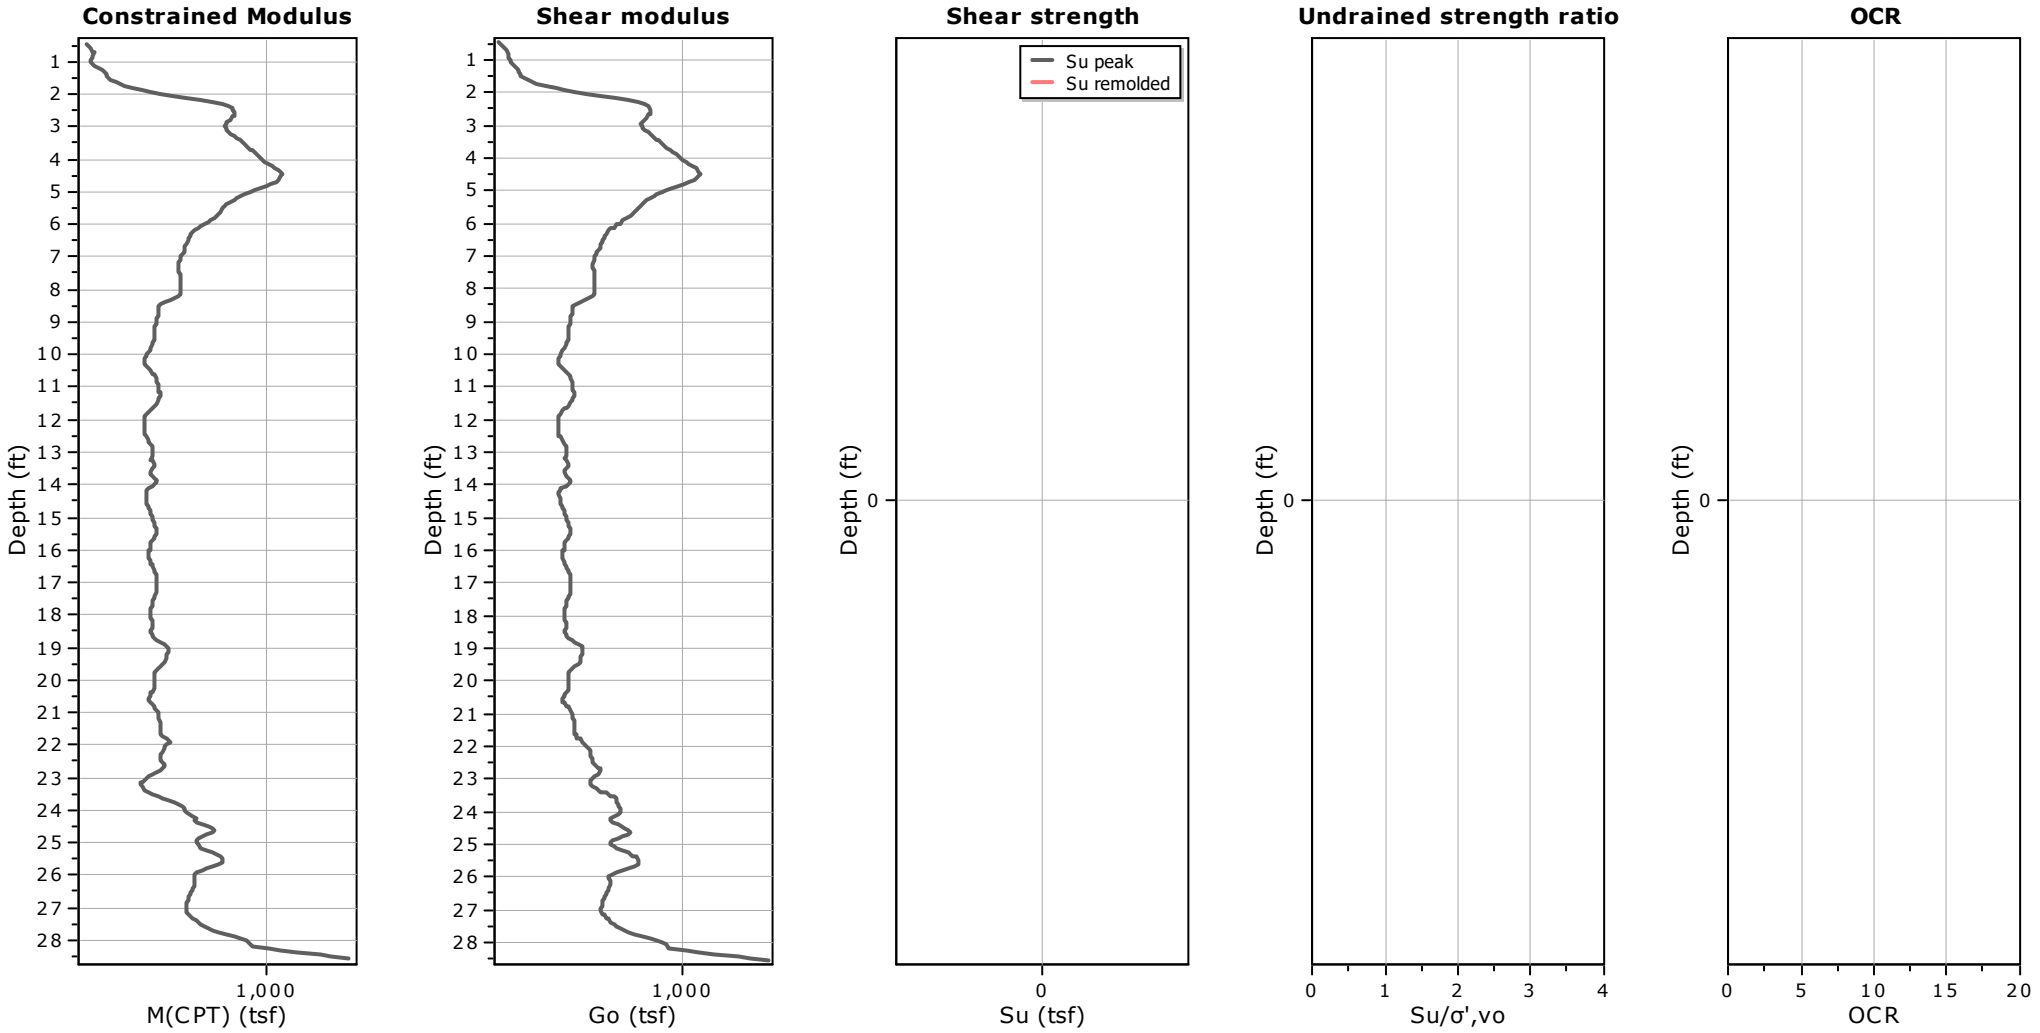

Calculation parameters


Constrained modulus: Based on variable *alpha* using I_c and Q_{tn} (Robertson, 2009)
Go: Based on variable *alpha* using I_c (Robertson, 2009)
Undrained shear strength cone factor for clays, N_{kt}: 14

OCR factor for clays, N_{kt}: 0.33
User defined estimation data
Flat Dilatometer Test data

GEO-TECHNOLOGY ASSOCIATES, INC.
GEOTECHNICAL & ENVIRONMENTAL CONSULTANTS
18 Boulden Circle, Suite 36
New Castle, DE 19720
(302) 326-2100
www.gtaeng.com

CPT: CPT-19
Total depth: 28.56 ft, Date: 12/20/2022
Surface Elevation: 80.00 ft
Cone Type: Hogentogler
Cone Operator: D. Hans

Project: **New Hodgson Vo-Tech School**
Location: **New Castle County, Delaware**

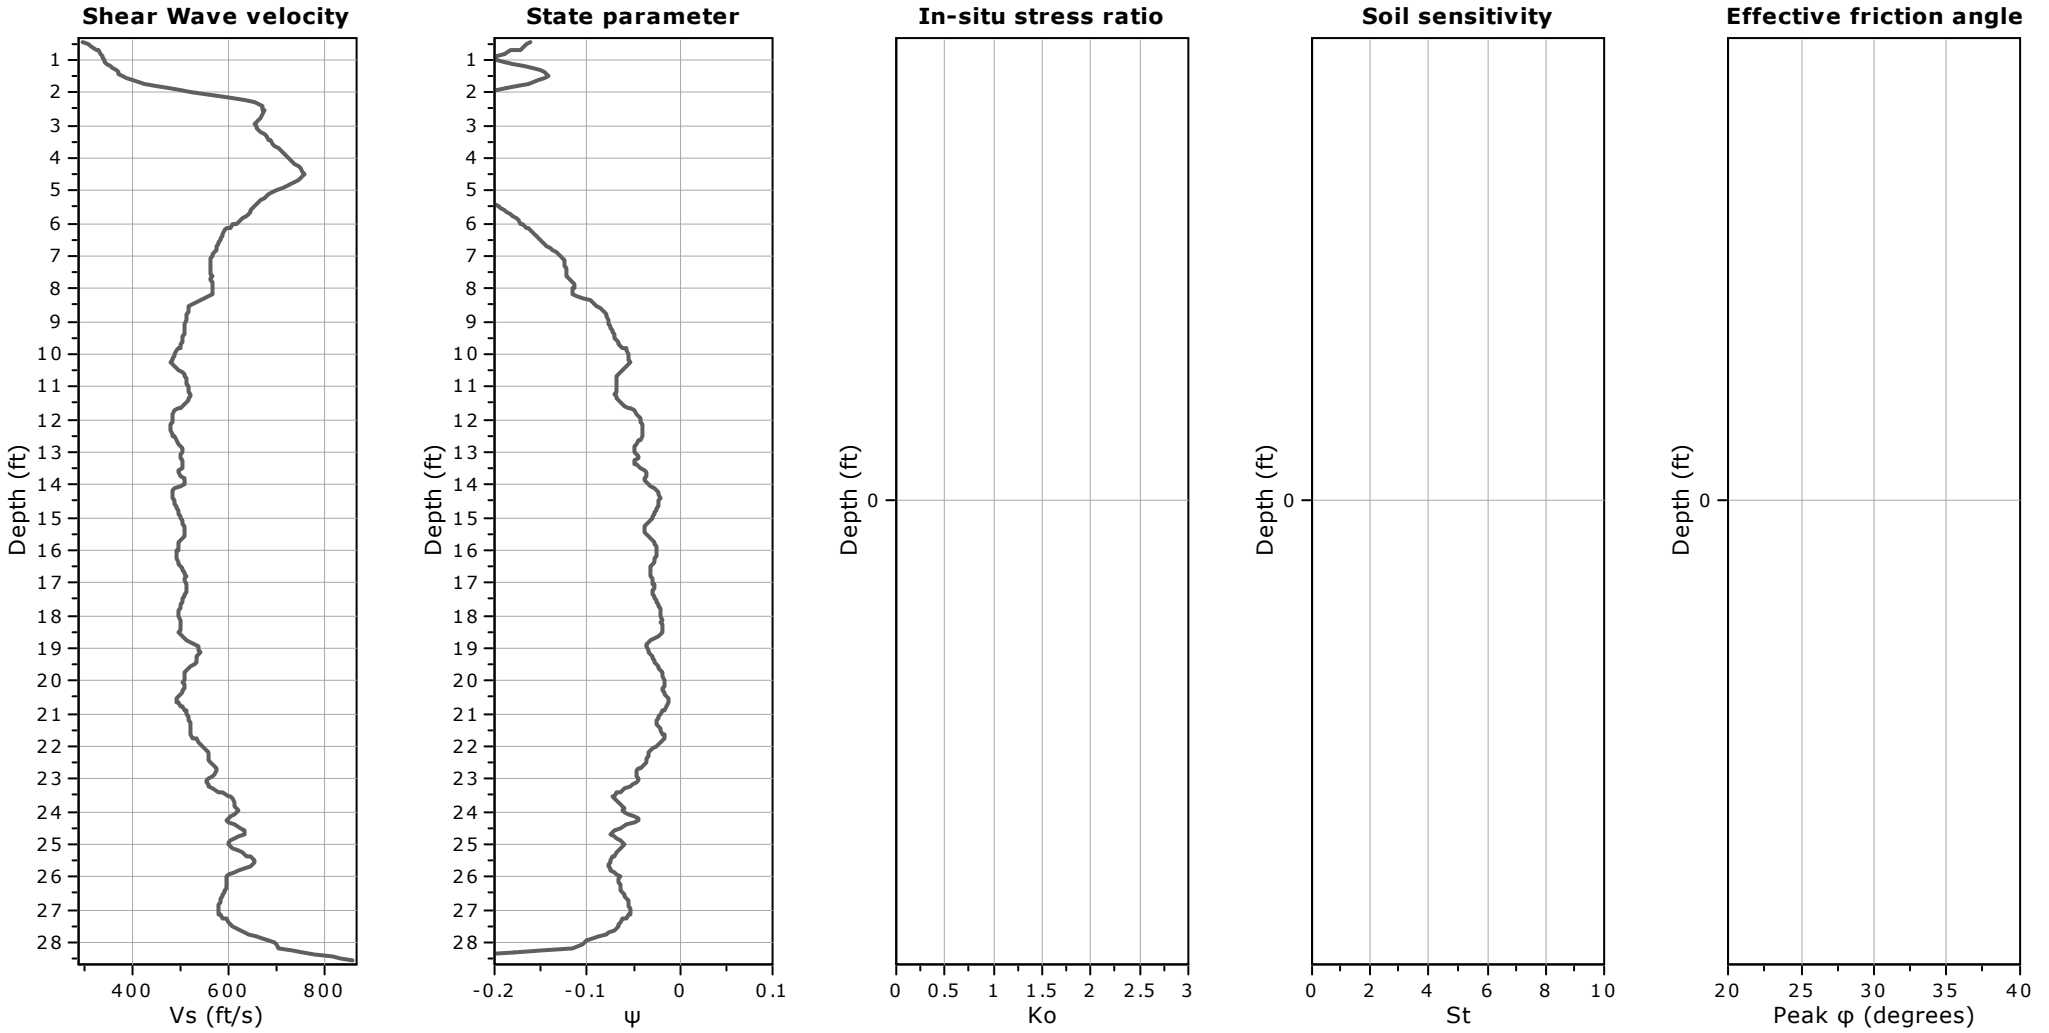


Calculation parameters

Soil Sensitivity factor, N_S: 7.00

User defined estimation data

APPENDIX C

Particle Size Distribution Report

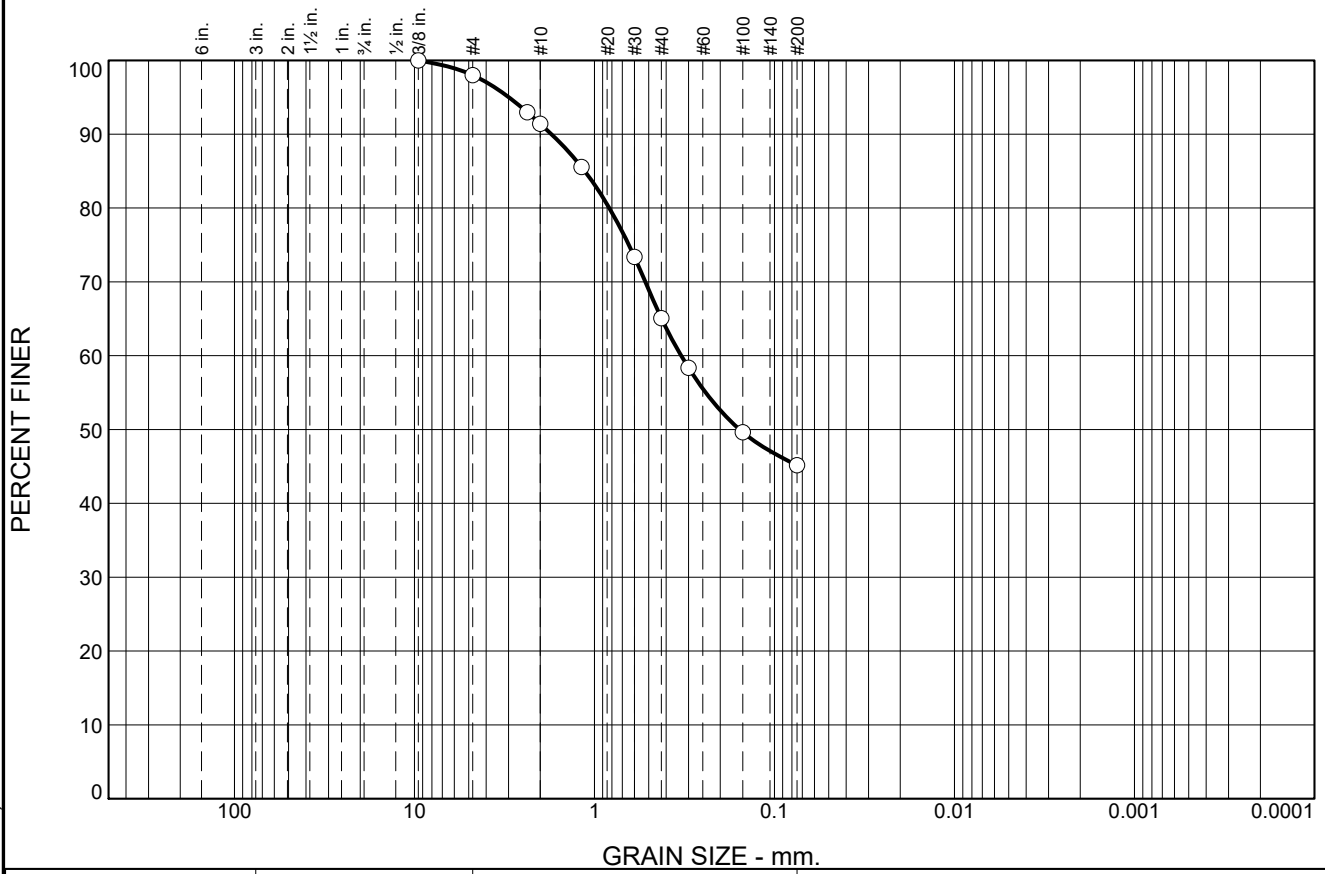

% +3"	% Gravel		% Sand			% Fines	
	Coarse	Fine	Coarse	Medium	Fine	Silt	Clay
0.0	0.0	2.0	6.6	26.3	19.9	45.2	

SIEVE SIZE	PERCENT FINER	SPEC.* PERCENT	PASS? (X=NO)
.375	100.0		
#4	98.0		
#8	93.0		
#10	91.4		
#16	85.6		
#30	73.4		
#40	65.1		
#50	58.4		
#100	49.6		
#200	45.2		

* (no specification provided)

Soil Description

Brown, Clayey SAND

Atterberg Limits

PL= 17 LL= 29 PI= 12 NM= 15.0

Coefficients

D_{90}= 1.7349 D_{85}= 1.1320 D_{60}= 0.3301
D_{50}= 0.1562 D_{30}= D_{15}=
D_{10}= C_u= C_c=

Classification

USCS= SC AASHTO= A-6(2)

Remarks

Source of Sample: B-10 **Depth:** 4.0
Sample Number: S-3

Date: 01/13/2023

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720


Client: New Castle County Vo-Tech School District
Project: NCCVT New Hodgson Vo-Tech High School

Project No: 220791 **Figure** 3

ASTM Specifications performed may include D422, D421, D6913, D2216, D2217, and D4318.

Tested By: A. Veith **Checked By:** M. McDonough

Particle Size Distribution Report

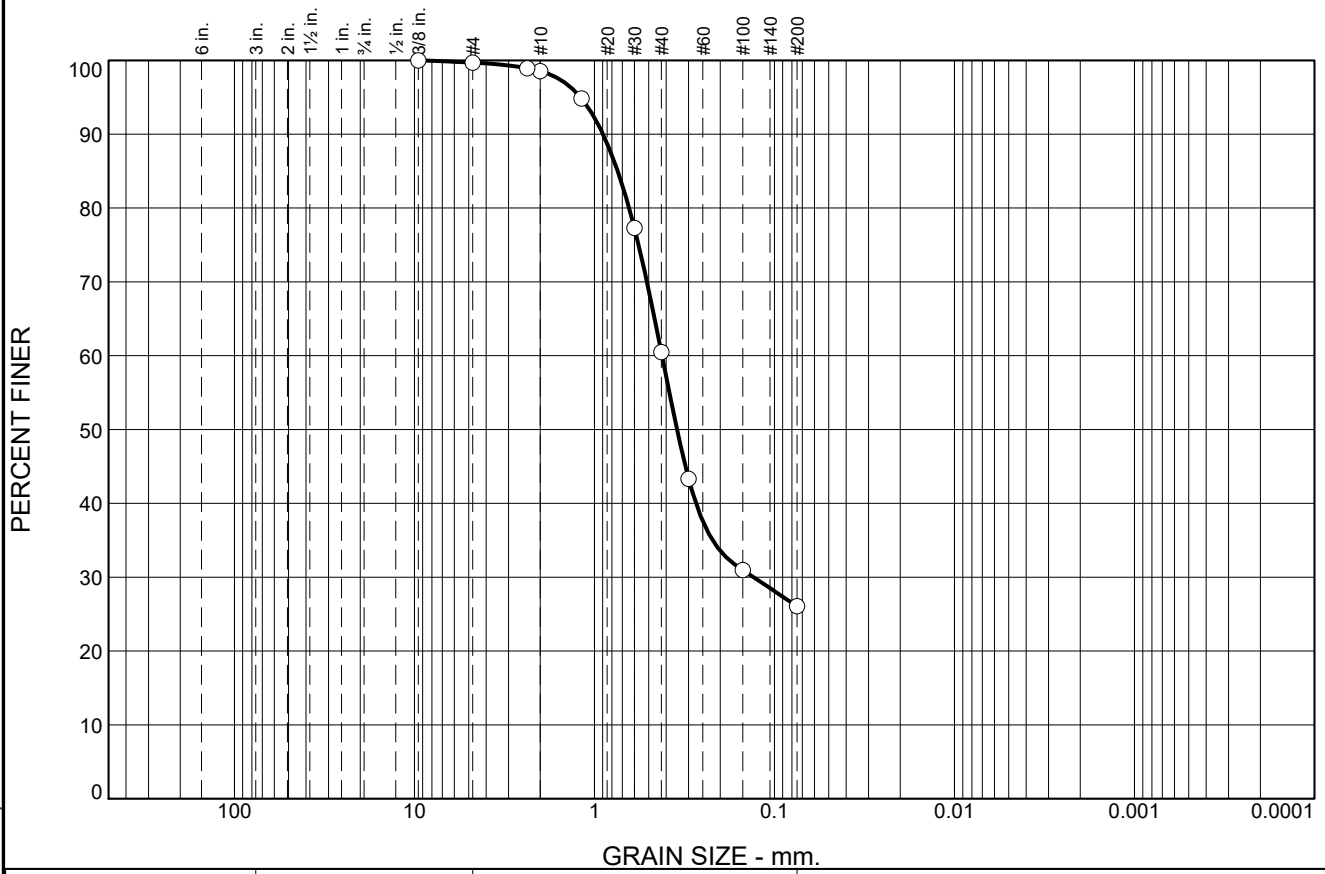

% +3"	% Gravel		% Sand			% Fines	
	Coarse	Fine	Coarse	Medium	Fine	Silt	Clay
0.0	0.0	0.3	1.2	38.0	34.4	26.1	

SIEVE SIZE	PERCENT FINER	SPEC.* PERCENT	PASS? (X=NO)
.375	100.0		
#4	99.7		
#8	98.9		
#10	98.5		
#16	94.8		
#30	77.3		
#40	60.5		
#50	43.3		
#100	31.0		
#200	26.1		

* (no specification provided)

Soil Description

Orange, Clayey SAND

Atterberg Limits

PL= 20 LL= 32 PI= 12 NM= 15.0

Coefficients

D_{90}= 0.8960 D_{85}= 0.7425 D_{60}= 0.4212
D_{50}= 0.3480 D_{30}= 0.1308 D_{15}=
D_{10}= C_u= C_c=

Classification

USCS= SC AASHTO= A-2-6(0)

Remarks

Source of Sample: B-14 **Depth:** 2.0
Sample Number: S-2

Date: 01/13/2023

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720


Client: New Castle County Vo-Tech School District
Project: NCCVT New Hodgson Vo-Tech High School

Project No: 220791 **Figure** 4

ASTM Specifications performed may include D422, D421, D6913, D2216, D2217, and D4318.

Tested By: A. Veith **Checked By:** M. McDonough

Particle Size Distribution Report

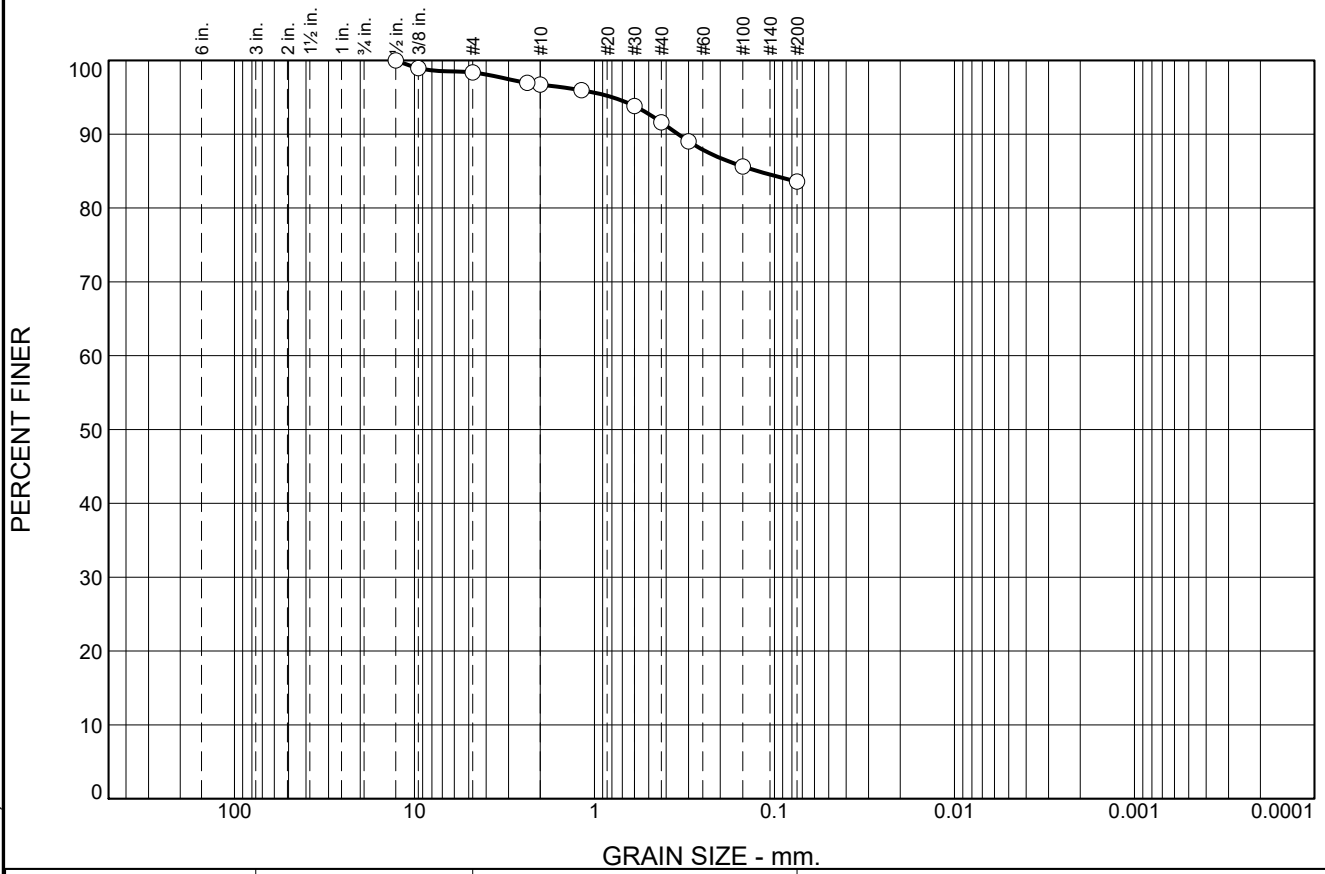

% +3"	% Gravel		% Sand			% Fines	
	Coarse	Fine	Coarse	Medium	Fine	Silt	Clay
0.0	0.0	1.6	1.7	5.1	8.0	83.6	

SIEVE SIZE	PERCENT FINER	SPEC.* PERCENT	PASS? (X=NO)
.5	100.0		
.375	99.0		
#4	98.4		
#8	97.0		
#10	96.7		
#16	96.0		
#30	93.8		
#40	91.6		
#50	89.0		
#100	85.6		
#200	83.6		

* (no specification provided)

Soil Description

Brown, Lean CLAY with sand

Atterberg Limits

PL= 19 LL= 29 PI= 10 NM= 18.2

Coefficients

D_{90}= 0.3433 D_{85}= 0.1239 D_{60}=
D_{50}= D_{30}= D_{15}=
D_{10}= C_u= C_c=

Classification

USCS= CL AASHTO= A-4(7)

Remarks

Source of Sample: INF-15 Bulk **Depth:** 0.0 to 5.0 feet

Date: 02/07/2023

GEO-TECHNOLOGY ASSOCIATES, INC.
18 Boulden Circle, Suite 36
New Castle, DE 19720

Client: New Castle County Vo-Tech School District
Project: NCCVT New Hodgson Vo-Tech High School

Project No: 220791 **Figure** 5

ASTM Specifications performed may include D422, D421, D6913, D2216, D2217, and D4318.

Tested By: A. Veith **Checked By:** M. McDonough

MOISTURE DENSITY RELATIONSHIP REPORT
ASTM D 698 Method B Standard

Project No.: 220791 **Date:** 02/07/2023

Project: NCCVT New Hodgson Vo-Tech High School

Client: New Castle County Vo-Tech School District

Source of Sample: INF-15 Bulk **Depth:** 0.0 to 5.0 feet

Remarks:

MATERIAL DESCRIPTION

Description: Brown, Lean CLAY with sand

Classifications - **USCS:** CL **AASHTO:** A-4(7)

Nat. Moist. = 18.2 % **Sp.G. =** 2.6

Liquid Limit = 29 **Plasticity Index =** 10

% < No.200 = 83.6 %

TEST RESULTS
Maximum dry density = 114.6 pcf
Optimum moisture = 14.6 %

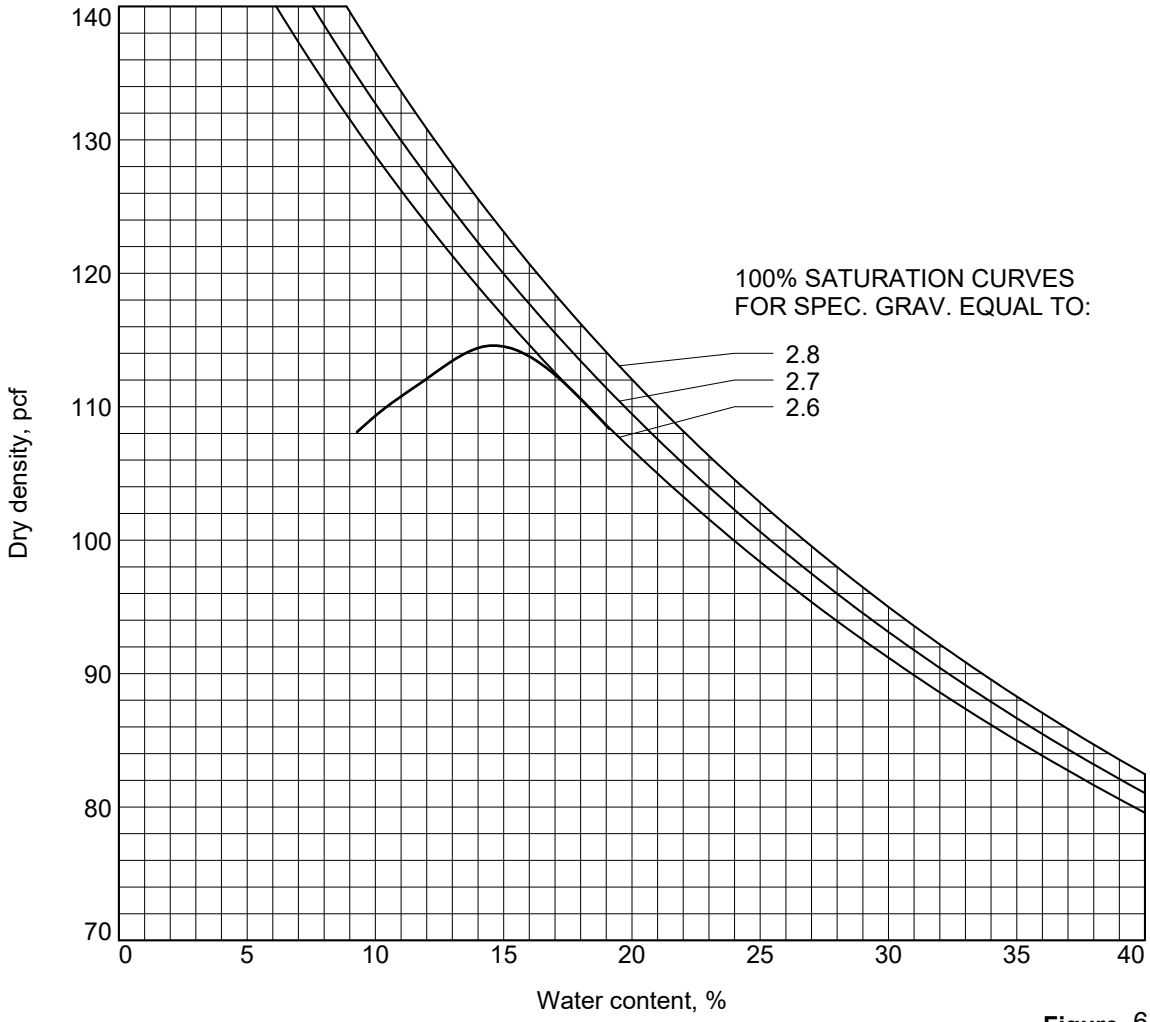


Figure 6

Geo-Technology Associates, Inc.

ASTM Specifications performed may include D422, D421, D6913, D2216, D2217, and D4318.

Tested By: A. Veith **Checked By:** M. McDonough

CONTRACT NO: D-01 UNIT MASONRY

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $40,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____($_____)

Alternate No. 9: Provide ground Face CMU at exterior watertable.

Add/Deduct _____($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____

(Authorized Signature)

(SEAL)

_____

(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Masonry			
2.	Sprayed Insulation			
3.				
4.				
5.				

6. NO ADDITIONAL ENTRIES REQUIRED

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-02 MISCELLANEOUS METALS, STAIRS, AND RAILS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $20,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____

(Authorized Signature)

(SEAL)

_____

(Title)

Date: _____

ATTACHMENTS

Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Miscellaneous Metals			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-03 EXTERIOR STRUCTURAL STUD ASSEMBLY

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $40,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion..

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Ext. Metal Framing/Sheathing			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-04 CARPENTRY AND GENERAL WORK

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $40,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____($_____)

Alternate No. 6: Provide 380 Salto wireless handle sets in lieu of manual locksets.

Add/Deduct _____ ($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2.

Add/Deduct _____ ($_____)

Alternate No. 13: Provide lightning protection system.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Carpentry			
2. Metal Fencing			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-05 EXTERIOR METAL PANELS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $30,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 15A: Provide custom color for window brows.

Add/Deduct _____ ($_____)

Alternate No. 15B: Provide custom color for main canopies.

Add/Deduct _____ ($_____)

Alternate No. 15C: Provide custom color for accent wall/exterior column wraps.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____

_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Metal Panels			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-06 DRYWALL AND INTERIOR METAL FRAMING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that Allowances in the amount of $175,000.00 and $30,000 have been included in the Base Bid price listed above. These allowances are to be used for scaffolding and at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Metal Framing			
2. Drywall			
3.			
4.			
5.			

6. NO ADDITIONAL ENTRIES REQUIRED

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-07 GENERAL LABOR AND CLEAN-UP

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

UNIT PRICES

Unit prices conform to applicable project specification section. Refer to the specifications for a complete description of the following Unit Prices:

	Add	Deduct	Add	Deduct
1. Addition or deletion of manhours from base contract.	_____	_____	_____	_____

NOTE: The difference in price between Add and Deduct in the above Unit Prices should not exceed fifteen percent (10%).

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	General Labor			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-08 ROOFING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $35,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Add exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 13: Provide lightning protection system.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Roofing			
2.			
3.			
4.			
5.			

6. NO ADDITIONAL ENTRIES REQUIRED

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-09 FIREPROOFING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $20,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 5: Provide Acoustical Sprayed insulation in rooms as indicated.

Add/Deduct _____($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Fireproofing			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-10 JOINT SEALANTS AND PREFORMED JOINT ASSEMBLIES

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that Allowances in the amount of $15,000.00 and $7,500 have been included in the Base Bid price listed above. These allowances are to be used for materials to be utilized for misc. fire safing and fire sealants and the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Caulking & Sealants			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-11 HOLLOW METAL, WOOD DOORS, AND FINISH HARDWARE

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Doors/Frames/Hardware			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-12 OVERHEAD COILING DOORS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL) _____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Overhead Doors			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-13 CURTAIN WALL/GLAZING/STOREFRONTS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $35,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Glass/Framing/Glazing			
2. Joint Sealants			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-14 TILING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $15,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Tiling			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____**.**

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-15 ACOUSTICAL AND SPECIALTY CEILINGS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $20,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2

Add/Deduct _____ ($_____)

Alternate No. 16: Provide 2′ x 2′ beveled tegular acoustical ceiling tile in lieu of 2′ x 2′ square lay-in where ACT -1 is indicated

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. ACT Ceilings & Grid			
2. Acoustical Panels			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-16 FLOORING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES
We/I confirm that an Allowances in the amount of $15,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES
Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 4A: Provide terrazzo and base in the following spaces: Lobby A102, Lobby E101, and Dining E103. Delete quartz tile and resilient base in the following spaces: Lobby A102, Lobby E101, and Dining E103.

Add/Deduct _____ ($_____)

Alternate No. 4B: Provide terrazzo and base in the following spaces: Corridors A100, B100A, C100B, C100A, D100A, D100B, and Lobby D117. Delete Quartz tile and resilient base in the following spaces: Corridors A100, B100A, C100B, C100A, D100A, D100B, and Lobby D117.

Add/Deduct _____ ($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____

(Authorized Signature)

(SEAL)

_____

(Title)

Date: _____

ATTACHMENTS

Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Flooring			
2.	Access Flooring			
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-17 RESILIENT ATHLETIC FLOORING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $15,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Resilient Athletic Flooring			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-18 RESILIENT MATRIX TERRAZZO FLOORING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 4A: Provide terrazzo and base in the following spaces: Lobby A102, Lobby E101, and Dining E103. Delete quartz tile and resilient base in the following spaces: Lobby A102, Lobby E101, and Dining E103.

Add/Deduct _____($_____)

Alternate No. 4B: Provide terrazzo and base in the following spaces: Corridors A100, B100A, C100B, C100A, D100A, D100B, and Lobby D117. Delete Quartz tile and resilient base in the following spaces: Corridors A100, B100A, C100B, C100A, D100A, D100B, and Lobby D117.

Add/Deduct _____ ($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Resinous Terrazzo			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-19 FLUID APPLIED FLOORING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Resinous Flooring			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____**.**

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-20 PAINT AND VWC

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $20,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Painting			
2.			
3.			
4.			
5.			

6. NO ADDITIONAL ENTRIES REQUIRED

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-21 WOOD STRIP FLOORING – GYM FLOORING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Wood Gym Flooring			
2. Wood Stage Flooring			
3.			
4.			
5.			

6. NO ADDITIONAL ENTRIES REQUIRED

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-22 SPECIALTIES

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $20,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 15A: Provide custom color for window brows.

Add/Deduct _____ ($_____)

Alternate No. 15B: Provide custom color for main canopies.

Add/Deduct _____ ($_____)

Alternate No. 15C: Provide custom color for accent wall/exterior column wraps.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Misc Specialty Div 10			
2. Metal Canopies			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-23 FOOD SERVICE EQUIPMENT

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $15,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Food Service			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-24 WINDOW SHADES AND ROLLER SHADES

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Window Shades			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-25 LAMINATE CLAD CASEWORK, COUNTERTOPS, AND SILLS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $15,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Laminate Clad Casework			
2.				
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-26 STAGE RIGGING, DRAPERIES AND LIGHTING ACCESSORIES

BID FORM

For Bids Due: _____ To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES
We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Stage Rigging, Draperies and Lighting			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-27 FIXED AUDITORIUM SEATING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Fixed Auditorium Seating			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____**.**

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-28 TELESCOPING BLEACHERS AND PLATFORMS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Telescoping Bleachers/Platforms			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-29 HYDRAULIC HOLELESS PASSENGER ELEVATOR

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.:_____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $10,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Elevators			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-30 FIRE PROTECTION

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $20,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Fire Sprinkler			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-31 PLUMBING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $75,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 11: Provide freeze protection pumps on (FPP-1-32, 34, 35, 37, 38, 40, 42, 44, 46, 49-61.)

Add/Deduct _____ ($_____)

Alternate No. 12: Provide rotary screw compressors and tanks for all shop compressed air systems.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____

(Authorized Signature)

(SEAL)

_____

(Title)

Date: _____

ATTACHMENTS

Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Plumbing			
2. Insulation			
3.			
4.			
5.			

6. NO ADDITIONAL ENTRIES REQUIRED

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-32 MECHANICAL PIPING - HVAC

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that Allowances in the amount of $75,000.00 and $200,000 have been included in the Base Bid price listed above. These allowances are to be used to provide temporary heating equipment and maintenance and to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 10: Provide additional costs, if any, to provide ATC system by Modern Controls.

Add/Deduct _____ ($_____)

Alternate No. 11: Provide freeze protection pumps on (FPP-1-32, 34, 35, 37, 38, 40, 42, 44, 46, 49-61.)

Add/Deduct _____ ($_____)

Alternate No. 12: Provide rotary screw compressors and tanks for all shop compressed air systems.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Mechanical Piping			
2. HVAC Ductwork			
3. Insulation			
4. ATC			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-33 TESTING, ADJUSTING, AND BALANCING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder:_____

Bidder Address:_____

_____

Contact Name:_____E-Mail Address: _____

Delaware Business License No.:_____Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____)_____-_____ Fax No.: (_____)_____- _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____($_____)

ALTERNATES
Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct_____($_____)

I/We acknowledge Addendums numbered_____and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By_____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness:_____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Testing, Adjusting, Balancing			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date_____.

All the terms and conditions of Contract:_____have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this_____day of_____20____.

My Commission expires_____. NOTARY PUBLIC_____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this_____day of_____20_____.

My Commission expires_____. NOTARY PUBLIC_____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this_____day of_____20____.

My Commission expires_____. NOTARY PUBLIC_____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-34 ELECTRICAL, LIGHTING, AND FIRE ALARM SYSTEMS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $75,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 6: Provide 380 Salto wireless handle sets in lieu of manual locksets.

Add/Deduct _____ ($_____)

Alternate No. 7: Provide monument stair #5 complete.

Add/Deduct _____ ($_____)

Alternate No. 11: Provide freeze protection pumps on (FPP-1-32, 34, 35, 37, 38, 40, 42, 44, 46, 49-61.)

Add/Deduct _____ ($_____)

Alternate No. 12: Provide rotary screw compressors and tanks for all shop compressed air systems.

Add/Deduct _____ ($_____)

Alternate No. 13: Provide lightning protection system.

Add/Deduct _____ ($_____)

Alternate No. 14: Provide additional costs, if any, for fire alarm system by Simplex.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1. Electrical			
2. Lighting Protection			
3. Fire Alarm System			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-35 SPECIAL SYSTEMS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES

We/I confirm that an Allowances in the amount of $30,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 3: Provide exterior shell of future tech and shop expansion.

Add/Deduct _____ ($_____)

Alternate No. 6: Provide 380 Salto wireless handle sets in lieu of manual locksets.

Add/Deduct _____ ($_____)

Alternate No. 12: Provide rotary screw compressors and tanks for all shop compressed air systems.

Add/Deduct _____ ($_____)

Alternate No. 14: Provide additional costs, if any, for fire alarm system by Simplex.

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Structured Cable			
2. Audio Video Systems			
3. Intrusion Detection System			
4. Access Control Systems			
5. Video Surveillance Systems			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-36 VERTICAL RETRACTABLE WALLS

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALTERNATES

Alternate prices conform to applicable project specification section. Refer to specifications for a complete description of the following Alternates. An "ADD" or "DEDUCT" amount is indicated by the crossed-out part that does not apply.

Alternate No. 8: Provide vertically retractable partition between room MP1 & MP2

Add/Deduct _____ ($_____)

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

Subcontractor Category	Subcontractor	Address (City & State)	Subcontractors tax-payer ID # or Delaware Business license #
1. Vertical Retractable Wall Sys			
2.			
3.			
4.			
5.			
6. NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

CONTRACT NO: D-37 MISCELLANEOUS CONCRETE AND GROUTING

BID FORM

For Bids Due: _____

To: NCCVT School District
1417 Newport Road
Wilmington, DE 19804

Name of Bidder: _____

Bidder Address: _____

_____

Contact Name: _____ E-Mail Address: _____

Delaware Business License No.: _____ Taxpayer ID No.: _____

(Other License Nos.): _____
(A copy of Bidder's Licenses must be attached to this form.)

Phone No.: (_____) _____ - _____ Fax No.: (_____) _____ - _____

The undersigned, representing that he has read and understands the Bidding Documents and that this bid is made in accordance therewith, that he has visited the site and has familiarized himself with the local conditions under which the Work is to be performed, and that his bid is based upon the materials, systems and equipment described in the Bidding Documents without exception, hereby proposes and agrees to provide all labor, materials, plant, equipment, supplies, transport and other facilities required to execute the work described by the aforesaid documents for the lump sum itemized below:

$_____ ($_____)

ALLOWANCES
We/I confirm that an Allowances in the amount of $15,000.00 have been included in the Base Bid price listed above. This allowance is to be used at the Owner and Construction Manager's discretion. All remaining allowance shall be returned to the Owner at completion.

I/We acknowledge Addendums numbered _____ and the price(s) submitted include any cost/schedule impact they may have.

This bid shall remain valid and cannot be withdrawn for sixty (60) days from the date of opening of bids, and the undersigned shall abide by the Bid Security forfeiture provisions. Bid Security is attached to this Bid (if required).

The Owner shall have the right to reject any or all bids, and to waive any informality or irregularity in any bid received.

This bid is based upon work being accomplished by the Sub-Contractors named on the list attached to this bid.

Should I/We be awarded this contract, I/We pledge to achieve substantial completion of all the work within the durations included in the BP-D bid schedule provided and Section 013216 Const. Schedule.

The undersigned represents and warrants that he has complied and shall comply with all requirements of local, state, and national laws; that no legal requirement has been or shall be violated in making or accepting this bid, in awarding the contract to him or in the prosecution of the work required; that the bid is legal and firm; that he has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken action in restraint of free competitive bidding.

Upon receipt of written notice of the acceptance of this Bid, the Bidder shall, within twenty (20) calendar days, execute the agreement in the required form and deliver the Contract Bonds, and Insurance Certificates, required by the Contract Documents.

I am/We are an Individual/a Partnership/a Corporation

By _____ Trading as _____
(Individual's / General Partner's / Corporate Name)

_____
(State of Corporation)

Business Address: _____
_____
_____
_____

Witness: _____ By: _____
(Authorized Signature)

(SEAL)

_____
(Title)

Date: _____

ATTACHMENTS
Sub-Contractor List
Non-Collusion Statement
Bid Bond
Consent of Surety
Affidavit of Employee Drug Testing Program
Affidavit of Contractor Qualifications
DBE Subcontractor List
New Castle County Contractor License
(Others as Required by Project Manuals)

SUBCONTRACTOR LIST

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b of the Delaware Code, the following subcontractor listing must accompany any bid submittal. The bidder must list **in each category** the full name and address (City & State) of the sub-contractor that the bidder will be using to perform the work and provide material for that subcontractor category. Should the bidder's listed subcontractor intend to provide any of their subcontractor category of work through a third-tier contractor, the bidder shall list that third-tier contractor's full name and address (City & State). **If the bidder intends to perform any category of work itself, it must list its full name and address.** For clarification, if the bidder intends to perform the work themselves, the bidder **may not** insert "not applicable", "N/A", "self" or anything other than its own full name and address (City & State). To do so shall cause the bid to be rejected. In addition, the failure to produce a completed subcontractor list with the bid submittal shall cause the bid to be rejected. If you have more than three (3) third-tier contractors to report in any subcontractor category, print out additional page(s) containing the appropriate category, complete the rest of your list of third-tier contractors for that category, notate the addition in parentheses as (CONTINUATION) next to the subcontractor category and an asterisk (*) next to any additional third-tier contractors, and submit it with your bid.

	Subcontractor Category	**Subcontractor**	**Address (City & State)**	**Subcontractors tax-payer ID # or Delaware Business license #**
1.	Concrete			
2.	Reinforcing Steel			
3.				
4.				
5.				
6.	NO ADDITIONAL ENTRIES REQUIRED			

NON-COLLUSION STATEMENT

This is to certify that the undersigned bidder has neither directly nor indirectly, entered into any agreement, participated in any collusion or otherwise taken any action in restraint of free competitive bidding in connection with this proposal submitted this date _____.

All the terms and conditions of Contract: _____ have been thoroughly examined and are understood.

NAME OF BIDDER: _____

AUTHORIZED REPRESENTATIVE (TYPED): _____

AUTHORIZED REPRESENTATIVE (SIGNATURE): _____

TITLE: _____

ADDRESS OF BIDDER: _____

_____

_____

E-MAIL: _____

PHONE NUMBER: _____

Sworn to and Subscribed before me this _____ day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

CONSENT OF SURETY

DATE_____

To: NCC Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

Gentlemen:

We, the _____

_____
(Surety Company's Address)

_____

a Surety Company authorized to do business in the State of Delaware hereby agrees that if

_____
(Contractor)

_____
(Address)

_____

is awarded the Contract No. _____

We will write the required Performance and/or Labor and Material Bond required by Paragraph 9 of the Instructions to Bidders.

_____
(Surety Company)

By _____
(Attorney-in-Fact)

AFFIDAVIT
OF
EMPLOYEE DRUG TESTING PROGRAM

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors implement a program of mandatory drug testing for Employees who work on Large Public Works Contracts funded all or in part with public funds.

We hereby certify that we have in place or will implement during the entire term of the contract a Mandatory Drug Testing Program for our employees on the jobsite, including subcontractors, that complies with this regulation:

Contractor/Subcontractor Name: _____

Contractor/Subcontractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of_____ 20_____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

AFFIDAVIT
OF
CONTRACTOR QUALIFICATIONS

We hereby certify that we will abide by the contractor's qualifications outlined in the construction bid specifications for the duration of the contract term.

In accordance with Title 29, Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code, after a contract has been awarded the successful bidder shall not substitute another subcontractor whose name was submitted on the Subcontractor Form except for the reasons in the statute and not without written consent from the awarding agency. Failure to utilize the subcontractors on the list will subject the successful bidder to penalties as outlined in the General Requirements Section 5.2 of the contract.

Contractor Name: _____

Contractor Address: _____

_____

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

Sworn to and Subscribed before me this _____day of _____ 20____.

My Commission expires _____. NOTARY PUBLIC _____.

THIS PAGE MUST BE SIGNED AND NOTARIZED FOR YOUR BID TO BE CONSIDERED.

DBE SUBCONTRACTOR LIST

DBE Name	DBE Address	DBE Phone Number	DBE Email address	DelDOT or OSD Registration Number	DBE Percentage of Contract	Description of Work

Total DBEs on project: _____

END OF SECTION

STATE OF DELAWARE
OFFICE OF MANAGEMENT AND BUDGET

BID BOND

KNOW ALL MEN BY THESE PRESENTS That: _____ _____of _____ in the County of _____ and State of _____as **Principal**, and _____ of _____ in the County of _____ and State of _____ as **Surety**, legally authorized to do business in the State of Delaware ("**State**"), are held and firmly unto the **State** in the sum of _____ Dollars ($_____ _____), or _____ percent not to exceed _____ _____ Dollars ($_____) of amount of bid on Contract No. _____ _____, to be paid to the **State** for the use and benefit of New Castle County Vocation Technical School District, 1417 Newport Road, Wilmington, DE 19804 for which payment well and truly to be made, we do bind ourselves, our and each of our heirs, executors, administrators, and successors, jointly and severally for and in the whole firmly by these presents.

NOW THE CONDITION OF THIS OBLIGATION IS SUCH That if the above bonded **Principal** who has submitted to the New Castle County Vocation Technical School District, 1417 Newport Road, Wilmington, DE 19804 a certain proposal to enter into this contract for the furnishing of certain material and/or services within the **State**, shall be awarded this Contract, and if said **Principal** shall well and truly enter into and execute this Contract as may be required by the terms of this Contract and approved by the New Castle County Vocation Technical School District, 1417 Newport Road, Wilmington, DE 19804 this Contract to be entered into within twenty days after the date of official notice of the award thereof in accordance with the terms of said proposal, then this obligation shall be void or else to be and remain in full force and virtue.

Sealed with _____ seal and dated this _____day of _____ in the year of our Lord two thousand and _____ (20____).

SEALED, AND DELIVERED IN THE
Presence of

_____
Name of Bidder (Organization)

Corporate Seal

By: _____
Authorized Signature

Attest _____

_____
Title

_____
Name of Surety

Witness:_____ By: _____

_____
Title

SECTION 005200 - AGREEMENT

1. SUMMARY

A. The Agreement Form for this Project is the American Institute of Architects Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition, AIA Document A132 – 2019 as modified by the Owner's standard amendment to the A132.

B. A copy of AIA Document A132 - 2019 Edition is bound into this Project Manual following this page.

1. Under Article 5.1.4.4 add the following:

"Upon completion of the work under the Contract, the Owner may release 60% of the amount then retained. The balance of the amount retained will be held until:

a. All reports required of the Contract are received;
b. All Subcontractors in trades listed on the Bid Form are paid by the Contractor, unless the amount owed to the Subcontractor is disputed, in which case the Owner may withhold 150% of the amount withheld by the Contractor in its dispute with the Subcontractor; and
c. Final payment is authorized by the Owner."

END OF SECTION

DRAFT

AIA® Document A132® – 2019

Standard Form of Agreement Between Owner and Contractor,
Construction Manager as Adviser Edition

AGREEMENT made as of the « » day of « » in the year « »
(In words, indicate day, month, and year.)

BETWEEN the Owner:
(Name, legal status, address, and other information)

New Castle County Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

and the Contractor:
(Name, legal status, address, and other information)

TBD

for the following Project:
(Name, location, and detailed description)

Hodgson Vocational Technical High School
2575 Glasgow Avenue
Newark, DE 19702

The Construction Manager:
(Name, legal status, address, and other information)

EDiS Company
110 South Poplar Street, Suite 400
Wilmington, DE 19801

The Architect:
(Name, legal status, address, and other information)

Joint Venture:
ABHA
1621 North Lincoln Street
Wilmington, DE 19806

BSA+A
954 Justison Street
Wilmington, DE 19801

The Owner and Contractor agree as follows.

ADDITIONS AND DELETIONS: The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be used in conjunction with AIA Documents A232™–2019, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition; B132™–2019, Standard Form of Agreement Between Owner and Architect, Construction Manager as Adviser Edition; and C132™–2019, Standard Form of Agreement Between Owner and Construction Manager as Adviser. AIA Document A232™–2019 is adopted in this document by reference. Do not use with other general conditions unless this document is modified.

ELECTRONIC COPYING of any portion of this AIA® Document to another electronic file is prohibited and constitutes a violation of copyright laws as set forth in the footer of this document.

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

TABLE OF ARTICLES

1 THE CONTRACT DOCUMENTS

2 THE WORK OF THIS CONTRACT

3 DATE OF COMMENCEMENT AND DATES OF SUBSTANTIAL COMPLETION

4 CONTRACT SUM

5 PAYMENTS

6 DISPUTE RESOLUTION

7 TERMINATION OR SUSPENSION

8 MISCELLANEOUS PROVISIONS

9 ENUMERATION OF CONTRACT DOCUMENTS

EXHIBIT A INSURANCE AND BONDS
EXHIBIT B DETERMINATION OF THE COST OF THE WORK

ARTICLE 1 THE CONTRACT DOCUMENTS

The Contract Documents consist of this Agreement, Conditions of the Contract (General, Supplementary, and other Conditions), Drawings, Specifications, Addenda issued prior to execution of this Agreement, other documents listed in this Agreement, and Modifications issued after execution of this Agreement, all of which form the Contract, and are as fully a part of the Contract as if attached to this Agreement or repeated herein. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations, or agreements, either written or oral. An enumeration of the Contract Documents, other than Modifications, appears in Article 9.

ARTICLE 2 THE WORK OF THIS CONTRACT

The Contractor shall fully execute the Work described in the Contract Documents, except as specifically indicated in the Contract Documents to be the responsibility of others.

ARTICLE 3 DATE OF COMMENCEMENT AND DATES OF SUBSTANTIAL COMPLETION

§ 3.1 The date of commencement of the Work shall be:
(Check one of the following boxes.)

[« »] The date of this Agreement.

[« »] A date set forth in a notice to proceed issued by the Owner.

[« »] Established as follows:
(Insert a date or a means to determine the date of commencement of the Work.)

« »

If a date of commencement of the Work is not selected, then the date of commencement shall be the date of this Agreement.

§ 3.2 The Contract Time shall be measured from the date of commencement of the Work.

§ 3.3 Substantial Completion of the Project or Portions Thereof

§ 3.3.1 Subject to adjustments of the Contract Time as provided in the Contract Documents, the date of Substantial Completion of the Work of all of the Contractors for the Project will be:
(Insert the date of Substantial Completion of the Work of all Contractors for the Project.)

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

« »

§ 3.3.2 Subject to adjustments of the Contract Time as provided in the Contract Documents, if portions of the Work of all of the Contractors for the Project are to be completed prior to Substantial Completion of the entire Work of all of the Contractors for the Project, the Contractors shall achieve Substantial Completion of such portions by the following dates:

Portion of Work	Substantial Completion Date

§ 3.4 When the Work of this Contract, or any Portion Thereof, is Substantially Complete

§ 3.4.1 Subject to adjustments of the Contract Time as provided in the Contract Documents, the Contractor shall substantially complete the entire Work of this Contract:
(Check one of the following boxes and complete the necessary information.)

[« »] Not later than « » (« ») calendar days from the date of commencement of the Work.

[« »] By the following date: « »

§ 3.4.2 Subject to adjustments of the Contract Time as provided in the Contract Documents, if portions of the Work of this Contract are to be substantially complete prior to when the entire Work of this Contract shall be substantially complete, the Contractor shall substantially complete such portions by the following dates:

Portion of Work	Date to be substantially complete

§ 3.4.3 If the Contractor fails to substantially complete the Work of this Contract, or portions thereof, as provided in this Section 3.4, liquidated damages, if any, shall be assessed as set forth in Section 4.5.

ARTICLE 4 CONTRACT SUM

§ 4.1 The Owner shall pay the Contractor the Contract Sum in current funds for the Contractor's performance of the Contract. The Contract Sum shall be one of the following:
(Check the appropriate box.)

[«X»] Stipulated Sum, in accordance with Section 4.2 below

[« »] Cost of the Work plus the Contractor's Fee, in accordance with Section 4.3 below

[« »] Cost of the Work plus the Contractor's Fee with a Guaranteed Maximum Price, in accordance with Section 4.4 below

(Based on the selection above, complete Section 4.2, 4.3 or 4.4 below.)

§ 4.2 Stipulated Sum

§ 4.2.1 The Contract Sum shall be « » ($ « »), subject to additions and deductions as provided in the Contract Documents.

§ 4.2.2 Alternates

§ 4.2.2.1 Alternates, if any, included in the Contract Sum:

Item	Price

§ 4.2.2.2 Subject to the conditions noted below, the following alternates may be accepted by the Owner following execution of this Agreement. Upon acceptance, the Owner shall issue a Modification to this Agreement.
(Insert below each alternate and the conditions that must be met for the Owner to accept the alternate.)

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

Item	Price	Conditions for Acceptance

§ 4.2.3 Allowances, if any, included in the Contract Sum:
(Identify each allowance.)

Item	Price

§ 4.2.4 Unit prices, if any:
(Identify the item and state the unit price, and quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price per Unit ($0.00)

§ 4.3 NOT USED - Cost of the Work Plus Contractor's Fee without a Guaranteed Maximum Price
~~**§ 4.3.1** The Cost of the Work is as defined in Exhibit B, Determination of the Cost of the Work.~~

~~**§ 4.3.2** The Contractor's Fee:~~
~~*(State a lump sum, percentage of Cost of the Work or other provision for determining the Contractor's Fee.)*~~

~~« »~~

~~**§ 4.3.3** The method of adjustment of the Contractor's Fee for changes in the Work:~~

~~« »~~

~~**§ 4.3.4** Limitations, if any, on a Subcontractor's overhead and profit for increases in the cost of its portion of the Work:~~

~~« »~~

~~**§ 4.3.5** Rental rates for Contractor-owned equipment shall not exceed « » percent (« » %) of the standard rental rate paid at the place of the Project.~~

~~**§ 4.3.6** Unit prices, if any:~~
~~*(Identify the item and state the unit price and quantity limitations, if any, to which the unit price will be applicable.)*~~

~~Item~~	~~Units and Limitations~~	~~Price per Unit ($0.00)~~

~~**§ 4.3.7** The Contractor shall prepare and submit to the Construction Manager, within 14 days of executing this Agreement, a written Control Estimate for the Owner's review and approval. The Control Estimate shall include the items in Section B.1 of Exhibit B, Determination of the Cost of the Work.~~

§ 4.4 NOT USED - Cost of the Work Plus Contractor's Fee with a Guaranteed Maximum Price
~~**§ 4.4.1** The Cost of the Work is as defined in Exhibit B, Determination of the Cost of the Work.~~

~~**§ 4.4.2** The Contractor's Fee:~~
~~*(State a lump sum, percentage of Cost of the Work or other provision for determining the Contractor's Fee.)*~~

~~« »~~

~~**§ 4.4.3** The method of adjustment of the Contractor's Fee for changes in the Work:~~

~~« »~~

~~**§ 4.4.4** Limitations, if any, on a Subcontractor's overhead and profit for increases in the cost of its portion of the Work:~~

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

« »

§ 4.4.5 Rental rates for Contractor-owned equipment shall not exceed « » percent (« » %) of the standard rental rate paid at the place of the Project.

§ 4.4.6 Unit Prices, if any:
(Identify the item and state the unit price and quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price per Unit ($0.00)

§ 4.4.7 Guaranteed Maximum Price
§ 4.4.7.1 The Contract Sum is guaranteed by the Contractor not to exceed « » ($ « »), subject to additions and deductions by Change Order as provided in the Contract Documents. This maximum sum is referred to in the Contract Documents as the Guaranteed Maximum Price. Costs which would cause the Guaranteed Maximum Price to be exceeded shall be paid by the Contractor without reimbursement by the Owner.

§ 4.4.7.2 Alternates
§ 4.4.7.2.1 Alternates, if any, included in the Guaranteed Maximum Price:

Item	Price

§ 4.4.7.2.2 Subject to the conditions noted below, the following alternates may be accepted by the Owner following execution of this Agreement. Upon acceptance, the Owner shall issue a Modification to this Agreement.
(Insert below each alternate and the conditions that must be met for the Owner to accept the alternate.)

Item	Price	Conditions for Acceptance

§ 4.4.7.3 Allowances, if any, included in the Guaranteed Maximum Price:
(Identify each allowance.)

Item	Price

§ 4.4.7.4 Assumptions, if any, upon which the Guaranteed Maximum Price is based:
(Identify each assumption.)

« »

§ 4.4.8 To the extent that the Contract Documents are anticipated to require further development, the Guaranteed Maximum Price includes the costs attributable to such further development consistent with the Contract Documents and reasonably inferable therefrom. Such further development does not include changes in scope, systems, kinds and quality of materials, finishes, or equipment, all of which, if required, shall be incorporated by Change Order.

§ 4.4.9 The Owner shall authorize preparation of revisions to the Contract Documents that incorporate the agreed-upon assumptions contained in Section 4.4.7.4. The Owner shall promptly furnish such revised Contract Documents to the Contractor. The Contractor shall notify the Owner and Architect of any inconsistencies between the agreed-upon assumptions contained in Section 4.4.7.4 and the revised Contract Documents.

§ 4.5 Liquidated damages, if any:
(Insert terms and conditions for liquidated damages, if any, to be assessed in accordance with Section 3.4.)

« »

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

§ 4.6 Other:
(Insert provisions for bonus, cost savings or other incentives, if any, that might result in a change to the Contract Sum.)

« »

ARTICLE 5 PAYMENTS

§ 5.1 Progress Payments

§ 5.1.1 Based upon Applications for Payment submitted to the Construction Manager by the Contractor, and Certificates for Payment issued by the Construction Manager and Architect, the Owner shall make progress payments on account of the Contract Sum, to the Contractor, as provided below and elsewhere in the Contract Documents.

§ 5.1.2 The period covered by each Application for Payment shall be one calendar month ending on the last day of the month, or as follows:

« »

§ 5.1.3 Provided that an Application for Payment is received by the Construction Manager not later than the « » day of a month, the Owner shall make payment of the amount certified to the Contractor not later than the « » day of the « » month. If an Application for Payment is received by the Construction Manager after the application date fixed above, payment of the amount certified shall be made by the Owner not later than « » (« ») days after the Construction Manager receives the Application for Payment.
(Federal, state or local laws may require payment within a certain period of time.)

§ 5.1.4 Progress Payments Where the Contract Sum is Based on a Stipulated Sum

§ 5.1.4.1 Each Application for Payment shall be based on the most recent schedule of values submitted by the Contractor in accordance with the Contract Documents. The schedule of values shall allocate the entire Contract Sum among the various portions of the Work. The schedule of values shall be prepared in such form, and supported by such data to substantiate its accuracy, as the Construction Manager and Architect may require. This schedule of values shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 5.1.4.2 Applications for Payment shall show the percentage of completion of each portion of the Work as of the end of the period covered by the Application for Payment.

§ 5.1.4.3 In accordance with AIA Document A232™–2019, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition, and subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

§ 5.1.4.3.1 The amount of each progress payment shall first include:

- **.1** That portion of the Contract Sum properly allocable to completed Work;
- **.2** That portion of the Contract Sum properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction, or, if approved in advance by the Owner, suitably stored off the site at a location agreed upon in writing; and
- **.3** That portion of Construction Change Directives that the Architect determines, in the Architect's professional judgment, to be reasonably justified.

§ 5.1.4.3.2 The amount of each progress payment shall then be reduced by:

- **.1** The aggregate of any amounts previously paid by the Owner;
- **.2** The amount, if any, for Work that remains uncorrected and for which the Architect has previously withheld a Certificate for Payment as provided in Article 9 of AIA Document A232–2019;
- **.3** Any amount for which the Contractor does not intend to pay a Subcontractor or material supplier, unless the Work has been performed by others the Contractor intends to pay;
- **.4** For Work performed or defects discovered since the last payment application, any amount for which the Architect may withhold payment, or nullify a Certificate of Payment in whole or in part, as provided in Article 9 of AIA Document A232–2019; and
- **.5** Retainage withheld pursuant to Section 5.1.7.

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

§ 5.1.5 NOT USED -
Progress Payments Where the Contract Sum is Based on the Cost of the Work without a Guaranteed Maximum Price

§ 5.1.5.1 With each Application for Payment, the Contractor shall submit the cost control information required in Exhibit B, Determination of the Cost of the Work, along with payrolls, petty cash accounts, receipted invoices, or invoices with check vouchers attached, and any other evidence required by the Owner, Construction Manager or Architect to demonstrate that payments already made by the Contractor on account of the Cost of the Work equal or exceed progress payments already received by the Contractor, plus payrolls for the period covered by the present Application for Payment, less that portion of the payments attributable to the Contractor's Fee.

§ 5.1.5.2 Applications for Payment shall show the Cost of the Work actually incurred by the Contractor through the end of the period covered by the Application for Payment and for which the Contractor has made or intends to make actual payment prior to the next Application for Payment.

§ 5.1.5.3 In accordance with AIA Document A232–2019 and subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

§ 5.1.5.3.1 The amount of each progress payment shall first include:

- **.1** The Cost of the Work as described in Exhibit B, Determination of the Cost of the Work;
- **.2** That portion of Construction Change Directives that the Architect determines, in the Architect's professional judgment, to be reasonably justified; and
- **.3** The Contractor's Fee computed upon the Cost of the Work described in the preceding Section 5.1.5.3.1.1 at the rate stated in Section 4.3.2; or if the Contractor's Fee is stated as a fixed sum in Section 4.3.2 an amount which bears the same ratio to that fixed-sum Fee as the Cost of the Work included in Section 5.1.5.3.1.1 bears to a reasonable estimate of the probable Cost of the Work upon its completion.

§ 5.1.5.3.2 The amount of each progress payment shall then be reduced by:

- **.1** The aggregate of any amounts previously paid by the Owner;
- **.2** The amount, if any, for Work that remains uncorrected and for which the Architect has previously withheld a Certificate for Payment as provided in Article 9 of AIA Document A232–2019;
- **.3** Any amount for which the Contractor does not intend to pay a Subcontractor or material supplier, unless the Work has been performed by others the Contractor intends to pay;
- **.4** For Work performed or defects discovered since the last payment application, any amount for which the Architect may withhold payment, or nullify a Certificate of Payment in whole or in part, as provided in Article 9 of AIA Document A232–2019;
- **.5** The shortfall, if any, indicated by the Contractor in the documentation required by Section 5.1.5.1 to substantiate prior Applications for Payment, or resulting from errors subsequently discovered by the Owner's auditors in such documentation; and
- **.6** Retainage withheld pursuant to Section 5.1.7.

§ 5.1.5.4 The Owner, Construction Manager and Contractor shall agree upon a mutually acceptable procedure for review and approval of payments to Subcontractors and the percentage of retainage held on Subcontracts, and the Contractor shall execute subcontracts in accordance with those agreements.

§ 5.1.5.5 In taking action on the Contractor's Applications for Payment, the Construction Manager and Architect shall be entitled to rely on the accuracy and completeness of the information furnished by the Contractor, and such action shall not be deemed to be a representation that (1) the Construction Manager and Architect have made a detailed examination, audit or arithmetic verification of the documentation submitted in accordance with Article 5 or other supporting data; (2) that the Construction Manager and Architect have made exhaustive or continuous on-site inspections; or (3) that the Construction Manager and Architect have made examinations to ascertain how or for what purposes the Contractor has used amounts previously paid on account of the Contract. Such examinations, audits and verifications, if required by the Owner, will be performed by the Owner's auditors acting in the sole interest of the Owner.

§ 5.1.5.6 Except with the Owner's prior approval, the Contractor shall not make advance payments to suppliers for materials or equipment which have not been delivered and stored at the site.

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

§ 5.1.5.7 If final completion of the Work is materially delayed through no fault of the Contractor, then the Owner shall pay the Contractor any additional amounts in accordance with Article 9 of AIA Document A232–2019.

§ 5.1.6 NOT USED -

Progress Payments Where the Contract Sum is Based on the Cost of the Work with a Guaranteed Maximum Price

§ 5.1.6.1 With each Application for Payment, the Contractor shall submit payrolls, petty cash accounts, receipted invoices or invoices with check vouchers attached, and any other evidence required by the Owner, Construction Manager or Architect to demonstrate that payments already made by the Contractor on account of the Cost of the Work equal or exceed progress payments already received by the Contractor plus payrolls for the period covered by the present Application for Payment, less that portion of the progress payments attributable to the Contractor's Fee.

§ 5.1.6.2 Each Application for Payment shall be based on the most recent schedule of values submitted by the Contractor in accordance with the Contract Documents. The schedule of values shall allocate the entire Guaranteed Maximum Price among: (1) the various portions of the Work; (2) any contingency for costs that are included in the Guaranteed Maximum Price but not otherwise allocated to another line item or included in a Change Order; and (3) the Contractor's Fee.

§ 5.1.6.2.1 The schedule of values shall be prepared in such form, and supported by such data to substantiate its accuracy, as the Construction Manager and Architect may require. This schedule of values shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 5.1.6.2.2 The allocation of the Guaranteed Maximum Price under this Section 5.1.6.2 shall not constitute a separate guaranteed maximum price for the Cost of the Work of each individual line item in the schedule of values.

§ 5.1.6.2.3 When the Contractor allocates costs from a contingency to another line item in the schedule of values, the Contractor shall submit supporting documentation to the Architect and Construction Manager.

§ 5.1.6.3 Applications for Payment shall show the percentage of completion of each portion of the Work as of the end of the period covered by the Application for Payment. The percentage of completion shall be the lesser of (1) the percentage of that portion of the Work which has actually been completed; or (2) the percentage obtained by dividing (a) the expense that has actually been incurred by the Contractor on account of that portion of the Work and for which the Contractor has made payment or intends to make payment prior to the next Application for Payment by (b) the share of the Guaranteed Maximum Price allocated to that portion of the Work in the schedule of values.

§ 5.1.6.4 In accordance with AIA Document A232–2019, and subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

§ 5.1.6.4.1 The amount of each progress payment shall first include:

- **.1** That portion of the Guaranteed Maximum Price properly allocable to completed Work as determined by multiplying the percentage of completion of each portion of the Work by the share of the Guaranteed Maximum Price allocated to that portion of the Work in the most recent schedule of values;
- **.2** That portion of the Guaranteed Maximum Price properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction or, if approved in writing in advance by the Owner, suitably stored off the site at a location agreed upon in writing;
- **.3** That portion of Construction Change Directives that the Architect determines, in the Architect's professional judgment, to be reasonably justified; and
- **.4** The Contractor's Fee, computed upon the Cost of the Work described in the preceding Sections 5.1.6.4.1.1 and 5.1.6.4.1.2 at the rate stated in Section 4.4.2 or, if the Contractor's Fee is stated as a fixed sum in that Section, an amount that bears the same ratio to that fixed-sum fee as the Cost of the Work included in Sections 5.1.6.4.1.1 and 5.1.6.4.1.2 bears to a reasonable estimate of the probable Cost of the Work upon its completion.

§ 5.1.6.4.2 The amount of each progress payment shall then be reduced by:

- **.1** The aggregate of any amounts previously paid by the Owner;
- **.2** The amount, if any, for Work that remains uncorrected and for which the Architect has previously withheld a Certificate for Payment as provided in Article 9 of AIA Document A232–2019;
- **.3** Any amount for which the Contractor does not intend to pay a Subcontractor or material supplier, unless the Work has been performed by others the Contractor intends to pay;

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

~~.4 For Work performed or defects discovered since the last payment application, any amount for which the Architect may withhold payment, or nullify a Certificate of Payment in whole or in part, as provided in Article 9 of AIA Document A232–2019;~~

~~.5 The shortfall, if any, indicated by the Contractor in the documentation required by Section 5.1.6.1 to substantiate prior Applications for Payment, or resulting from errors subsequently discovered by the Owner's auditors in such documentation; and~~

~~.6 Retainage withheld pursuant to Section 5.1.7.~~

~~**§ 5.1.6.5** The Owner and the Contractor shall agree upon a mutually acceptable procedure for review and approval of payments to Subcontractors and the percentage of retainage held on Subcontracts, and the Contractor shall execute subcontracts in accordance with those agreements.~~

~~**§ 5.1.6.6** In taking action on the Contractor's Applications for Payment, the Construction Manager and Architect shall be entitled to rely on the accuracy and completeness of the information furnished by the Contractor and such action shall not be deemed to be a representation that (1) the Construction Manager or Architect have made a detailed examination, audit, or arithmetic verification of the documentation submitted in accordance with Section 5.1.6.1 or other supporting data; (2) that the Construction Manager or Architect have made exhaustive or continuous on-site inspections; or (3) that the Construction Manager or Architect have made examinations to ascertain how or for what purposes the Contractor has used amounts previously paid on account of the Contract. Such examinations, audits, and verifications, if required by the Owner, will be performed by the Owner's auditors acting in the sole interest of the Owner.~~

~~**§ 5.1.6.7** Except with the Owner's prior approval, the Contractor shall not make advance payments to suppliers for materials or equipment which have not been delivered and stored at the site.~~

~~**§ 5.1.6.8** If final completion of the Work is materially delayed through no fault of the Contractor, then the Owner shall pay the Contractor any additional amounts in accordance with Article 9 of AIA Document A232–2019.~~

§ 5.1.7 Retainage

§ 5.1.7.1 For each progress payment made prior to when the Work of this Contract is substantially complete, the Owner may withhold the following amount, as retainage, from the payment otherwise due:
(Insert a percentage or amount to be withheld as retainage from each Application for Payment. The amount of retainage may be limited by governing law.)

« »

§ 5.1.7.1.1 The following items are not subject to retainage:
(Insert any items not subject to the withholding of retainage, such as general conditions, insurance, etc.)

« »

§ 5.1.7.2 Reduction or limitation of retainage, if any, shall be as follows:
(If the retainage established in Section 5.1.7.1 is to be modified prior to when the entire Work of this Contract is substantially complete, including modifications for completion of portions of the Work as provided in Section 3.4.2, insert provisions for such modifications.)

« »

§ 5.1.7.3 Except as set forth in this Section 5.1.7.3, when the Work of this Contract is substantially complete, the Contractor may submit an Application for Payment that includes the retainage withheld from prior Applications for Payment pursuant to this Section 5.1.7. The Application for Payment submitted when the Work of this Contract is substantially complete shall not include retainage as follows:
(Insert any other conditions for release of retainage when the Work of this Contract is substantially complete, or upon Substantial Completion of the Work of all Contractors on the Project or portions thereof.)

« »

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

§ 5.2 Final Payment

§ 5.2.1 Final Payment Where the Contract Sum is Based on a Stipulated Sum

§ 5.2.1.1 Final payment, constituting the entire unpaid balance of the Contract Sum, shall be made by the Owner to the Contractor when

.1 the Contractor has fully performed the Contract except for the Contractor's responsibility to correct Work as provided in Article 12 of AIA Document A232–2019, and to satisfy other requirements, if any, which extend beyond final payment; and

.2 a final Certificate for Payment or Project Certificate for Payment has been issued by the Architect.

§ 5.2.1.2 The Owner's final payment to the Contractor shall be made no later than 30 days after the issuance of the final Certificate for Payment or Project Certificate for Payment, or as follows:

« »

§ 5.2.2 NOT USED - Final Payment Where the Contract Sum is Based on the Cost of the Work with or without a Guaranteed Maximum Price

~~**§ 5.2.2.1** Final payment, constituting the entire unpaid balance of the Contract Sum, shall be made by the Owner to the Contractor when~~

~~**.1** the Contractor has fully performed the Contract except for the Contractor's responsibility to correct Work as provided in Article 12 of AIA Document A232–2019, and to satisfy other requirements, if any, which extend beyond final payment;~~

~~**.2** the Contractor has submitted a final accounting for the Cost of the Work, pursuant to Exhibit B, Determination of the Cost of the Work and a final Application for Payment; and~~

~~**.3** a final Certificate for Payment or Project Certificate for Payment has been issued by the Architect in accordance with Exhibit B, Determination of the Cost of the Work.~~

~~**§ 5.2.2.2** The Owner's final payment to the Contractor shall be made no later than 30 days after the issuance of the final Certificate for Payment or Project Certificate for Payment, or as follows:~~

~~« »~~

§ 5.3 Payments due and unpaid under the Contract shall bear interest from the date payment is due at the rate stated below, or in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.
(Insert rate of interest agreed upon, if any.)

« » % « »

ARTICLE 6 DISPUTE RESOLUTION

§ 6.1 Initial Decision Maker

The Architect will serve as Initial Decision Maker pursuant to Article 15 of AIA Document A232–2019, unless the parties appoint below another individual, not a party to this Agreement, to serve as Initial Decision Maker.
(If the parties mutually agree, insert the name, address and other contact information of the Initial Decision Maker, if other than the Architect.)

« »
« »
« »
« »

§ 6.2 Binding Dispute Resolution

For any Claim subject to, but not resolved by, mediation pursuant to Article 15 of AIA Document A232–2019, the method of binding dispute resolution shall be as follows:
(Check the appropriate box.)

[« »] Arbitration pursuant to Article 15 of AIA Document A232–2019.

[« »] Litigation in a court of competent jurisdiction.

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

[« »] Other: *(Specify)*

« »

If the Owner and Contractor do not select a method of binding dispute resolution, or do not subsequently agree in writing to a binding dispute resolution method other than litigation, Claims will be resolved by litigation in a court of competent jurisdiction.

ARTICLE 7 TERMINATION OR SUSPENSION

§ 7.1 Where the Contract Sum is a Stipulated Sum

§ 7.1.1 The Contract may be terminated by the Owner or the Contractor as provided in Article 14 of AIA Document A232–2019.

§ 7.1.1.1 If the Contract is terminated for the Owner's convenience in accordance with Article 14 of AIA Document A232–2019, then the Owner shall pay the Contractor a termination fee as follows:
(Insert the amount of, or method for determining, the fee, if any, payable to the Contractor following a termination for the Owner's convenience.)

« »

§ 7.1.2 The Work may be suspended by the Owner as provided in Article 14 of AIA Document A232–2019.

§ 7.2 Where the Contract Sum is Based on the Cost of the Work with or without a Guaranteed Maximum Price

§ 7.2.1 Termination

§ 7.2.1.1 The Contract may be terminated by the Owner or the Contractor as provided in Article 14 of AIA Document A232–2019.

§ 7.2.1.2 Termination by the Owner for Cause

§ 7.2.1.2.1 If the Owner terminates the Contract for cause as provided in Article 14 of AIA Document A232–2019, the Owner shall then only pay the Contractor an amount as follows:

.1 Take the Cost of the Work incurred by the Contractor to the date of termination;

.2 Add the Contractor's Fee, computed upon the Cost of the Work to the date of termination at the rate stated in Section 4.3.2 or 4.4.2, as applicable, or, if the Contractor's Fee is stated as a fixed sum in that Section, an amount that bears the same ratio to that fixed-sum Fee as the Cost of the Work at the time of termination bears to a reasonable estimate of the probable Cost of the Work upon its completion;

.3 Subtract the aggregate of previous payments made by the Owner; and

.4 Subtract the costs and damages incurred, or to be incurred, by the Owner under Article 14 of AIA Document A232–2019.

§ 7.2.1.2.2 When the Contract Sum is based on the Cost of the Work with a Guaranteed Maximum Price, if the Owner terminates the Contract for cause as provided in Article 14 of AIA Document A232-2019, the amount, if any, to be paid to the Contractor under Article 14 of AIA Document A232-2019 shall not cause the Guaranteed Maximum Price to be exceeded, nor shall it exceed the amount calculated in Section 7.2.1.2.1.

§ 7.2.1.2.3 The Owner shall also pay the Contractor fair compensation, either by purchase or rental at the election of the Owner, for any equipment owned by the Contractor that the Owner elects to retain and that is not otherwise included in the Cost of the Work under Section 7.2.1.2.1.1. To the extent that the Owner elects to take legal assignment of subcontracts and purchase orders (including rental agreements), the Contractor shall, as a condition of receiving the payments referred to in this Article 7, execute and deliver all such papers and take all such steps, including the legal assignment of such subcontracts and other contractual rights of the Contractor, as the Owner may require for the purpose of fully vesting in the Owner the rights and benefits of the Contractor under such subcontracts or purchase orders. All Subcontracts, purchase orders and rental agreements entered into by the Contractor will contain provisions allowing for assignment to the Owner as described above.

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

§ 7.2.1.3 Termination by the Owner for Convenience

If the Owner terminates the Contract for convenience in accordance with Article 14 of AIA Document A232–2019, then the Owner shall pay the Contractor a termination fee as follows:
(Insert the amount of or method for determining the fee, if any, payable to the Contractor following a termination for the Owner's convenience.)

« »

§ 7.3 Suspension

The Work may be suspended by the Owner as provided in Article 14 of AIA Document A232–2019; in such case, the Contract Sum and Contract Time shall be increased as provided in Article 14 of AIA Document A232–2019, except that the term "profit" shall be understood to mean the Contractor's Fee as described in Section 4.3.2 or 4.4.2, as applicable, of this Agreement.

ARTICLE 8 MISCELLANEOUS PROVISIONS

§ 8.1 Where reference is made in this Agreement to a provision of AIA Document A232–2019 or another Contract Document, the reference refers to that provision as amended or supplemented by other provisions of the Contract Documents.

§ 8.2 The Owner's representative:
(Name, address, email address, and other information)

« »
« »
« »
« »
« »
« »

§ 8.3 The Contractor's representative:
(Name, address, email address, and other information)

« »
« »
« »
« »
« »
« »

§ 8.4 Neither the Owner's nor the Contractor's representative shall be changed without ten days' prior notice to the other party.

§ 8.5 Insurance and Bonds

§ 8.5.1 The Owner and the Contractor shall purchase and maintain insurance as set forth in AIA Document A132™–2019, Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition, Exhibit A, Insurance and Bonds, and elsewhere in the Contract Documents.

§ 8.5.2 The Contractor shall provide bonds as set forth in AIA Document A132™–2019, Exhibit A, and elsewhere in the Contract Documents.

§ 8.6 Notice in electronic format, pursuant to Article 1 of AIA Document A232–2019, may be given in accordance with AIA Document E203™–2013, Building Information Modeling and Digital Data Exhibit, if completed, or as otherwise set forth below:
(If other than in accordance with AIA Document E203–2013, insert requirements for delivering notice in electronic format such as name, title, and email address of the recipient and whether and how the system will be required to generate a read receipt for the transmission.)

« »

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

§ 8.7 Relationship of the Parties

Where the Contract is based on the Cost of the Work plus the Contractor's Fee, with or without a Guaranteed Maximum Price, the Contractor accepts the relationship of trust and confidence established by this Agreement and covenants with the Owner to cooperate with the Architect and exercise the Contractor's skill and judgment in furthering the interests of the Owner; to furnish efficient business administration and supervision; to furnish at all times an adequate supply of workers and materials; and to perform the Work in an expeditious and economical manner consistent with the Owner's interests. The Owner agrees to furnish and approve, in a timely manner, information required by the Contractor and to make payments to the Contractor in accordance with the requirements of the Contract Documents.

§ 8.8 Other provisions:

« »

ARTICLE 9 ENUMERATION OF CONTRACT DOCUMENTS

§ 9.1 This Agreement is comprised of the following documents:

.1 AIA Document A132™–2019, Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition

.2 AIA Document A132™–2019, Exhibit A, Insurance and Bonds Exhibit

.3 AIA Document A232™–2019, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition

.4 AIA Document E203™–2013, Building Information Modeling and Digital Data Exhibit, dated as indicated below:
(Insert the date of the E203-2013 incorporated into this Agreement.)

« »

.5 Drawings

Number	Title	Date

.6 Specifications

Section	Title	Date	Pages

.7 Addenda, if any:

Number	Date	Pages

Portions of Addenda relating to bidding or proposal requirements are not part of the Contract Documents unless the bidding or proposal requirements are also enumerated in this Article 9.

.8 Other Exhibits:
(Check all boxes that apply and include appropriate information identifying the exhibit where required.)

~~[« »] AIA Document A132™–2019, Exhibit B, Determination of the Cost of the Work~~

[« »] AIA Document E235™–2019, Sustainable Projects Exhibit, Construction Manager as Adviser Edition, dated as indicated below:
(Insert the date of the E235-2019 incorporated into this Agreement.)

« »

[« »] The Sustainability Plan:

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

Title	Date	Pages

[« »] Supplementary and other Conditions of the Contract:

Document	Title	Date	Pages

.9 Other documents, if any, listed below:
(List here any additional documents that are intended to form part of the Contract Documents. AIA Document A232–2019 provides that the advertisement or invitation to bid, Instructions to Bidders, sample forms, the Contractor's bid or proposal, portions of Addenda relating to bidding or proposal requirements, and other information furnished by the Owner in anticipation of receiving bids or proposals, are not part of the Contract Documents unless enumerated in this Agreement. Any such documents should be listed here only if intended to be part of the Contract Documents.)

« »

This Agreement is entered into as of the day and year first written above.

OWNER *(Signature)*	**CONTRACTOR** *(Signature)*
« »« »	« »« »
(Printed name and title)	*(Printed name and title)*

DRAFT

AIA Document A132 – 2019. Copyright © 1975, 1980, 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 10:15:46 ET on 02/20/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1246710833)

DRAFT AIA® Document A132® – 2019 Exhibit A

Insurance and Bonds

This Insurance and Bonds Exhibit is part of the Agreement, between the Owner and the Contractor, dated the « » day of « » in the year « »
(In words, indicate day, month, and year.)

for the following **PROJECT**:
(Name and location or address)

«Hodgson Vocational Technical High School»
«2575 Glasgow Avenue
Newark, DE 19702»

THE OWNER:
(Name, legal status, and address)

«New Castle County Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804»

THE CONTRACTOR:
(Name, legal status, and address)

« »« »
« »

TABLE OF ARTICLES

A.1 GENERAL

A.2 OWNER'S INSURANCE

A.3 CONTRACTOR'S INSURANCE AND BONDS

A.4 SPECIAL TERMS AND CONDITIONS

ARTICLE A.1 GENERAL

The Owner and Contractor shall purchase and maintain insurance, and provide bonds, as set forth in this Exhibit. As used in this Exhibit, the term General Conditions refers to AIA Document A232™–2019, General Conditions of the Contract for Construction.

ARTICLE A.2 OWNER'S INSURANCE

§ A.2.1 General

Prior to commencement of the Work, the Owner shall secure the insurance, and provide evidence of the coverage, required under this Article A.2 and, upon the Contractor's request, provide a copy of the property insurance policy or policies required by Section A.2.3. The copy of the policy or policies provided shall contain all applicable conditions, definitions, exclusions, and endorsements.

§ A.2.2 Liability Insurance

The Owner shall be responsible for purchasing and maintaining the Owner's usual general liability insurance.

ADDITIONS AND DELETIONS: The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be used in conjunction with AIA Document A232™–2019, General Conditions of the Contract for Construction. Article 11 of A232™–2019 contains additional insurance provisions

ELECTRONIC COPYING of any portion of this AIA® Document to another electronic file is prohibited and constitutes a violation of copyright laws as set forth in the footer of this document.

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

§ A.2.3 Required Property Insurance

§ A.2.3.1 Unless this obligation is placed on the Contractor pursuant to Section A.3.3.2.1, the Owner shall purchase and maintain, from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located, property insurance written on a builder's risk "all-risks" completed value or equivalent policy form and sufficient to cover the total value of the entire Project on a replacement cost basis. The Owner's property insurance coverage shall be no less than the amount of the initial Contract Sum, plus the value of subsequent Modifications and labor performed and materials or equipment supplied by others. The property insurance shall be maintained until Substantial Completion and thereafter as provided in Section A.2.3.1.3, unless otherwise provided in the Contract Documents or otherwise agreed in writing by the parties to this Agreement. This insurance shall include the interests of the Owner, Contractor, Subcontractors, and Sub-subcontractors in the Project as insureds. This insurance shall include the interests of mortgagees as loss payees.

§ A.2.3.1.1 Causes of Loss. The insurance required by this Section A.2.3.1 shall provide coverage for direct physical loss or damage, and shall not exclude the risks of fire, explosion, theft, vandalism, malicious mischief, collapse, earthquake, flood, or windstorm. The insurance shall also provide coverage for ensuing loss or resulting damage from error, omission, or deficiency in construction methods, design, specifications, workmanship, or materials. Sub-limits, if any, are as follows:
(Indicate below the cause of loss and any applicable sub-limit.)

Causes of Loss	Sub-Limit

§ A.2.3.1.2 Specific Required Coverages. The insurance required by this Section A.2.3.1 shall provide coverage for loss or damage to false work and other temporary structures, and to building systems from testing and startup. The insurance shall also cover debris removal, including demolition occasioned by enforcement of any applicable legal requirements, and reasonable compensation for the Architect's, Construction Manager's, and Contractor's services and expenses required as a result of such insured loss, including claim preparation expenses. Sub-limits, if any, are as follows:
(Indicate below type of coverage and any applicable sub-limit for specific required coverages.)

Coverage	Sub-Limit

§ A.2.3.1.3 Unless the parties agree otherwise, upon Substantial Completion, the Owner shall continue the insurance required by Section A.2.3.1 or, if necessary, replace the insurance policy required under Section A.2.3.1 with property insurance written for the total value of the Project that shall remain in effect until expiration of the period for correction of the Work set forth in Section 12.2.2 of the General Conditions.

§ A.2.3.1.4 Deductibles and Self-Insured Retentions. If the insurance required by this Section A.2.3 is subject to deductibles or self-insured retentions, the Owner shall be responsible for all loss not covered because of such deductibles or retentions.

§ A.2.3.2 Occupancy or Use Prior to Substantial Completion. The Owner's occupancy or use of any completed or partially completed portion of the Work prior to Substantial Completion shall not commence until the insurance company or companies providing the insurance under Section A.2.3.1 have consented in writing to the continuance of coverage. The Owner and the Contractor shall take no action with respect to partial occupancy or use that would cause cancellation, lapse, or reduction of insurance, unless they agree otherwise in writing.

§ A.2.3.3 Insurance for Existing Structures

If the Work involves remodeling an existing structure or constructing an addition to an existing structure, the Owner shall purchase and maintain, until the expiration of the period for correction of Work as set forth in Section 12.2.2 of the General Conditions, "all-risks" property insurance, on a replacement cost basis, protecting the existing structure against direct physical loss or damage from the causes of loss identified in Section A.2.3.1, notwithstanding the undertaking of the Work. The Owner shall be responsible for all co-insurance penalties.

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

§ A.2.4 Optional Extended Property Insurance.

The Owner shall purchase and maintain the insurance selected and described below.

(Select the types of insurance the Owner is required to purchase and maintain by placing an X in the box(es) next to the description(s) of selected insurance. For each type of insurance selected, indicate applicable limits of coverage or other conditions in the fill point below the selected item.)

[« »] **§ A.2.4.1 Loss of Use, Business Interruption, and Delay in Completion Insurance**, to reimburse the Owner for loss of use of the Owner's property, or the inability to conduct normal operations due to a covered cause of loss.

« »

[« »] **§ A.2.4.2 Ordinance or Law Insurance**, for the reasonable and necessary costs to satisfy the minimum requirements of the enforcement of any law or ordinance regulating the demolition, construction, repair, replacement or use of the Project.

« »

[« »] **§ A.2.4.3 Expediting Cost Insurance**, for the reasonable and necessary costs for the temporary repair of damage to insured property, and to expedite the permanent repair or replacement of the damaged property.

« »

[« »] **§ A.2.4.4 Extra Expense Insurance**, to provide reimbursement of the reasonable and necessary excess costs incurred during the period of restoration or repair of the damaged property that are over and above the total costs that would normally have been incurred during the same period of time had no loss or damage occurred.

« »

[« »] **§ A.2.4.5 Civil Authority Insurance**, for losses or costs arising from an order of a civil authority prohibiting access to the Project, provided such order is the direct result of physical damage covered under the required property insurance.

« »

[« »] **§ A.2.4.6 Ingress/Egress Insurance**, for loss due to the necessary interruption of the insured's business due to physical prevention of ingress to, or egress from, the Project as a direct result of physical damage.

« »

[« »] **§ A.2.4.7 Soft Costs Insurance**, to reimburse the Owner for costs due to the delay of completion of the Work, arising out of physical loss or damage covered by the required property insurance: including construction loan fees; leasing and marketing expenses; additional fees, including those of architects, engineers, consultants, attorneys and accountants, needed for the completion of the construction, repairs, or reconstruction; and carrying costs such as property taxes, building permits, additional interest on loans, realty taxes, and insurance premiums over and above normal expenses.

« »

§ A.2.5 Other Optional Insurance.

The Owner shall purchase and maintain the insurance selected below.

(Select the types of insurance the Owner is required to purchase and maintain by placing an X in the box(es) next to the description(s) of selected insurance.)

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

[« »] **§ A.2.5.1 Cyber Security Insurance** for loss to the Owner due to data security and privacy breach, including costs of investigating a potential or actual breach of confidential or private information. *(Indicate applicable limits of coverage or other conditions in the fill point below.)*

« »

[« »] **§ A.2.5.2 Other Insurance**
(List below any other insurance coverage to be provided by the Owner and any applicable limits.)

Coverage	Limits

ARTICLE A.3 CONTRACTOR'S INSURANCE AND BONDS

§ A.3.1 General

§ A.3.1.1 Certificates of Insurance. The Contractor shall provide certificates of insurance acceptable to the Owner evidencing compliance with the requirements in this Article A.3 at the following times: (1) prior to commencement of the Work; (2) upon renewal or replacement of each required policy of insurance; and (3) upon the Owner's written request. An additional certificate evidencing continuation of commercial liability coverage, including coverage for completed operations, shall be submitted with the final Application for Payment and thereafter upon renewal or replacement of such coverage until the expiration of the periods required by Section A.3.2.1 and Section A.3.3.1. The certificates will show the Owner as an additional insured on the Contractor's Commercial General Liability and excess or umbrella liability policy or policies.

§ A.3.1.2 Deductibles and Self-Insured Retentions. The Contractor shall disclose to the Owner any deductible or self-insured retentions applicable to any insurance required to be provided by the Contractor.

§ A.3.1.3 Additional Insured Obligations. To the fullest extent permitted by law, the Contractor shall cause the commercial general liability coverage to include (1) the Owner, the Architect and the Architect's consultants, and the Construction Manager and the Construction Manager's consultants, as additional insureds for claims caused in whole or in part by the Contractor's negligent acts or omissions during the Contractor's operations; and (2) the Owner as an additional insured for claims caused in whole or in part by the Contractor's negligent acts or omissions for which loss occurs during completed operations. The additional insured coverage shall be primary and non-contributory to any of the Owner's general liability insurance policies and shall apply to both ongoing and completed operations. To the extent commercially available, the additional insured coverage shall be no less than that provided by Insurance Services Office, Inc. (ISO) forms CG 20 10 07 04, CG 20 37 07 04, and, with respect to the Architect and the Architect's consultants, and the Construction Manager and the Construction Manager's consultants, CG 20 32 07 04.

§ A.3.2 Contractor's Required Insurance Coverage

§ A.3.2.1 The Contractor shall purchase and maintain the following types and limits of insurance from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located. The Contractor shall maintain the required insurance until the expiration of the period for correction of Work as set forth in Section 12.2.2 of the General Conditions, unless a different duration is stated below:
(If the Contractor is required to maintain insurance for a duration other than the expiration of the period for correction of Work, state the duration.)

« »

§ A.3.2.2 Commercial General Liability

§ A.3.2.2.1 Commercial General Liability insurance for the Project written on an occurrence form with policy limits of not less than « » ($ « ») each occurrence, « » ($ « ») general aggregate, and « » ($ « ») aggregate for products-completed operations hazard, providing coverage for claims including

.1 damages because of bodily injury, sickness or disease, including occupational sickness or disease, and death of any person;

.2 personal injury and advertising injury;

.3 damages because of physical damage to or destruction of tangible property, including the loss of use of such property;

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

.4 bodily injury or property damage arising out of completed operations; and
.5 the Contractor's indemnity obligations under Section 3.18 of the General Conditions.

§ A.3.2.2.2 The Contractor's Commercial General Liability policy under this Section A.3.2.2 shall not contain an exclusion or restriction of coverage for the following:

.1 Claims by one insured against another insured, if the exclusion or restriction is based solely on the fact that the claimant is an insured, and there would otherwise be coverage for the claim.
.2 Claims for property damage to the Contractor's Work arising out of the products-completed operations hazard where the damaged Work or the Work out of which the damage arises was performed by a Subcontractor.
.3 Claims for bodily injury other than to employees of the insured.
.4 Claims for indemnity under Section 3.18 of the General Conditions arising out of injury to employees of the insured.
.5 Claims or loss excluded under a prior work endorsement or other similar exclusionary language.
.6 Claims or loss due to physical damage under a prior injury endorsement or similar exclusionary language.
.7 Claims related to residential, multi-family, or other habitational projects, if the Work is to be performed on such a project.
.8 Claims related to roofing, if the Work involves roofing.
.9 Claims related to exterior insulation finish systems (EIFS), synthetic stucco or similar exterior coatings or surfaces, if the Work involves such coatings or surfaces.
.10 Claims related to earth subsidence or movement, where the Work involves such hazards.
.11 Claims related to explosion, collapse and underground hazards, where the Work involves such hazards.

§ A.3.2.3 Automobile Liability covering vehicles owned, and non-owned vehicles used, by the Contractor, with policy limits of not less than « » ($ « ») per accident, for bodily injury, death of any person, and property damage arising out of the ownership, maintenance and use of those motor vehicles along with any other statutorily required automobile coverage.

§ A.3.2.4 The Contractor may achieve the required limits and coverage for Commercial General Liability and Automobile Liability through a combination of primary and excess or umbrella liability insurance, provided such primary and excess or umbrella insurance policies result in the same or greater coverage as the coverages required under Section A.3.2.2 and A.3.2.3, and in no event shall any excess or umbrella liability insurance provide narrower coverage than the primary policy. The excess policy shall not require the exhaustion of the underlying limits only through the actual payment by the underlying insurers.

§ A.3.2.5 Workers' Compensation at statutory limits.

§ A.3.2.6 Employers' Liability with policy limits not less than « » ($ « ») each accident, « » ($ « ») each employee, and « » ($ « ») policy limit.

§ A.3.2.7 Jones Act, and the Longshore & Harbor Workers' Compensation Act, as required, if the Work involves hazards arising from work on or near navigable waterways, including vessels and docks

§ A.3.2.8 If the Contractor is required to furnish professional services as part of the Work, the Contractor shall procure Professional Liability insurance covering performance of the professional services, with policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate.

§ A.3.2.9 If the Work involves the transport, dissemination, use, or release of pollutants, the Contractor shall procure Pollution Liability insurance, with policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate.

§ A.3.2.10 Coverage under Sections A.3.2.8 and A.3.2.9 may be procured through a Combined Professional Liability and Pollution Liability insurance policy, with combined policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate.

§ A.3.2.11 Insurance for maritime liability risks associated with the operation of a vessel, if the Work requires such activities, with policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate.

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

§ A.3.2.12 Insurance for the use or operation of manned or unmanned aircraft, if the Work requires such activities, with policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate.

§ A.3.3 Contractor's Other Insurance Coverage

§ A.3.3.1 Insurance selected and described in this Section A.3.3 shall be purchased from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located. The Contractor shall maintain the required insurance until the expiration of the period for correction of Work as set forth in Section 12.2.2 of the General Conditions, unless a different duration is stated below:
(If the Contractor is required to maintain any of the types of insurance selected below for a duration other than the expiration of the period for correction of Work, state the duration.)

« »

§ A.3.3.2 The Contractor shall purchase and maintain the following types and limits of insurance in accordance with Section A.3.3.1.
(Select the types of insurance the Contractor is required to purchase and maintain by placing an X in the box(es) next to the description(s) of selected insurance. Where policy limits are provided, include the policy limit in the appropriate fill point.)

[« »] **§ A.3.3.2.1** If there is only one Contractor performing the Work on the Project, property insurance of the same type and scope satisfying the requirements identified in Section A.2.3, which, if selected in this section A.3.3.2.1, relieves the Owner of the responsibility to purchase and maintain such insurance except insurance required by Section A.2.3.1.3 and Section A.2.3.3. The Contractor shall comply with all obligations of the Owner under Section A.2.3 except to the extent provided below. The Contractor shall disclose to the Owner the amount of any deductible, and the Owner shall be responsible for losses within the deductible. Upon request, the Contractor shall provide the Owner with a copy of the property insurance policy or policies required. The Owner shall adjust and settle the loss with the insurer and be the trustee of the proceeds of the property insurance in accordance with Article 11 of the General Conditions unless otherwise set forth below:
(Where the Contractor's obligation to provide property insurance differs from the Owner's obligations as described under Section A.2.3, indicate such differences in the space below. Additionally, if a party other than the Owner will be responsible for adjusting and settling a loss with the insurer and acting as the trustee of the proceeds of property insurance in accordance with Article 11 of the General Conditions, indicate the responsible party below.)

« »

[« »] **§ A.3.3.2.2 Railroad Protective Liability Insurance**, with policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate, for Work within fifty (50) feet of railroad property.

[« »] **§ A.3.3.2.3 Asbestos Abatement Liability Insurance**, with policy limits of not less than « » ($ « ») per claim and « » ($ « ») in the aggregate, for liability arising from the encapsulation, removal, handling, storage, transportation, and disposal of asbestos-containing materials.

[« »] **§ A.3.3.2.4** Insurance for physical damage to property while it is in storage and in transit to the construction site on an "all-risks" completed value form.

[« »] **§ A.3.3.2.5** Property insurance on an "all-risks" completed value form, covering property owned by the Contractor and used on the Project, including scaffolding and other equipment.

[« »] **§ A.3.3.2.6 Other Insurance**
(List below any other insurance coverage to be provided by the Contractor and any applicable limits.)

Coverage	Limits

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

§ A.3.4 Performance Bond and Payment Bond

The Contractor shall provide surety bonds, from a company or companies lawfully authorized to issue surety bonds in the jurisdiction where the Project is located, as follows:
(Specify type and penal sum of bonds.)

Type	Penal Sum ($0.00)
Payment Bond	« »
Performance Bond	

Payment and Performance Bonds shall be AIA Document A312™, Payment Bond and Performance Bond, or contain provisions identical to AIA Document A312™, current as of the date of this Agreement.

ARTICLE A.4 SPECIAL TERMS AND CONDITIONS

Special terms and conditions that modify this Insurance and Bonds Exhibit, if any, are as follows:

« »

DRAFT

AIA Document A132 – 2019 Exhibit A. Copyright © 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This draft was produced at 15:16:27 ET on 05/04/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1649568621)

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

SECTION 00 54 13

SUPPLEMENT TO AGREEMENT BETWEEN OWNER AND CONTRACTOR A132-2019

The following supplements modify the "Standard Form of Agreement Between Owner and Contractor, Construction Manager as Advisor Edition" AIA Document A132-2019. Where a portion of the Standard Form of Agreement is modified or deleted by the following, the unaltered portions of the Standard Form of Agreement shall remain in effect.

ARTICLE 3: DATE OF COMMENCEMENT AND DATES OF SUBSTANTIAL COMPLETION

3.1 Delete paragraph 3.1 in its entirety and replace with the following:

"The date of Commencement of the Work shall be a date set forth in a notice to proceed issued by the Owner."

3.3.1 In the space provided, insert "As defined in Article 9.8 of AIA Document A232-2019 and amended by the Owner's 'Supplementary General Conditions A232-2019'"

ARTICLE 4: CONTRACT SUM

4.1 Delete paragraph 4.1 in its entirety and replace with the following:

"The Owner shall pay the Contractor the Contract Sum in current funds for the Contractor's performance of the Contract. The Contract Sum shall be a Stipulated Sum, in accordance with Section 4.2 below.

4.3 Delete paragraph 4.3 in its entirety.

4.4 Delete paragraph 4.4 in its entirety.

ARTICLE 5: PAYMENTS

5.1 PROGRESS PAYMENTS

5.1.3 Delete paragraph 5.1.3 in its entirety and replace with the following:

"Provided that a valid Application for Payment is received by the Architect that meets all requirements of the Contract, payment shall be made by the Owner not later than 30 days after the Owner receives the valid Application for Payment."

5.1.5 Delete paragraph 5.1.5 in its entirety.

5.1.6 Delete paragraph 5.1.6 in its entirety.

5.2.2 Delete paragraph 5.2.2 in its entirety.

5.3 Insert the interest rate of "1% per month not to exceed 12% per annum."

ARTICLE 6: DISPUTE RESOLUTION

6.2 BINDING DISPUTE RESOLUTION

Check the box “Other” – and add the following sentence:

"Any remedies available in law or in equity."

ARTICLE 7: TERMINATION or SUSPENSION

7.1.1.1 Delete paragraph 7.1.1.1 in its entirety.

7.2 Delete paragraph 7.2 in its entirety.

ARTICLE 8: MISCELLANEOUS PROVISIONS

8.4 Delete paragraph 8.4 in its entirety and replace with the following:

“The Contractor’s representative shall not be changed without ten days written notice to the Owner.”

8.7 Delete paragraph 8.7 in its entirety.

ARTICLE 9: ENUMERATION OF CONTRACT DOCUMENTS

9.1.9 Insert “Supplement to Agreement Between Owner and Contractor A132-2019”

9.1.9 Insert “Supplementary General Conditions A232-2019”

END OF SECTION

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

SECTION 00 54 14

SUPPLEMENT TO A132-2019 – EXHIBIT A - INSURANCE AND BONDS

The following supplements modify the "Standard Form of Agreement Between Owner and Contractor, *Construction Manager as Adviser Edition*" AIA Document A132-2019 Exhibit A Insurance and Bonds. Where a portion of the Standard Form of Agreement, Exhibit A is modified or deleted by the following, the unaltered portions of the Standard Form of Agreement, Exhibit A shall remain in effect.

ARTICLE A.2 OWNER'S INSURANCE

A.2.1 General

Delete paragraph A.2.1 in its entirety.

A.2.2 Liability Insurance

Delete paragraph A.2.2 in its entirety, except in the case of school projects this paragraph shall remain.

A.2.3 Required Property Insurance

Delete paragraph A.2.3 in its entirety.

A.2.4 Optional Extended Property Insurance

Delete paragraph A.2.4 in its entirety.

A.2.5 Other Optional Insurance

Delete paragraph A.2.5 in its entirety.

ARTICLE A.3 CONTRACTORS INSURANCE AND BONDS

A.3.1.1 Strike the last sentence of the paragraph.

A.3.1.3 Additional Insured Obligations

In the first sentence after "coverage to include (1)" delete "(1) the Owner,".

Strike the remainder of the first sentence beginning at the semicolon "; and (2) the Owner" through the end of the sentence.

Delete the second sentence in its entirety.

A.3.2.2.1 Insert "$1,000,000.00" in the blank for each occurrence.
Insert "$3,000,000.00" in the blank for general aggregate.
Insert "$3,000,000.00" in the blank for aggregate for products-completed operations hazard.

A.3.2.3 Insert “$1,000,000.00” in the blank for per accident.

A.3.2.6 Insert “$500,000.00” in the blank for each accident.
Insert “$500,000.00” in the blank for each employee.
Insert “$500,000.00” in the blank for policy limit.

A.3.2.8 Insert “$1,000,000.00” in the blank for per claim.
Insert “$3,000,000.00” in the blank for in the aggregate.

A.3.2.9 Insert “$1,000,000.00” in the blank for per claim.
Insert “$3,000,000.00” in the blank for in the aggregate.

A.3.2.10 Insert “$2,000,000.00” in the blank for per claim.
Insert “$4,000,000.00” in the blank for in the aggregate.

A.3.2.11 Strike in its entirety.

A.3.2.12 Strike in its entirety.

A.3.3.2.1 Delete paragraph 3.3.2.1 in its entirety

A.3.3.2.2 Strike in its entirety.

A.3.3.2.3 Insert “$1,000,000.00” in the blanks for per claim.
Insert “$3,000,000.00” in the blanks for in the aggregate.

A.3.4 Insert the actual contract price in both the Payment Bond and the Performance Bond Penal Sum blanks. It must be 100% of the contract price.

Strike the last sentence in this section and replace with “Payment and Performance Bonds shall be in the standard form issued by the Delaware Office of Management and Budget.”

END OF SECTION

SECTION 006113 – PERFORMANCE AND PAYMENT BONDS

1. PERFORMANCE AND PAYMENT BONDS

1.1 Bonds must be in the following form:

1. Form of Performance Bond (006113.13 attached).
2. Form of Payment Bond (006113.16 attached).

STATE OF DELAWARE
OFFICE OF MANAGEMENT AND BUDGET

PERFORMANCE BOND

Bond Number: _____

KNOW ALL PERSONS BY THESE PRESENTS, that we, _____, as principal ("**Principal**"), and _____, a _____ corporation, legally authorized to do business in the State of _____, as surety ("**Surety**"), are held and firmly bound unto the New Castle County Vocational Technical School District 1417 Newport Road Wilmington, DE 19804 ("**Owner**"), in the amount of _____ ($_____), to be paid to **Owner**, for which payment well and truly to be made, we do bind ourselves, our and each and every of our heirs, executors, administrations, successors and assigns, jointly and severally, for and in the whole firmly by these presents.
.

Sealed with our seals and dated this _____ day of _____, 20___.

NOW THE CONDITION OF THIS OBLIGATION IS SUCH, that if **Principal**, who has been awarded by **Owner** that certain contract known as Contract No. _____ dated the _____ day of _____, 20__ (the "Contract"), which Contract is incorporated herein by reference, shall well and truly provide and furnish all materials, appliances and tools and perform all the work required under and pursuant to the terms and conditions of the Contract and the Contract Documents (as defined in the Contract) or any changes or modifications thereto made as therein provided, shall make good and reimburse **Owner** sufficient funds to pay the costs of completing the Contract that **Owner** may sustain by reason of any failure or default on the part of **Principal**, and shall also indemnify and save harmless **Owner** from all costs, damages and expenses arising out of or by reason of the performance of the Contract and for as long as provided by the Contract; then this obligation shall be void, otherwise to be and remain in full force and effect.

Surety, for value received, hereby stipulates and agrees, if requested to do so by **Owner**, to fully perform and complete the work to be performed under the Contract pursuant to the terms, conditions and covenants thereof, if for any cause **Principal** fails or neglects to so fully perform and complete such work.

Surety, for value received, for itself and its successors and assigns, hereby stipulates and agrees that the obligation of **Surety** and its bond shall be in no way impaired or affected by any extension of time, modification, omission, addition or change in or to the Contract or the work to be performed thereunder, or by any payment thereunder before the time required therein, or by any waiver of any provisions thereof, or by any assignment, subletting or other transfer thereof or of any work to be performed or any monies due or to become due thereunder; and **Surety** hereby waives notice of any and all such extensions, modifications, omissions, additions, changes, payments, waivers,

assignments, subcontracts and transfers and hereby expressly stipulates and agrees that any and all things done and omitted to be done by and in relation to assignees, subcontractors, and other transferees shall have the same effect as to **Surety** as though done or omitted to be done by or in relation to **Principal**.

Surety hereby stipulates and agrees that no modifications, omissions or additions in or to the terms of the Contract shall in any way whatsoever affect the obligation of **Surety** and its bond.

Any proceeding, legal or equitable, under this Bond may be brought in any court of competent jurisdiction in the State of Delaware. Notices to **Surety** or Contractor may be mailed or delivered to them at their respective addresses shown below.

IN WITNESS WHEREOF, **Principal** and **Surety** have hereunto set their hand and seals, and such of them as are corporations have caused their corporate seal to be hereto affixed and these presents to be signed by their duly authorized officers, the day and year first above written.

PRINCIPAL

Name: _____

Witness or Attest: Address: _____

_____ By: _____(SEAL)
Name: Name:
Title:

(Corporate Seal)

SURETY

Name: _____

Witness or Attest: Address: _____

_____ By: _____ (SEAL)
Name: Name:
Title:

(Corporate Seal)

STATE OF DELAWARE
OFFICE OF MANAGEMENT AND BUDGET

PAYMENT BOND

Bond Number: _____

KNOW ALL PERSONS BY THESE PRESENTS, that we, _____, as principal ("**Principal**"), and _____, a _____ _____ corporation, legally authorized to do business in the State of _____, as surety ("**Surety**"), are held and firmly bound unto the New Castle County Vocational Technical School District 1417 Newport Road Wilmington, DE 19804 ("**Owner**"), in the amount of _____ ($_____), to be paid to **Owner**, for which payment well and truly to be made, we do bind ourselves, our and each and every of our heirs, executors, administrations, successors and assigns, jointly and severally, for and in the whole firmly by these presents.

Sealed with our seals and dated this _____ day of_____, 20____.

NOW THE CONDITION OF THIS OBLIGATION IS SUCH, that if **Principal**, who has been awarded by **Owner** that certain contract known as Contract No._____ _____dated the _____ day of _____, 20____ (the "Contract"), which Contract is incorporated herein by reference, shall well and truly pay all and every person furnishing materials or performing labor or service in and about the performance of the work under the Contract, all and every sums of money due him, her, them or any of them, for all such materials, labor and service for which **Principal** is liable, shall make good and reimburse **Owner** sufficient funds to pay such costs in the completion of the Contract as **Owner** may sustain by reason of any failure or default on the part of **Principal**, and shall also indemnify and save harmless **Owner** from all costs, damages and expenses arising out of or by reason of the performance of the Contract and for as long as provided by the Contract; then this obligation shall be void, otherwise to be and remain in full force and effect.

Surety, for value received, for itself and its successors and assigns, hereby stipulates and agrees that the obligation of **Surety** and its bond shall be in no way impaired or affected by any extension of time, modification, omission, addition or change in or to the Contract or the work to be performed thereunder, or by any payment thereunder before the time required therein, or by any waiver of any provisions thereof, or by any assignment, subletting or other transfer thereof or of any work to be performed or any monies due or to become due thereunder; and **Surety** hereby waives notice of any and all such extensions, modifications, omissions, additions, changes, payments, waivers, assignments, subcontracts and transfers and hereby expressly stipulates and agrees that any and all things done and omitted to be done by and in relation to assignees, subcontractors, and other transferees shall have the same effect as to **Surety** as though done or omitted to be done by or in relation to **Principal**.

Surety hereby stipulates and agrees that no modifications, omission or additions in or to the terms of the Contract shall in any way whatsoever affect the obligation of **Surety** and its bond.

Any proceeding, legal or equitable, under this Bond may be brought in any court of competent jurisdiction in the State of Delaware. Notices to **Surety** or Contractor may be mailed or delivered to them at their respective addresses shown below.

IN WITNESS WHEREOF, **Principal** and **Surety** have hereunto set their hand and seals, and such of them as are corporations have caused their corporate seal to be hereto affixed and these presents to be signed by their duly authorized officers, the day and year first above written.

PRINCIPAL

Name: _____

Witness or Attest: Address: _____

_____ By: _____(SEAL)
Name: Name:
Title:

(Corporate Seal)

SURETY

Name: _____

Witness or Attest: Address: _____

_____ By: _____(SEAL)
Name: Name:
Title:

(Corporate Seal)

SECTION 006216 – CERTIFICATE OF INSURANCE

In conjunction with Insurance Requirements AIA General Conditions, Article 11, the Contractor shall be bound by the following limits of liability insurance (for Contracts under this Bid Pac). The Contractor shall use the standard "ACCORD" for titled "Certificate of Insurance" in submitting his liability insurance limits. The required limits to be inserted in accordance with the sample "ACCORD" form in this section:

GENERAL NOTES

1. Other Insurance

    A. Contractor shall carry any necessary insurance required to cover Owned and Rental equipment that may be necessary for them to use in the performance of the Work.

2. Contractor shall have the following additional items added to his required "ACCORD" form Certificate of Insurance:

    A. Name and Address of Insured (Contractor).

    B. Description of Operations/Locations – Hodgson Vocational Technical High School 2575 Glasgow Avenue, Newark, DE 19702

3. Added Insured – New Castle County Vocational Technical School District and EDiS Company

4. Certificate Holder – New Castle County Vocational Technical School District
    1415 Newport Road
    Wilmington, Delaware 19804

Contractors shall note that although not a part of AIA Document A232 - 2019 Edition, these additional articles apply as noted to this Project.

A sample certificate is bound into the Project Manual immediately following this Document.

END OF SECTION

ACORD — CERTIFICATE OF LIABILITY INSURANCE

Date (MM/DD/YYYY)

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER **SAMPLE CERTIFICATE**	CONTACT NAME:	
	PHONE (A/C, No, Ext):	FAX (A/C, No):
	E-MAIL ADDRESS:	
	PRODUCER CUSTOMER ID #:	
	INSURER(S) AFFORDING COVERAGE	NAIC #
INSURED	INSURER A:	
	INSURER B:	
	INSURER C:	
	INSURER D:	

COVERAGES **CERTIFICATE NUMBER:** **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS	
X	**GENERAL LIABILITY** X COMMERCIAL GENERAL LIABILITY [ ] CLAIMS-MADE [X] OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: [ ] POLICY [X] PROJECT [ ] LOC	X	X	XXXXXXX	XX/XX/XXXX	XX/XX/XXXX	EACH OCCURENCE DAMAGE TO RENTED PREMISES (Ea occurrence) MED EXP (Any one person) PERSONAL & ADV INJURY GENERAL AGGREGATE PRODUCTS – COMP/OP AGG	**$1,000,000** **$100,000** **$10,000** **$1,000,000** **$3,000,000** **$2,000,000**
X	**AUTOMOBILE LIABILITY** X ANY AUTO [ ] ALL OWNED AUTOS [ ] SCHEDULED AUTOS X HIRED AUTOS X NON-OWNED AUTOS	X	X	XXXXXXX	XX/XX/XXXX	XX/XX/XXXX	COMBINED SINGLE LIMIT (Ea accident) BODILY INJURY (Per person) BODILY INJURY (Per accident) PROPERTY DAMAGE (Per accident)	**$1,000,000**
X	X **UMBRELLA LIAB** [X] OCCUR [ ] **EXCESS LIAB** [ ] CLAIMS-MADE [ ] DEDUCTIBLE [ ] RETENTION $	X	X	XXXXXXXX	XX/XX/XXXX	XX/XX/XXXX	EACH OCCURRENCE AGGREGATE EACH OCCURRENCE AGGREGATE	**$5,000,000** **$5,000,000**
X	**WORKERS COMPENSATION AND EMPLOYERS' LIABILITY** Y / N ANY PROPRIETOR / PARTNER / EXECUTIVE OFFICER / MEMBER EXCLUDED? If yes, describe under DESCRIPTION OF OPERATIONS below		X	XXXXXXXX	XX/XX/XXXX	XX/XX/XXXX	X WC STATUTORY LIMITS [ ] OTH-ER E.L. EACH ACCIDENT E.L. DISEASE - EACH EMPLOYEE E.L. DISEASE - POLICY LIMIT	 **$500,000** **$500,000** **$500,000**
X	**POLLUTION LIABILITY (For Hazardous material, site excavation/utility, and building envelope subcontractors)** X CLAIMS MADE FORM	X	X	XXXXXXXX	XX/XX/XXXX	XX/XX/XXXX	EACH CLAIM POLICY AGGREGATE	**$2,000,000** **$2,000,000**
X	**PROFESSIONAL LIABILITY (for all Design and Professional Service subcontractors)** X CLAIMS MADE FORM			XXXXXXXX	XX/XX/XXXX	XX/XX/XXXX	EACH CLAIM POLICY AGGREGATE	**$2,000,000** **$2,000,000**

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

Project: Hodgson Vocational Technical High School

Added Insured: New Castle County Vocational Technical School District and EDiS Company, as well as any other party as required by contract are listed as additional insureds under all policies (except Workers Compensation and Professional Liability) for all work performed by the named insured. The General Liability and Umbrella/Excess Liability aggregate shall apply on a per-project basis and all policies shall be primary and non-contributing with respects to any insurance maintained by the additional insureds. Umbrella policy follows form as respects to Additional Insured status on the CGL, Employers Liability and Automobile Liability policies. A waiver of subrogation applies in favor of the additional insureds under all policies.

In addition to the above language, please provide the General Liability, On-going and Completed Operations Additional Insured endorsements with all required additional insureds listed in the Schedule box (if not a blanket policy), the Primary and Non-Contributory Endorsements, and the Waiver of Subrogation endorsements for all policies with all required additional insured entities listed (if not a blanket policy). Provide evidence of no EIFS exclusions, if within scope of work.]

CERTIFICATE HOLDER	CANCELLATION
New Castle County Vocational Technical School District 1417 Newport Road Wilmington, DE 19804	**SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.** AUTHORIZED REPRESENTATIVE

SAMPLE

Professional Liability and Pollution Insurance Requirements

Contract Number	Contract Name	Professional Liability Insurance	Pollution Insurance
Contract D-01:	Unit Masonry		X
Contract D-02:	Miscellaneous Metals, Stairs, and Rails	X	X
Contract D-03:	Exterior Structural Stud Assembly	X	X
Contract D-04:	Carpentry and General Work	X	X
Contract D-05:	Exterior Metal Panels	X	X
Contract D-06:	Drywall and Interior Metal Framing	X	X
Contract D-07:	General Labor and Clean-up		
Contract D-08:	Roofing	X	X
Contract D-09:	Fireproofing	X	X
Contract D-10:	Joint Sealants and Preformed Joint Assemblies		X
Contract D-11:	Hollow Metal, Wood Doors, and Finish Hardware		
Contract D-12:	Overhead Coiling Doors and Grates		X
Contract D-13:	Curtainwall/Glazing/Storefronts	X	X
Contract D-14:	Tiling		
Contract D-15:	Acoustical and Specialty Ceilings	X	
Contract D-16:	Flooring		
Contract D-17:	Resilient Athletic Flooring		X
Contract D-18:	Resinous Matrix Terrazzo Flooring		X
Contract D-19:	Fluid Applied Flooring		X
Contract D-20:	Paint and VWC		
Contract D-21:	Wood Strip Flooring-Gym Flooring	X	
Contract D-22:	Specialties	X	X
Contract D-23:	Food Service Equipment	X	
Contract D-24:	Window Shades and Electric Roller Shades		
Contract D-25:	Laminate Clad Casework, Countertops, and Sills		
Contract D-26:	Stage Rigging, Lighting, and Accessories	X	X
Contract D-27:	Fixed Auditorium Seating		
Contract D-28:	Wood Laboratory Furniture and Specialty Casework		
Contract D-29:	Telescoping Bleachers and Platforms	X	
Contract D-30:	Hydraulic Holeless Passenger Elevator	X	X
Contract D-31:	Fire Protection	X	X
Contract D-32:	Plumbing	X	X
Contract D-33:	Mechanical Piping - HVAC	X	X
Contract D-34:	Testing, Adjusting, and Balancing		
Contract D-35:	Electrical, Lighting and Fire Alarm Systems	X	X
Contract D-36:	Special Systems	X	
Contract D-37:	Vertical Retracting Walls	X	
Contract D-38:	Miscellaneous Concrete and Grouting		X

SECTION 007200 – GENERAL CONDITIONS

1. SUMMARY

   A. The General Conditions for this Project are the American Institute of Architects General Conditions of the Contract for Construction, Construction Manager as Advisor Edition, AIA Document A232 - 2019 Edition.

   B. A copy of AIA Document A232 - 2019 Edition is bound into this Project Manual following this page

END OF SECTION

AIA® Document A232® – 2019

General Conditions of the Contract for Construction, Construction Manager as Adviser Edition

for the following PROJECT:
(Name, and location or address)

Hodgson Vocational Technical High School
2575 Glasgow Avenue
Newark, DE 19702

THE CONSTRUCTION MANAGER:
(Name, legal status, and address)

EDiS Company
110 South Poplar Street, Suite 400
Wilmington, DE 19801

THE OWNER:
(Name, legal status, and address)

New Castle County Vocational Technical School District
1417 Newport Road
Wilmington, DE 19804

THE ARCHITECT:
(Name, legal status, and address)

Joint Venture:
ABHA
1621 North Lincoln Street
Wilmington, DE 19806

BSA+A
954 Justison Street
Wilmington, DE 19801

ADDITIONS AND DELETIONS:
The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be used in conjunction with AIA Documents A132™–2019, Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition; B132™–2019, Standard Form of Agreement Between Owner and Architect, Construction Manager as Adviser Edition; and C132™–2019, Standard Form of Agreement Between Owner and Construction Manager as Adviser.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

TABLE OF ARTICLES

1 GENERAL PROVISIONS

2 OWNER

3 CONTRACTOR

4 ARCHITECT AND CONSTRUCTION MANAGER

5 SUBCONTRACTORS

6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

7 CHANGES IN THE WORK

8 TIME

9 PAYMENTS AND COMPLETION

10 PROTECTION OF PERSONS AND PROPERTY

11 INSURANCE AND BONDS

12 UNCOVERING AND CORRECTION OF WORK

13 MISCELLANEOUS PROVISIONS

14 TERMINATION OR SUSPENSION OF THE CONTRACT

15 CLAIMS AND DISPUTES

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

ARTICLE 1 GENERAL PROVISIONS

§ 1.1 Basic Definitions

§ 1.1.1 The Contract Documents. The Contract Documents are enumerated in the Agreement between the Owner and Contractor (hereinafter the Agreement) and consist of the Agreement, Conditions of the Contract (General, Supplementary and other Conditions), Drawings, Specifications, Addenda issued prior to execution of the Contract, other documents listed in the Agreement, and Modifications issued after execution of the Contract. A Modification is (1) a written amendment to the Contract signed by both parties, (2) a Change Order, (3) a Construction Change Directive, or (4) a written order for a minor change in the Work issued by the Architect. Unless specifically enumerated in the Agreement, the Contract Documents do not include the advertisement or invitation to bid, Instructions to Bidders, sample forms, other information furnished by the Owner in anticipation of receiving bids or proposals, the Contractor's bid or proposal, or portions of addenda relating to bidding or proposal requirements.

§ 1.1.2 The Contract. The Contract Documents form the Contract for Construction. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations, or agreements, either written or oral. The Contract may be amended or modified only by a Modification. The Contract Documents shall not be construed to create a contractual relationship of any kind (1) between the Contractor and the Architect or the Architect's consultants, (2) between the Owner and the Construction Manager or the Construction Manager's consultants, (3) between the Owner and the Architect or the Architect's consultants, (4) between the Contractor and the Construction Manager or the Construction Manager's consultants, (5) between the Owner and a Subcontractor or Sub-subcontractor (6) between the Construction Manager and the Architect, or (7) between any persons or entities other than the Owner and Contractor. The Construction Manager and Architect shall, however, be entitled to performance and enforcement of obligations under the Contract intended to facilitate performance of their duties.

§ 1.1.3 The Work. The term "Work" means the construction and services required by the Contract Documents, whether completed or partially completed, and includes all other labor, materials, equipment, and services provided or to be provided by the Contractor to fulfill the Contractor's obligations. The Work may constitute the whole or a part of the Project.

§ 1.1.4 The Project. The Project is the total construction of which the Work performed under the Contract Documents may be the whole or a part and which may include construction by other Contractors, and by the Owner's own forces and Separate Contractors.

§ 1.1.5 Contractors. Contractors are persons or entities, other than the Contractor or Separate Contractors, who perform Work under contracts with the Owner that are administered by the Architect and Construction Manager.

§ 1.1.6 Separate Contractors. Separate Contractors are persons or entities who perform construction under separate contracts with the Owner not administered by the Architect and Construction Manager.

§ 1.1.7 The Drawings. The Drawings are the graphic and pictorial portions of the Contract Documents showing the design, location and dimensions of the Work, generally including plans, elevations, sections, details, schedules, and diagrams.

§ 1.1.8 The Specifications. The Specifications are that portion of the Contract Documents consisting of the written requirements for materials, equipment, systems, standards and workmanship for the Work, and performance of related services.

§ 1.1.9 Instruments of Service. Instruments of Service are representations, in any medium of expression now known or later developed, of the tangible and intangible creative work performed by the Architect and the Architect's consultants under their respective professional services agreements. Instruments of Service may include, without limitation, studies, surveys, models, sketches, drawings, specifications, and other similar materials.

§ 1.1.10 Initial Decision Maker. The Initial Decision Maker is the person identified in the Agreement to render initial decisions on Claims in accordance with Section 15.2. The Initial Decision Maker shall not show partiality to the Owner or Contractor and shall not be liable for results of interpretations or decisions rendered in good faith.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

§ 1.2 Correlation and Intent of the Contract Documents

§ 1.2.1 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary, and what is required by one shall be as binding as if required by all; performance by the Contractor shall be required only to the extent consistent with the Contract Documents and reasonably inferable from them as being necessary to produce the indicated results.

§ 1.2.1.1 The invalidity of any provision of the Contract Documents shall not invalidate the Contract or its remaining provisions. If it is determined that any provision of the Contract Documents violates any law, or is otherwise invalid or unenforceable, then that provision shall be revised to the extent necessary to make that provision legal and enforceable. In such case the Contract Documents shall be construed, to the fullest extent permitted by law, to give effect to the parties' intentions and purposes in executing the Contract.

§ 1.2.2 Organization of the Specifications into divisions, sections and articles, and arrangement of Drawings shall not control the Contractor in dividing the Work among Subcontractors or in establishing the extent of Work to be performed by any trade.

§ 1.2.3 Unless otherwise stated in the Contract Documents, words that have well-known technical or construction industry meanings are used in the Contract Documents in accordance with such recognized meanings.

§ 1.3 Capitalization

Terms capitalized in these General Conditions include those that are (1) specifically defined, (2) the titles of numbered articles, or (3) the titles of other documents published by the American Institute of Architects.

§ 1.4 Interpretation

In the interest of brevity the Contract Documents frequently omit modifying words such as "all" and "any" and articles such as "the" and "an," but the fact that a modifier or an article is absent from one statement and appears in another is not intended to affect the interpretation of either statement.

§ 1.5 Ownership and Use of Drawings, Specifications, and Other Instruments of Service

§ 1.5.1 The Architect and the Architect's consultants shall be deemed the authors and owners of their respective Instruments of Service, including the Drawings and Specifications, and retain all common law, statutory, and other reserved rights in their Instruments of Service, including copyrights. The Contractor, Subcontractors, sub-subcontractors, and suppliers shall not own or claim a copyright in the Instruments of Service. Submittal or distribution to meet official regulatory requirements or for other purposes in connection with the Project is not to be construed as publication in derogation of the Architect's or Architect's consultants' reserved rights.

§ 1.5.2 The Contractor, Subcontractors, Sub-subcontractors, and suppliers are authorized to use and reproduce the Instruments of Service provided to them, subject to any protocols established pursuant to Sections 1.7 and 1.8, solely and exclusively for execution of the Work. All copies made under this authorization shall bear the copyright notice, if any, shown on the Instruments of Service. The Contractor, Subcontractors, Sub-subcontractors, and suppliers may not use the Instruments of Service on other projects or for additions to the Project outside the scope of the Work without the specific written consent of the Owner, Architect, and the Architect's consultants.

§ 1.6 Notice

§ 1.6.1 Except as otherwise provided in Section 1.6.2, where the Contract Documents require one party to notify or give notice to the other party, such notice shall be provided in writing to the designated representative of the party to whom the notice is addressed and shall be deemed to have been duly served if delivered in person, by mail, by courier, or by electronic transmission if a method for electronic transmission is set forth in the Agreement.

§ 1.6.2 Notice of Claims as provided in Section 15.1.3 shall be provided in writing and shall be deemed to have been duly served only if delivered to the designated representative of the party to whom the notice is addressed by certified or registered mail, or by courier providing proof of delivery.

§ 1.7 Digital Data Use and Transmission

The parties shall agree upon protocols governing the transmission and use of Instruments of Service or any other information or documentation in digital form. The parties will use AIA Document E203™–2013, Building

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

Information Modeling and Digital Data Exhibit, to establish the protocols for the development, use, transmission, and exchange of digital data.

§ 1.8 Building Information Models Use and Reliance

Any use of, or reliance on, all or a portion of a building information model without agreement to protocols governing the use of, and reliance on, the information contained in the model and without having those protocols set forth in AIA Document E203™–2013, Building Information Modeling and Digital Data Exhibit, and the requisite AIA Document G202™–2013, Project Building Information Modeling Protocol Form, shall be at the using or relying party's sole risk and without liability to the other party and its contractors or consultants, the authors of, or contributors to, the building information model, and each of their agents and employees.

ARTICLE 2 OWNER

§ 2.1 General

§ 2.1.1 The Owner is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Owner shall designate in writing a representative who shall have express authority to bind the Owner with respect to all matters requiring the Owner's approval or authorization. Except as otherwise provided in Section 4.2.1, the Construction Manager and the Architect do not have such authority. The term "Owner" means the Owner or the Owner's authorized representative.

§ 2.1.2 The Owner shall furnish to the Contractor, within fifteen days after receipt of a written request, information necessary and relevant for the Contractor to evaluate, give notice of, or enforce mechanic's lien rights. Such information shall include a correct statement of the record legal title to the property on which the Project is located, usually referred to as the site, and the Owner's interest therein.

§ 2.2 Evidence of the Owner's Financial Arrangements

§ 2.2.1 Prior to commencement of the Work, and upon written request by the Contractor, the Owner shall furnish to the Contractor reasonable evidence that the Owner has made financial arrangements to fulfill the Owner's obligations under the Contract. The Contractor shall have no obligation to commence the Work until the Owner provides such evidence. If commencement of the Work is delayed under this Section 2.2.1, the Contract Time shall be extended appropriately.

§ 2.2.2 Following commencement of the Work and upon written request by the Contractor, the Owner shall furnish to the Contractor reasonable evidence that the Owner has made financial arrangements to fulfill the Owner's obligations under the Contract only if (1) the Owner fails to make payments to the Contractor as the Contract Documents require; (2) the Contractor identifies in writing a reasonable concern regarding the Owner's ability to make payment when due; or (3) a change in the Work materially changes the Contract Sum. If the Owner fails to provide such evidence, as required, within fourteen days of the Contractor's request, the Contractor may immediately stop the Work and, in that event, shall notify the Owner that the Work has stopped. However, if the request is made because a change in the Work materially changes the Contract Sum under (3) above, the Contractor may immediately stop only that portion of the Work affected by the change until reasonable evidence is provided. If the Work is stopped under this Section 2.2.2, the Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shutdown, delay and start-up, plus interest as provided in the Contract Documents.

§ 2.2.3 After the Owner furnishes evidence of financial arrangements under this Section 2.2, the Owner shall not materially vary such financial arrangements without prior notice to the Contractor.

§ 2.2.4 Where the Owner has designated information furnished under this Section 2.2 as "confidential," the Contractor shall keep the information confidential and shall not disclose it to any other person. However, the Contractor may disclose "confidential" information, after seven (7) days' notice to the Owner, where disclosure is required by law, including a subpoena or other form of compulsory legal process issued by a court or governmental entity, or by court or arbitrator(s) order. The Contractor may also disclose "confidential" information to its employees, consultants, sureties, Subcontractors and their employees, Sub-subcontractors, and others who need to know the content of such information solely and exclusively for the Project and who agree to maintain the confidentiality of such information.

§ 2.3 Information and Services Required of the Owner

§ 2.3.1 Except for permits and fees that are the responsibility of the Contractor under the Contract Documents, including those required under Section 3.7.1, the Owner shall secure and pay for necessary approvals, easements,

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

assessments and charges required for construction, use or occupancy of permanent structures or for permanent changes in existing facilities. Unless otherwise provided under the Contract Documents, the Owner, assisted by the Construction Manager, shall secure and pay for the building permit.

§ 2.3.2 The Owner shall retain an architect lawfully licensed to practice architecture, or an entity lawfully practicing architecture, in the jurisdiction where the Project is located. That person or entity is identified as the Architect in the Agreement and is referred to throughout the Contract Documents as if singular in number.

§ 2.3.3 The Owner shall retain a construction manager adviser lawfully practicing construction management in the jurisdiction where the Project is located. That person or entity is identified as the Construction Manager in the Agreement and is referred to throughout the Contract Documents as if singular in number.

§ 2.3.4 If the employment of the Construction Manager or Architect terminates, the Owner shall employ a successor construction manager or architect to whom the Contractor has no reasonable objection and whose status under the Contract Documents shall be that of the Construction Manager or Architect, respectively.

§ 2.3.5 The Owner shall furnish surveys describing physical characteristics, legal limitations and utility locations for the site of the Project, and a legal description of the site. The Contractor shall be entitled to rely on the accuracy of information furnished by the Owner but shall exercise proper precautions relating to the safe performance of the Work.

§ 2.3.6 The Owner shall furnish information or services required of the Owner by the Contract Documents with reasonable promptness. The Owner shall also furnish any other information or services under the Owner's control and relevant to the Contractor's performance of the Work with reasonable promptness after receiving the Contractor's written request for such information or services.

§ 2.3.7 Unless otherwise provided in the Contract Documents, the Owner shall furnish to the Contractor one copy of the Contract Documents for purposes of making reproductions pursuant to Section 1.5.2.

§ 2.3.8 The Owner shall forward all communications to the Contractor through the Construction Manager. Other communication shall be made as set forth in Section 4.2.6.

§ 2.4 Owner's Right to Stop the Work

If the Contractor fails to correct Work that is not in accordance with the requirements of the Contract Documents as required by Section 12.2 or repeatedly fails to carry out Work in accordance with the Contract Documents, the Owner may issue a written order to the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, the right of the Owner to stop the Work shall not give rise to a duty on the part of the Owner to exercise this right for the benefit of the Contractor or any other person or entity, except to the extent required by Section 6.1.3.

§ 2.5 Owner's Right to Carry Out the Work

If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a ten-day period after receipt of notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may, without prejudice to other remedies the Owner may have, correct such default or neglect. Such action by the Owner and amounts charged to the Contractor are both subject to review by the Construction Manager and prior approval of the Architect, and the Construction Manager or Architect may, pursuant to Section 9.5.1, withhold or nullify a Certificate for Payment in whole or in part, to the extent reasonably necessary to reimburse the Owner for the reasonable cost of correcting such deficiencies, including Owner's expenses and compensation for the Construction Manager's and Architect's and their respective consultants' additional services made necessary by such default, neglect, or failure. If current and future payments are not sufficient to cover such amounts, the Contractor shall pay the difference to the Owner. If the Contractor disagrees with the actions of the Owner or the Architect, or the amounts claimed as costs to the Owner, the Contractor may file a Claim pursuant to Article 15.

ARTICLE 3 CONTRACTOR

§ 3.1 General

§ 3.1.1 The Contractor is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Contractor shall be lawfully licensed, if required in the jurisdiction

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

where the Project is located. The Contractor shall designate in writing a representative who shall have express authority to bind the Contractor with respect to all matters under this Contract. The term "Contractor" means the Contractor or the Contractor's authorized representative.

§ 3.1.2 The Contractor shall perform the Work in accordance with the Contract Documents.

§ 3.1.3 The Contractor shall not be relieved of its obligations to perform the Work in accordance with the Contract Documents either by activities or duties of the Construction Manager or Architect in their administration of the Contract, or by tests, inspections or approvals required or performed by persons or entities other than the Contractor.

§ 3.2 Review of Contract Documents and Field Conditions by Contractor

§ 3.2.1 Execution of the Contract by the Contractor is a representation that the Contractor has visited the site, become generally familiar with local conditions under which the Work is to be performed, and correlated personal observations with requirements of the Contract Documents.

§ 3.2.2 Because the Contract Documents are complementary, the Contractor shall, before starting each portion of the Work, carefully study and compare the various Contract Documents relative to that portion of the Work, as well as the information furnished by the Owner pursuant to Section 2.3.5, shall take field measurements of any existing conditions related to that portion of the Work, and shall observe any conditions at the site affecting it. These obligations are for the purpose of facilitating coordination and construction by the Contractor and are not for the purpose of discovering errors, omissions, or inconsistencies in the Contract Documents; however, the Contractor shall promptly report to the Construction Manager and Architect any errors, inconsistencies or omissions discovered by or made known to the Contractor as a request for information submitted to the Construction Manager in such form as the Construction Manager and Architect may require. It is recognized that the Contractor's review is made in the Contractor's capacity as a contractor and not as a licensed design professional, unless otherwise specifically provided in the Contract Documents.

§ 3.2.3 The Contractor is not required to ascertain that the Contract Documents are in accordance with applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, but the Contractor shall promptly report to the Construction Manager and Architect any nonconformity discovered by or made known to the Contractor as a request for information submitted to Construction Manager in such form as the Construction Manager and Architect may require.

§ 3.2.4 If the Contractor believes that additional cost or time is involved because of clarifications or instructions the Architect issues in response to the Contractor's notices or requests for information pursuant to Sections 3.2.2 or 3.2.3, the Contractor shall submit Claims as provided in Article 15. If the Contractor fails to perform the obligations of Sections 3.2.2 or 3.2.3, the Contractor shall pay such costs and damages to the Owner, subject to section 15.1.7, as would have been avoided if the Contractor had performed such obligations. If the Contractor performs those obligations, the Contractor shall not be liable to the Owner or Architect for damages resulting from errors, inconsistencies or omissions in the Contract Documents, for differences between field measurements or conditions and the Contract Documents, or for nonconformities of the Contract Documents to applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities.

§ 3.3 Supervision and Construction Procedures

§ 3.3.1 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for, and have control over, construction means, methods, techniques, sequences, and procedures, and for coordinating all portions of the Work under the Contract. If the Contract Documents give specific instructions concerning construction means, methods, techniques, sequences, or procedures, the Contractor shall evaluate the jobsite safety thereof and shall be solely responsible for the jobsite safety of such means, methods, techniques, sequences, or procedures. If the Contractor determines that such means, methods, techniques, sequences or procedures may not be safe, the Contractor shall give timely notice to the Owner, the Construction Manager, and the Architect, and shall propose alternative means, methods, techniques, sequences, or procedures. The Architect shall evaluate the proposed alternative solely for conformance with the design intent for the completed construction. The Construction Manager shall review the proposed alternative for sequencing, constructability, and coordination impacts on the other Contractors. Unless the Architect or the Construction Manager objects to the Contractor's proposed alternative, the Contractor shall perform the Work using its alternative means, methods, techniques, sequences, or procedures.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

§ 3.3.2 The Contractor shall be responsible to the Owner for acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons or entities performing portions of the Work for, or on behalf of, the Contractor or any of its Subcontractors.

§ 3.3.3 The Contractor shall be responsible for inspection of portions of the Project already performed to determine that such portions are in proper condition to receive subsequent Work.

§ 3.4 Labor and Materials

§ 3.4.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for proper execution and completion of the Work, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work.

§ 3.4.2 Except in the case of minor changes in the Work approved by the Architect in accordance with Section 3.12.8 or ordered by the Architect in accordance with Section 7.4, the Contractor may make substitutions only with the consent of the Owner, after evaluation by the Architect, in consultation with the Construction Manager, and in accordance with a Change Order or Construction Change Directive.

§ 3.4.3 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Work. The Contractor shall not permit employment of unfit persons or persons not properly skilled in tasks assigned to them.

§ 3.5 Warranty

§ 3.5.1 The Contractor warrants to the Owner, Construction Manager, and Architect that materials and equipment furnished under the Contract will be of good quality and new unless the Contract Documents require or permit otherwise. The Contractor further warrants that the Work will conform to the requirements of the Contract Documents and will be free from defects, except for those inherent in the quality of the Work the Contract Documents require or permit. Work, materials, or equipment not conforming to these requirements may be considered defective. The Contractor's warranty excludes remedy for damage or defect caused by abuse, alterations to the Work not executed by the Contractor, improper or insufficient maintenance, improper operation, or normal wear and tear and normal usage. If required by the Construction Manager or Architect, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment.

§ 3.5.2 All material, equipment, or other special warranties required by the Contract Documents shall be issued in the name of the Owner, or shall be transferable to the Owner, and shall commence in accordance with Section 9.8.4.

§ 3.6 Taxes

The Contractor shall pay sales, consumer, use and similar taxes for the Work or portions thereof provided by the Contractor that are legally enacted when bids are received or negotiations concluded, whether or not yet effective or merely scheduled to go into effect.

§ 3.7 Permits, Fees, Notices, and Compliance with Laws

§ 3.7.1 Unless otherwise provided in the Contract Documents, the Owner, assisted by the Construction Manager, shall secure and pay for the building permit. The Contractor shall secure and pay for other permits, fees, licenses, and inspections by government agencies necessary for proper execution and completion of the Work that are customarily secured after execution of the Contract and legally required at the time bids are received or negotiations concluded.

§ 3.7.2 The Contractor shall comply with and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities applicable to performance of the Work.

§ 3.7.3 If the Contractor performs Work knowing it to be contrary to applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, the Contractor shall assume appropriate responsibility for such Work and shall bear the costs attributable to correction.

§ 3.7.4 Concealed or Unknown Conditions. If the Contractor encounters conditions at the site that are (1) subsurface or otherwise concealed physical conditions that differ materially from those indicated in the Contract Documents or

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

(2) unknown physical conditions of an unusual nature that differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, the Contractor shall promptly provide notice to the Owner, Construction Manager, and the Architect before conditions are disturbed and in no event later than 14 days after first observance of the conditions. The Architect and Construction Manager will promptly investigate such conditions and, if the Architect, in consultation with the Construction Manager, determines that they differ materially and cause an increase or decrease in the Contractor's cost of, or time required for, performance of any part of the Work, will recommend that an equitable adjustment be made in the Contract Sum or Contract Time, or both. If the Architect, in consultation with the Construction Manager, determines that the conditions at the site are not materially different from those indicated in the Contract Documents and that no change in the terms of the Contract is justified, the Architect shall promptly notify the Owner, Construction Manager, and Contractor, stating the reasons. If the Owner or Contractor disputes the Architect's determination or recommendation, either party may submit a Claim as provided in Article 15.

§ 3.7.5 If, in the course of the Work, the Contractor encounters human remains or recognizes the existence of burial markers, archaeological sites or wetlands not indicated in the Contract Documents, the Contractor shall immediately suspend any operations that would affect them and shall notify the Owner, Construction Manager, and Architect. Upon receipt of such notice, the Owner shall promptly take any action necessary to obtain governmental authorization required to resume the operations. The Contractor shall continue to suspend such operations until otherwise instructed by the Owner but shall continue with all other operations that do not affect those remains or features. Requests for adjustments in the Contract Sum and Contract Time arising from the existence of such remains or features may be made as provided in Article 15.

§ 3.8 Allowances

§ 3.8.1 The Contractor shall include in the Contract Sum all allowances stated in the Contract Documents. Items covered by allowances shall be supplied for such amounts and by such persons or entities as the Owner may direct, but the Contractor shall not be required to employ persons or entities to whom the Contractor has reasonable objection.

§ 3.8.2 Unless otherwise provided in the Contract Documents:

- **.1** allowances shall cover the cost to the Contractor of materials and equipment delivered at the site and all required taxes, less applicable trade discounts;
- **.2** Contractor's costs for unloading and handling at the site, labor, installation costs, overhead, profit, and other expenses contemplated for stated allowance amounts shall be included in the Contract Sum but not in the allowances; and
- **.3** whenever costs are more than or less than allowances, the Contract Sum shall be adjusted accordingly by Change Order. The amount of the Change Order shall reflect (1) the difference between actual costs and the allowances under Section 3.8.2.1 and (2) changes in Contractor's costs under Section 3.8.2.2.

§ 3.8.3 Materials and equipment under an allowance shall be selected by the Owner with reasonable promptness.

§ 3.9 Superintendent

§ 3.9.1 The Contractor shall employ a competent superintendent and necessary assistants who shall be in attendance at the Project site during performance of the Work. The superintendent shall represent the Contractor, and communications given to the superintendent shall be as binding as if given to the Contractor.

§ 3.9.2 The Contractor, as soon as practicable after award of the Contract, shall notify the Owner and Architect, through the Construction Manager, of the name and qualifications of a proposed superintendent. Within 14 days of receipt of the information, the Construction Manager may notify the Contractor, stating whether the Owner, the Construction Manager, or the Architect (1) has reasonable objection to the proposed superintendent or (2) require additional time for review. Failure of the Construction Manager to provide notice within the 14-day period shall constitute notice of no reasonable objection.

§ 3.9.3 The Contractor shall not employ a proposed superintendent to whom the Owner, Construction Manager, or Architect has made reasonable and timely objection. The Contractor shall not change the superintendent without the Owner's consent, which shall not unreasonably be withheld or delayed.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 3.10 Contractor's Construction and Submittal Schedules

§ 3.10.1 The Contractor, promptly after being awarded the Contract, shall submit for the Owner's and Architect's information, and the Construction Manager's use in developing the Project schedule, a Contractor's construction schedule for the Work. The schedule shall contain detail appropriate for the Project, including (1) the date of commencement of the Work, interim schedule milestone dates, and the date of Substantial Completion; (2) an apportionment of the Work by construction activity; and (3) the time required for completion of each portion of the Work. The schedule shall provide for the orderly progression of the Work to completion and shall not exceed time limits current under the Contract Documents. The schedule shall be revised at appropriate intervals as required by the conditions of the Work and Project. The Contractor shall cooperate with the Construction Manager in scheduling and performing the Contractor's Work to avoid conflict with, and as to cause no delay in, the work or activities of other Contractors, or the construction or operations of the Owner's own forces or Separate Contractors.

§ 3.10.2 The Contractor, promptly after being awarded the Contract and thereafter as necessary to maintain a current submittal schedule, shall submit a submittal schedule for the Construction Manager's and Architect's approval. The Architect and Construction Manager's approval shall not be unreasonably delayed or withheld. The submittal schedule shall (1) be coordinated with the Contractor's construction schedule, and (2) allow the Construction Manager and Architect reasonable time to review submittals. If the Contractor fails to submit a submittal schedule, or fails to provide submittals in accordance with the approved submittal schedule, the Contractor shall not be entitled to any increase in Contract Sum or extension of Contract Time based on the time required for review of submittals.

§ 3.10.3 The Contractor shall participate with other Contractors, the Construction Manager, and the Owner in reviewing and coordinating all schedules for incorporation into the Project schedule that is prepared by the Construction Manager. The Contractor shall make revisions to the construction schedule and submittal schedule as deemed necessary by the Construction Manager to conform to the Project schedule.

§ 3.10.4 The Contractor shall perform the Work in general accordance with the most recent schedules submitted to the Owner, Construction Manager, and Architect, and incorporated into the approved Project schedule.

§ 3.11 Documents and Samples at the Site

The Contractor shall make available, at the Project site, the Contract Documents, including Change Orders, Construction Change Directives, and other Modifications, in good order and marked currently to indicate field changes and selections made during construction, and the approved Shop Drawings, Product Data, Samples, and similar required submittals. These shall be in electronic form or paper copy, available to the Construction Manager, Architect, and Owner, and delivered to the Construction Manager for submittal to the Owner upon completion of the Work as a record of the Work as constructed.

§ 3.12 Shop Drawings, Product Data, and Samples

§ 3.12.1 Shop Drawings are drawings, diagrams, schedules, and other data specially prepared for the Work by the Contractor or a Subcontractor, Sub-subcontractor, manufacturer, supplier, or distributor to illustrate some portion of the Work.

§ 3.12.2 Product Data are illustrations, standard schedules, performance charts, instructions, brochures, diagrams, and other information furnished by the Contractor to illustrate materials or equipment for some portion of the Work.

§ 3.12.3 Samples are physical examples that illustrate materials, equipment, or workmanship, and establish standards by which the Work will be judged.

§ 3.12.4 Shop Drawings, Product Data, Samples, and similar submittals are not Contract Documents. Their purpose is to demonstrate how the Contractor proposes to conform to the information given and the design concept expressed in the Contract Documents for those portions of the Work for which the Contract Documents require submittals. Review by the Architect and Construction Manager is subject to the limitations of Sections 4.2.10 through 4.2.12. Informational submittals upon which the Construction Manager and Architect are not expected to take responsive action may be so identified in the Contract Documents. Submittals that are not required by the Contract Documents may be returned by the Construction Manager or Architect without action.

§ 3.12.5 The Contractor shall review for compliance with the Contract Documents, approve, and submit to the Construction Manager, Shop Drawings, Product Data, Samples, and similar submittals required by the Contract

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

Documents, in accordance with the Project submittal schedule approved by the Construction Manager and Architect or, in the absence of an approved Project submittal schedule, with reasonable promptness and in such sequence as to cause no delay in the Work or in the activities of other Contractors, Separate Contractors, or the Owner's own forces. The Contractor shall cooperate with the Construction Manager in the coordination of the Contractor's Shop Drawings, Product Data, Samples, and similar submittals with related documents submitted by other Contractors.

§ 3.12.6 By submitting Shop Drawings, Product Data, Samples, and similar submittals, the Contractor represents to the Owner, Construction Manager, and Architect, that the Contractor has (1) reviewed and approved them, (2) determined and verified materials, field measurements and field construction criteria related thereto, or will do so, and (3) checked and coordinated the information contained within such submittals with the requirements of the Work and of the Contract Documents.

§ 3.12.7 The Contractor shall perform no portion of the Work for which the Contract Documents require submittal and review of Shop Drawings, Product Data, Samples, or similar submittals, until the respective submittal has been reviewed and approved by the Architect.

§ 3.12.8 The Work shall be in accordance with approved submittals except that the Contractor shall not be relieved of responsibility for deviations from the requirements of the Contract Documents by the Architect's approval of Shop Drawings, Product Data, Samples, or similar submittals, unless the Contractor has specifically notified the Construction Manager and Architect of such deviation at the time of submittal and (1) the Architect has given written approval to the specific deviation as a minor change in the Work, or (2) a Change Order or Construction Change Directive has been issued authorizing the deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Shop Drawings, Product Data, Samples, or similar submittals, by the Architect's approval thereof.

§ 3.12.9 The Contractor shall direct specific attention, in writing or on resubmitted Shop Drawings, Product Data, Samples, or similar submittals, to revisions other than those requested by the Construction Manager and Architect on previous submittals. In the absence of such notice, the Architect's approval of a resubmission shall not apply to such revisions.

§ 3.12.10 The Contractor shall not be required to provide professional services that constitute the practice of architecture or engineering unless such services are specifically required by the Contract Documents for a portion of the Work or unless the Contractor needs to provide such services in order to carry out the Contractor's responsibilities for construction means, methods, techniques, sequences, and procedures. The Contractor shall not be required to provide professional services in violation of applicable law.

§ 3.12.10.1 If professional design services or certifications by a design professional related to systems, materials, or equipment are specifically required of the Contractor by the Contract Documents, the Owner and the Architect will specify all performance and design criteria that such services must satisfy. The Contractor shall be entitled to rely upon the adequacy and accuracy of the performance and design criteria provided in the Contract Documents. The Contractor shall cause such services or certifications to be provided by an appropriately licensed design professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, Shop Drawings, and other submittals prepared by such professional. Shop Drawings, and other submittals related to the Work, designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to the Architect. The Owner, the Architect, and the Construction Manager shall be entitled to rely upon the adequacy and accuracy of the services, certifications, and approvals performed or provided by such design professionals, provided the Owner and Architect have specified to the Contractor the performance and design criteria that such services must satisfy. Pursuant to this Section 3.12.10, the Architect will review and approve or take other appropriate action on submittals only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Construction Manager shall review submittals for sequencing, constructability, and coordination impacts on other Contractors.

§ 3.12.10.2 If the Contract Documents require the Contractor's design professional to certify that the Work has been performed in accordance with the design criteria, the Contractor shall furnish such certifications to the Construction Manager and Architect at the time and in the form specified by the Architect.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

§ 3.13 Use of Site

§ 3.13.1 The Contractor shall confine operations at the site to areas permitted by applicable laws, statutes, ordinances, codes, rules and regulations, lawful orders of public authorities, and the Contract Documents and shall not unreasonably encumber the site with materials or equipment.

§ 3.13.2 The Contractor shall coordinate the Contractor's operations with, and secure the approval of, the Construction Manager before using any portion of the site.

§ 3.14 Cutting and Patching

§ 3.14.1 The Contractor shall be responsible for cutting, fitting, or patching required to complete the Work or to make its parts fit together properly. All areas requiring cutting, fitting, or patching shall be restored to the condition existing prior to the cutting, fitting, or patching, unless otherwise required by the Contract Documents.

§ 3.14.2 The Contractor shall not damage or endanger a portion of the Work or fully or partially completed construction of the Owner, Separate Contractors, or of other Contractors by cutting, patching, or otherwise altering such construction, or by excavation. The Contractor shall not cut or otherwise alter construction by the Owner, Separate Contractors, or by other Contractors except with written consent of the Construction Manager, Owner, and such other Contractors or Separate Contractors. Consent shall not be unreasonably withheld. The Contractor shall not unreasonably withhold, from the Separate Contractors, other Contractors, or the Owner, its consent to cutting or otherwise altering the Work.

§ 3.15 Cleaning Up

§ 3.15.1 The Contractor shall keep the premises and surrounding area free from accumulation of waste materials and rubbish caused by operations under the Contract. At completion of the Work, the Contractor shall remove waste materials, rubbish, the Contractor's tools, construction equipment, machinery, and surplus materials from and about the Project.

§ 3.15.2 If the Contractor fails to clean up as provided in the Contract Documents, the Owner, or Construction Manager with the Owner's approval, may do so and the Owner shall be entitled to reimbursement from the Contractor.

§ 3.16 Access to Work

The Contractor shall provide the Owner, Construction Manager, and Architect with access to the Work in preparation and progress wherever located.

§ 3.17 Royalties, Patents and Copyrights

The Contractor shall pay all royalties and license fees. The Contractor shall defend suits or claims for infringement of copyrights and patent rights and shall hold the Owner, Construction Manager, and Architect harmless from loss on account thereof, but shall not be responsible for defense or loss when a particular design, process, or product of a particular manufacturer or manufacturers is required by the Contract Documents, or where the copyright violations are contained in Drawings, Specifications, or other documents prepared by the Owner, Architect, or Construction Manager. However, if an infringement of a copyright or patent is discovered by, or made known to, the Contractor, the Contractor shall be responsible for the loss unless the information is promptly furnished to the Architect through the Construction Manager.

§ 3.18 Indemnification

§ 3.18.1 To the fullest extent permitted by law, the Contractor shall indemnify and hold harmless the Owner, Construction Manager, Architect, Construction Manager's and Architect's consultants, and agents and employees of any of them from and against claims, damages, losses, and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work, provided that such claim, damage, loss, or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself), but only to the extent caused by the negligent acts or omissions of the Contractor, a Subcontractor, anyone directly or indirectly employed by them, or anyone for whose acts they may be liable, regardless of whether or not such claim, damage, loss, or expense is caused in part by a party indemnified hereunder. Such obligation shall not be construed to negate, abridge, or reduce other rights or obligations of indemnity that would otherwise exist as to a party or person described in this Section 3.18.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

§ 3.18.2 In claims against any person or entity indemnified under this Section 3.18 by an employee of the Contractor, a Subcontractor, anyone directly or indirectly employed by them, or anyone for whose acts they may be liable, the indemnification obligation under Section 3.18.1 shall not be limited by a limitation on amount or type of damages, compensation, or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefit acts, or other employee benefit acts.

ARTICLE 4 ARCHITECT AND CONSTRUCTION MANAGER

§ 4.1 General

§ 4.1.1 The Architect is the person or entity retained by the Owner pursuant to Section 2.3.2 and identified as such in the Agreement.

§ 4.1.2 The Construction Manager is the person or entity retained by the Owner pursuant to Section 2.3.3 and identified as such in the Agreement.

§ 4.1.3 Duties, responsibilities, and limitations of authority of the Construction Manager and Architect as set forth in the Contract Documents shall not be restricted, modified, or extended without written consent of the Owner, Construction Manager, Architect, and Contractor. Consent shall not be unreasonably withheld.

§ 4.2 Administration of the Contract

§ 4.2.1 The Construction Manager and Architect will provide administration of the Contract as described in the Contract Documents and will be the Owner's representatives during construction until the date the Architect issues the final Certificate for Payment. The Construction Manager and Architect will have authority to act on behalf of the Owner only to the extent provided in the Contract Documents.

§ 4.2.2 The Architect will visit the site at intervals appropriate to the stage of construction, or as otherwise agreed with the Owner, to become generally familiar with the progress and quality of the portion of the Work completed, and to determine in general if the Work observed is being performed in a manner indicating that the Work, when fully completed, will be in accordance with the Contract Documents. However, the Architect will not be required to make exhaustive or continuous on-site inspections to check the quality or quantity of the Work. On the basis of the site visits, the Architect will keep the Owner and the Construction Manager reasonably informed about the progress and quality of the portion of the Work completed, and promptly report to the Owner and Construction Manager known deviations from the Contract Documents and defects and deficiencies observed in the Work.

§ 4.2.3 The Construction Manager shall provide one or more representatives who shall be in attendance at the Project site whenever the Work is being performed. The Construction Manager will determine in general if the Work observed is being performed in accordance with the Contract Documents, will keep the Owner and Architect reasonably informed of the progress of the Work, and will promptly report to the Owner and Architect known deviations from the Contract Documents and the most recent Project schedule, and defects and deficiencies observed in the Work.

§ 4.2.4 The Construction Manager will schedule and coordinate the activities of the Contractor and other Contractors in accordance with the latest approved Project schedule.

§ 4.2.5 The Construction Manager, except to the extent required by Section 4.2.4, and Architect will not have control over, charge of, or responsibility for, the construction means, methods, techniques, sequences or procedures, or for the safety precautions and programs in connection with the Work, since these are solely the Contractor's rights and responsibilities under the Contract Documents, and neither will be responsible for the Contractor's failure to perform the Work in accordance with the requirements of the Contract Documents. Neither the Construction Manager nor the Architect will have control over or charge of, or be responsible for acts or omissions of, the Contractor, Subcontractors, or their agents or employees, or of any other persons or entities performing portions of the Work.

§ 4.2.6 Communications. The Owner shall communicate with the Contractor and the Construction Manager's consultants through the Construction Manager about matters arising out of or relating to the Contract Documents. The Owner and Construction Manager shall include the Architect in all communications that relate to or affect the Architect's services or professional responsibilities. The Owner shall promptly notify the Architect of the substance of any direct communications between the Owner and the Construction Manager otherwise relating to the Project. Communications by and with the Architect's consultants shall be through the Architect. Communications by and with Subcontractors and suppliers shall be through the Contractor. Communications by and with other Contractors shall be

Init.
/
AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

through the Construction Manager. Communications by and with the Owner's own forces and Separate Contractors shall be through the Owner. The Contract Documents may specify other communication protocols.

§ 4.2.7 The Construction Manager and Architect will review and certify all Applications for Payment by the Contractor, in accordance with the provisions of Article 9.

§ 4.2.8 The Architect and Construction Manager have authority to reject Work that does not conform to the Contract Documents, and will notify each other about the rejection. Whenever the Construction Manager considers it necessary or advisable, the Construction Manager will have authority to require inspection or testing of the Work in accordance with Sections 13.4.2 and 13.4.3, upon written authorization of the Owner, whether or not the Work is fabricated, installed or completed. The foregoing authority of the Construction Manager will be subject to the provisions of Sections 4.2.18 through 4.2.20 inclusive, with respect to interpretations and decisions of the Architect. However, neither the Architect's nor the Construction Manager's authority to act under this Section 4.2.8 nor a decision made by either of them in good faith either to exercise or not to exercise such authority shall give rise to a duty or responsibility of the Architect or the Construction Manager to the Contractor, Subcontractors, suppliers, their agents or employees, or other persons performing any of the Work.

§ 4.2.9 Utilizing the submittal schedule provided by the Contractor, the Construction Manager shall prepare, and revise as necessary, a Project submittal schedule incorporating information from other Contractors, the Owner, Owner's consultants, Owner's Separate Contractors and vendors, governmental agencies, and participants in the Project under the management of the Construction Manager. The Project submittal schedule and any revisions shall be submitted to the Architect for approval.

§ 4.2.10 The Construction Manager will receive and promptly review for conformance with the submittal requirements of the Contract Documents, all submittals from the Contractor such as Shop Drawings, Product Data, and Samples. Where there are other Contractors, the Construction Manager will also check and coordinate the information contained within each submittal received from the Contractor and other Contractors, and transmit to the Architect those recommended for approval. By submitting Shop Drawings, Product Data, Samples, and similar submittals, the Construction Manager represents to the Owner and Architect that the Construction Manager has reviewed and recommended them for approval. The Construction Manager's actions will be taken in accordance with the Project submittal schedule approved by the Architect or, in the absence of an approved Project submittal schedule, with reasonable promptness while allowing sufficient time to permit adequate review by the Architect.

§ 4.2.11 The Architect will review and approve, or take other appropriate action upon, the Contractor's submittals such as Shop Drawings, Product Data, and Samples, but only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Architect's action will be taken in accordance with the submittal schedule approved by the Architect or, in the absence of an approved submittal schedule, with reasonable promptness while allowing sufficient time in the Architect's professional judgment to permit adequate review. Upon the Architect's completed review, the Architect shall transmit its submittal review to the Construction Manager.

§ 4.2.12 Review of the Contractor's submittals by the Construction Manager and Architect is not conducted for the purpose of determining the accuracy and completeness of other details such as dimensions and quantities, or for substantiating instructions for installation or performance of equipment or systems, all of which remain the responsibility of the Contractor as required by the Contract Documents. The Construction Manager and Architect's review of the Contractor's submittals shall not relieve the Contractor of the obligations under Sections 3.3, 3.5, and 3.12. The Construction Manager and Architect's review shall not constitute approval of safety precautions or of any construction means, methods, techniques, sequences, or procedures. The Architect's approval of a specific item shall not indicate approval of an assembly of which the item is a component.

§ 4.2.13 The Construction Manager will prepare Change Orders and Construction Change Directives.

§ 4.2.14 The Construction Manager and the Architect will take appropriate action on Change Orders or Construction Change Directives in accordance with Article 7, and the Architect will have authority to order minor changes in the Work as provided in Section 7.4. The Architect, in consultation with the Construction Manager, will investigate and make determinations and recommendations regarding concealed and unknown conditions as provided in Section 3.7.4.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 4.2.15 Utilizing the documents provided by the Contractor, the Construction Manager will maintain at the site for the Owner one copy of all Contract Documents, approved Shop Drawings, Product Data, Samples, and similar required submittals, in good order and marked currently to record all changes and selections made during construction. These will be available to the Architect and the Contractor, and will be delivered to the Owner upon completion of the Project.

§ 4.2.16 The Construction Manager will assist the Architect in conducting inspections to determine the date or dates of Substantial Completion and the date of final completion; issue Certificates of Substantial Completion in conjunction with the Architect pursuant to Section 9.8; and receive and forward to the Owner written warranties and related documents required by the Contract and assembled by the Contractor pursuant to Section 9.10. The Construction Manager will forward to the Architect a final Application and Certificate for Payment or final Project Application and Project Certificate for Payment upon the Contractor's compliance with the requirements of the Contract Documents.

§ 4.2.17 If the Owner and Architect agree, the Architect will provide one or more Project representatives to assist in carrying out the Architect's responsibilities at the site. The Owner shall notify the Construction Manager of any change in the duties, responsibilities and limitations of authority of the Project representatives.

§ 4.2.18 The Architect will interpret and decide matters concerning performance under, and requirements of, the Contract Documents on written request of the Construction Manager, Owner, or Contractor through the Construction Manager. The Architect's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness.

§ 4.2.19 Interpretations and decisions of the Architect will be consistent with the intent of, and reasonably inferable from, the Contract Documents and will be in writing or in the form of drawings. When making such interpretations and decisions, the Architect will endeavor to secure faithful performance by both Owner and Contractor, will not show partiality to either, and will not be liable for results of interpretations or decisions so rendered in good faith.

§ 4.2.20 The Architect's decisions on matters relating to aesthetic effect will be final if consistent with the intent expressed in the Contract Documents.

§ 4.2.21 The Construction Manager will receive and review requests for information from the Contractor, and forward each request for information to the Architect, with the Construction Manager's recommendation. The Architect will review and respond in writing, through the Construction Manager, to requests for information about the Contract Documents. The Construction Manager's recommendation and the Architect's response to each request will be made in writing within any time limits agreed upon or otherwise with reasonable promptness. If appropriate, the Architect will prepare and issue supplemental Drawings and Specifications in response to the requests for information.

ARTICLE 5 SUBCONTRACTORS

§ 5.1 Definitions

§ 5.1.1 A Subcontractor is a person or entity who has a direct contract with the Contractor to perform a portion of the Work at the site. The term "Subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Subcontractor or an authorized representative of the Subcontractor. The term "Subcontractor" does not include other Contractors or Separate Contractors or the subcontractors of other Contractors or Separate Contractors.

§ 5.1.2 A Sub-subcontractor is a person or entity who has a direct or indirect contract with a Subcontractor to perform a portion of the Work at the site. The term "Sub-subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Sub-subcontractor or an authorized representative of the Sub-subcontractor.

§ 5.2 Award of Subcontracts and Other Contracts for Portions of the Work

§ 5.2.1 Unless otherwise stated in the Contract Documents, the Contractor, as soon as practicable after award of the Contract, shall notify the Construction Manager, for review by the Owner, Construction Manager and Architect, of the persons or entities proposed for each principal portion of the Work, including those who are to furnish materials or equipment fabricated to a special design. Within 14 days of receipt of the information, the Construction Manager may notify the Contractor whether the Owner, the Construction Manager or the Architect (1) has reasonable objection to any such proposed person or entity or, (2) requires additional time for review. Failure of the Construction Manager to provide notice within the 14-day period shall constitute notice of no reasonable objection.

Init.
/
AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

§ 5.2.2 The Contractor shall not contract with a proposed person or entity to whom the Owner, Construction Manager or Architect has made reasonable and timely objection. The Contractor shall not be required to contract with anyone to whom the Contractor has made reasonable objection.

§ 5.2.3 If the Owner, Construction Manager or Architect has reasonable objection to a person or entity proposed by the Contractor, the Contractor shall propose another to whom the Owner, Construction Manager or Architect has no reasonable objection. If the proposed but rejected Subcontractor was reasonably capable of performing the Work, the Contract Sum and Contract Time shall be increased or decreased by the difference, if any, occasioned by such change, and an appropriate Change Order shall be issued before commencement of the substitute Subcontractor's Work. However, no increase in the Contract Sum or Contract Time shall be allowed for such change unless the Contractor has acted promptly and responsively in submitting names as required.

§ 5.2.4 The Contractor shall not substitute a Subcontractor, person, or entity for one previously selected if the Owner, Construction Manager or Architect makes reasonable objection to such substitution.

§ 5.3 Subcontractual Relations

By appropriate written agreement, the Contractor shall require each Subcontractor, to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor by terms of the Contract Documents, and to assume toward the Contractor all the obligations and responsibilities, including the responsibility for safety of the Subcontractor's Work, that the Contractor, by these Contract Documents, assumes toward the Owner, Construction Manager and Architect. Each subcontract agreement shall preserve and protect the rights of the Owner, Construction Manager and Architect under the Contract Documents with respect to the Work to be performed by the Subcontractor so that subcontracting thereof will not prejudice such rights, and shall allow to the Subcontractor, unless specifically provided otherwise in the subcontract agreement, the benefit of all rights, remedies, and redress against the Contractor that the Contractor, by the Contract Documents, has against the Owner. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with Sub-subcontractors. The Contractor shall make available to each proposed Subcontractor, prior to the execution of the subcontract agreement, copies of the Contract Documents to which the Subcontractor will be bound, and, upon written request of the Subcontractor, identify to the Subcontractor terms and conditions of the proposed subcontract agreement that may be at variance with the Contract Documents. Subcontractors will similarly make copies of applicable portions of such documents available to their respective proposed Sub-subcontractors.

§ 5.4 Contingent Assignment of Subcontracts

§ 5.4.1 Each subcontract agreement for a portion of the Work is assigned by the Contractor to the Owner, provided that

- **.1** assignment is effective only after termination of the Contract by the Owner for cause pursuant to Section 14.2 and only for those subcontract agreements that the Owner accepts by notifying the Subcontractor and Contractor; and
- **.2** assignment is subject to the prior rights of the surety, if any, obligated under bond relating to the Contract.

When the Owner accepts the assignment of a subcontract agreement, the Owner assumes the Contractor's rights and obligations under the subcontract.

§ 5.4.2 Upon such assignment, if the Work has been suspended for more than 30 days, the Subcontractor's compensation shall be equitably adjusted for increases in cost resulting from the suspension.

§ 5.4.3 Upon assignment to the Owner under this Section 5.4, the Owner may further assign the subcontract to a successor Contractor or other entity. If the Owner assigns the subcontract to a successor Contractor or other entity, the Owner shall nevertheless remain legally responsible for all of the successor Contractor's obligations under the subcontract.

ARTICLE 6 CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

§ 6.1 Owner's Right to Perform Construction with Own Forces and to Award Other Contracts

§ 6.1.1 The Owner reserves the right to perform construction or operations related to the Project with the Owner's own forces, and with Separate Contractors retained under Conditions of the Contract substantially similar to those of this Contract, including those provisions of the Conditions of the Contract related to insurance and waiver of subrogation.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 6.1.2 When the Owner performs construction or operations with the Owner's own forces or Separate Contractors, the Owner shall provide for coordination of such forces and Separate Contractors with the Work of the Contractor, who shall cooperate with them.

§ 6.1.3 Unless otherwise provided in the Contract Documents, when the Owner performs construction or operations related to the Project with the Owner's own forces or with Separate Contractors, the Owner or its Separate Contractors shall have the same obligations and rights that the Contractor has under the Conditions of the Contract, including, without excluding others, those stated in Article 3, this Article 6, and Articles 10, 11, and 12.

§ 6.2 Mutual Responsibility

§ 6.2.1 The Contractor shall afford the Owner's own forces, Separate Contractors, Construction Manager and other Contractors reasonable opportunity for introduction and storage of their materials and equipment and performance of their activities, and shall connect and coordinate the Contractor's construction and operations with theirs as required by the Contract Documents.

§ 6.2.2 If part of the Contractor's Work depends for proper execution or results upon construction or operations by the Owner's own forces, Separate Contractors or other Contractors, the Contractor shall, prior to proceeding with that portion of the Work, promptly notify the Construction Manager and Architect of apparent discrepancies or defects in the construction or operations by the Owner or Separate Contractor or other Contractors that would render it unsuitable for proper execution and results of the Contractor's Work. Failure of the Contractor to notify the Construction Manager and the Architect of apparent discrepancies or defects prior to proceeding with the Work shall constitute an acknowledgment that the Owner's or Separate Contractor's or other Contractors' completed or partially completed construction is fit and proper to receive the Contractor's Work. The Contractor shall not be responsible for discrepancies or defects in the construction or operations by the Owner or Separate Contractors or other Contractors that are not apparent.

§ 6.2.3 The Contractor shall reimburse the Owner for costs the Owner incurs, including costs that are payable to a Separate Contractors or to other Contractors, because of the Contractor's delays, improperly timed activities or defective construction. The Owner shall be responsible to the Contractor for costs the Contractor incurs because of delays, improperly timed activities, damage to the Work or defective construction by the Owner's own forces, Separate Contractors, or other Contractors.

§ 6.2.4 The Contractor shall promptly remedy damage that the Contractor wrongfully causes to completed or partially completed construction, or to property of the Owner, Separate Contractors, or other Contractors as provided in Section 10.2.5.

§ 6.2.5 The Owner, Separate Contractors, and other Contractors shall have the same responsibilities for cutting and patching as are described for the Contractor in Section 3.14.

§ 6.3 Owner's Right to Clean Up

If a dispute arises among the Contractor, Separate Contractors, other Contractors, and the Owner as to the responsibility under their respective contracts for maintaining the premises and surrounding area free from waste materials and rubbish, the Owner may clean up and the Construction Manager, with notice to the Architect, will allocate the cost among those responsible.

ARTICLE 7 CHANGES IN THE WORK

§ 7.1 General

§ 7.1.1 Changes in the Work may be accomplished after execution of the Contract, and without invalidating the Contract, by Change Order, Construction Change Directive or order for a minor change in the Work, subject to the limitations stated in this Article 7 and elsewhere in the Contract Documents.

§ 7.1.2 A Change Order shall be based upon agreement among the Owner, Construction Manager, Architect and Contractor. A Construction Change Directive requires agreement by the Owner, Construction Manager and Architect and may or may not be agreed to by the Contractor. An order for a minor change in the Work may be issued by the Architect alone.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 7.1.3 Changes in the Work shall be performed under applicable provisions of the Contract Documents. The Contractor shall proceed promptly with changes in the Work, unless otherwise provided in the Change Order, Construction Change Directive, or order for a minor change in the Work.

§ 7.2 Change Orders

A Change Order is a written instrument prepared by the Construction Manager and signed by the Owner, Construction Manager, Architect, and Contractor, stating their agreement upon all of the following:

.1 The change in the Work;
.2 The amount of the adjustment, if any, in the Contract Sum; and
.3 The extent of the adjustment, if any, in the Contract Time.

§ 7.3 Construction Change Directives

§ 7.3.1 A Construction Change Directive is a written order prepared by the Construction Manager and signed by the Owner, Construction Manager and Architect, directing a change in the Work prior to agreement on adjustment, if any, in the Contract Sum or Contract Time, or both. The Owner may by Construction Change Directive, without invalidating the Contract, order changes in the Work within the general scope of the Contract consisting of additions, deletions, or other revisions, the Contract Sum and Contract Time being adjusted accordingly.

§ 7.3.2 A Construction Change Directive shall be used in the absence of total agreement on the terms of a Change Order.

§ 7.3.3 If the Construction Change Directive provides for an adjustment to the Contract Sum, the adjustment shall be based on one of the following methods:

.1 Mutual acceptance of a lump sum properly itemized and supported by sufficient substantiating data to permit evaluation;
.2 Unit prices stated in the Contract Documents or subsequently agreed upon;
.3 Cost to be determined in a manner agreed upon by the parties and a mutually acceptable fixed or percentage fee; or
.4 As provided in Section 7.3.4.

§ 7.3.4 If the Contractor does not respond promptly or disagrees with the method for adjustment in the Contract Sum, the Construction Manager shall determine the adjustment on the basis of reasonable expenditures and savings of those performing the Work attributable to the change, including, in case of an increase in the Contract Sum, an amount for overhead and profit as set forth in the Agreement, or if no such amount is set forth in the Agreement, a reasonable amount. In such case, and also under Section 7.3.3.3, the Contractor shall keep and present, in such form as the Construction Manager may prescribe, an itemized accounting together with appropriate supporting data. Unless otherwise provided in the Contract Documents, costs for the purposes of this Section 7.3.4 shall be limited to the following:

.1 Costs of labor, including applicable payroll taxes, fringe benefits required by agreement or custom, workers' compensation insurance, and other employee costs approved by the Construction Manager and Architect;
.2 Costs of materials, supplies, and equipment, including cost of transportation, whether incorporated or consumed;
.3 Rental costs of machinery and equipment, exclusive of hand tools, whether rented from the Contractor or others;
.4 Costs of premiums for all bonds and insurance, permit fees, and sales, use, or similar taxes, directly related to the change; and
.5 Costs of supervision and field office personnel directly attributable to the change.

§ 7.3.5 If the Contractor disagrees with the adjustment in the Contract Time, the Contractor may make a Claim in accordance with applicable provisions of Article 15.

§ 7.3.6 Upon receipt of a Construction Change Directive, the Contractor shall promptly proceed with the change in the Work involved and advise the Construction Manager of the Contractor's agreement or disagreement with the method, if any, provided in the Construction Change Directive for determining the proposed adjustment in the Contract Sum or Contract Time.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 7.3.7 A Construction Change Directive signed by the Contractor indicates the Contractor's agreement therewith, including adjustment in Contract Sum and Contract Time or the method for determining them. Such agreement shall be effective immediately and shall be recorded as a Change Order.

§ 7.3.8 The amount of credit to be allowed by the Contractor to the Owner for a deletion or change that results in a net decrease in the Contract Sum shall be actual net cost as confirmed by the Construction Manager and Architect. When both additions and credits covering related Work or substitutions are involved in a change, the allowance for overhead and profit shall be figured on the basis of net increase, if any, with respect to that change.

§ 7.3.9 Pending final determination of the total cost of a Construction Change Directive to the Owner, the Contractor may request payment for Work completed under the Construction Change Directive in Applications for Payment. The Construction Manager and Architect will make an interim determination for purposes of monthly certification for payment for those costs and certify for payment the amount that the Construction Manager and Architect determine to be reasonably justified. The interim determination of cost shall adjust the Contract Sum on the same basis as a Change Order, subject to the right of either party to disagree and assert a Claim in accordance with Article 15.

§ 7.3.10 When the Owner and Contractor agree with a determination made by the Construction Manager and Architect concerning the adjustments in the Contract Sum and Contract Time, or otherwise reach agreement upon the adjustments, such agreement shall be effective immediately and the Construction Manager shall prepare a Change Order. Change Orders may be issued for all or any part of a Construction Change Directive.

§ 7.4 Minor Changes in the Work

The Architect may order minor changes in the Work that are consistent with the intent of the Contract Documents and do not involve an adjustment in the Contract Sum or an extension of the Contract Time. The Architect's order for minor changes shall be in writing. If the Contractor believes that the proposed minor change in the Work will affect the Contract Sum or Contract Time, the Contractor shall notify the Construction Manager and shall not proceed to implement the change in the Work. If the Contractor performs the Work set forth in the Architect's order for a minor change without prior notice to the Construction Manager that such change will affect the Contract Sum or Contract Time, the Contractor waives any adjustment to the Contract Sum or extension of the Contract Time.

ARTICLE 8 TIME

§ 8.1 Definitions

§ 8.1.1 Unless otherwise provided, Contract Time is the period of time, including authorized adjustments, allotted in the Contract Documents for Substantial Completion of the Work.

§ 8.1.2 The date of commencement of the Work is the date established in the Agreement.

§ 8.1.3 The date of Substantial Completion is the date certified by the Architect in accordance with Section 9.8.

§ 8.1.4 The term "day" as used in the Contract Documents shall mean calendar day unless otherwise specifically defined.

§ 8.2 Progress and Completion

§ 8.2.1 Time limits stated in the Contract Documents are of the essence of the Contract. By executing the Agreement, the Contractor confirms that the Contract Time is a reasonable period for performing the Work.

§ 8.2.2 The Contractor shall not knowingly, except by agreement or instruction of the Owner in writing, commence the Work prior to the effective date of insurance required to be furnished by the Contractor and Owner.

§ 8.2.3 The Contractor shall proceed expeditiously with adequate forces and shall achieve Substantial Completion within the Contract Time.

§ 8.3 Delays and Extensions of Time

§ 8.3.1 If the Contractor is delayed at any time in the commencement or progress of the Work by (1) an act or neglect of the Owner, Architect, Construction Manager, or an employee of any of them, or of the Owner's own forces, Separate Contractors, or other Contractors; (2) by changes ordered in the Work; (3) by labor disputes, fire, unusual delay in deliveries, unavoidable casualties, adverse weather conditions documented in accordance with Section

Init.
/
AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

15.1.6.2, or other causes beyond the Contractor's control; (4) by delay authorized by the Owner pending mediation and binding dispute resolution; or (5) by other causes that the Contractor asserts and the Architect, based on the recommendation of the Construction Manager, determines justify delay, then the Contract Time shall be extended for such reasonable time as the Architect may determine.

§ 8.3.2 Claims relating to time shall be made in accordance with applicable provisions of Article 15.

§ 8.3.3 This Section 8.3 does not preclude recovery of damages for delay by either party under other provisions of the Contract Documents.

ARTICLE 9 PAYMENTS AND COMPLETION

§ 9.1 Contract Sum

§ 9.1.1 The Contract Sum is stated in the Agreement and, including authorized adjustments, is the total amount payable by the Owner to the Contractor for performance of the Work under the Contract Documents.

§ 9.1.2 If unit prices are stated in the Contract Documents or subsequently agreed upon, and if quantities originally contemplated are materially changed so that application of such unit prices to the actual quantities causes substantial inequity to the Owner or Contractor, the applicable unit prices shall be equitably adjusted.

§ 9.2 Schedule of Values

Where the Contract is based on a stipulated sum or Guaranteed Maximum Price, the Contractor shall submit a schedule of values to the Construction Manager, before the first Application for Payment, allocating the entire Contract Sum to the various portions of the Work. The schedule of values shall be prepared in the form, and supported by the data to substantiate its accuracy, required by the Construction Manager and the Architect. This schedule, unless objected to by the Construction Manager or Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment. The Construction Manager shall forward to the Architect the Contractor's schedule of values. Any changes to the schedule of values shall be submitted to the Construction Manager and supported by such data to substantiate its accuracy as the Construction Manager and the Architect may require, and unless objected to by the Construction Manager or the Architect, shall be used as a basis for reviewing the Contractor's subsequent Applications for Payment.

§ 9.3 Applications for Payment

§ 9.3.1 At least fifteen days before the date established for each progress payment, the Contractor shall submit to the Construction Manager an itemized Application for Payment prepared in accordance with the schedule of values, if required under Section 9.2, for completed portions of the Work. The application shall be notarized, if required, and supported by all data substantiating the Contractor's right to payment that the Owner, Construction Manager or Architect require, such as copies of requisitions, and releases of waivers of lien from Subcontractors and suppliers, and shall reflect retainage if provided for in the Contract Documents.

§ 9.3.1.1 As provided in Section 7.3.9, such applications may include requests for payment on account of changes in the Work that have been properly authorized by Construction Change Directives, or by interim determinations of the Construction Manager and Architect, but not yet included in Change Orders.

§ 9.3.1.2 Applications for Payment shall not include requests for payment for portions of the Work for which the Contractor does not intend to pay a Subcontractor or supplier, unless such Work has been performed by others whom the Contractor intends to pay.

§ 9.3.2 Unless otherwise provided in the Contract Documents, payments shall be made on account of materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work. If approved in advance by the Owner, payment may similarly be made for materials and equipment suitably stored off the site at a location agreed upon in writing. Payment for materials and equipment stored on or off the site shall be conditioned upon compliance by the Contractor with procedures satisfactory to the Owner to establish the Owner's title to such materials and equipment or otherwise protect the Owner's interest, and shall include the costs of applicable insurance, storage, and transportation to the site, for such materials and equipment stored off the site.

§ 9.3.3 The Contractor warrants that title to all Work covered by an Application for Payment will pass to the Owner no later than the time of payment. The Contractor further warrants that upon submittal of an Application for Payment all

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

Work for which Certificates for Payment have been previously issued and payments received from the Owner shall, to the best of the Contractor's knowledge, information, and belief, be free and clear of liens, claims, security interests, or encumbrances, in favor of the Contractor, Subcontractors, suppliers, or other persons or entities that provided labor, materials and equipment relating to the Work.

§ 9.4 Certificates for Payment

§ 9.4.1 Where there is only one Contractor, the Construction Manager will, within seven days after the Construction Manager's receipt of the Contractor's Application for Payment, review the Application, certify the amount the Construction Manager determines is due the Contractor, and forward the Contractor's Application and Certificate for Payment to the Architect. Within seven days after the Architect receives the Contractor's Application for Payment from the Construction Manager, the Architect will either (1) issue to the Owner a Certificate for Payment, in the full amount of the Application for Payment, with a copy to the Construction Manager; or (2) issue to the Owner a Certificate for Payment for such amount as the Architect determines is properly due, and notify the Construction Manager and Owner of the Architect's reasons for withholding certification in part as provided in Section 9.5.1; or (3) withhold certification of the entire Application for Payment, and notify the Construction Manager and Owner of the Architect's reason for withholding certification in whole as provided in Section 9.5.1. The Construction Manager will promptly forward to the Contractor the Architect's notice of withholding certification.

§ 9.4.2 Where there is more than one Contractor performing portions of the Project, the Construction Manager will, within seven days after the Construction Manager receives all of the Contractors' Applications for Payment: (1) review the Applications and certify the amount the Construction Manager determines is due each of the Contractors; (2) prepare a Summary of Contractors' Applications for Payment by combining information from each Contractor's application with information from similar applications for progress payments from the other Contractors; (3) prepare a Project Application and Certificate for Payment; (4) certify the amount the Construction Manager determines is due all Contractors; and (5) forward the Summary of Contractors' Applications for Payment and Project Application and Certificate for Payment to the Architect.

§ 9.4.2.1 Within seven days after the Architect receives the Project Application and Project Certificate for Payment and the Summary of Contractors' Applications for Payment from the Construction Manager, the Architect will either (1) issue to the Owner a Project Certificate for Payment, with a copy to the Construction Manager; or (2) issue to the Owner a Project Certificate for Payment for such amount as the Architect determines is properly due, and notify the Construction Manager and Owner of the Architect's reasons for withholding certification in part as provided in Section 9.5.1; or (3) withhold certification of the entire Project Application for Payment, and notify the Construction Manager and Owner of the Architect's reason for withholding certification in whole as provided in Section 9.5.1. The Construction Manager will promptly forward the Architect's notice of withholding certification to the Contractors.

§ 9.4.3 The Construction Manager's certification of an Application for Payment or, in the case of more than one Contractor, a Project Application and Certificate for Payment, shall be based upon the Construction Manager's evaluation of the Work and the data in the Application or Applications for Payment. The Construction Manager's certification will constitute a representation that, to the best of the Construction Manager's knowledge, information, and belief, the Work has progressed to the point indicated, the quality of the Work is in accordance with the Contract Documents, and that the Contractor is, or Contractors are, entitled to payment in the amount certified.

§ 9.4.4 The Architect's issuance of a Certificate for Payment or, in the case of more than one Contractor, Project Application and Certificate for Payment, shall be based upon the Architect's evaluation of the Work, the recommendation of the Construction Manager, and data in the Application for Payment or Project Application for Payment. The Architect's certification will constitute a representation that, to the best of the Architect's knowledge, information, and belief, the Work has progressed to the point indicated, the quality of the Work is in accordance with the Contract Documents, and that the Contractor is, or Contractors are, entitled to payment in the amount certified.

§ 9.4.5 The representations made pursuant to Sections 9.4.3 and 9.4.4 are subject to an evaluation of the Work for conformance with the Contract Documents upon Substantial Completion, to results of subsequent tests and inspections, to correction of minor deviations from the Contract Documents prior to completion, and to specific qualifications expressed by the Construction Manager or Architect.

§ 9.4.6 The issuance of a Certificate for Payment or a Project Certificate for Payment will not be a representation that the Construction Manager or Architect has (1) made exhaustive or continuous on-site inspections to check the quality

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

or quantity of the Work; (2) reviewed construction means, methods, techniques, sequences, or procedures; (3) reviewed copies of requisitions received from Subcontractors and suppliers and other data requested by the Owner to substantiate the Contractor's right to payment; or (4) made examination to ascertain how or for what purpose the Contractor has used money previously paid on account of the Contract Sum.

§ 9.5 Decisions to Withhold Certification

§ 9.5.1 The Construction Manager or Architect may withhold a Certificate for Payment or Project Certificate for Payment in whole or in part, to the extent reasonably necessary to protect the Owner, if in the Construction Manager's or Architect's opinion the representations to the Owner required by Section 9.4.3 and 9.4.4 cannot be made. If the Construction Manager or Architect is unable to certify payment in the amount of the Application, the Construction Manager will notify the Contractor and Owner as provided in Section 9.4.1 and 9.4.2. If the Contractor, Construction Manager and Architect cannot agree on a revised amount, the Architect will promptly issue a Certificate for Payment or a Project Certificate for Payment for the amount for which the Architect is able to make such representations to the Owner. The Construction Manager or Architect may also withhold a Certificate for Payment or, because of subsequently discovered evidence, may nullify the whole or a part of a Certificate for Payment or Project Certificate for Payment previously issued, to such extent as may be necessary in the Construction Manager's or Architect's opinion to protect the Owner from loss for which the Contractor is responsible, including loss resulting from the acts and omissions described in Section 3.3.2 because of

- **.1** defective Work not remedied;
- **.2** third party claims filed or reasonable evidence indicating probable filing of such claims, unless security acceptable to the Owner is provided by the Contractor;
- **.3** failure of the Contractor to make payments properly to Subcontractors or suppliers for labor, materials or equipment;
- **.4** reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Sum;
- **.5** damage to the Owner or a Separate Contractor or other Contractor;
- **.6** reasonable evidence that the Work will not be completed within the Contract Time, and that the unpaid balance would not be adequate to cover actual or liquidated damages for the anticipated delay; or
- **.7** repeated failure to carry out the Work in accordance with the Contract Documents.

§ 9.5.2 When either party disputes the Architect's decision regarding a Certificate for Payment under Section 9.5.1, in whole or in part, that party may submit a Claim in accordance with Article 15.

§ 9.5.3 When the reasons for withholding certification are removed, certification will be made for amounts previously withheld.

§ 9.5.4 If the Architect or Construction Manager withholds certification for payment under Section 9.5.1, the Owner may, at its sole option, issue joint checks to the Contractor and to any Subcontractor or supplier to whom the Contractor failed to make payment for Work properly performed or material or equipment suitably delivered. If the Owner makes payments by joint check, the Owner shall notify the Architect and the Construction Manager, and both will reflect such payment on the next Certificate for Payment.

§ 9.6 Progress Payments

§ 9.6.1 After the Architect has issued a Certificate for Payment or Project Certificate for Payment, the Owner shall make payment in the manner and within the time provided in the Contract Documents, and shall so notify the Construction Manager and Architect.

§ 9.6.2 The Contractor shall pay each Subcontractor, no later than seven days after receipt of payment from the Owner, the amount to which the Subcontractor is entitled, reflecting percentages actually retained from payments to the Contractor on account of the Subcontractor's portion of the Work. The Contractor shall, by appropriate agreement with each Subcontractor, require each Subcontractor to make payments to Sub-subcontractors in a similar manner.

§ 9.6.3 The Construction Manager will, on request, furnish to a Subcontractor, if practicable, information regarding percentages of completion or amounts applied for by the Contractor and action taken thereon by the Owner, Construction Manager and Architect on account of portions of the Work done by such Subcontractor.

§ 9.6.4 The Owner has the right to request written evidence from the Contractor that the Contractor has properly paid Subcontractors and suppliers amounts paid by the Owner to the Contractor for subcontracted Work. If the Contractor

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

fails to furnish such evidence within seven days, the Owner shall have the right to contact Subcontractors and suppliers to ascertain whether they have been properly paid. Neither the Owner, Construction Manager nor Architect shall have an obligation to pay, or to see to the payment of money to, a Subcontractor or supplier, except as may otherwise be required by law.

§ 9.6.5 The Contractor's payments to suppliers shall be treated in a manner similar to that provided in Sections 9.6.2, 9.6.3 and 9.6.4.

§ 9.6.6 A Certificate for Payment, a progress payment, or partial or entire use or occupancy of the Project by the Owner shall not constitute acceptance of Work not in accordance with the Contract Documents.

§ 9.6.7 Unless the Contractor provides the Owner with a payment bond in the full penal sum of the Contract Sum, payments received by the Contractor for Work properly performed by Subcontractors or provided by suppliers shall be held by the Contractor for those Subcontractors or suppliers who performed Work or furnished materials, or both, under contract with the Contractor for which payment was made by the Owner. Nothing contained herein shall require money to be placed in a separate account and not commingled with money of the Contractor, create any fiduciary liability or tort liability on the part of the Contractor for breach of trust, or entitle any person or entity to an award of punitive damages against the Contractor for breach of the requirements of this provision.

§ 9.6.8 Provided the Owner has fulfilled its payment obligations under the Contract Documents, the Contractor shall defend and indemnify the Owner from all loss, liability, damage or expense, including reasonable attorney's fees and litigation expenses, arising out of any lien claim or other claim for payment by any Subcontractor or supplier of any tier. Upon receipt of notice of a lien claim or other claim for payment, the Owner shall notify the Contractor. If approved by the applicable court, when required, the Contractor may substitute a surety bond for the property against which the lien or other claim for payment has been asserted.

§ 9.7 Failure of Payment

If the Construction Manager and Architect do not issue a Certificate for Payment or a Project Certificate for Payment, through no fault of the Contractor, within fourteen days after the Construction Manager's receipt of the Contractor's Application for Payment, or if the Owner does not pay the Contractor within seven days after the date established in the Contract Documents, the amount certified by the Construction Manager and Architect or awarded by binding dispute resolution, then the Contractor may, upon seven additional days' notice to the Owner, Construction Manager and Architect, stop the Work until payment of the amount owing has been received. The Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shutdown, delay and start-up, plus interest as provided for in the Contract Documents.

§ 9.8 Substantial Completion

§ 9.8.1 Substantial Completion is the stage in the progress of the Work when the Work or designated portion thereof is sufficiently complete in accordance with the Contract Documents so the Owner can occupy or utilize the Work for its intended use.

§ 9.8.2 When the Contractor considers that the Work, or a portion thereof which the Owner agrees to accept separately, is substantially complete, the Contractor shall notify the Construction Manager, and the Contractor and Construction Manager shall jointly prepare and submit to the Architect a comprehensive list of items to be completed or corrected prior to final payment. Failure to include an item on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents.

§ 9.8.3 Upon receipt of the list, the Architect, assisted by the Construction Manager, will make an inspection to determine whether the Work or designated portion thereof is substantially complete. If the Architect's inspection discloses any item, whether or not included on the list, which is not sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work or designated portion thereof for its intended use, the Contractor shall, before issuance of the Certificate of Substantial Completion, complete or correct such item upon notification by the Architect. In such case, the Contractor shall then submit a request for another inspection by the Architect, assisted by the Construction Manager, to determine Substantial Completion.

§ 9.8.4 When the Architect, assisted by the Construction Manager, determines that the Work of all of the Contractors, or designated portion thereof, is substantially complete, the Construction Manager will prepare, and the Construction

Init.
/
AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

Manager and Architect shall execute, a Certificate of Substantial Completion that shall establish the date of Substantial Completion; establish responsibilities of the Owner and Contractor for security, maintenance, heat, utilities, damage to the Work and insurance; and fix the time within which the Contractor shall finish all items on the list accompanying the Certificate. Warranties required by the Contract Documents shall commence on the date of Substantial Completion of the Work or designated portion thereof unless otherwise provided in the Certificate of Substantial Completion.

§ 9.8.5 The Certificate of Substantial Completion shall be submitted to the Owner and Contractor for their written acceptance of responsibilities assigned to them in the Certificate. Upon such acceptance, and consent of surety if any, the Owner shall make payment of retainage applying to the Work or designated portion thereof. Such payment shall be adjusted for Work that is incomplete or not in accordance with the requirements of the Contract Documents.

§ 9.9 Partial Occupancy or Use

§ 9.9.1 The Owner may occupy or use any completed or partially completed portion of the Work at any stage when such portion is designated by separate agreement with the Contractor, provided such occupancy or use is consented to by the insurer and authorized by public authorities having jurisdiction over the Project. Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner and Contractor have accepted in writing the responsibilities assigned to each of them for payments, retainage if any, security, maintenance, heat, utilities, damage to the Work and insurance, and have agreed in writing concerning the period for correction of the Work and commencement of warranties required by the Contract Documents. When the Contractor considers a portion substantially complete, the Contractor and Construction Manager shall jointly prepare and submit a list to the Architect as provided under Section 9.8.2. Consent of the Contractor to partial occupancy or use shall not be unreasonably withheld. The stage of the progress of the Work shall be determined by written agreement between the Owner and Contractor or, if no agreement is reached, by decision of the Architect after consultation with the Construction Manager.

§ 9.9.2 Immediately prior to such partial occupancy or use, the Owner, Construction Manager, Contractor, and Architect shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

§ 9.9.3 Unless otherwise agreed upon, partial occupancy or use of a portion or portions of the Work shall not constitute acceptance of Work not complying with the requirements of the Contract Documents.

§ 9.10 Final Completion and Final Payment

§ 9.10.1 Upon completion of the Work, the Contractor shall forward to the Construction Manager a notice that the Work is ready for final inspection and acceptance, and shall also forward to the Construction Manager a final Contractor's Application for Payment. Upon receipt, the Construction Manager shall perform an inspection to confirm the completion of Work of the Contractor. The Construction Manager shall make recommendations to the Architect when the Work of all of the Contractors is ready for final inspection, and shall then forward the Contractors' notices and Application for Payment or Project Application for Payment, to the Architect, who will promptly make such inspection. When the Architect finds the Work acceptable under the Contract Documents and the Contract fully performed, the Construction Manager and Architect will promptly issue a final Certificate for Payment or Project Certificate for Payment stating that to the best of their knowledge, information and belief, and on the basis of their on-site visits and inspections, the Work has been completed in accordance with the Contract Documents and that the entire balance found to be due the Contractor and noted in the final Certificate is due and payable. The Construction Manager's and Architect's final Certificate for Payment or Project Certificate for Payment will constitute a further representation that conditions listed in Section 9.10.2 as precedent to the Contractor's being entitled to final payment have been fulfilled.

§ 9.10.2 Neither final payment nor any remaining retained percentage shall become due until the Contractor submits to the Architect through the Construction Manager (1) an affidavit that payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or the Owner's property might be responsible or encumbered (less amounts withheld by Owner) have been paid or otherwise satisfied, (2) a certificate evidencing that insurance required by the Contract Documents to remain in force after final payment is currently in effect, (3) a written statement that the Contractor knows of no reason that the insurance will not be renewable to cover the period required by the Contract Documents, (4) consent of surety, if any, to final payment (5) documentation of any special warranties, such as manufacturers' warranties or specific Subcontractor warranties, and (6), if required by the Owner, other data

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

establishing payment or satisfaction of obligations, such as receipts and releases and waivers of liens, claims, security interests, or encumbrances arising out of the Contract, to the extent and in such form as may be designated by the Owner. If a Subcontractor refuses to furnish a release or waiver required by the Owner, the Contractor may furnish a bond satisfactory to the Owner to indemnify the Owner against such lien, claim, security interest, or encumbrance. If a lien, claim, security interest, or encumbrance remains unsatisfied after payments are made, the Contractor shall refund to the Owner all money that the Owner may be compelled to pay in discharging the lien, claim, security interest, or encumbrance, including all costs and reasonable attorneys' fees.

§ 9.10.3 If, after Substantial Completion of the Work, final completion thereof is materially delayed through no fault of the Contractor or by issuance of Change Orders affecting final completion, and the Construction Manager and Architect so confirm, the Owner shall, upon application by the Contractor and certification by the Construction Manager and Architect, and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed, corrected, and accepted. If the remaining balance for Work not fully completed or corrected is less than retainage stipulated in the Contract Documents, and if bonds have been furnished, the written consent of the surety to payment of the balance due for that portion of the Work fully completed and accepted shall be submitted by the Contractor to the Architect through the Construction Manager prior to certification of such payment. Such payment shall be made under terms and conditions governing final payment, except that it shall not constitute a waiver of Claims.

§ 9.10.4 The making of final payment shall constitute a waiver of Claims by the Owner except those arising from

- **.1** liens, Claims, security interests, or encumbrances arising out of the Contract and unsettled;
- **.2** failure of the Work to comply with the requirements of the Contract Documents;
- **.3** terms of special warranties required by the Contract Documents; or
- **.4** audits performed by the Owner, if permitted by the Contract Documents, after final payment.

§ 9.10.5 Acceptance of final payment by the Contractor, a Subcontractor, or a supplier, shall constitute a waiver of claims by that payee except those previously made in writing and identified by that payee as unsettled at the time of final Application for Payment.

ARTICLE 10 PROTECTION OF PERSONS AND PROPERTY

§ 10.1 Safety Precautions and Programs

The Contractor shall be responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the performance of the Contract. The Contractor shall submit the Contractor's safety program to the Construction Manager for review and coordination with the safety programs of other Contractors. The Construction Manager's responsibilities for review and coordination of safety programs shall not extend to direct control over or charge of the acts or omissions of the Contractors, Subcontractors, agents or employees of the Contractors or Subcontractors, or any other persons performing portions of the Work and not directly employed by the Construction Manager.

§ 10.2 Safety of Persons and Property

§ 10.2.1 The Contractor shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, injury, or loss to

- **.1** employees on the Work and other persons who may be affected thereby;
- **.2** the Work and materials and equipment to be incorporated therein, whether in storage on or off the site, under care, custody, or control of the Contractor, a Subcontractor, or a Sub-subcontractor;
- **.3** other property at the site or adjacent thereto, such as trees, shrubs, lawns, walks, pavements, roadways, structures, and utilities not designated for removal, relocation, or replacement in the course of construction; and
- **.4** construction or operations by the Owner, Separate Contractors, or other Contractors.

§ 10.2.2 The Contractor shall comply with, and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities, bearing on safety of persons or property or their protection from damage, injury, or loss.

§ 10.2.3 The Contractor shall implement, erect, and maintain, as required by existing conditions and performance of the Contract, reasonable safeguards for safety and protection, including posting danger signs and other warnings against hazards; promulgating safety regulations; and notifying the owners and users of adjacent sites and utilities of the safeguards.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 10.2.4 When use or storage of explosives or other hazardous materials or equipment or unusual methods are necessary for execution of the Work, the Contractor shall exercise utmost care and carry on such activities under supervision of properly qualified personnel.

§ 10.2.5 The Contractor shall promptly remedy damage and loss (other than damage or loss insured under property insurance required by the Contract Documents) to property referred to in Sections 10.2.1.2, 10.2.1.3 and 10.2.1.4 caused in whole or in part by the Contractor, a Subcontractor, a Sub-subcontractor, or anyone directly or indirectly employed by any of them, or by anyone for whose acts they may be liable and for which the Contractor is responsible under Sections 10.2.1.2, 10.2.1.3 and 10.2.1.4. The Contractor may make a Claim for the cost to remedy the damage or loss to the extent such damage or loss is attributable to acts or omissions of the Owner, Construction Manager or Architect or anyone directly or indirectly employed by any of them, or by anyone for whose acts any of them may be liable, and not attributable to the fault or negligence of the Contractor. The foregoing obligations of the Contractor are in addition to the Contractor's obligations under Section 3.18.

§ 10.2.6 The Contractor shall designate a responsible member of the Contractor's organization at the site whose duty shall be the prevention of accidents. This person shall be the Contractor's superintendent unless otherwise designated by the Contractor in writing to the Owner, Construction Manager and Architect.

§ 10.2.7 The Contractor shall not permit any part of the construction or site to be loaded so as to cause damage or create an unsafe condition.

§ 10.2.8 Injury or Damage to Person or Property

If either party suffers injury or damage to person or property because of an act or omission of the other party, or of others for whose acts such party is legally responsible, notice of the injury or damage, whether or not insured, shall be given to the other party within a reasonable time not exceeding 21 days after discovery. The notice shall provide sufficient detail to enable the other party to investigate the matter.

§ 10.3 Hazardous Materials

§ 10.3.1 The Contractor is responsible for compliance with any requirements included in the Contract Documents regarding hazardous materials or substances. If the Contractor encounters a hazardous material or substance not addressed in the Contract Documents and if reasonable precautions will be inadequate to prevent foreseeable bodily injury or death to persons resulting from a material or substance, including but not limited to asbestos or polychlorinated biphenyl (PCB), encountered on the site by the Contractor, the Contractor shall, upon recognizing the condition, immediately stop Work in the affected area and notify the Owner, Construction Manager and Architect of the condition.

§ 10.3.2 Upon receipt of the Contractor's notice, the Owner shall obtain the services of a licensed laboratory to verify the presence or absence of the material or substance reported by the Contractor and, in the event such material or substance is found to be present, to cause it to be rendered harmless. Unless otherwise required by the Contract Documents, the Owner shall furnish in writing to the Contractor, Construction Manager and Architect the names and qualifications of persons or entities who are to perform tests verifying the presence or absence of the material or substance or who are to perform the task of removal or safe containment of the material or substance. The Contractor, the Construction Manager and the Architect will promptly reply to the Owner in writing stating whether or not any of them has reasonable objection to the persons or entities proposed by the Owner. If the Contractor, Construction Manager or Architect has an objection to a person or entity proposed by the Owner, the Owner shall propose another to whom the Contractor, the Construction Manager and the Architect have no reasonable objection. When the material or substance has been rendered harmless, Work in the affected area shall resume upon written agreement of the Owner and Contractor. By Change Order, the Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable additional costs of shutdown, delay, and start-up.

§ 10.3.3 To the fullest extent permitted by law, the Owner shall indemnify and hold harmless the Contractor, Subcontractors, Construction Manager, Architect, their consultants, and agents and employees of any of them from and against claims, damages, losses, and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work in the affected area if in fact the material or substance presents the risk of bodily injury or death as described in Section 10.3.1 and has not been rendered harmless, provided that such claim, damage, loss, or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of

Init.
/
AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

tangible property (other than the Work itself), except to the extent that such damage, loss, or expense is due to the fault or negligence of the party seeking indemnity.

§ 10.3.4 The Owner shall not be responsible under this Section 10.3 for hazardous materials or substances the Contractor brings to the site unless such materials or substances are required by the Contract Documents. The Owner shall be responsible for hazardous materials or substances required by the Contract Documents, except to the extent of the Contractor's fault or negligence in the use and handling of such materials or substances.

§ 10.3.5 The Contractor shall reimburse the Owner for the cost and expense the Owner incurs (1) for remediation of hazardous materials or substances the Contractor brings to the site and negligently handles, or (2) where the Contractor fails to perform its obligations under Section 10.3.1, except to the extent that the cost and expense are due to the Owner's fault or negligence.

§ 10.3.6 If, without negligence on the part of the Contractor, the Contractor is held liable by a government agency for the cost of remediation of a hazardous material or substance solely by reason of performing Work as required by the Contract Documents, the Owner shall reimburse the Contractor for all cost and expense thereby incurred.

§ 10.4 Emergencies

In an emergency affecting safety of persons or property, the Contractor shall act, at the Contractor's discretion, to prevent threatened damage, injury, or loss. Additional compensation or extension of time claimed by the Contractor on account of an emergency shall be determined as provided in Article 15 and Article 7.

ARTICLE 11 INSURANCE AND BONDS

§ 11.1 Contractor's Insurance and Bonds

§ 11.1.1 The Contractor shall purchase and maintain insurance of the types and limits of liability, containing the endorsements, and subject to the terms and conditions, as described in the Agreement or elsewhere in the Contract Documents. The Contractor shall purchase and maintain the required insurance from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located. The Owner, Construction Manager and Construction Manager's consultants, and the Architect and Architect's consultants, shall be named as additional insureds under the Contractor's commercial general liability policy or as otherwise described in the Contract Documents.

§ 11.1.2 The Contractor shall provide surety bonds of the types, for such penal sums, and subject to such terms and conditions as required by the Contract Documents. The Contractor shall purchase and maintain the required bonds from a company or companies lawfully authorized to issue surety bonds in the jurisdiction where the Project is located.

§ 11.1.3 Upon the request of any person or entity appearing to be a potential beneficiary of bonds covering payment of obligations arising under the Contract, the Contractor shall promptly furnish a copy of the bonds or shall authorize a copy to be furnished.

§ 11.1.4 Notice of Cancellation or Expiration of Contractor's Required Insurance. Within three (3) business days of the date the Contractor becomes aware of an impending or actual cancellation or expiration of any insurance required by the Contract Documents, the Contractor shall provide notice directly to the Owner, and separately to the Construction Manager, of such impending or actual cancellation or expiration. Upon receipt of notice from the Contractor, the Owner shall, unless the lapse in coverage arises from an act or omission of the Owner, have the right to stop the Work until the lapse in coverage has been cured by the procurement of replacement coverage by the Contractor. The furnishing of notice by the Contractor shall not relieve the Contractor of any contractual obligation to provide any required coverage.

§ 11.2 Owner's Insurance

§ 11.2.1 The Owner shall purchase and maintain insurance of the types and limits of liability, containing the endorsements, and subject to the terms and conditions, as described in the Agreement or elsewhere in the Contract Documents. The Owner shall purchase and maintain the required insurance from an insurance company or insurance companies lawfully authorized to issue insurance in the jurisdiction where the Project is located.

§ 11.2.2 Failure to Purchase Required Property Insurance. If the Owner fails to purchase and maintain the required property insurance, with all of the coverages and in the amounts described in the Agreement or elsewhere in the

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

Contract Documents, the Owner shall inform both the Contractor and the Construction Manager, separately and in writing, prior to commencement of the Work. Upon receipt of notice from the Owner, the Contractor may delay commencement of the Work and may obtain insurance that will protect the interests of the Contractor, Subcontractors, and Sub-Subcontractors in the Work. When the failure to provide coverage has been cured or resolved, the Contract Sum and Contract Time shall be equitably adjusted. In the event the Owner fails to procure coverage, the Owner waives all rights against the Contractor, Subcontractors, and Sub-subcontractors to the extent the loss to the Owner would have been covered by the insurance to have been procured by the Owner. The cost of the insurance shall be charged to the Owner by a Change Order. If the Owner does not provide written notice, and the Contractor is damaged by the failure or neglect of the Owner to purchase or maintain the required insurance, the Owner shall reimburse the Contractor for all reasonable costs and damages attributable thereto.

§ 11.2.3 Notice of Cancellation or Expiration of Owner's Required Property Insurance. Within three (3) business days of the date the Owner becomes aware of an impending or actual cancellation or expiration of any property insurance required by the Contract Documents, the Owner shall provide notice directly to the Contractor, and separately to the Construction Manager, of such impending or actual cancellation or expiration. Unless the lapse in coverage arises from an act or omission of the Contractor: (1) the Contractor, upon receipt of notice from the Owner, shall have the right to stop the Work until the lapse in coverage has been cured by the procurement of replacement coverage by either the Owner or the Contractor; (2) the Contract Time and Contract Sum shall be equitably adjusted; and (3) the Owner waives all rights against the Contractor, Subcontractors, and Sub-subcontractors to the extent any loss to the Owner would have been covered by the insurance had it not expired or been cancelled. If the Contractor purchases replacement coverage, the cost of the insurance shall be charged to the Owner by an appropriate Change Order. The furnishing of notice by the Owner shall not relieve the Owner of any contractual obligation to provide required insurance.

§ 11.3 Waivers of Subrogation

§ 11.3.1 The Owner and Contractor waive all rights against (1) each other and any of their subcontractors, sub-subcontractors, agents, and employees, each of the other; (2) the Construction Manager and Construction Manager's consultants; (3) the Architect and Architect's consultants; (4) other Contractors and any of their subcontractors, sub-subcontractors, agents, and employees; and (5) Separate Contractors, if any, and any of their subcontractors, sub-subcontractors, agents, and employees, for damages caused by fire, or other causes of loss, to the extent those losses are covered by property insurance required by the Agreement or other property insurance applicable to the Project, except such rights as they have to proceeds of such insurance. The Owner or Contractor, as appropriate, shall require similar written waivers in favor of the individuals and entities identified above from the Construction Manager, Construction Manager's consultants, Architect, Architect's consultants, other Contractors, Separate Contractors, subcontractors, and sub-subcontractors. The policies of insurance purchased and maintained by each person or entity agreeing to waive claims pursuant to this Section 11.3.1 shall not prohibit this waiver of subrogation. This waiver of subrogation shall be effective as to a person or entity (1) even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, (2) even though that person or entity did not pay the insurance premium directly or indirectly, or (3) whether or not the person or entity had an insurable interest in the damaged property.

§ 11.3.2 If during the Project construction period the Owner insures properties, real or personal or both, at or adjacent to the site by property insurance under policies separate from those insuring the Project, or if after final payment property insurance is to be provided on the completed Project through a policy or policies other than those insuring the Project during the construction period, to the extent permissible by such policies, the Owner waives all rights in accordance with the terms of Section 11.3.1 for damages caused by fire or other causes of loss covered by this separate property insurance.

§ 11.4 Loss of Use, Business Interruption, and Delay in Completion Insurance

The Owner, at the Owner's option, may purchase and maintain insurance that will protect the Owner against loss of use of the Owner's property, or the inability to conduct normal operations, due to fire or other causes of loss. The Owner waives all rights of action against the Contractor, Architect, and Construction Manager for loss of use of the Owner's property, due to fire or other hazards however caused.

§ 11.5 Adjustment and Settlement of Insured Loss

§ 11.5.1 A loss insured under the property insurance required by the Agreement shall be adjusted by the Owner as fiduciary and made payable to the Owner as fiduciary for the insureds, as their interests may appear, subject to

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

requirements of any applicable mortgagee clause and of Section 11.5.2. The Owner shall pay the Construction Manager, Architect and Contractor their just shares of insurance proceeds received by the Owner, and by appropriate agreements the Construction Manager, Architect and Contractor shall make payments to their consultants and Subcontractors in similar manner.

§ 11.5.2 Prior to settlement of an insured loss, the Owner shall notify the Contractor of the terms of the proposed settlement as well as the proposed allocation of the insurance proceeds. The Contractor shall have 14 days from receipt of notice to object to the proposed settlement or allocation of the proceeds. If the Contractor does not object, the Owner shall settle the loss and the Contractor shall be bound by the settlement and allocation. Upon receipt, the Owner shall deposit the insurance proceeds in a separate account and make the appropriate distributions. Thereafter, if no other agreement is made or the Owner does not terminate the Contract for convenience, the Owner and Contractor shall execute a Change Order for reconstruction of the damaged or destroyed Work in the amount allocated for that purpose. If the Contractor timely objects to either the terms of the proposed settlement or the allocation of the proceeds, the Owner may proceed to settle the insured loss, and any dispute between the Owner and Contractor arising out of the settlement or allocation of the proceeds shall be resolved pursuant to Article 15. Pending resolution of any dispute, the Owner may issue a Construction Change Directive for the reconstruction of the damaged or destroyed Work.

ARTICLE 12 UNCOVERING AND CORRECTION OF WORK

§ 12.1 Uncovering of Work

§ 12.1.1 If a portion of the Work is covered contrary to the Construction Manager's or Architect's request or to requirements specifically expressed in the Contract Documents, it must, if requested in writing by either, be uncovered for their examination and be replaced at the Contractor's expense without change in the Contract Time.

§ 12.1.2 If a portion of the Work has been covered that the Construction Manager or Architect has not specifically requested to examine prior to its being covered, the Construction Manager or Architect may request to see such Work and it shall be uncovered by the Contractor. If such Work is in accordance with the Contract Documents, the Contractor shall be entitled to an equitable adjustment to the Contract Sum and Contract Time as may be appropriate. If such Work is not in accordance with the Contract Documents, the costs of uncovering the Work, and the cost of correction, shall be at the Contractor's expense.

§ 12.2 Correction of Work

§ 12.2.1 Before Substantial Completion

The Contractor shall promptly correct Work rejected by the Construction Manager or Architect or failing to conform to the requirements of the Contract Documents, discovered before Substantial Completion, and whether or not fabricated, installed or completed. Costs of correcting such rejected Work, including additional testing and inspections, the cost of uncovering and replacement, and compensation for the Construction Manager's and Architect's services and expenses made necessary thereby, shall be at the Contractor's expense.

§ 12.2.2 After Substantial Completion

§ 12.2.2.1 In addition to the Contractor's obligations under Section 3.5, if, within one year after the date of Substantial Completion of the Work or designated portion thereof, or after the date for commencement of warranties established under Section 9.9.1, or by terms of any applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, the Contractor shall correct it promptly after receipt of notice from the Owner to do so, unless the Owner has previously given the Contractor a written acceptance of such condition. The Owner shall give such notice promptly after discovery of the condition. During the one-year period for correction of Work, if the Owner fails to notify the Contractor and give the Contractor an opportunity to make the correction, the Owner waives the rights to require correction by the Contractor and to make a claim for breach of warranty. If the Contractor fails to correct nonconforming Work within a reasonable time during that period after receipt of notice from the Owner, Construction Manager or Architect, the Owner may correct it in accordance with Section 2.5.

§ 12.2.2.2 The one-year period for correction of Work shall be extended with respect to portions of Work first performed after Substantial Completion by the period of time between Substantial Completion and the actual completion of that portion of the Work.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 12.2.2.3 The one-year period for correction of Work shall not be extended by corrective Work performed by the Contractor pursuant to this Section 12.2.

§ 12.2.3 The Contractor shall remove from the site portions of the Work that are not in accordance with the requirements of the Contract Documents and are neither corrected by the Contractor nor accepted by the Owner.

§ 12.2.4 The Contractor shall bear the cost of correcting destroyed or damaged construction of the Owner, Separate Contractors, or other Contractors, whether completed or partially completed, caused by the Contractor's correction or removal of Work that is not in accordance with the requirements of the Contract Documents.

§ 12.2.5 Nothing contained in this Section 12.2 shall be construed to establish a period of limitation with respect to other obligations the Contractor has under the Contract Documents. Establishment of the one-year period for correction of Work as described in Section 12.2.2 relates only to the specific obligation of the Contractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Contractor's liability with respect to the Contractor's obligations other than specifically to correct the Work.

§ 12.3 Acceptance of Nonconforming Work

If the Owner prefers to accept Work that is not in accordance with the requirements of the Contract Documents, the Owner may do so instead of requiring its removal and correction, in which case the Contract Sum will be reduced as appropriate and equitable. Such adjustment shall be effected whether or not final payment has been made.

ARTICLE 13 MISCELLANEOUS PROVISIONS

§ 13.1 Governing Law

The Contract shall be governed by the law of the place where the Project is located excluding that jurisdiction's choice of law rules. If the parties have selected arbitration as the method of binding dispute resolution, the Federal Arbitration Act shall govern Section 15.4.

§ 13.2 Successors and Assigns

§ 13.2.1 The Owner and Contractor respectively bind themselves, their partners, successors, assigns, and legal representatives to covenants, agreements, and obligations contained in the Contract Documents. Except as provided in Section 13.2.2, neither party to the Contract shall assign the Contract as a whole without written consent of the other. If either party attempts to make an assignment without such consent, that party shall nevertheless remain legally responsible for all obligations under the Contract.

§ 13.2.2 The Owner may, without consent of the Contractor, assign the Contract to a lender providing construction financing for the Project, if the lender assumes the Owner's rights and obligations under the Contract Documents. The Contractor shall execute all consents reasonably required to facilitate the assignment.

§ 13.3 Rights and Remedies

§ 13.3.1 Duties and obligations imposed by the Contract Documents and rights and remedies available thereunder shall be in addition to and not a limitation of duties, obligations, rights, and remedies otherwise imposed or available by law.

§ 13.3.2 No action or failure to act by the Owner, Construction Manager, Architect, or Contractor shall constitute a waiver of a right or duty afforded them under the Contract, nor shall such action or failure to act constitute approval of or acquiescence in a breach thereunder, except as may be specifically agreed upon in writing.

§ 13.4 Tests and Inspections

§ 13.4.1 Tests, inspections, and approvals of portions of the Work shall be made as required by the Contract Documents and by applicable laws, statutes, ordinances, codes, rules, and regulations or lawful orders of public authorities. Unless otherwise provided, the Contractor shall make arrangements for such tests, inspections, and approvals with an independent testing laboratory or entity acceptable to the Owner, or with the appropriate public authority, and shall bear all related costs of tests, inspections, and approvals. The Contractor shall give the Construction Manager and Architect timely notice of when and where tests and inspections are to be made so that the Construction Manager and Architect may be present for such procedures. The Owner shall bear costs of tests, inspections, or approvals that do not become

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

requirements until after bids are received or negotiations concluded. The Owner shall directly arrange and pay for tests, inspections, or approvals where building codes or applicable laws or regulations so require.

§ 13.4.2 If the Construction Manager, Architect, Owner, or public authorities having jurisdiction determine that portions of the Work require additional testing, inspection, or approval not included under Section 13.4.1, the Construction Manager and Architect will, upon written authorization from the Owner, instruct the Contractor to make arrangements for such additional testing, inspection, or approval, by an entity acceptable to the Owner, and the Contractor shall give timely notice to the Construction Manager and Architect of when and where tests and inspections are to be made so that the Construction Manager and Architect may be present for such procedures. Such costs, except as provided in Section 13.4.3, shall be at the Owner's expense.

§ 13.4.3 If procedures for testing, inspection, or approval under Sections 13.4.1 and 13.4.2 reveal failure of the portions of the Work to comply with requirements established by the Contract Documents, all costs made necessary by such failure, including those of repeated procedures and compensation for the Construction Manager's and Architect's services and expenses, shall be at the Contractor's expense.

§ 13.4.4 Required certificates of testing, inspection, or approval shall, unless otherwise required by the Contract Documents, be secured by the Contractor and promptly delivered to the Construction Manager for transmittal to the Architect.

§ 13.4.5 If the Construction Manager or Architect is to observe tests, inspections, or approvals required by the Contract Documents, the Construction Manager or Architect will do so promptly and, where practicable, at the normal place of testing.

§ 13.4.6 Tests or inspections conducted pursuant to the Contract Documents shall be made promptly to avoid unreasonable delay in the Work.

§ 13.5 Interest

Payments due and unpaid under the Contract Documents shall bear interest from the date payment is due at the rate the parties agree upon in writing or, in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.

ARTICLE 14 TERMINATION OR SUSPENSION OF THE CONTRACT

§ 14.1 Termination by the Contractor

§ 14.1.1 The Contractor may terminate the Contract if the Work is stopped for a period of 30 consecutive days through no act or fault of the Contractor, a Subcontractor, a Sub-subcontractor, their agents or employees, or any other persons or entities performing portions of the Work, for any of the following reasons:

- **.1** Issuance of an order of a court or other public authority having jurisdiction that requires all Work to be stopped;
- **.2** An act of government, such as a declaration of national emergency, that requires all Work to be stopped;
- **.3** Because the Construction Manager has not certified or the Architect has not issued a Certificate for Payment and has not notified the Contractor of the reason for withholding certification as provided in Section 9.4, or because the Owner has not made payment on a Certificate for Payment within the time stated in the Contract Documents; or
- **.4** The Owner has failed to furnish to the Contractor reasonable evidence as required by Section 2.2.

§ 14.1.2 The Contractor may terminate the Contract if, through no act or fault of the Contractor, a Subcontractor, a Sub-subcontractor, their agents or employees, or any other persons or entities performing portions of the Work, repeated suspensions, delays, or interruptions of the entire Work by the Owner as described in Section 14.3, constitute in the aggregate more than 100 percent of the total number of days scheduled for completion, or 120 days in any 365-day period, whichever is less.

§ 14.1.3 If one of the reasons described in Section 14.1.1 or 14.1.2 exists, the Contractor may, upon seven days' notice to the Owner, Construction Manager and Architect, terminate the Contract and recover from the Owner payment for Work executed, as well as reasonable overhead and profit on Work not executed, and costs incurred by reason of such termination.

Init.
/
AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

§ 14.1.4 If the Work is stopped for a period of 60 consecutive days through no act or fault of the Contractor, a Subcontractor, a Sub-subcontractor, or their agents or employees, or any other persons performing portions of the Work because the Owner has repeatedly failed to fulfill the Owner's obligations under the Contract Documents with respect to matters important to the progress of the Work, the Contractor may, upon seven additional days' notice to the Owner, Construction Manager and Architect, terminate the Contract and recover from the Owner as provided in Section 14.1.3.

§ 14.2 Termination by the Owner for Cause

§ 14.2.1 The Owner may terminate the Contract if the Contractor

- **.1** repeatedly refuses or fails to supply enough properly skilled workers or proper materials;
- **.2** fails to make payment to Subcontractors or suppliers in accordance with the respective agreements between the Contractor and the Subcontractors or suppliers;
- **.3** repeatedly disregards applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of a public authority; or
- **.4** otherwise is guilty of substantial breach of a provision of the Contract Documents.

§ 14.2.2 When any of the reasons described in Section 14.2.1 exist, after consultation with the Construction Manager, and upon certification by the Architect that sufficient cause exists to justify such action, the Owner may, without prejudice to any other rights or remedies of the Owner and after giving the Contractor and the Contractor's surety, if any, seven days' notice, terminate employment of the Contractor and may, subject to any prior rights of the surety:

- **.1** Exclude the Contractor from the site and take possession of all materials, equipment, tools, and construction equipment and machinery thereon owned by the Contractor;
- **.2** Accept assignment of subcontracts pursuant to Section 5.4; and
- **.3** Finish the Work by whatever reasonable method the Owner may deem expedient. Upon written request of the Contractor, the Owner shall furnish to the Contractor a detailed accounting of the costs incurred by the Owner in finishing the Work.

§ 14.2.3 When the Owner terminates the Contract for one of the reasons stated in Section 14.2.1, the Contractor shall not be entitled to receive further payment until the Work is finished.

§ 14.2.4 If the unpaid balance of the Contract Sum exceeds costs of finishing the Work, including compensation for the Construction Manager's and Architect's services and expenses made necessary thereby, and other damages incurred by the Owner and not expressly waived, such excess shall be paid to the Contractor. If such costs and damages exceed the unpaid balance, the Contractor shall pay the difference to the Owner. The amount to be paid to the Contractor or Owner, as the case may be, shall, upon application, be certified by the Initial Decision Maker after consultation with the Construction Manager, and this obligation for payment shall survive termination of the Contract.

§ 14.3 Suspension by the Owner for Convenience

§ 14.3.1 The Owner may, without cause, order the Contractor in writing to suspend, delay or interrupt the Work, in whole or in part for such period of time as the Owner may determine.

§ 14.3.2 The Contract Sum and the Contract Time shall be adjusted for increases in the cost and time caused by suspension, delay, or interruption under Section 14.3.1. Adjustment of the Contract Sum shall include profit. No adjustment shall be made to the extent:

- **.1** that performance is, was, or would have been, so suspended, delayed, or interrupted, by another cause for which the Contractor is responsible; or
- **.2** that an equitable adjustment is made or denied under another provision of this Contract.

§ 14.4 Termination by the Owner for Convenience

§ 14.4.1 The Owner may, at any time, terminate the Contract for the Owner's convenience and without cause.

§ 14.4.2 Upon receipt of notice from the Owner of such termination for the Owner's convenience, the Contractor shall

- **.1** cease operations as directed by the Owner in the notice;
- **.2** take actions necessary, or that the Owner may direct, for the protection and preservation of the Work; and

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

.3 except for Work directed to be performed prior to the effective date of termination stated in the notice, terminate all existing subcontracts and purchase orders and enter into no further subcontracts and purchase orders.

§ 14.4.3 In case of such termination for the Owner's convenience, the Owner shall pay the Contractor for Work properly executed; costs incurred by reason of the termination, including costs attributable to termination of Subcontracts; and the termination fee, if any, set forth in the Agreement.

ARTICLE 15 CLAIMS AND DISPUTES

§ 15.1 Claims

§ 15.1.1 Definition. A Claim is a demand or assertion by one of the parties seeking, as a matter of right, payment of money, a change in the Contract Time, or other relief with respect to the terms of the Contract. The term "Claim" also includes other disputes and matters in question between the Owner and Contractor arising out of or relating to the Contract. The responsibility to substantiate Claims shall rest with the party making the Claim. This Section 15.1.1 does not require the Owner to file a Claim in order to impose liquidated damages in accordance with the Contract Documents.

§ 15.1.2 Time Limits on Claims

The Owner and Contractor shall commence all Claims and causes of action against the other and arising out of or related to the Contract, whether in contract, tort, breach of warranty or otherwise, in accordance with the requirements of the binding dispute resolution method selected in the Agreement and within the period specified by applicable law, but in any case not more than 10 years after the date of Substantial Completion of the Work. The Owner and Contractor waive all Claims and causes of action not commenced in accordance with this Section 15.1.2.

§ 15.1.3 Notice of Claims

§ 15.1.3.1 Claims by either the Owner or Contractor, where the condition giving rise to the Claim is first discovered prior to expiration of the period for correction of the Work set forth in Section 12.2.2, shall be initiated by notice to the other party and to the Initial Decision Maker with a copy sent to the Construction Manager and Architect, if the Architect is not serving as the Initial Decision Maker. Claims by either party under this Section 15.1.3.1 shall be initiated within 21 days after occurrence of the event giving rise to such Claim or within 21 days after the claimant first recognizes the condition giving rise to the Claim, whichever is later.

§ 15.1.3.2 Claims by either the Owner or Contractor, where the condition giving rise to the Claim is first discovered after expiration of the period for correction of the Work set forth in Section 12.2.2, shall be initiated by notice to the other party. In such event, no decision by the Initial Decision Maker is required.

§ 15.1.4 Continuing Contract Performance

§ 15.1.4.1 Pending final resolution of a Claim, except as otherwise agreed in writing or as provided in Section 9.7 and Article 14, the Contractor shall proceed diligently with performance of the Contract and the Owner shall continue to make payments in accordance with the Contract Documents.

§ 15.1.4.2 The Contract Sum and Contract Time shall be adjusted in accordance with the Initial Decision Maker's decision, subject to the right of either party to proceed in accordance with this Article 15. The Architect will issue Certificates for Payment in accordance with the decision of the Initial Decision Maker.

§ 15.1.5 Claims for Additional Cost. If the Contractor wishes to make a Claim for an increase in the Contract Sum, notice as provided in Section 15.1.3 shall be given before proceeding to execute the portion of the Work that is the subject of the Claim. Prior notice is not required for Claims relating to an emergency endangering life or property arising under Section 10.4.

§ 15.1.6 Claims for Additional Time

§ 15.1.6.1 If the Contractor wishes to make a Claim for an increase in the Contract Time, notice as provided in Section 15.1.3 shall be given. The Contractor's Claim shall include an estimate of cost and of probable effect of delay on progress of the Work. In the case of a continuing delay only one Claim is necessary.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 15.1.6.2 If adverse weather conditions are the basis for a Claim for additional time, such Claim shall be documented by data substantiating that weather conditions were abnormal for the period of time, could not have been reasonably anticipated and had an adverse effect on the scheduled construction.

§ 15.1.7 Waiver of Claims for Consequential Damages. The Contractor and Owner waive Claims against each other for consequential damages arising out of or relating to this Contract. This mutual waiver includes

.1 damages incurred by the Owner for rental expenses, for losses of use, income, profit, financing, business and reputation, and for loss of management or employee productivity or of the services of such persons; and

.2 damages incurred by the Contractor for principal office expenses including the compensation of personnel stationed there, for losses of financing, business and reputation, and for loss of profit except anticipated profit arising directly from the Work.

This mutual waiver is applicable, without limitation, to all consequential damages due to either party's termination in accordance with Article 14. Nothing contained in this Section 15.1.7 shall be deemed to preclude assessment of liquidated damages, when applicable, in accordance with the requirements of the Contract Documents.

§ 15.2 Initial Decision

§ 15.2.1 Claims, excluding those where the condition giving rise to the Claim is first discovered after expiration of the period for correction of the Work set forth in Section 12.2.2 or arising under Sections 10.3, 10.4, and 11.5, shall be referred to the Initial Decision Maker for initial decision. The Architect will serve as the Initial Decision Maker, unless otherwise indicated in the Agreement. Except for those Claims excluded by this Section 15.2.1, an initial decision shall be required as a condition precedent to mediation of any Claim. If an initial decision has not been rendered within 30 days after the Claim has been referred to the Initial Decision Maker, the party asserting the Claim may demand mediation and binding dispute resolution without a decision having been rendered. Unless the Initial Decision Maker and all affected parties agree, the Initial Decision Maker will not decide disputes between the Contractor and persons or entities other than the Owner.

§ 15.2.2 The Initial Decision Maker will review Claims and within ten days of the receipt of a Claim take one or more of the following actions: (1) request additional supporting data from the claimant or a response with supporting data from the other party, (2) reject the Claim in whole or in part, (3) approve the Claim, (4) suggest a compromise, or (5) advise the parties that the Initial Decision Maker is unable to resolve the Claim if the Initial Decision Maker lacks sufficient information to evaluate the merits of the Claim or if the Initial Decision Maker concludes that, in the Initial Decision Maker's sole discretion, it would be inappropriate for the Initial Decision Maker to resolve the Claim.

§ 15.2.3 In evaluating Claims, the Initial Decision Maker may, but shall not be obligated to, consult with or seek information from either party or from persons with special knowledge or expertise who may assist the Initial Decision Maker in rendering a decision. The Initial Decision Maker may request the Owner to authorize retention of such persons at the Owner's expense.

§ 15.2.4 If the Initial Decision Maker requests a party to provide a response to a Claim or to furnish additional supporting data, such party shall respond, within ten days after receipt of the request, and shall either (1) provide a response on the requested supporting data, (2) advise the Initial Decision Maker when the response or supporting data will be furnished, or (3) advise the Initial Decision Maker that no supporting data will be furnished. Upon receipt of the response or supporting data, if any, the Initial Decision Maker will either reject or approve the Claim in whole or in part.

§ 15.2.5 The Initial Decision Maker will render an initial decision approving or rejecting the Claim, or indicating that the Initial Decision Maker is unable to resolve the Claim. This initial decision shall (1) be in writing; (2) state the reasons therefor; and (3) notify the parties, the Construction Manager, and the Architect, if the Architect is not serving as the Initial Decision Maker, of any change in the Contract Sum or Contract Time or both. The initial decision shall be final and binding on the parties but subject to mediation and, if the parties fail to resolve their dispute through mediation, to binding dispute resolution.

§ 15.2.6 Either party may file for mediation of an initial decision at any time, subject to the terms of Section 15.2.6.1.

§ 15.2.6.1 Either party may, within 30 days from the date of receipt of an initial decision, demand in writing that the other party file for mediation. If such a demand is made and the party receiving the demand fails to file for mediation

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1832333410)

within 30 days of receipt thereof, then both parties waive their rights to mediate or pursue binding dispute resolution proceedings with respect to the initial decision.

§ 15.2.7 In the event of a Claim against the Contractor, the Owner may, but is not obligated to, notify the surety, if any, of the nature and amount of the Claim. If the Claim relates to a possibility of a Contractor's default, the Owner may, but is not obligated to, notify the surety and request the surety's assistance in resolving the controversy.

§ 15.2.8 If a Claim relates to or is the subject of a mechanic's lien, the party asserting such Claim may proceed in accordance with applicable law to comply with the lien notice or filing deadlines.

§ 15.3 Mediation

§ 15.3.1 Claims, disputes, or other matters in controversy arising out of or related to the Contract, except those waived as provided for in Sections 9.10.4, 9.10.5, and 15.1.7, shall be subject to mediation as a condition precedent to binding dispute resolution.

§ 15.3.2 The parties shall endeavor to resolve their Claims by mediation which, unless the parties mutually agree otherwise, shall be administered by the American Arbitration Association in accordance with its Construction Industry Mediation Procedures in effect on the date of the Agreement. A request for mediation shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the mediation. The request may be made concurrently with the filing of binding dispute resolution proceedings but, in such event, mediation shall proceed in advance of binding dispute resolution proceedings, which shall be stayed pending mediation for a period of 60 days from the date of filing, unless stayed for a longer period by agreement of the parties or court order. If an arbitration is stayed pursuant to this Section 15.3.2, the parties may nonetheless proceed to the selection of the arbitrator(s) and agree upon a schedule for later proceedings.

§ 15.3.3 Either party may, within 30 days from the date that mediation has been concluded without resolution of the dispute or 60 days after mediation has been demanded without resolution of the dispute, demand in writing that the other party file for binding dispute resolution. If such a demand is made and the party receiving the demand fails to file for binding dispute resolution within 60 days after receipt thereof, then both parties waive their rights to binding dispute resolution proceedings with respect to the initial decision.

§ 15.3.4 The parties shall share the mediator's fee and any filing fees equally. The mediation shall be held in the place where the Project is located, unless another location is mutually agreed upon. Agreements reached in mediation shall be enforceable as settlement agreements in any court having jurisdiction thereof.

§ 15.4 Arbitration

§ 15.4.1 If the parties have selected arbitration as the method for binding dispute resolution in the Agreement, any Claim subject to, but not resolved by, mediation shall be subject to arbitration which, unless the parties mutually agree otherwise, shall be administered by the American Arbitration Association in accordance with its Construction Industry Arbitration Rules in effect on the date of the Agreement. The Arbitration shall be conducted in the place where the Project is located, unless another location is mutually agreed upon. A demand for arbitration shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the arbitration. The party filing a notice of demand for arbitration must assert in the demand all Claims then known to that party on which arbitration is permitted to be demanded.

§ 15.4.1.1 A demand for arbitration shall be made no earlier than concurrently with the filing of a request for mediation, but in no event shall it be made after the date when the institution of legal or equitable proceedings based on the Claim would be barred by the applicable statute of limitations. For statute of limitations purposes, receipt of a written demand for arbitration by the person or entity administering the arbitration shall constitute the institution of legal or equitable proceedings based on the Claim.

§ 15.4.2 The award rendered by the arbitrator or arbitrators shall be final, and judgment may be entered upon it in accordance with applicable law in any court having jurisdiction thereof.

§ 15.4.3 The foregoing agreement to arbitrate and other agreements to arbitrate with an additional person or entity duly consented to by parties to the Agreement, shall be specifically enforceable under applicable law in any court having jurisdiction thereof.

Init.
/

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

§ 15.4.4 Consolidation or Joinder

§ 15.4.4.1 Subject to the rules of the American Arbitration Association or other applicable arbitration rules, either party may consolidate an arbitration conducted under this Agreement with any other arbitration to which it is a party provided that (1) the arbitration agreement governing the other arbitration permits consolidation, (2) the arbitrations to be consolidated substantially involve common questions of law or fact, and (3) the arbitrations employ materially similar procedural rules and methods for selecting arbitrator(s).

§ 15.4.4.2 Subject to the rules of the American Arbitration Association or other applicable arbitration rules, either party may include by joinder persons or entities substantially involved in a common question of law or fact whose presence is required if complete relief is to be accorded in arbitration, provided that the party sought to be joined consents in writing to such joinder. Consent to arbitration involving an additional person or entity shall not constitute consent to arbitration of any claim, dispute or other matter in question not described in the written consent.

§ 15.4.4.3 The Owner and Contractor grant to any person or entity made a party to an arbitration conducted under this Section 15.4, whether by joinder or consolidation, the same rights of joinder and consolidation as those of the Owner and Contractor under this Agreement.

AIA Document A232 – 2019. Copyright © 1992, 2009, and 2019. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are registered trademarks of The American Institute of Architects. This document was produced at 09:27:22 ET on 02/24/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1832333410)

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

SECTION 00 73 13

SUPPLEMENTARY GENERAL CONDITIONS A232-2019

The following supplements modify the "General Conditions of the Contract for Construction, Construction Manager as Advisor Edition." AIA Document A232-2019. Where a portion of the General Conditions is modified or deleted by the Supplementary Conditions, the unaltered portions of the General Conditions shall remain in effect.

TABLE OF ARTICLES

1. GENERAL PROVISIONS
2. OWNER
3. CONTRACTOR
4. ARCHITECT AND CONSTRUCTION MANAGER
5. SUBCONTRACTORS
6. CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS
7. CHANGES IN THE WORK
8. TIME
9. PAYMENTS AND COMPLETION
10. PROTECTION OF PERSONS AND PROPERTY
11. INSURANCE AND BONDS
12. UNCOVERING AND CORRECTION OF WORK
13. MISCELLANEOUS PROVISIONS
14. TERMINATION OR SUSPENSION OF THE CONTRACT
15. CLAIMS AND DISPUTES

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

ARTICLE 1: GENERAL PROVISIONS

1.1 BASIC DEFINITIONS

1.1.1 THE CONTRACT DOCUMENTS

Delete the last sentence in its entirety and replace with the following:

"The Contract Documents also include Advertisement for Bid, Instructions to Bidder, sample forms, the Bid Form, the Contractor's completed Bid and the Award Letter."

1.2 CORRELATION AND INTENT OF THE CONTRACT DOCUMENTS

Add the following Paragraphs:

1.2.4 In the case of an inconsistency between the Drawings and the Specifications, or within either document not clarified by addendum, the better quality or greater quantity of work shall be provided in accordance with the Architect's interpretation.

1.2.5 The word "PROVIDE" as used in the Contract Documents shall mean "FURNISH AND INSTALL" and shall include, without limitation, all labor, materials, equipment, transportation, services and other items required to complete the Work.

1.2.6 The word "PRODUCT" as used in the Contract Documents means all materials, systems and equipment.

1.5 OWNERSHIP AND USE OF DRAWINGS, SPECIFICATIONS AND OTHER INSTRUMENTS OF SERVICE

Delete Paragraph 1.5.1 in its entirety and replace with the following:

"All pre-design studies, drawings, specifications and other documents, including those in electronic form, prepared by the Architect under this Agreement are, and shall remain, the property of the Owner whether the Project for which they are made is executed or not. As for the Project for which the Architect is hired, the Architect still remain liable for any claim relating to the design that arises from the Project.

However, such documents may be used by the Owner to construct one or more like projects without the approval of, or additional compensation to, the Architect. The Contractor, Subcontractors, Sub-subcontractors and Material or Equipment Suppliers are authorized to use and reproduce applicable portions of the Drawings, Specifications and other documents prepared by the Architect and the Architect's consultants appropriate to and for use in the execution of their Work under the Contract Documents. They are not to be used by the Contractor or any Subcontractor, Sub-subcontractor or Material and Equipment Supplier on other Projects or for additions to this Project outside the scope of the Work without the specific written consent of the Owner, Architect and Architect's consultants.

The Architect shall not be liable for injury or damage resulting from the re-use of drawings and specifications if the Architect is not involved in the re-use Project."

1.6 NOTICE

1.6.1 Insert the following sentence at the end of the paragraph:

"Electronic mail, also known as email, is an acceptable form of electronic transmission of notices under this Agreement."

ARTICLE 2: OWNER

2.1 General

2.1.2 Delete Paragraph 2.1.2 in its entirety.

2.2 INFORMATION AND SERVICES REQUIRED OF THE OWNER

2.2.1 Delete the second sentence in this paragraph and replace with the following: "The Contractor shall have no obligation to commence the Work until the Owner issues a Purchase Order for the Project."

2.2.2 Delete the last three sentences in this paragraph.

ARTICLE 3: CONTRACTOR

3.2 REVIEW OF CONTRACT DOCUMENTS AND FIELD CONDITIONS BY CONTRACTOR

3.2.4 Delete the third sentence in Paragraph 3.2.4.

3.3 SUPERVISION AND CONSTRUCTION PROCEDURES

Add the following Paragraphs:

3.3.2.1 The Contractor shall immediately remove from the Work, whenever requested to do so by the Owner, any person who is considered by the Owner or Architect to be incompetent or disposed to be disorderly, or who for any reason is not satisfactory to the Owner, and that person shall not again be employed on the Work without the consent of the Owner or the Architect.

3.3.4 The Contractor must provide suitable storage facilities at the Site, or an alternative site as approved by the Owner, for the proper protection and safe storage of their materials. Consult the Owner and the Architect before storing any materials.

3.3.5 When any room is used as a shop, storeroom, office, etc., by the Contractor or Subcontractor(s) during the construction of the Work, the Contractor making use of these areas will be held responsible for any repairs, patching or cleaning arising from such use.

3.4 LABOR AND MATERIALS

3.4.1.1 Add a new section 3.4.1.1:

"The Contractor, at their expense shall bear the costs to accurately identify the location of all underground utilities in the area of their excavation and shall bear all cost for any repairs required, out of failure to accurately identify said utilities."

Add the Following Paragraphs:

3.4.4 Before starting the Work, each Contractor shall carefully examine all preparatory Work that has been executed to receive their Work. Check carefully, by whatever means are required, to insure that its Work and adjacent, related Work, will finish to proper contours, planes and levels. Promptly notify the General Contractor/Construction Manager of any defects or imperfections in preparatory Work which will in any way affect satisfactory completion of its Work. Absence of such notification will be construed as an acceptance of preparatory Work and later claims of defects will not be recognized.

3.4.5 Under no circumstances shall the Contractor's Work proceed prior to preparatory Work having been completely cured, dried and/or otherwise made satisfactory to receive this Work. Responsibility for timely installation of all materials rests solely with the Contractor responsible for that Work, who shall maintain coordination at all times.

3.5 WARRANTY

Add the following Paragraphs:

3.5.3 The Contractor will warrant all materials and workmanship against original defects, except injury from proper and usual wear when used for the purpose intended, for two years after Substantial Completion of the project in accordance with Section 9.8.4 of this Agreement, and will maintain all items in condition that conforms with the Contract Documents during the period of warranty.

3.5.4 Non-conforming work during the period of warranty will be corrected by the Contractor at its expense upon demand of the Owner, it being required that the Work conforms to the Contract Documents at the expiration of the warranty period.

3.5.5 In addition to the General Warranty there are other warranties required for certain items for different periods of time than the two years as above and are particularly so stated in that part of the specifications referring to same. The said warranties will commence at the same time as the General Warranty.

3.5.6 If the Contractor fails to remedy any failure, defect or damage within a reasonable time after receipt of notice, the Owner will have the right to replace, repair, or otherwise remedy the failure, defect or damage at the Contractor's expense.

3.11 DOCUMENTS AND SAMPLES AT THE SITE

Add the following Paragraphs:

3.11.1 During the course of the Work, the Contractor shall maintain a record set of drawings on which the Contractor shall mark the actual physical location of all piping, valves, equipment, conduit, outlets, access panels, controls, actuators, including all appurtenances that will be concealed once construction is complete, etc., including all invert elevations.

3.11.2 At the completion of the project, the Contractor shall obtain a set of reproducible drawings from the Architect, and neatly transfer all information outlined in 3.11.1 to provide a complete record of the as-built conditions.

3.11.3 The Contractor shall provide two (2) prints of the as-built conditions, along with the reproducible drawings themselves, to the Owner and one (1) set to the Architect. In addition, attach one complete set to each of the Operating and Maintenance Instructions/Manuals.

3.15 CLEANING UP

3.15.2 Strike sentence in its entirety and replace with the following:

"If the Contractor fails to clean up as provided in the Contract Documents, the Owner, or Construction Manager with the Owner's approval, may do so and the Owner shall withhold the amount that reflects the cost of the cleanup from any moneys owed the Contractor. If the cost of cleanup exceeds the moneys owed to the Contractor, the Owner shall be entitled to reimbursement from the Contractor for the amount exceeding what is withheld.

3.17 In the second sentence of 3.17, insert "indemnify and" between "shall" and "hold".

ARTICLE 4: ARCHITECT AND CONSTRUCTION MANAGER

4.2 Administration of the Contract

Delete the first sentence of Paragraph 4.2.11 and replace with the following:

The Architect will review and approve or take other appropriate action upon the Contractor's submittals such as Shop Drawings, Product Data and Samples for the purpose of checking for conformance with the Contract Documents.

Delete the second sentence of Paragraph 4.2.11 and replace with the following:

The Architect's action will be taken with such reasonable promptness as to cause no delay in the Work in the activities of the Owner, Contractor or separate Contractors, while allowing sufficient time in the Owner's professional judgment to permit adequate review.

Add the following to Paragraph 4.2.17:

There will be no full-time Project representative provided by the Owner or Architect on site for this Project.

Add to Paragraph 4.2.20 “and in compliance with all applicable codes, regulations and ordinances.” to the end of the sentence.

ARTICLE 5: SUBCONTRACTORS

5.2 AWARD OF SUBCONTRACTS AND OTHER CONTRACTS FOR PORTIONS OF THE WORK

Delete Paragraph 5.2.3 in its entirety and replace with the following:

5.2.3 If the Owner, Architect or Construction Manager has reasonable objection to a person or entity proposed by the Contractor, the Contractor shall propose another to whom the Owner, Architect or Construction Manager has no reasonable objection, subject to the statutory requirements of 29 Delaware Code § 6962(d)(10)b.3 and 4.

ARTICLE 6: CONSTRUCTION BY OWNER OR BY SEPARATE CONTRACTORS

6.1 OWNER’S RIGHT TO PERFORM CONSTRUCTION AND TO AWARD SEPARATE CONTRACTS

6.1.1 Delete “and waiver of subrogation” from the last sentence.

6.1.3 Delete Paragraph 6.1.3 in its entirety and replace with the following:

“When separate contracts are awarded for different portions of the Project or other construction or operations on the site, the term “Contractor” in the Contract Documents in each case shall mean the Constructor who executes each separate Owner-Contractor Agreement.”

6.2 MUTUAL RESPONSIBILITY

6.2.3 In the second sentence, strike the word “shall” and insert the word “may”.

ARTICLE 7: CHANGES IN THE WORK

(SEE ARTICLE 7: CHANGES IN WORK IN THE GENERAL REQUIREMENTS)

ARTICLE 8: TIME

8.2 PROGRESS AND COMPLETION

Add the following Paragraphs:

8.2.1.1 Refer to Specification Section SUMMARY OF WORK for Contract time requirements.

8.2.4 If the Work falls behind the Progress Schedule as submitted by the Contractor, the Contractor shall employ additional labor and/or equipment necessary to bring the Work into compliance with the Progress Schedule at no additional cost to the Owner.

8.3 DELAYS AND EXTENSION OF TIME

8.3.1 Strike “binding dispute resolution” and insert “remedies at law or in equity”.

Add the following Paragraph:

8.3.2.1 The Contractor shall update the status of the suspension, delay, or interruption of the Work with each Application for Payment. (The Contractor shall report the termination of such cause immediately upon the termination thereof.) Failure to comply with this procedure shall constitute a waiver for any claim for adjustment of time or price based upon said cause.

Delete Paragraph 8.3.3 in its entirety and replace with the following:

8.3.3 Except in the case of a suspension of the Work directed by the Owner, an extension of time under the provisions of Paragraph 8.3.1 shall be the Contractor’s sole remedy in the progress of the Work and there shall be no payment or compensation to the Contractor for any expense or damage resulting from the delay.

Add the following Paragraph:

8.3.4 By permitting the Contractor to work after the expired time for completion of the project, the Owner does not waive its rights under the Contract.

8.3.5 The parties agree that Paragraph 8.3.3 of the Supplementary General Conditions does not apply to the Construction Manager in the event of a delay caused by a party other than the Construction Manager.

ARTICLE 9: PAYMENTS AND COMPLETION

9.1 CONTRACT SUM
9.1.2 Strike Section 9.1.2 in its entirety.

9.2 SCHEDULE OF VALUES

Add the following Paragraphs:

9.2.1 The Schedule of Values shall be submitted using AIA Document G732, Continuation Sheet to G703.

9.3 APPLICATIONS FOR PAYMENT

Add the following Paragraph:

9.3.1.3 Application for Payment shall be submitted on AIA Document G732 “Application and Certificate for Payment”, supported by AIA Document G703 “Continuation Sheet”. Said Applications shall be fully executed and notarized.

Add the following Paragraphs:

9.3.4 Until Closeout Documents have been received and outstanding items completed the Owner will pay 95% (ninety-five percent) of the amount due the Contractor on account of progress payments.

9.3.5 The Contractor shall provide a current and updated Progress Schedule to the Architect with each Application for Payment. Failure to provide Schedule will be just cause for rejection of Application for Payment.

9.5 DECISIONS TO WITHHOLD CERTIFICATION

Add the following to 9.5.1:

.8 failure to provide a current Progress Schedule;
.9 a lien or attachment is filed;
.10 failure to comply with mandatory requirements for maintaining Record Documents.

9.6 PROGRESS PAYMENTS

Delete Paragraph 9.6.1 in its entirety and replace with the following:

9.6.1 After the Architect and the Construction Manager have approved and issued a Certificate for Payment, payment shall be made by the Owner within 30 days after Owner's receipt of the Certificate for Payment.

9.6.8 Strike "Provided the Owner has fulfilled its payment obligations under the Contract Documents, the" and replace with "The".

9.7 FAILURE OF PAYMENT

In first sentence, strike the first reference to "seven" and insert "thirty (30)". Also strike "binding dispute resolution" and insert "remedies at law or in equity".

9.8 SUBSTANTIAL COMPLETION

9.8.5 In the second sentence, strike "shall" and insert "may".

ARTICLE 10: PROTECTION OF PERSONS AND PROPERTY

10.1 SAFETY PRECAUTIONS AND PROGRAMS

Add the following Paragraphs:

10.1.1 Each Contractor shall develop a safety program in accordance with the Occupational Safety and Health Act of 1970. A copy of said plan shall be furnished to the Owner and Architect prior to the commencement of that Contractor's Work.

10.1.2 Each Contractor shall appoint a Safety Representative. Safety Representatives shall be someone who is on site on a full-time basis. If deemed necessary by the Owner or Architect, Contractor Safety meetings will be scheduled. The attendance of all Safety Representatives will be required. Minutes will be recorded of said meetings by the Contractor and will be distributed to all parties as well as posted in all job offices/trailers etc.

10.2 SAFETY OF PERSONS AND PROPERTY

Add the following Paragraph:

10.2.4.1 As required in the Hazardous Chemical Act of June 1984, all vendors supplying any material that may be defined as hazardous must provide Material Safety Data Sheets for those products. Any chemical product should be considered hazardous if it has a caution warning on the label relating to a potential physical or health hazard, if it is known to be present in the workplace, and if employees may be exposed under normal conditions or in foreseeable emergency situations. Material Safety Data Sheets shall be provided directly to the Owner or its designee, along with the shipping slips that include those products.

10.3 HAZARDOUS MATERIALS

Delete Paragraph 10.3.3 in its entirety.

Delete Paragraphs 10.3.6 in its entirety.

ARTICLE 11: INSURANCE AND BONDS

11.1 CONTRACTOR'S INSURANCE AND BONDS

11.1.1 Strike "Owner," at the beginning of the third sentence.

11.1.2 Add the following sentence at the end of the paragraph: "The bonds will conform to those forms approved by the Office of Management and Budget."

11.2 OWNER'S INSURANCE

Delete Paragraph 11.2 in its entirety and replace with the following:

11.2 The Owner will not provide Builder's All Risk Insurance for the Project. The Construction Manager will provide Builder's All Risk Insurance for the Project. The Contractor and all Subcontractors shall provide coverage for materials, fixtures and/or equipment being used in the construction or renovation of a building or structure should those items sustain physical loss or damage from a covered cause.

11.3 WAIVERS OF SUBROGATION

Delete Paragraph 11.3 and its subparagraphs in their entirety. Substitute the following:
The Construction Manager and Contractor waive all rights against (1) each other and any of their subcontractors, sub-subcontractors, agents, consultants and employees, each of the other; (2) the Architect and Architect's consultants; (3) other Contractors and any of their subcontractors, sub-subcontractors, agents, and employees; and (4) Separate Contractors, if any, and any of their subcontractors, sub-subcontractors, agents, and employees, for damages caused by fire, or other causes of loss, to the extent those losses are covered by property insurance required by the Agreement or other property insurance applicable to the Project, except such rights as they have to proceeds of such insurance. The policies of insurance purchased and maintained by each person or entity agreeing to waive claims pursuant to this Article shall not prohibit this waiver of subrogation. This waiver of subrogation shall be effective as to a person or entity (1) even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, (2) even though

that person or entity did not pay the insurance premium directly or indirectly, or (3) whether or not the person or entity had an insurable interest in the damaged property. For clarity, the Owner does not waive any of its subrogation rights.

11.4 LOSS OF USE, BUSINESS INTERRUPTION, AND DELAY IN COMPLETION INSURANCE

Delete Paragraph 11.4 in its entirety.

11.5 ADJUSTMENT AND SETTLEMENT OF INSURED LOSS

Delete Paragraph 11.5 in its entirety. Substitute the following:

A loss insured under the property insurance required by the Agreement shall be adjusted by the Construction Manager and made payable to the Construction Manager. The Construction Manager shall pay the Architect and Contractor their just shares of insurance proceeds received by the Construction Manager, and by appropriate agreements the Architect and Contractor shall make payments to their consultants and Subcontractors in similar manner. Prior to settlement of an insured loss, the Construction Manager shall notify the Contractor of the terms of the proposed settlement as well as the proposed allocation of the insurance proceeds. The Contractor shall have 14 days from receipt of notice to object to the proposed settlement or allocation of the proceeds. If the Contractor does not object, the Construction Manager shall settle the loss and the Contractor shall be bound by the settlement and allocation. If the Contractor timely objects to either the terms of the proposed settlement or the allocation of the proceeds, the Construction Manager may proceed to settle the insured loss, and any dispute between the Construction Manager and Contractor arising out of the settlement or allocation of the proceeds shall be resolved pursuant remedies at law and in equity. For clarity, the Owner shall be listed as an Additional Insured to protect the Owner's property interest on the Project under the Builder's Risk Insurance.

ARTICLE 12: UNCOVERING AND CORRECTION OF WORK

12.2.2 AFTER SUBSTANTIAL COMPLETION

12.2.2.1 In the first sentence, strike "within one year after the date of Substantial Completion of the Work or designated portion thereof" and replace with "within two years after the date of Substantial Completion of the Project in accordance with Section 9.8.4 of this Agreement or designated portion thereof".

12.2.2.1 In the third sentence of the paragraph, strike "one year period" and replace it with "two year period".

Add the following Paragraph:

12.2.2.1.1 At any time during the progress of the Work, or in any case where the nature of the defects will be such that it is not expedient to have corrected, the Owner, at its option, will have the right to deduct such sum, or sums, of money from the amount of the Contract as it considers justified to adjust the difference in value between the defective work and that required under contract including any damage to the structure.

12.2.2.2 Strike "one" and insert "two".

12.2.2.3 Strike "one" and insert "two".

12.2.5 In second sentence, strike “one” and insert “two”.

ARTICLE 13: MISCELLANEOUS PROVISIONS

13.1 GOVERNING LAW

13.1 Strike the second sentence in its entirety.

13.5 INTEREST

13.5 Strike 13.5 in its entirety and replace with the following:
"Payments are due 30 days after receipt of a valid Application for Payment. After that 30 day period, interest may be charged at the rate of 1% per month not to exceed 12% per annum."

Add the following Paragraph:

13.6 CONFLICTS WITH FEDERAL STATUTES OR REGULATIONS

13.6.1 If any provision, specifications or requirement of the Contract Documents conflict or is inconsistent with any statute, law or regulation of the government of the United State of America, the Contractor shall notify the Architect and Owner immediately upon discovery.

ARTICLE 14: TERMINATION OR SUSPENSION OF THE CONTRACT

14.4 TERMINATION BY THE OWNER FOR CONVENIENCE

Delete Paragraph 14.4.3 in its entirety and replace with the following:

14.4.3 In case of such termination for the Owner’s convenience, the Contractor shall be entitled to receive payment for Work executed, and cost incurred by reason of such termination along with reasonable overhead.

ARTICLE 15: CLAIMS AND DISPUTES

15.1.2 TIME LIMITS ON CLAIMS.

15.1.2 Strike “in accordance with the requirements of the binding dispute resolution method selected in the Agreement and” from the first sentence.
Strike the second sentence in its entirety.

15.1.4 CONTINUING CONTRACT PERFORMANCE

15.1.4.2 Strike in its entirety.

15.1.7 CLAIMS FOR CONSEQUENTIAL DAMAGES

Delete Paragraph 15.1.7 and its subparagraphs in their entirety.

15.2 INITIAL DECISION

15.2.1 Delete “and binding dispute resolution”

15.2.5 Delete in its entirety and replace with the following:

15.2.5 The Architect will approve or reject Claims by written decision, which shall state the reasons therefore and shall notify the parties of any change in the Contract Sum or Contract Time or both. The approval or rejection of a Claim by the Architect shall be subject to mediation and other remedies at law or in equity.

Delete Paragraph 15.2.6 and its subparagraphs in their entirety.

15.3 MEDIATION

15.3.1 Strike “binding dispute resolution” and insert “any or all remedies at law or in equity”.

15.3.2 In the first sentence, delete “administered by the American Arbitration Association in accordance with its Construction Industry Mediation Procedure in effect on the date of the Agreement,”. Also strike “binding dispute resolution” and insert “remedies at law and in equity”.

15.3.3 Strike in its entirety.

15.4 ARBITRATION

Delete Paragraph 15.4 and its subparagraphs in their entirety.

END OF SECTION

SECTION 007343 – WAGE RATE REQUIREMENTS

1. SUMMARY

A. In accordance with Delaware Code, Title 29, Chapter 69, Section 6912, all laborers and mechanics of the Contractor and all subcontractors employed to perform work directly upon the site of the work shall be paid unconditionally and not less often than once a week and without subsequent deduction or rebate on any account the full amounts accrued at the time of payment computed at wage rates not less than those determined by the Division of Industrial Affairs, Department of Labor, State of Delaware, as the prevailing rates in this area.

B. This approved scale of wages must be posted by the Contractor in a prominent and easily accessible place at the site of the work.

C. It is further stipulated that there may be withheld from the Contractor such accrued payment as may be considered necessary by the contracting officer to pay laborers and mechanics employed by the Contractor or any subcontractors on the work the difference between the rates of wages required and the rate of wages received by such laborers and mechanics and not refunded to the Contractor, subcontractor or their agents.

D. Where wage rates are published in this Manual they are issued by the State Department of Labor on the date indicated and are included for the convenience of Bidders. The Owner, the Architect, and the Construction Manager, accept no responsibility for the accuracy or applicability of any rates included herein. The actual wage rate determinations which will apply to the work will be those in effect on the first day of public advertisement for bids as determined by the State Department of Labor. It will be the responsibility of each bidder to contact the State Department of Labor and to incorporate these rates in his bid.

E. "In accordance with Delaware Code, Title 29, Section 6912, as amended July 5, 1994, contractors shall furnish sworn payroll information to the Department of Labor on a weekly basis for each contract which exceeds $15,000 for renovation work and $100,000 for new construction. The construction contract amount is based on a cumulative total of all contracts bid for a specific project. Payroll forms for submission may be obtained from the Department of Labor."

1. A Payroll Report, available from the Department of Labor is to be used to provide this information.

F. A copy of the Prevailing Wages for the project is attached hereto.

G. For this pilot project, includes a cooperative program in which students from Vocational Technical schools will work on the project in compliance with Title 19, Chapter 5 of the Delaware Code. The wage rate of $16.50 per hour has been established by the Office of Management and Budget (OMB) and the New Castle County Vocational Technical School District. This wage rate shall be recognized by the Delaware Department of Labor as “OMB Pilot Program Coop Student Rate” in lieu of a Prevailing Wage rate on the pilot project. This Student Rate is applicable to this pilot project only.

END OF SECTION

STATE OF DELAWARE
DEPARTMENT OF LABOR
DIVISION OF INDUSTRIAL AFFAIRS
4425 NORTH MARKET STREET
WILMINGTON, DELAWARE 19802

TELEPHONE (302) 761-8200

RECEIVED
APR 28 2023
EDis Co.

Via Electronic and Regular Mail

April 25, 2023

Mr. Kevin Lucas
EDiS Company
110 S. Poplar Street
Suite 400
Wilmington, DE 19801

Re: NCCVT HS Hodgson - BP-B and BP-C - New Castle County, DE

Dear Mr. Lucas:

I am responding to your request for a category determination for the BP-B and BP-C NCCVT HS Hodgson - BP-B and BP-C, which is a state funded construction project located in New Castle County, DE. The work consists of BP-B includes construction entrance, demo of existing structures in PH 1, site preparation, utility installation and building pad. BP - C and D includes the construction of the building ready for occupancy. You estimate the total cost of construction for this project to be $142,000,000.00.

Based upon the information you provided the Department of Labor has determined that this project is a Building Construction project.

Delaware's Prevailing Wage Regulations provide that the rates applicable to a project are the rates in effect on the date of publication of the specifications for that project. I have enclosed a certified copy of the March 15, 2023, prevailing wage rates for Building Construction to be included in your bid specification. However, please be advised that, in the event that a contract for a project is not executed within one hundred and twenty (120) days from the earliest date the specifications were published, the rates in effect at the time of the execution of the contract shall be the applicable rates for the project.

This determination is directed solely to the parties identified herein. It is based on the unique facts relevant to this matter. It does not constitute precedent and should not be cited as such by future parties.

Pursuant to 19 Del. Chapter 36, All contractors must obtain their Contractor Registration Certificate prior to performing construction services or maintenance work throughout Delaware. Contractors can submit an application by visiting the Delaware One Stop https://onestop.delaware.gov/Operate_Contractors.

Lastly, please see the enclosed debarment list. Entities/individuals listed shall not be permitted to bid on, be awarded or work on Delaware State funded construction projects, in the timeframe specified, as provided for under 29 Del.C.6960 or other applicable State statutes.

If you have any questions or I can provide any additional assistance, please do not hesitate to contact me at (302) 761- 8174.

Sincerely,

Francis Chudzik Administrator
Delaware Department of Labor
francis.chudzik@delaware.gov

Enclosures

STATE OF DELAWARE
DEPARTMENT OF LABOR
DIVISION OF INDUSTRIAL AFFAIRS
OFFICE OF LABOR LAW ENFORCEMENT
PHONE: (302) 761-8327

Mailing Address:
4425 North Market Street
3rd Floor
Wilmington, DE 19802

Located at:
4425 North Market Street
3rd Floor
Wilmington, DE 19802

PREVAILING WAGES FOR **BUILDING CONSTRUCTION** EFFECTIVE MARCH 15, 2023

CLASSIFICATION	NEW CASTLE	KENT	SUSSEX
ASBESTOS WORKERS	27.88	34.33	49.97
BOILERMAKERS	83.46	42.35	62.25
BRICKLAYERS	63.49	63.49	63.49
CARPENTERS	59.56	59.56	47.80
CEMENT FINISHERS	88.04	62.61	27.02
ELECTRICAL LINE WORKERS	55.44	47.54	36.25
ELECTRICIANS	79.17	79.17	79.17
ELEVATOR CONSTRUCTORS	109.83	78.64	99.36
GLAZIERS	81.60	81.60	69.08
INSULATORS	65.34	65.34	65.34
IRON WORKERS	73.31	73.31	73.31
LABORERS	53.65	53.65	53.65
MILLWRIGHTS	82.08	82.08	65.93
PAINTERS	56.66	56.66	56.66
PILEDRIVERS	85.37	47.99	38.81
PLASTERERS	36.39	36.39	26.97
PLUMBERS/PIPEFITTERS/STEAMFITTERS	75.55	77.38	68.46
POWER EQUIPMENT OPERATORS	79.29	79.29	83.48
ROOFERS-COMPOSITION	28.01	28.25	30.56
ROOFERS-SHINGLE/SLATE/TILE	22.42	26.67	20.97
SHEET METAL WORKERS	82.28	82.28	82.28
SOFT FLOOR LAYERS	58.52	58.52	58.52
SPRINKLER FITTERS	68.00	68.00	68.00
TERRAZZO/MARBLE/TILE FNRS	70.42	70.42	76.40
TERRAZZO/MARBLE/TILE STRS	78.27	78.27	84.73
TRUCK DRIVERS	53.07	33.45	26.04

CERTIFIED: 04/25/2023 BY: _____
ADMINISTRATOR, OFFICE OF LABOR LAW ENFORCEMENT

NOTE: THESE RATES ARE PROMULGATED AND ENFORCED PURSUANT TO THE PREVAILING WAGE REGULATIONS ADOPTED BY THE DEPARTMENT OF LABOR ON APRIL 3, 1992.

CLASSIFICATIONS OF WORKERS ARE DETERMINED BY THE DEPARTMENT OF LABOR. FOR ASSISTANCE IN CLASSIFYING WORKERS, OR FOR A COPY OF THE REGULATIONS OR CLASSIFICATIONS, PHONE (302) 761-8327.

NON-REGISTERED APPRENTICES MUST BE PAID THE MECHANIC'S RATE.

PROJECT: BP-B and BP-C NCCVT HS Hodgson - BP-B and BP-C, New Castle County

PREVAILING WAGE DEBARMENT LIST

The following contractors have been debarred for violations of the prevailing wage law 29Del.C. §6960 or other applicable State statutes.

Therefore, no public construction contract in this State shall be bid on, awarded to, or received by contractors and individuals on this list for a period of (3) three years from the date of the judgment or as deemed by a court of competent jurisdiction.

Contractor	Address	Date of Debarment
Mullen Brothers, Inc. and Daniel Mullen, individually	3375 Garnett Road, Boothwyn, PA 19060	Indefinite/ Civil Contempt
State Contractors Corporation, and Jose Oscar Rivera, individually	13004 Hathaway Drive Silver Spring, MD 20906	Indefinite/ 19 Del.C. 2374(f)
Green Granite and Jason Green, individually	604 Heatherbrooke Court Avondale, PA 19311	Indefinite/ Civil Contempt
Pro Image Landscaping, Inc. and Owner(s) individually	23 Commerce Street Wilmington, DE 19801 and/or 2 Cameo Road Claymont, DE 19703	Indefinite/19 Del.C. §108 & 10 Del.C. 542(c)
Liberty Mechanical, LLC and Owner(s), individually	2032 Duncan Road Wilmington, DE 19801	Indefinite/ 19 Del.C. 2374(f)
Integrated Mechanical and Fire Systems Inc. and Allison Sheldon, individually	4601 Governor Printz Boulevard Wilmington, DE 19809	Indefinite/19 Del.C. §108 & 10 Del.C. 542(c)
ACH 1, INC.	873 Salem Church Road Newark, DE 19702	Indefinite/19 Del.C.6960

Updated: July 6, 2022

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

SECTION 00 81 13

GENERAL REQUIREMENTS

TABLE OF ARTICLES

1. GENERAL
2. OWNER
3. CONTRACTOR
4. ADMINISTRATION OF THE CONTRACT
5. SUBCONTRACTORS
6. CONSTRUCTION BY OWNER OR SEPARATE CONTRACTORS
7. CHANGES IN THE WORK
8. TIME
9. PAYMENTS AND COMPLETION
10. PROTECTION OF PERSONS AND PROPERTY
11. INSURANCE AND BONDS
12. UNCOVERING AND CORRECTION OF WORK
13. MISCELLANEOUS PROVISIONS
14. TERMINATION OR SUSPENSION OF THE CONTRACT

ARTICLE 1: GENERAL

1.1 CONTRACT DOCUMENTS

1.1.1 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary and what is required by one shall be as binding as if required by all. Performance by the Contractor shall be required to an extent consistent with the Contract Documents and reasonably inferable from them as being necessary to produce the intended results.

1.1.2 Work including material purchases shall not begin until the Contractor is in receipt of a bonafide State of Delaware Purchase Order. Any work performed or material purchases prior to the issuance of the Purchase Order is done at the Contractor's own risk and cost.

1.2 EQUALITY OF EMPLOYMENT OPPORTUNITY ON PUBLIC WORKS

1.2.1 For Public Works Projects financed in whole or in part by state appropriation the Contractor agrees that during the performance of this contract:

1. The Contractor will not discriminate against any employee or applicant for employment because of race, creed, sex, color, sexual orientation, gender identity or national origin. The Contractor will take positive steps to ensure that applicants are employed and that employees are treated during employment without regard to their race, creed, sex, color, sexual orientation, gender identity or national origin. Such action shall include, but not be limited to, the following: employment, upgrading, demotion or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places available to employees and applicants for employment notices to be provided by the contracting agency setting forth this nondiscrimination clause.

2. The Contractor will, in all solicitations or advertisements for employees placed by or on behalf of the Contractor, state that all qualified applicants will receive consideration for employment without regard to race, creed, sex, color, sexual orientation, gender identity or national origin."

1.3 PILOT PROGRAM FOR DISADVANTAGED BUSINESS ENTITIES (DBE)

This is a pilot project in which goals are set to increase the participation of DBEs in capital projects. A DBE is a for-profit business in which at least 51% of the business is owned by one or more individuals who are both socially and economically disadvantaged; and whose daily operations are managed by one or more individuals who are both socially and economically disadvantaged. OMB has developed the DBE goals based on an analysis of the opportunities available on the project and qualified DBE firms available for participation. The DBE pilot has a cooperative program ("coop") requirement which will allow students in the Vo-Tech School District to work on the project.

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

ARTICLE 2: OWNER

(NO ADDITIONAL GENERAL REQUIREMENTS – SEE SUPPLEMENTARY GENERAL CONDITIONS A232-2019)

ARTICLE 3: CONTRACTOR

3.1 Schedule of Values: The successful Bidder shall within twenty (20) days after receiving notice to proceed with the work, furnish to the Owner a complete schedule of values on the various items comprising the work, including a list of all subcontractors and materialmen and their DBE status.

3.2 Subcontracts: Upon approval of Subcontractors, the Contractor shall award their Subcontracts as soon as possible after the signing of their own contract and see that all material, their own and those of their Subcontractors, are promptly ordered so that the work will not be delayed by failure of materials to arrive on time.

3.3 Before commencing any work or construction, the General Contractor is to consult with the Owner as to matters in connection with access to the site and the allocation of Ground Areas for the various features of hauling, storage, etc.

3.4 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for and have control over construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work under the Contract, unless the Contract Documents give other specific instructions.

3.5 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Contract. The Contractor shall not permit employment of unfit persons or persons not skilled in tasks assigned to them.

3.6 The Contractor warrants to the Owner that materials and equipment furnished will be new and of good quality, unless otherwise permitted, and that the work will be free from defects and in conformance with the Contract Documents. Work not conforming to these requirements, including substitutions not properly approved, may be considered defective. If required by the Owner, the Contractor shall furnish evidence as to the kind and quality of materials and equipment provided.

3.7 Unless otherwise provided, the Contractor shall pay all sales, consumer, use and other similar taxes, and shall secure and pay for required permits, fees, licenses, and inspections necessary for proper execution of the Work.

3.8 The Contractor shall comply with and give notices required by laws, ordinances, rules, regulations, and lawful orders of public authorities bearing on performance of the Work. The Contractor shall promptly notify the Owner if the Drawings and Specifications are observed to be at variance therewith.

3.9 The Contractor shall be responsible to the Owner for the acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons performing portions of the Work under contract with the Contractor.

3.10 The Contractor shall keep the premises and surrounding area free from accumulation of waste materials or rubbish caused by operations under the Contract. At completion of the Work the Contractor shall remove from and about the Project all waste materials, rubbish, the Contractor's tools, construction equipment, machinery and surplus materials. The Contractor shall be responsible for returning all damaged areas to their original conditions.

3.11 STATE LICENSE AND TAX REQUIREMENTS

3.11.1 Each Contractor and Subcontractor shall be licensed to do business in the State of Delaware and shall pay all fees and taxes due under State laws. In conformance with Section 2503, Chapter 25, Title 30, Delaware Code, "the Contractor shall furnish the Delaware Department of Finance within ten (10) days after entering into any contract with a contractor or subcontractor not a resident of this State, a statement of total value of such contract or contracts together with the names and addresses of the contracting parties."

3.12 The Contractor shall comply with all requirements set forth in Section 6962, Chapter 69, Title 29 of the Delaware Code.

3.13 During the contract Work, the Contractor and each Subcontractor, shall implement an Employee Drug Testing Program in accordance with OMB Regulation 4104 - "Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on "Large Public Works Projects". "Large Public Works" is based upon the current threshold required for bidding Public Works as set by the Purchasing and Contracting Advisory Council.

ARTICLE 4: ADMINISTRATION OF THE CONTRACT

4.1 CONTRACT SURETY

4.1.1 PERFORMANCE BOND AND LABOR AND MATERIAL PAYMENT BOND

4.1.2 All bonds will be required as follows unless specifically waived elsewhere in the Bidding Documents.

4.1.3 Contents of Performance Bonds – The bond shall be in the form approved by the Office of Management and Budget. The bond shall be conditioned upon the faithful compliance and performance by the successful bidder of each and every term and condition of the contract and the proposal, plans, specifications, and bid documents thereof. Each term and condition shall be met at the time and in the manner prescribed by the Contract, Bid documents and the specifications, including the payment in full to every person furnishing materiel or performing labor in the performance of the Contract, of all sums of money due the person for such labor and materiel. (The bond shall also contain the successful bidder's guarantee to indemnify and save harmless the State and the agency from all costs, damages and expenses growing out of or by reason of the Contract in accordance with the Contract.)

4.1.4 Invoking a Performance Bond – The agency may, when it considers that the interest of the State so requires, cause judgement to be confessed upon the bond.

4.1.5 Within twenty (20) days after the date of notice of award of contract, the Bidder to whom the award is made shall furnish a Performance Bond and Labor and Material Payment Bond, each equal to the full amount of the Contract price to guarantee the faithful performance of all terms, covenants and conditions of the same. The bonds are to be issued by an acceptable Bonding Company licensed to do business in the State of Delaware and shall be issued in duplicate.

4.1.6 Performance and Payment Bonds shall be maintained in full force (warranty bond) for a period of two (2) years after the date of the Certificate for Final Payment. The Performance Bond shall guarantee the satisfactory completion of the Project and that the Contractor will make good any faults or defects in his work which may develop during the period of said guarantees as a result of improper or defective workmanship, material or apparatus, whether furnished by themselves or their Sub-Contractors. The Payment Bond shall guarantee that the Contractor shall pay in full all persons, firms or corporations who furnish labor or material or both labor and material for, or on account of, the work included herein. The bonds shall be paid for by this Contractor. The Owner shall have the right to demand that the proof parties signing the bonds are duly authorized to do so.

4.2 FAILURE TO COMPLY WITH CONTRACT

4.2.1 If any firm entering into a contract with the State, or Agency that neglects or refuses to perform or fails to comply with the terms thereof, the Agency which signed the Contract may terminate the Contract and proceed to award a new contract in accordance with this Chapter 69, Title 29 of the Delaware Code or may require the Surety on the Performance Bond to complete the Contract in accordance with the terms of the Performance Bond. Nothing herein shall preclude the Agency from pursing additional remedies as otherwise provided by law.

4.3 CONTRACT INSURANCE AND CONTRACT LIABILITY

4.3.1 In addition to the bond requirements stated in the Bid Documents, each successful Bidder shall purchase adequate insurance for the performance of the Contract and, by submission of a Bid, agrees to indemnify and save harmless and to defend all legal or equitable actions brought against the State, any Agency, officer and/or employee of the State, for and from all claims of liability which is or may be the result of the successful Bidder’s actions during the performance of the Contract.

4.3.2 The purchase or nonpurchase of such insurance or the involvement of the successful Bidder in any legal or equitable defense of any action brought against the successful Bidder based upon work performed pursuant to the Contract will not waive any defense which the State, its agencies and their respective officers, employees and agents might otherwise have against such claims, specifically including the defense of sovereign immunity, where applicable, and by the terms of this section, the State and all agencies, officers and employees thereof shall not be financially responsible for the consequences of work performed, pursuant to said contract.

4.4 RIGHT TO AUDIT RECORDS

4.4.1 The Owner shall have the right to audit the books and records of a Contractor or any Subcontractor under any Contract or Subcontract to the extent that the books and records relate to the performance of the Contract or Subcontract.

4.4.2 Said books and records shall be maintained by the Contractor for a period of seven (7) years from the date of final payment under the Prime Contract and by the Subcontractor for a period of seven (7) years from the date of final payment under the Subcontract.

ARTICLE 5: SUBCONTRACTORS

5.0 PILOT PROGRAM REQUIREMENTS
The goal set for this pilot program is for 7% of the contract value shall be provided by DBEs. To achieve that goal, the Contractor shall use best efforts to hire subcontractors or purchase material from DBEs to reflect at least 7% of the contract value.

5.1 SUBCONTRACTING REQUIREMENTS

5.1.1 All contracts for the construction, reconstruction, alteration or repair of any public building (not a road, street or highway) shall be subject to the following provisions:

1. A contract shall be awarded only to a Bidder whose Bid is accompanied by a statement containing, for each Subcontractor category, the name and address (city or town and State only – street number and P.O. Box addresses not required) of the subcontractor whose services the Bidder intends to use in performing the Work and providing the material for such Subcontractor category.

2. A Bid will not be accepted nor will an award of any Contract be made to any Bidder which, as the Prime Contractor, has listed itself as the Subcontractor for any Subcontractor unless:

   A. It has been established to the satisfaction of the awarding Agency that the Bidder has customarily performed the specialty work of such Subcontractor category by artisans regularly employed by the Bidder's firm;

   B. That the Bidder is duly licensed by the State to engage in such specialty work, if the State requires licenses; and

   C. That the Bidder is recognized in the industry as a bona fide Subcontractor or Contractor in such specialty work and Subcontractor category.

5.1.2 The decision of the awarding Agency as to whether a Bidder who list itself as the Subcontractor for a Subcontractor category shall be final and binding upon all Bidders, and no action of any nature shall lie against any awarding agency or its employees or officers because of its decision in this regard.

5.1.3 After such a Contract has been awarded, the successful Bidder shall not substitute another Subcontractor for any Subcontractor whose name was set forth in the statement which accompanied the Bid without the written consent of the awarding Agency.

5.1.4 No Agency shall consent to any substitution of Subcontractors unless the Agency is satisfied that the Subcontractor whose name is on the Bidders accompanying statement:

A. Is unqualified to perform the work required;

B. Has failed to execute a timely reasonable Subcontract;

C. Has defaulted in the performance on the portion of the work covered by the Subcontract; or

D. Is no longer engaged in such business.

5.1.5 Should a Bidder be awarded a contract, such successful Bidder shall provide to the agency the taxpayer identification license numbers of such subcontractors. Such numbers shall be provided on the later of the date on which such subcontractor is required to be identified or the time the contract is executed. The successful Bidder shall provide to the agency to which it is contracting, within 30 days of entering into such public works contract, copies of all Delaware Business licenses of subcontractors and/or independent contractors that will perform work for such public works contract. However, if a subcontractor or independent contractor is hired or contracted more than 20 days after the Bidder entered the public works contract the Delaware Business license of such subcontractor or independent contractor shall be provided to the agency within 10 days of being contracted or hired.

5.1.6 The Contractor may employ additional Subcontractors on the jobsite only after submitting a copy of the Subcontractor's Employee Drug Testing Program to the Owner for approval. A Contractor or Subcontractor shall not commence work until the Owner has concluded its review and determined that the submitted Employee Drug Testing Program complies with OMB Regulation 4104.

5.2 PENALTY FOR SUBSTITUTION OF SUBCONTRACTORS

5.2.1 Should the Contractor fail to utilize any or all of the Subcontractors in the Contractor's Bid statement in the performance of the Work on the public bidding, the Contractor shall be penalized in the amount of (project specific amount*). The Agency may determine to deduct payments of the penalty from the Contractor or have the amount paid directly to the Agency. Any penalty amount assessed against the Contractor may be remitted or refunded, in whole or in part, by the Agency awarding the Contract, only if it is established to the satisfaction of the Agency that the Subcontractor in question has defaulted or is no longer engaged in such business. No claim for the remission or refund of any penalty shall be granted unless an application is filed within one year after the liability of the successful Bidder accrues. All penalty amounts assessed and not refunded or remitted to the contractor shall be reverted to the State.

For the purpose of this pilot project, any substitution of a listed subcontractor whether requested in compliance with Title 29. Chapter 69, Section 6962(d)(10)b.3 of the Delaware Code or in violation of that statue will not change the DBE requirement. It remains at 7% of the contract value.

*one (1) percent of contract amount not to exceed $10,000

5.3 ASBESTOS ABATEMENT

5.3.1 The selection of any Contractor to perform asbestos abatement for State-funded projects shall be approved by the Office of Management and Budget, Division of Facilities Management pursuant to Chapter 78 of Title 16.

5.4 STANDARDS OF CONSTRUCTION FOR THE PROTECTION OF THE PHYSICALLY HANDICAPPED

5.4.1 All Contracts shall conform with the standard established by the Delaware Architectural Accessibility Board unless otherwise exempted by the Board.

5.5 CONTRACT PERFORMANCE

5.5.1 Any firm entering into a Public Works Contract that neglects or refuses to perform or fails to comply with its terms, the Agency may terminate the Contract and proceed to award a new Contract or may require the Surety on the Performance Bond to complete the Contract in accordance with the terms of the Performance Bond.

ARTICLE 6: CONSTRUCTION BY OWNER OR SEPARATE CONTRACTORS

6.1 The Owner reserves the right to simultaneously perform other construction or operations related to the Project with the Owner's own forces, and to award separate contracts in connection with other portions of the Project or other Projects at the same site.

6.2 The Contractor shall afford the Owner and other Contractors reasonable opportunity for access and storage of materials and equipment, and for the performance of their activities, and shall connect and coordinate their activities with other forces as required by the Contract Documents.

ARTICLE 7: CHANGES IN THE WORK

7.1 The Owner, without invalidating the Contract, may order changes in the Work consisting of Additions, Deletions, Modifications or Substitutions, with the Contract Sum and Contract completion date being adjusted accordingly. Such changes in the Work shall be authorized by written Change Order signed by the Professional, as the duly authorized agent, the Contractor and the Owner.

7.2 The Contract Sum and Contract Completion Date shall be adjusted only by a fully executed Change Order.

7.3 The additional cost, or credit to the Owner resulting from a change in the Work shall be by mutual agreement of the Owner, Contractor and the Architect. In all cases, this cost or credit shall be based on the ‘DPE’ wages required and the “invoice price” of the materials/equipment needed.

7.3.1 "DPE" shall be defined to mean "direct personnel expense". Direct payroll expense includes prevailing wage rates plus a maximum multiplier of 1.35 times DPE. For example, if the prevailing wage rate is $50/hour, the DPE would be $67.50/hour (50 x 1.35).

7.3.2 "Invoice price" of materials/equipment shall be defined to mean the actual cost of materials and/or equipment that is paid by the Contractor, (or subcontractor), to a material distributor, direct factory vendor, store, material provider, or equipment leasing entity. Rates for equipment that is leased and/or owned by the Contractor or subcontractor(s) shall not exceed those listed in the latest version of the "Means Building Construction Cost Data" publication.

7.3.3 In addition to the above, the General Contractor is allowed a fifteen percent (15%) markup for overhead and profit for additional work performed by the General Contractor's own forces. For additional subcontractor work, the Subcontractor is allowed a fifteen (15) percent overhead and profit on change order work above and beyond the direct costs stated previously. To this amount, the General Contractor will be allowed a mark-up not exceeding seven and one half percent (7.5%) on the subcontractors work. These mark-ups shall include all costs including, but not limited to: overhead, profit, bonds, insurance, supervision, etc. No markup is permitted on the work of the subcontractors subcontractor. No additional costs shall be allowed for changes related to the Contractor's onsite superintendent/staff, or project manager, unless a change in the work changes the project duration and is identified by the CPM schedule. There will be no other costs associated with the change order.

ARTICLE 8: TIME

8.1 Time limits, if any, are as stated in the Project Manual. By executing the Agreement, the Contractor confirms that the stipulated limits are reasonable, and that the Work will be completed within the anticipated time frame.

8.2 If progress of the Work is delayed at any time by changes ordered by the Owner, by labor disputes, fire, unusual delay in deliveries, abnormal adverse weather conditions, unavoidable casualties or other causes beyond the Contractor's control, the Contract Time shall be extended for such reasonable time as the Owner may determine.

8.3 Any extension of time beyond the date fixed for completion of the construction and acceptance of any part of the Work called for by the Contract, or the occupancy of the building by the Owner, in whole or in part, previous to the completion shall not be deemed a waiver by the Owner of his right to annul or terminate the Contract for abandonment or delay in the matter provided for, nor relieve the Contractor of full responsibility

8.4 SUSPENSION AND DEBARMENT

8.4.1 Per Section 6962(d)(14), Title 29, Delaware Code, "Any Contractor who fails to perform a public works contract or complete a public works project within the time schedule established by the Agency in the Invitation To Bid, may be subject to Suspension or Debarment for one or more of the following reasons: a) failure to supply the adequate labor supply ratio for the project; b) inadequate financial resources; or, c) poor performance on the Project."

8.4.2 "Upon such failure for any of the above stated reasons, the Agency that contracted for the public works project may petition the Director of the Office of Management and Budget for Suspension or Debarment of the Contractor. The Agency shall send a copy of the petition to the Contractor within three (3) working days of filing with the Director. If the Director concludes that the petition has merit, the Director shall schedule and hold a hearing to determine whether to suspend the Contractor, debar the Contractor or deny the petition. The Agency shall have the burden of proving, by a preponderance of the evidence, that the Contractor failed to perform or complete the public works project within the time schedule established by the Agency and failed to do so for one or more of the following reasons: a) failure to supply the adequate labor supply ratio for the project; b) inadequate financial resources; or c) poor performance on the project. Upon a finding in favor of the Agency, the Director may suspend a Contractor from Bidding on any project funded, in whole or in part, with public funds for up to 1 year for a first offense, up to 3 years for a second offense and permanently debar the Contractor for a third offense. The Director shall issue a written decision and shall send a copy to the Contractor and the Agency. Such decision may be appealed to the Superior Court within thirty (30) days for a review on the record."

8.5 RETAINAGE

8.5.1 Per Section 6962(d)(5) a.3, Title 29, Delaware Code: The Agency may at the beginning of each public works project establish a time schedule for the completion of the project. If the project is delayed beyond the completion date due to the Contractor's failure to meet their responsibilities, the Agency may forfeit, at its discretion, all or part of the Contractor's retainage.

8.5.2 This forfeiture of retainage also applies to the timely completion of the punchlist. A punchlist will only be prepared upon the mutual agreement of the Owner, Architect and Contractor. Once the punchlist is prepared, all three parties will by mutual agreement, establish a schedule for its completion. Should completion of the punchlist be delayed beyond the established date due to the Contractor's failure to meet their responsibilities, the Agency may hold permanently, at its discretion, all or part of the Contractor's retainage.

ARTICLE 9: PAYMENTS AND COMPLETION

9.1 APPLICATION FOR PAYMENT

9.1.1 Applications for payment shall be made upon AIA Document G702. There will be a five percent (5%) retainage on all Contractor's monthly invoices until completion of the project. This retainage may become payable upon receipt of all required closeout documentation, provided all other requirements of the Contract Documents have been met.

9.1.2 A date will be fixed for the taking of the monthly account of work done. Upon receipt of Contractor's itemized application for payment, such application will be audited, modified, if found necessary, and approved for the amount. Statement shall be submitted to the Owner.

9.1.3 Section 6516, Title 29 of the Delaware Code annualized interest is not to exceed 12% per annum beginning thirty (30) days after the "presentment" (as opposed to the date) of the invoice.

9.2 PARTIAL PAYMENTS

9.2.1 Any public works Contract executed by any Agency may provide for partial payments at the option of the Owner with respect to materials placed along or upon the sites or stored at secured locations, which are suitable for use in the performance of the contract.

9.2.2 When approved by the agency, partial payment may include the values of tested and acceptable materials of a nonperishable or noncontaminative nature which have been produced or furnished for incorporation as a permanent part of the work yet to be completed, provided acceptable provisions have been made for storage.

9.2.2.1 Any allowance made for materials on hand will not exceed the delivered cost of the materials as verified by invoices furnished by the Contractor, nor will it exceed the contract bid price for the material complete in place.

9.2.3 If requested by the Agency, receipted bills from all Contractors, Subcontractors, and material, men, etc., for the previous payment must accompany each application for payment. Following such a request, no payment will be made until these receipted bills have been received by the Owner.

9.3 SUBSTANTIAL COMPLETION

9.3.1 When the building has been made suitable for occupancy, but still requires small items of miscellaneous work, the Owner will determine the date when the project has been substantially completed.

9.3.2 If, after the Work has been substantially completed, full completion thereof is materially delayed through no fault of the Contractor, and without terminating the Contract, the Owner may make payment of the balance due for the portion of the Work fully completed and accepted. Such payment shall be made under the terms and conditions governing final payment that it shall not constitute a waiver of claims.

9.3.3 On projects where commissioning is included, the commissioning work as defined in the specifications must be complete prior to the issuance of substantial completion.

9.4 FINAL PAYMENT

9.4.1 Final payment, including the five percent (5%) retainage if determined appropriate, shall be made within thirty (30) days after the Work is fully completed and the Contract fully performed and provided that the Contractor has submitted the following closeout documentation (in addition to any other documentation required elsewhere in the Contract Documents):

9.4.1.1 Evidence satisfactory to the Owner that all payrolls, material bills, and other indebtedness connected with the work have been paid,

9.4.1.2 An acceptable RELEASE OF LIENS,

9.4.1.3 Copies of all applicable warranties,

9.4.1.4 As-built drawings,

9.4.1.5 Operations and Maintenance Manuals,

9.4.1.6 Instruction Manuals,

9.4.1.7 Consent of Surety to final payment.

9.4.1.8 The Owner reserves the right to retain payments, or parts thereof, for its protection until the foregoing conditions have been complied with, defective work corrected and all unsatisfactory conditions remedied.

ARTICLE 10: PROTECTION OF PERSONS AND PROPERTY

10.1 The Contractor shall be responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the performance of the Contract. The Contractor shall take all reasonable precautions to prevent damage, injury or loss to: workers, persons nearby who may be affected, the Work, materials and equipment to be incorporated, and existing property at the site or adjacent thereto. The Contractor shall give notices and comply with applicable laws ordinances, rules regulations, and lawful orders of public authorities bearing on the safety of persons and property and their protection from injury, damage, or loss. The Contractor shall promptly remedy damage and loss to property at the site caused in whole or in part by the Contractor, a Subcontractor, or anyone directly or indirectly employed by any of them, or by anyone for whose acts they may be liable.

10.2 The Contractor shall notify the Owner in the event any existing hazardous material such as lead, PCBs, asbestos, etc. is encountered on the project. The Owner will arrange with a qualified specialist for the identification, testing, removal, handling and protection against exposure or environmental pollution, to comply with applicable regulation laws and ordinances. The Contractor and Architect will not be required to participate in or to perform this operation. Upon completion of this work, the Owner will notify the Contractor and Architect in writing the area has been cleared and approved by the authorities in order for the work to proceed. The Contractor shall attach documentation from the authorities of said approval.

10.3 As required in the Hazardous Chemical Information Act of June 1984, all vendors supplying any materials that may be defined as hazardous, must provide Material Safety Data Sheets for those products. Any chemical product should be considered hazardous if it has a warning caution on the label relating to a potential physical or health hazard, if it is known to be present in the workplace, and if employees may be exposed under normal conditions or in any foreseeable emergency situation. Material Safety Data Sheets must be provided directly to the Owner along with the shipping slips that include those products.

10.4 The Contractor shall certify to the Owner that materials incorporated into the Work are free of all asbestos. This certification may be in the form of Material Safety Data Sheet (MSDS) provided by the product manufacturer for the materials used in construction, as specified or as provided by the Contractor.

ARTICLE 11: INSURANCE AND BONDS

11.1 The Contractor shall carry all insurance required by law, such as Unemployment Insurance, etc. The Contractor shall carry such insurance coverage as they desire on their own property such as a field office, storage sheds or other structures erected upon the project site that belong to them and for their own use. The Subcontractors involved with this project shall carry whatever insurance protection they consider necessary to cover the loss of any of their personal property, etc.

11.2 Upon being awarded the Contract, the Contractor shall obtain a minimum of two (2) copies of all required insurance certificates called for herein, and submit one (1) copy of each certificate, to the Owner, within 20 days of contract award.

11.3 Bodily Injury Liability and Property Damage Liability Insurance shall, in addition to the coverage included herein, include coverage for injury to or destruction of any property arising out of the collapse of or structural injury to any building or structure due to demolition work and evidence of these coverages shall be filed with and approved by the Owner.

11.4 The Contractor's Property Damage Liability Insurance shall, in addition to the coverage noted herein, include coverage on all real and personal property in their care, custody and control damaged in any way by the Contractor or their Subcontractors during the entire construction period on this project.

11.5 Builders Risk (including Standard Extended Coverage Insurance) on the existing building during the entire construction period, may be provided by the Contractor under this contract. The Owner shall insure the existing building and all of its contents and all this new alteration work under this contract during entire construction period for the full insurable value of the entire work at the site. Note, however, that the Contractor and their Subcontractors shall be responsible for insuring building materials (installed and stored) and their tools and equipment whenever in use on the project, against fire damage, theft, vandalism, etc.

11.6 Certificates of the insurance company or companies stating the amount and type of coverage, terms of policies, etc., shall be furnished to the Owner, within 20 days of contract award.

11.7 The Contractor shall, at their own expense, (in addition to the above) carry the following forms of insurance:

11.7.1 Contractor's Contractual Liability Insurance

Minimum coverage to be:

Bodily Injury		
	$1,000,000	for each occurrence
	$3,000,000	aggregate
Property Damage	$1,000,000	for each occurrence
	$3,000,000	aggregate

11.7.2 Contractor's Protective Liability Insurance

Minimum coverage to be:

Bodily Injury		
	$1,000,000	for each occurrence
	$3,000,000	aggregate
Property Damage	$1,000,000	for each occurrence
	$3,000,000	aggregate

11.7.3 Automobile Liability Insurance

Minimum coverage to be:

Bodily Injury	$1,000,000	for each person
	$1,000,000	for each occurrence
Property Damage	$500,000	per accident

11.7.4 Prime Contractor's and Subcontractors' policies shall include contingent and contractual liability coverage in the same minimum amounts as 11.7.1 above.

11.7.5 Workmen's Compensation (including Employer's Liability):

11.7.5.1 Minimum Limit on employer's liability to be as required by law.

11.7.5.2 Minimum Limit for all employees working at one site.

11.7.6 Certificates of Insurance must be filed with the Owner guaranteeing fifteen (15) days prior notice of cancellation, non-renewal, or any change in coverages and limits of liability shown as included on certificates.

11.7.7 Social Security Liability

11.7.7.1 With respect to all persons at any time employed by or on the payroll of the Contractor or performing any work for or on their behalf, or in connection with or arising out of the Contractor's business, the Contractor shall accept full and exclusive liability for the payment of any and all contributions or taxes or unemployment insurance, or old age retirement benefits, pensions or annuities now or hereafter imposed by the Government of the United States and the State or political subdivision thereof, whether the same be measured by wages, salaries or other remuneration paid to such persons or otherwise.

11.7.7.2 Upon request, the Contractor shall furnish Owner such information on payrolls or employment records as may be necessary to enable it to fully comply with the law imposing the aforesaid contributions or taxes.

11.7.7.3 If the Owner is required by law to and does pay any and/or all of the aforesaid contributions or taxes, the Contractor shall forthwith reimburse the Owner for the entire amount so paid by the Owner.

ARTICLE 12: UNCOVERING AND CORRECTION OF WORK

12.1 The Contractor shall promptly correct Work rejected by the Owner or failing to conform to the requirements of the Contract Documents, whether observed before or after Substantial Completion and whether or not fabricated, installed or completed, and shall correct any Work found to be not in accordance with the requirements of the Contract Documents within a period of two years from the date of Substantial Completion, or by terms of an applicable special warranty required by the Contract Documents. The provisions of this Article apply to work done by Subcontractors as well as to Work done by direct employees of the Contractor.

12.2 At any time during the progress of the work, or in any case where the nature of the defects shall be such that it is not expedient to have them corrected, the Owner, at their option, shall have the right to deduct such sum, or sums, of money from the amount of the contract as they consider justified to adjust the difference in value between the defective work and that required under contract including any damage to the structure.

ARTICLE 13: MISCELLANEOUS PROVISIONS

13.1 CUTTING AND PATCHING

13.1.1 The Contractor shall be responsible for all cutting and patching. The Contractor shall coordinate the work of the various trades involved.

13.2 DIMENSIONS

13.2.1 All dimensions shown shall be verified by the Contractor by actual measurements at the project site. Any discrepancies between the drawings and specifications and the existing conditions shall be referred to the Owner for adjustment before any work affected thereby has been performed.

13.3 LABORATORY TESTS

13.3.1 Any specified laboratory tests of material and finished articles to be incorporated in the work shall be made by bureaus, laboratories or agencies approved by the Owner and reports of such tests shall be submitted to the Owner. The cost of the testing shall be paid for by the Contractor.

13.3.2 The Contractor shall furnish all sample materials required for these tests and shall deliver same without charge to the testing laboratory or other designated agency when and where directed by the Owner.

13.4 ARCHAEOLOGICAL EVIDENCE

13.4.1 Whenever, in the course of construction, any archaeological evidence is encountered on the surface or below the surface of the ground, the Contractor shall notify the authorities of the State Historic Preservation Office and suspend work in the immediate area for a reasonable time to permit those authorities, or persons designated by them, to examine the area and ensure the proper removal of the archaeological evidence for suitable preservation by the Division of Historical and Cultural Affairs.

13.5 GLASS REPLACEMENT AND CLEANING

13.5.1 The General Contractor shall replace without expense to the Owner all glass broken during the construction of the project. If job conditions warrant, at completion of the job the General Contractor shall have all glass cleaned and polished.

13.6 WARRANTY

13.6.1 For a period of two (2) years from the date of substantial completion, as evidenced by the date of final acceptance of the work, the contractor warrants that work performed under this contract conforms to the contract requirements and is free of any defect of equipment, material or workmanship performed by the contractor or any of his subcontractors or suppliers. However, manufacturer's warranties and guarantees, if for a period longer than two (2) years, shall take precedence over the above warranties. The contractor shall remedy, at his own expense, any such failure to conform or any such defect. The protection of this warranty shall be included in the Contractor's Performance Bond.

ARTICLE 14: TERMINATION OR SUSPENSION OF THE CONTRACT

14.1 If the Contractor defaults or persistently fails or neglects to carry out the Work in accordance with the Contract Documents or fails to perform a provision of the Contract, the Owner, after seven days written notice to the Contractor, may make good such deficiencies and may deduct the cost thereof from the payment then or thereafter due the Contractor. Alternatively, at the Owner's option, and the Owner may terminate the Contract and take possession of the site and of all materials, equipment, tools, and machinery thereon owned by the Contractor and may finish the Work by whatever method the Owner may deem expedient. If the costs of finishing the Work exceed any unpaid compensation due the Contractor, the Contractor shall pay the difference to the Owner.

14.2 “If the continuation of this Agreement is contingent upon the appropriation of adequate state, or federal funds, this Agreement may be terminated on the date beginning on the first fiscal year for which funds are not appropriated or at the exhaustion of the appropriation. The Owner may terminate this Agreement by providing written notice to the parties of such non-appropriation. All payment obligations of the Owner will cease upon the date of termination. Notwithstanding the foregoing, the Owner agrees that it will use its best efforts to obtain approval of necessary funds to continue the Agreement by taking appropriate action to request adequate funds to continue the Agreement.”

END OF SECTION

QUARTERLY DBE REPORT

DBE Name	DBE Address	DBE Phone Number	DBE email address	DelDOT or OSD Registration number	DBE Percentage of Contract Value	Description of Work	Status of DBE's work: complete or in progress

Total DBEs on project: _____

SECTION 008114 – DRUG TESTING PROGRAM AND FORMS

1. SUMMARY

A. Pursuant to 4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors who work on Large Public Works Contracts funded all or in part with public funds submit with their bid an Affidavit of Employee Drug Testing Program. A copy of the current Regulation is attached hereto.

B. Each Contractor shall provide two (2) business days prior to contract execution, copies of the Employee Drug Testing Program for the Contractor and all Subcontractors.

C. Initial Drug Testing - Employees commencing work on a Jobsite must be tested within the past 180 days from the date of commencing work, with the exception that an Employee who has passed a random or scheduled drug test within that time frame, or an Employee who passed a pre-employment drug test administered pursuant to a Contractor's or Subcontractor's Program and is subject to testing as part of a Contractor's or Subcontractor's ongoing Program or as part of a Consortium shall be permitted to work at the Jobsite without further testing; however, the Employee is still subject to random testing.

D. A Contractor or Subcontractor's Program shall provide that no less than 5% of a Contractor's or Subcontractor's employees shall be randomly selected each month for drug testing and no less than 2.5% of a Contractor or Subcontractor's employees be randomly selected for alcohol testing. Test results must be kept by a Contractor or Subcontractor for a minimum of 1 year subsequent to the date of close out of the Public Works project. See the form attached hereto.

E. The Contractor will notify the Owner in writing of any positive results of random drug testing. See the form attached hereto. The results must be reported to the Owner within 24 hours of receipt of the test results.

EMPLOYEE DRUG TESTING REPORT FORM
Period Ending:_____

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors who work on Large Public Works Contracts funded all or in part with public funds maintain testing data that includes but is not limited to the data elements below.

Project Number: _____
Project Name: _____
Contractor/Subcontractor Name: _____
Contractor/Subcontractor Address: _____

_____

_____

Number of employees who worked on the jobsite during the report period:_____

Number of employees subject to random testing during the report period:_____

Number of Negative Results_____Number of Positive Results _____

Action taken on employee(s) in response to a failed or positive random test:

_____

_____

_____

Date: _____

Authorized Representative of Contractor/Subcontractor: _____
(typed or printed)

Authorized Representative of Contractor/Subcontractor: _____
(signature)

This form is not required to be submitted to the Owner. Included as a reference to show information required to be maintained by the Contractor. The Owner shall have the right to periodically audit all Contractor and Subcontractor test results at the Contractor's or Subcontractor's offices (or by other means to make the data available for inspection by the Owner).

EMPLOYEE DRUG TESTING
REPORT OF POSITIVE RESULTS

4104 Regulations for the Drug Testing of Contractor and Subcontractor Employees Working on Large Public Works Projects requires that Contractors and Subcontractors who work on Large Public Works Contracts funded all or in part with public funds to notify the Owner in writing of a positive random drug test.

Project Number: _____
Project Name: _____
Contractor/Subcontractor Name: _____
Contractor/Subcontractor Address: _____

_____

_____

Name of employee with positive test result:_____

Last 4 digits of employee SSN:_____

Date test results received:_____

Action taken on employee in response to a positive test result:

_____

_____

_____

Authorized Representative of Contractor/Subcontractor: _____
(typed or printed)

Authorized Representative of Contractor/Subcontractor: _____
(signature)

Date: _____

This form shall be sent by mail to the Owner within 24 hours of receipt of test results.

Enclose this test results form in a sealed envelope with the notation "Drug Testing Form – DO NOT OPEN" on the face thereof and place in a separate mailing envelope.

END OF SECTION

SECTION 008115 – AFFIDAVIT OF CRAFT TRAINING

1. AFFIDAVIT OF CRAFT TRAINING

1.1 Form Affidavit of Craft Training Compliance (008115 attached).

(PROJECT NAME),
(PROJECT LOCATION)
(PROJECT OR CONTRACT NUMBER)

AFFIDAVIT OF CRAFT TRAINING COMPLIANCE

We, the contractor, hereby certify that we and all applicable subcontractors will abide by the contractor and subcontractor craft training requirements outlined below for the duration of the contract. Craft training must be provided by a contractor and/or subcontractor for each craft on a project for which there are Delaware Department of Labor approved and registered training programs or, if the contractor and/or subcontractor meets the requirements under Title 29, Chapter 69, Section 6960A.(b)(1)c.1.-3., payment may be made in accordance with Title 29, Chapter 69, Section 6960A.(b)(1)d. A list of crafts for which there are approved and registered training programs is maintained by the Delaware Department of Labor and can be found at: https://laborfiles.delaware.gov/main/det/apprenticeship/DE%20Craft%20Training%20Occupation%20List%20Effective%20March%201%202022.pdf. If you have questions regarding craft training programs, please submit all questions in writing to the Delaware Department of Labor at: apprenticeship@delaware.gov. ***This Affidavit of Craft Training Compliance must be submitted prior to contract execution***.

In accordance with Title 29, Chapter 69, Section 6960A.(a)(1), a contract relating to a public works project under § 6962 of Title 29 must include a craft training program for each craft in the project if at the time the contractor executes a public works contract, all of the following apply:

a. A project meets the prevailing wage requirement under Section 6960 of Title 29.
b. The contractor employs 10 or more total employees.
c. The project is not a federal highway project, except for the project under Section 6962(c)(11) of Title 29.
d. There is an apprenticeship program for a craft in the project on the list of crafts under Section 204(b)(2) of Title 19.

Pursuant to Title 29, Chapter 69, Section 6960A.(a)(2), ***a contractor must commit that all subcontractors provide craft training*** if paragraph (a)(1) of this section applies to the subcontractor. Failure to provide required craft training or payment on the project may subject the successful contractor and/or subcontractor(s) to penalties as outlined in Title 29, Chapter 69, Section 6960A.(d)(1)-(3).

Craft(s): _____

Contractor Name: _____

Contractor Address: _____

_____

_____

Contractor Program Registration Number(s) _____
On this line also indicate whether DE, Other State (identify) or US Registration Number

Or

☐ **A payment has been made in the amount established under Section 204(b)(2)b.2. of Title 19, for the craft into the Delaware Department of Labor's Apprenticeship and Training Fund.**

Or

☐ **Craft Training requirements are not applicable because:**

_____

Authorized Representative (typed or printed): _____

Authorized Representative (signature): _____

Title: _____

State of Delaware)
) ss:
County of _____)

Before me, a notary public, in and for said county and state, personally appeared, _____, who acknowledged to me that she/he did execute the foregoing instrument on behalf of _____.

IN TESTIMONY WHEREOF, I have subscribed my name and affixed my official seal this ____ day of _____ 20___.

_____
Notary Public
Commission Expires _____

THIS PAGE MUST BE SIGNED AND NOTARIZED TO BE CONSIDERED.

SECTION 011100 - SUMMARY OF WORK

1. RELATED DOCUMENTS

   A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 1 Sections, apply to work of this Section.

2. CONTRACTS

   A. The work will be performed under separate prime contracts managed by the Construction Manager.

3. ALTERATIONS & COORDINATION

   A. Contractor shall be responsible to coordinate their work with the work of others, including, but not limited to, the preparation of general coordination drawings, diagrams and schedules, and control of site utilization, from the beginning of activity, through project close-out and warranty periods.

4. KNOWLEDGE OF CONTRACT REQUIREMENTS

   A. The Contractor and his Subcontractors, Sub-subcontractors and material men shall consult in detail the Contract Documents for instructions and requirements pertaining to the Work, and at his and their cost, shall provide all labor, materials, equipment and services necessary to furnish, install and complete the work in strict conformance with all provisions thereof.

   B. The Contractor will be held to have examined the site of the Work prior to submitting his proposal and informed himself, his Subcontractors, Sub-subcontractors and material men of all existing conditions affecting the execution of the Work.

   C. The Contractor will be held to have examined the Contract Documents and modifications thereto, as they may affect subdivisions of the Work and informed himself, his Subcontractors, Sub-subcontractors and material men of all conditions thereof affecting the execution of the Work.

   D. The Scope of Work for the Contract is not necessarily limited to the description of each section of the Specifications and the illustrations shown on the Drawings. Include all minor items not expressly indicated in the Contract Documents, or as might be found necessary as a result of field conditions, in order to complete the Work as it is intended, without any gaps between the various subdivisions of work.

   E. The Contractor will be held to be thoroughly familiar with all conditions affecting labor in the area of the Project including, but not limited to, Unions, incentive pay, procurements, living, parking and commuting conditions and to have informed his Subcontractors and Sub-subcontractors thereof.

5. CONTRACT DOCUMENTS INFORMATION

   A. The Contract Documents are prepared in accordance with available information as to existing

conditions and locations. If, during construction, conditions are revealed at variance with the Contract Documents, notify the Construction Manager immediately, but no more than three (3) days from the day the variance is first known. Failure to give timely notice shall operate to waive any claim Contractor might otherwise have for an adjustment to Contract Time or Sum as a consequence of such variance.

B. The Specifications determine the kinds and methods of installation of the various materials, the Drawings establish the quantities, dimensions and details of materials, the schedules on the Drawings give the location, type and extent of the materials.

C. Dimensions given on the Drawings govern scale measurements and large scale drawings govern small scale drawings, except as to anything omitted unless such omission is expressly noted on the large scale drawings.

D. The techniques or methods of specifying to record requirements varies throughout text, and may include “prescriptive”, “open generic/descriptive”, “compliance with standards”, “performance”, “proprietary”, or a combination of these. The methods used for specifying one unit of work has no bearing on requirements for another unit of work.

E. Whenever a material, article or piece of equipment is referred to in the singular number in the Contract Documents, it shall be the same as referring to it in the plural. As many such materials, articles or pieces of equipment shall be provided as are required to complete the Work.

F. Whenever a material, article or piece of equipment is specified by reference to a governmental, trade association of similar standard, it shall comply with the requirements of the latest publication thereof and amendments thereto in effect on the bid date.

G. In addition to the requirements of the Contract Documents, Contractor’s work shall also comply with applicable standards of the construction industry and those industry standards are made a part of Contract Documents by reference, as if copied directly into Contract Documents, or as if published copies were bound herein.

H. Where compliance with two (2) or more industry standards, contract requirements, or sets of requirements is specified, and overlapping of those different standards or requirements establishes different or conflicting minimums or levels of quality, then the most stringent requirements, which are generally recognized to be also the most costly, is intended and will be enforced, unless specifically detailed language written into the Contract Documents clearly indicates that a less stringent requirement is to be fulfilled. Refer apparently equal but different requirements, and uncertainties as to which level of quality is more stringent, to Architect for decision before proceeding.

I. Reference standards referenced directly in Contract Documents or by governing regulations have precedence over non-reference standards which are recognized in industry for applicability of work.

J. Contractor’s bid is based on the complete set of Contract Documents including documents not specifically issued as part of the bid pack but referenced in same.

6. SCOPE OF WORK/GENERAL INFORMATION

A. A Scope of Work for each contract to be awarded on the project follows in this section. When a Contract has been awarded to a Contractor, the successful Contractor will be listed after the title of the Contract. When no Contract has yet been awarded, no Contractor's name will be listed. Previous Scopes of Work include addendum changes.

B. Contractor is responsible for performing the work listed in the Summary of Work for his contract. Contractor is also responsible for knowing the work that has been assigned to preceding contracts. No additional compensation or extension of time will be allowed a Contractor due to his ignorance of the work assigned to his Contract or to other contracts which may affect his work. The Contractor is responsible, however, for all items which are covered in the Specifications and Drawings relating to their Contract if not specifically mentioned in the Summary of Work.

C. The Construction Manager will provide on-site a source for temporary electric, temporary water and portable sanitation facilities only. It is each Contractor's responsibility to make the necessary connections, including all material for temporary electric and water. Please note that utility charges for office trailers will be the responsibility of the individual Contractors.

D. A dumpster will be provided on site for free use by Contractors to dispose of non-hazardous, common, work-related refuse. Clean-up is the responsibility of each Contractor. Clean up shall be performed on a daily basis. Contractors not complying will be advised in writing and back charged for all costs associated with the cleanup of their work.

E. Contractors are reminded that there are limited storage areas available on site. Off-site storage will be the responsibility of each individual Contractor.

F. Office trailer permits off site will be the responsibility of each individual Contractor. On site Contractor’s field offices, one (1) per Contractor, if required, will be located as directed by the Construction Manager.

G. Contractor will be prepared to discuss and submit a detailed project schedule seven (7) days after receipt of Notice to Proceed and to begin its submittal process. The Project Schedule is an integral part of this contract. Certain construction sequences and priorities must take place in order to meet the target dates. Concentrated work periods will occur and each Contractor is responsible to staff the project as required by the current Construction Schedule or as directed by the Construction Manager. Contractor will cooperate with the Construction Manager in planning and meeting the required sequences of work and Project Schedule as periodically updated by the Construction Manager.

H. All bids must include insurance limits in accordance with Article 11 of the Section 007300 SUPPLEMENTARY CONDITIONS.

I. Hoisting, scaffolding and material handling is the responsibility of each Contractor, unless otherwise noted.

J. Contractor will be responsible for layout of its own work. The Construction Manager will provide benchmark and layout of the building line.

K. Contractor will be responsible to keep clean public roadways soiled by construction traffic on a daily basis. If cleaning is not done, the Construction Manager may perform the cleaning on an overtime basis and backcharge the Contractor responsible.

L. Contractor Scopes of Work and Schedule are interrelated. Familiarity with each is required.

M. The Construction Manager will provide testing services for soil, concrete and steel. Other testing as required by the Contract Documents will be in accordance with the technical specifications and/or the individual scope of work. Refer to Specification Section 004500 - QUALITY CONTROL.

N. Safety is the responsibility of each individual Contractor. The project will be governed under the guidelines of OSHA.

O. Inter-Contractor shop drawing distribution will be performed by the Construction Manager. Contractor is individually responsible for either coordinating his work with these distributed drawings or notifying the Construction Manager, in writing, of any discrepancies.

P. Coordination with other trades will be required. The Contractor will be required to attend periodic coordination meetings with other trades where requirements, conflicts and coordination issues will be discussed and resolved. Attendance when requested will be mandatory. If inter-Contractor coordination is not satisfactorily performed, the conflicting Contractors shall mutually share the cost to relocate and/or reinstall their work.

Q. Contractor shall submit a schedule of values to the Construction Manager prior to the submission of their first invoice for approval through Building Blok.

R. Contractor is expected to review and coordinate its Work with the complete set of Contract Documents, including all items noted as by his trade whether or not shown on that particular set of drawings. Documents are available at the site for review.

S. Contractor is responsible for obtaining all necessary permits required for his work, including street permits. Unless otherwise noted, building permit shall be secured by the Construction Manager. Any subcontractor who will be restricting access to street, right of way or adjacent property must notify the Construction Manager 48 hours in advance.

T. Contractor's License: Submit a copy of all business licenses required by local and state agencies.

U. Contractor shall absorb, without additional compensation, any and all costs of working beyond normal hours to maintain job progress in accordance with the current construction schedule.

V. No asbestos or PCB's in or on any material or equipment will be accepted or allowed on this project. All hazardous materials will be treated in accordance with all State and Federal regulations.

W. Daily cleanup of the work is the responsibility of each individual Contractor which includes broom cleaning of their debris as required. Contractor will be individually back charged by the

Construction Manager for cleanup not satisfactorily performed by the Contractor.

X. In the event asbestos is uncovered, the Contractor shall notify the Construction Manager of the areas requiring removal of asbestos. The Construction Manager shall then coordinate the removal with the Owner.

Y. This project is to be constructed adjacent to existing buildings. Contractor shall exercise all due precautions to minimize noise, air pollution and any other construction hazards which in any way would cause discomfort or danger to the occupants of the existing building in the area.

Z. The Safety Cable System shall not be altered or removed without a written request submitted to the Project Manager with a copy to the Field Manager. It shall be the responsibility of each and every Contractor that is removing or altering the Safety Cable System to maintain the fall protection safety provided by the safety cable and not leave the area unprotected. Each and every Contractor shall be responsible to re-install the Safety Cable System immediately after work is completed. Each and every Contractor shall be responsible to re-install the Safety Cable System in accordance to OSHA standards.

AA. Normal work hours for this project are from 7:00 a.m. to 3:30 p.m. Any work to be performed outside of these hours must receive prior approval from the Construction Manager. Requests to work beyond normal work hours shall be submitted at least 48 hours prior.

AB. Contractor is responsible for having a competent project superintendent/foreman on-site during all work performed under its contract.

AC. In the event the Contractor has non-English speaking employees or subcontractors on the project, they shall have a superintendent or foreman on site, at all times, who speaks English and can communicate with Contractor's employees. Should the Contractor fail to meet this requirement, at any time, Construction Manager may direct all Work to stop until the proper supervision is on site. The Contractor will be responsible for maintaining the project work schedule and make up at its own expense, any delay to the Schedule resulting from the work stoppage.

AD. Punch List Procedures: Contractor shall be given a copy of the punch list with his appropriate work identified. Contractor shall have nine (9) calendar work days to complete its punch list work. On the 10th day or as determined by the Construction Manager, the Construction Manager shall employ other contractors, as required, to complete any incomplete punch list work and retain from the appropriate Contractors retainage all costs incurred.

AE. Contractor shall provide the necessary safety barricades and railings required to complete their work and comply with all OSHA, local code and contract specifications.

AF. **Prohibition of Using Photographs on EDiS Projects**: The Contractor and all associated subcontractors agrees to not issue any news release or advertising pertaining to the Work or the Project, including references to the Project on the Contractor's/subcontractor website or other social media outlets, without obtaining EDiS' prior written approval, in each instance. The Contractor, for itself, its employees, vendors and subcontractors, agrees to not use the name of the Owner, the Project, EDiS or any photographs, videos, or other images of the Project in connection with any of

Contractor's business promotion activities, advertising, website, social media outlets, or operations, without EDiS' prior written approval in each instance.

AG. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

AH. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

AI. All contractors must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented into the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

AJ. All contractors shall be responsible to protect all non-metallic piping within the building envelope from overspray of the Applied Fireproofing, intumescent coatings, fire caulking and fire safing as it pertains to the scope of your course of work. The contractor shall be familiar with and comply with the NFPA regulations, including but not limited to the following 6.3.7.5 Firestopping materials intended for use on nonmetallic piping penetrations shall be investigated for compatibility with the nonmetallic pipe materials. 6.3.7.5 Protection plan shall be submitted and reviewed with the CM prior to implementation.

AK. For all contracts which include allocations for COOP hours with NCCVT students, any unutilized COOP hours shall be returned to the district at the rates published in the documents, as a credit change order.

CONTRACT NO. D-01 - UNIT MASONRY

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 033000	Concrete (coordination)
Section 042000	Unit Masonry
Section 047200	Cast Stone Masonry
Section 321413.13	Interlocking Concrete Unit Paving
Section 070553	Fire and Smoke Assembly Identification
Section 072100	Insulation
Section 072640	Sprayed Polyurethane Foam Insulating Air Barrier
Section 072500	Weather Barriers
Section 076200	Sheet Metal Flashing and Trim
Section 078400	Firestopping
Section 079100	Preformed Joint Sealers
Section 007900	Joint Sealers

This contract provides and includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide masonry units, cast stone, reinforcing, accessories and related work. This contract includes all masonry work except the work provided by BP-C Foundation Masonry contract. This contractor owns coordination with the BP-C contractor and must review and understand the BP-C scope of work.

2. Provide all concrete interlocking pavers, grading, subbase, concrete substrate, grouting and cleaning as required to provide a complete brick pavers system.

3. Provide all special shape, cast stone masonry and custom masonry units as defined in the construction documents.

4. This contract shall provide all Sprayed Polyurethane Foam Insulating Air Barrier with intumescent coatings, special paint layer per NFPA 285, and all “Self-Adhering Flashing Tape” at all locations (vertical and horizontal) behind vertical brick, block, metal panels, canopies and overhangs. The Flashing tape shall be applied to seal all exterior openings, including but not limited to doors, louvers, windows, curtain walls, storefronts etc. This includes all exterior sheathed areas, and block back up areas, whether behind masonry or not. Include spray insulation termination angles as needed for the spray foam insulation installation Coordination of work with other trades shall be required and final installation work to be coordinated with project schedule and CM. Provide a “complete system” in its entirety for this project.

5. This contractor shall include multiple mobilizations within their base bid amount to accommodate the exposure time recommendation for the sprayed insulation, special coatings and self-adhering flashing tape in all areas per the construction schedule and project phasing.

6. This contractor shall provide installation and coordination of sleeves required to go through any masonry walls above finished floor elev. 0.00. Coordinate with the MEP contractors for sleeves (to be provided by MEP contractor) and coordinated/installed by the Masonry contractor.

7. Provide Fire and Smoke Identify markings on all masonry walls that require marking per governing jurisdictions. Coordinate marking walls with pant.\/stencils with the CM on site.

8. Provide all caulking and sealants for masonry to masonry conditions. Masonry to dissimilar materials provided by Caulking contractor.

9. Integral masonry flashings, expansion joints, insulation and other related items as required.

10. Mock up as required. Provide a complete mockup of all masonry items within a sample wall to be coordinated by the CM. This contractor to provide and install the concrete footing required for the mock up. Include demolition, removal and clean up of the mock up area.

11. This contractor shall include within their bid the incorporation of **2000 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5.

12. Grouting of door frames at all masonry openings. Include grouting of HM vision panels in CMU and grouting of after-set frames in stair towers built by BP-C masonry contractor.

13. Weather protection and temporary heat as required to perform the work and maintain the project schedule. This would include tenting, tarping, heating (providing fuel and equipment), installation, maintenance and removal. Kerosene is not an acceptable fuel for work within the interior spaces.

14. Layout of the work including responsibility for all elevations and dimensions as they affect other Contractor's work.

15. Lintels either required by this Contract or install loose lintels furnished by others. Include bolting or welding of lintels as per details.

16. Provide mixing stations as required to perform your work. The station locations shall be coordinated with the CM (include 5 separate locations and the remobilization of the station 5 times) The mixing area shall be protect as required by DNREC and it shall be this contractors responsibility to maintain the station area at all times. Remove all components and restore area when work of this contract complete.

17. Concrete fill/grout at all masonry units as identified.

18. Purchasing and installing reinforcing steel in block walls.

19. Provide all fire safing/fire stopping, and continuous fire sealant at top and bottom of masonry walls as shown on the contract documents. Also include these sealants at all steel penetrations through the provided masonry.

20. Silicone waterproofing/sealant if specified.

21. This contractor shall provide the required firewall/smoke wall assembly identification for work of this contract. (labelling of the walls with fire rating)

22. Interior exposed masonry walls shall be cleaned and scraped thoroughly; a second pass of scraping and refining the cleaning shall be included in the base bid. CM to review and coordinate second pass with the masonry foreman in the field.

23. Temporary protection for final wash down/cleaning of masonry. This includes covering and protecting the curtain wall, storefronts, Kalwall and all door window openings.

24. This contractor shall supply and install straw at the base of wall when work of this contract has been completed to stop splashing of mud and water on completed walls.

25. Flashing at locations indicated on drawings for your work.

    a) Thru wall and cavity flashing below the roof line shall be by the Masonry Contractor.
    b) Thru wall and cavity flashing above the roof line shall be by the Roofing Contractor.
    c) Flashings at rising wall conditions shall be provided by this contractor.

26. Cutting, fitting and building into masonry work, embedments provided by others. Coordinate all work with other trades as required.

27. Provide all firesafing and fire caulking as required for your course of work.

28. Provide masonry veneer anchors as required for your course of work.

29. Bond beams including supplying and installing reinforcing and fill.

30. Elevator shaft masonry block in BP-C contractors scope. All veneer and finish masonry shall be provided by this contractor. Include the final infill toothing of the block around the elevator door frames at each level in this contract. Include sealing and fire safing as required at top of shaft wall.

31. Furnish and install all masonry veneer anchors where required. Welding of anchors that are not shown to be fabricated with the structural steel shall be welded in place as needed by this contractor.

32. Masonry contractor shall supply and manage dumpsters for use in removal of masonry debris. The project dumpsters may not be used for masonry debris.

33. Mock up as required. Provide your portion of a complete mock-up of the exterior wall assembly for areas of masonry, metal panel, translucent panels and others as detailed. within a sample wall to be coordinated by the CM.

34. Provide generators and services as required to provide temp power, water etc. as needed for your course of work.

35. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any

materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

36. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

37. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

38. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented into the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

39. Include within this contracts base bid an allocation of $40,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-02 - MISCELLANEOUS METALS, STAIRS, AND RAILS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 055000	Metal Fabrications
Section 055100	Metal Stairs
Section 055133	Metal Ladders
Section 055213	Pipe and Tube Railings
Section 057300	Decorative Metal Railing

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide stairs, loose lintels, misc. metal angles, plates, handrails, railings, metal ladders and accessories.

2. Furnish loose steel lintels, angles, plates and embedded items to the Concrete and Masonry contractors.

3. Review Alternates as per the Bid Form and Alternate section for work related to Stair #5.

4. **This contractor will be required to coordinate work of this contract with the Structural Steel, Joist and Deck contract which is part of BP-C. Review and understand the BP-C contract as it relates to your work.**

5. This is not a secure site. All contractors are responsible for concealing , locking and/or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

6. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

7. Provide miscellaneous rough hardware, iron shapes, framing and support angles.

8. Provide pipe bollards and specified covers per spec section 055000-11.

9. Provide powder coated downspout boots per section 055000-10.

10. Provide stair nosing's.

11. Provide gratings.

12. Overhead door frames, furnished and installed.

13. Elevator hoist beams, provide and coordinate installation with BP-C masonry contractor.

14. Elevator sill angles, provide and coordinate anchoring systems, bolts etc. and installation with other trades.

15. Toilet partition supports, if not part of the manufactured toilet partition frame shall be supplied by this contractor.

16. Dock bumpers and loading dock equipment. Provide (furnish and install.)

17. Provide ships ladder, access ladders and related fastening devices and accessories.

18. Galvanizing and other special coatings as required.

19. Anchoring devices, fasteners, inserts and other related items associated with the installation of the above items.

20. Field touch-up paint.

21. No electrical power for welders will be provided.

22. Verify all field dimensions prior to fabrication.

23. No electrical power for this contractors equipment or welders will be provided. Electrical power to be provided as needed by this contractor.

24. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

25. Include within this contracts base bid an allocation of $20,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-03 - EXTERIOR STRUCTURAL STUD ASSEMBLY

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 054000	Cold-Formed Metal Framing
Section 070553	Fire and Smoke Assembly Identification
Section 072100	Thermal Insulation
Section 072129	Sprayed Acoustical Insulation (coordination)
Section 072640	Spray Polyurethane Foam Insulating Air barrier (coordination)
Section 072500	Weather Barriers (coordination with mason contractor)
Section 079100	Preformed Joint Sealants
Section 079200	Joint Sealants
Section 078400	Firestopping
Section 092116	Gypsum Board Assemblies

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide structural stud assembly for the exterior skin of the building. Including but not limited to Metal Studs, gyp sheathing, Fire safing and delegated design on the exterior wall assembly.

2. Provide rock wool thermal insulation at area where exterior walls create parapets and at edge of floor slab connections.

3. This contractor shall be responsible to coordinate with the masonry contractor as related to the exterior wall assembly and the installation of the spray foam insulation system.

4. Steel stud construction as related to the roof parapet construction.

5. Steel stud construction related to framing out for openings in exterior walls.

6. Provide secondary support framing as required.

7. Clips, anchors, supports and other accessories that interface between steel framing and steel studding and steel studding with masonry interaction.

8. Expansion systems as required for performance of your course of work.

9. Scaffolding, lifts, and all necessary equipment required for your contract's course of work.

10. Provide engineered drawings (delegated design requirements.)

11. This contractor shall be responsible for coordinating with other trades for exterior openings and layout of design features.

12. Comebacks and out-of-sequence work may be required and as such should be included in your base bid proposal.

13. No power for welding equipment will be provided. This contractor shall provide portable generators, fuel, etc.to power equipment required for their scope of work.

14. Coordinate Self Sealing Flashing installation at base of wall assemblies and flashed areas. with Masonry contractor who is providing. This contract (D-30 Ext Wall) to provide any required metal flashings for your course of work.

15. This contractor shall supply and install any access panels in the exterior wall assembly that are required by the contract documents. In addition the contractor shall install (40) 2'X2' Access panels provided by other. (exterior walls only)

16. Provide fire resistant joint sealants, fire safing, fire stopping, as it relates the work of your contract.

17. Bidders are advised to pay particular attention to top of wall conditions, fire and smoke safing of slabs and acoustical sealants.

18. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

19. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented into the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

20. Layout of the work including responsibility for all elevations and dimensions as they affect other Contractor's work.

21. Mock up as required. Provide your portion of a complete mock-up of the exterior wall assembly for areas of masonry, metal panel, translucent panels and others as detailed. within a sample wall to be coordinated by the CM.

22. This contractor shall include within their bid the incorporation of **750 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5.

23. This contract shall include in their bid the necessary crews to complete the work as per the project schedule. Provide additional crews as required to maintain schedule at no additional cost to the project.

24. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

25. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

26. Include within this contracts base bid an allocation of $40,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-04 - CARPENTRY AND GENERAL WORK

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 055800	Architectural Metal Column Covers
Section 06100	Rough Carpentry
Section 06200	Finish Carpentry
Section 062023	Interior Finish Carpentry
Section 079200	Joint Sealants
Section 081113	Hollow Metal Doors and Frames (coordination, handing, installation)
Section 081416	Flush Wood Doors (coordination, handing, installation)
Section 081613	Integrated Door Opening Assemblies
Section 083100	Access Doors and Panels
Section 087100	Door Hardware (coordination, handing, installation)
Section 087106	Door Hardware Schedule (coordination, handing, installation)
Section 089100	Louvers
Section 101101	Visual Display Boards and Display Cases (coordinate blocking and supports)
Section 102113	Plastic Toilet Compartments (coordinate blocking and supports)
Section 102123	Cubicle Curtains and Track(coordinate blocking and supports)
Section 102601	Door and Wall Protection (coordinate blocking and supports)
Section 102800	Toilet Accessories (coordinate blocking and supports)
Section 104400	Fire Protection Specialties (coordinate blocking and supports)
Section 129300	Site Furnishings
Section 116625	Gymnasium Equipment
Section 116653	Gymnasium Dividers
Section 323119	Decorative Metal Fences and Gates

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide labor and materials to perform the work related to all carpentry and general work.

2. All rough carpentry related to the exterior skin of the building and roof areas, including wood nailers and blocking, roof blocking, curb blocking, MEP blocking coordinated with MEP trade, fire shutter blocking etc. as required. Include blocking for roller shades.

3. All rough carpentry related to the interior of the building including blocking, wood nailers, etc. for the installation of fire extinguishers, doors, windows, toilet accessories, cabinets, toilet partitions, casework, millwork, AED's, gas and air cabinets, rollup doors, coiling doors, kitchen equipment and accessory blocking, etc. including fire treating as required.

4. Provide interior architectural metal column covers as required. (Note the MCM exterior column enclosures are provided by the Metal Panel contractor)

5. Provide all decorative metal fencing and gates as per contract documents. Include complete installation and coordination with electrical and special systems contractor for the locking interface and card access.

6. Provide and install plywood back boards on all wall areas, floor to ceiling in all electric, MDF and IDF rooms. Backboards to be ¾ inch plywood, painted one side with white Fire Proof paint and fire caulked to the walls tightly.

7. This contractor shall include the installation of the key box system and all required blocking and anchoring systems.

8. Provide blocking and anchoring for all roof ladders, TV and monitor mounts, Smart Board displays, Visual display boards, chalk, tack and white board assemblies. Coordinate with other trades for locations and installation direction.

9. Provide blocking for door hold opens, wall mounted closers, and wall door stops.

10. Provide all Gymnasium equipment and Gymnasium dividers as part of this contract.

11. Install metal and wood doors and frames, including receipt of doors and frames at the curb side. Contractor shall receive the doors, frames and hardware and inventory immediately. This contractor responsible for safe keeping of all materials and shall provide written documentation that all materials were received. All hardware shall be secured in a fully locked and protected area. By this contractor.

12. Install finish hardware related to all doors (hollow metal, wood and coordinate keying with aluminum hardware) including receipt of hardware at the curb side. This contractor is responsible for coordinating door hardware with their work to ensure each opening is properly prepped for hardware being supplied by others. All low voltage wiring within the doors and frames to be installed by this contractor. Conduits and raceways will be provided by the electrical contractor, as well as installation of the electrical supply power and the final power connections to equipment. Final connections of low voltage wiring to hardware to be provided by the Special Systems contractor. This contractor to work with the electrical contractor and Special Systems contractor to provide a complete installation.

13. This contractor shall advise the hardware supply contractor of any deficiencies or missing item immediately after initial inventory (in writing) as installation takes place. Reporting and tracking is the responsibility of this contractor.

14. All field trimming required to adjust to the existing in place conditions shall be part of this contractors scope of work. Field measuring and verification is to be included.

15. Anchoring devices, fasteners, inserts and other related items associated with the installation of the above items.

16. Provide all architectural louvers, including insulated panels etc. All louvers are to be included within this contract, they are shown on the architectural drawings and specs and referenced by MEP documents. Provide ‘custom” color costs in the base bid. Coordinate the louvers provided within the Kalwall System for custom color, sizing, design or other integrated features. This contractor shall coordinate with other trades for integration of the louvers into their course of work. All material

handling and on site protection of the louvers is this contractors responsibility.

17. Provide blocking and support for the Visual Display Boards and Display Cases.

18. Provide all blocking as required for Toilet Partitions, Cubicle Curtains, Door and Wall Protection, Toilet Accessories and Fire Protection Specialties. Coordinate with the BP-D contract for "Specialties" on all required blocking. Volleyball sleeves and installation shall be coordinated and installed by this contractor,

19. This contractor shall provide and install all Gymnasium Equipment a per contract documents, to include blocking, supports, material handling etc. 100% protection of the gym floor while performing your work is required by this contract. Floor protection shall be as provided by the wood floor manufacturers recommendations.

20. This contractor shall provide al Gymnasium scoreboards as indicated on A-111 (3 scoreboards in total)

21. This contractor shall provide and install all Site Furnishings as detailed in the contract documents. Include all work related to this course of work, concrete pads, anchoring, touch up paint etc.

22. This contractor to coordinate all card reader blocking requirements with Special Systems contractor.

23. Provide protection at Elevator door openings at each floor. Include the required mesh protection fabric and the necessary wooden framing that allow easy access by other trades. Include maintenance for a period of 30 months from initial installation. Once elevator is installed, provide ¾" blue board foam insulation on all surfaces taped and secured so as not to damage finishes of elevator. Provide maintenance of this protection until substantial completion of project.

24. Provide and maintain temporary wood railings and handrails at stairs. Provide wood infill of stair pans and landing pans. Each tread to have abrasive edge tape applied immediately after installation of infill.

25. This Contractor shall include in the base bid 600 hours of Journeyman carpenter time and 250 hours of common labor time for work to be directed by the Construction Manager.

26. This Subcontractor shall at a minimum provided, maintained, and inspect for the length of the project, one temporary fire extinguisher for each 3,000 sq. ft of the protected building area. Travel distance from any point of the protected area to the nearest fire extinguisher shall not exceed 100 feet. In multistory buildings, at least one fire extinguisher shall be located adjacent to stairway. Fire extinguishers shall be at least 10lb, Multi-Purpose (ABC) dry chemical, UL labeled, with a rating of 3a:40bc. Maintain for the duration of the project until substantial completion to insure coverage and compliance.

27. Coordinate electrical requirements with any automatic door operations. This contractor owns all controls, switches and wiring as required for a complete system. Power to be supplied by Electrical contractor.

28. Gate hardware provided by others shall be installed and completed by this contract.

29. Provide three Knox Boxes coordinated with the local fire company for installation at locations identified

by the owner/CM.

30. Coordinate and install hold open closers with fire alarm interface. Power wiring by Electrical Contractor. Fire alarm ties in by Electrical Contractor.

31. This contractor will work with the Special Systems contract to allow the installation of harnesses, whips and connections while installing frames, doors, hardware and access controls.

32. Provide (2) separate scaffold stairways, each must be erected to accommodate access to the roof area from the exterior of the building. The scaffold must provide a landing with stairs at the roof area. Each scaffold leg should have adjustable base plates to accommodate the installation of roofing material without the disassembly of the unit. An 8 foot plywood "wall" must surround the bottom of the stairway with a hinged plywood door installed with a hasp to accept a lock. The scaffold must be installed per OSHA regulations, inspected and tagged for use.

33. Provide and maintain perimeter netting at each floor level including all floor openings. Perimeter rail or cable to be provided by the steel contractor. This work shall include toe boards at all location. **Netting to be included as detailed on the "Perimeter Safety Netting at Leading Edge Conditions" sketch included as part of this scope of work.**

34. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

35. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented into the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

36. Layout of the work including responsibility for all elevations and dimensions as they affect other Contractor's work.

37. Provide all work related to the building mock up, blocking, installation of door frame, doors, hardware, flashings, fasteners etc. as it relates to mocking up of the systems included in the Carpentry Scope.

38. This contractor shall include within their bid the incorporation of **2000 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5.

39. Provide and maintain temporary handrails per OSHA standards at all stair assemblies. <u>The below section is a guideline and doesn't replace the OSHA regulations</u> Stairs having two or more risers or rising more than 30 inches (76 cm), whichever is less, shall be equipped with: At least one handrail; and one stairrail system along each unprotected side or edge. The height of stairrails shall be not less than 36 inches from the upper surface of the stairrail system to the surface of the tread, in line with the face of the riser at the forward edge of the tread. Handrails shall provide an adequate handhold for employees grasping them to avoid falling. Handrails that will not be a permanent part of the structure being built shall have a minimum clearance of 3 inches (8 cm) between the handrail and walls, stairrail

systems, and other objects. Midrails, and intermediate vertical members, or equivalent intermediate structural members, shall be provided between the top rail of the stairrail system and the stairway steps. Midrails, when used, shall be located at a height midway between the top edge of the stairrail system and the stairway steps. When intermediate vertical members, such as balusters, are used between posts, they shall not be more than 19 inches (48 cm) apart.

40. This contractor shall provide temporary rails at all exterior opening on the building until permanent window/doors/curtainwall etc. installed.

41. This contractor shall include protective wooden covers and marking for any floor openings, holes, shafts etc. Include labelling of the covers with clear ad readable markings or stickers.

42. Provide temporary protective handrails at stage front, steps, stairs and ramp locations.

43. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

44. Provide **fall** protection at Elevator door openings at each floor. Include the required mesh protection fabric and the necessary wooden framing that allow easy access by other trades. Include maintenance for a period of 30 months from initial installation. Meeting the minimum requirements provided by the elevator vendor.


45. This contractor shall provide within the base bid, (8) sets of exterior steps to be constructed to create safe and easy access to the building first floor from the exterior grade. The step assemblies shall be figured to manage a 24" rise from grade to the first floor elevation, be 40" wide and shall have no-slip tread tape applied to each tread.

46. Provide, maintain and remove a prefabricated manufactured trash chute from the second floor to the dumpster below for a period of 24 months. This chute shall be maintained and all safety barriers, restraints etc. managed until substantial completion of the project.

47. This contractor shall provide and include all costs associated with installing temporary doors at the exterior of the building (all openings) and a cattle chute on the 2nd floor for accepting deliveries to the second floor. Safety equipment, gates, railings and tie-offs as required by OSHA safety standards shall be included.

48. Provide wood safety barricades to extend top of roof parapets to OSHA required height during construction. Coordinate removal and replacement of wood safety barricades with metal wall cap installation.

49. Provide within this contracts base bid an allocation of $40,000 for work to be directed by the owner and CM. Unused portions of the allocation shall be returned to the owner.

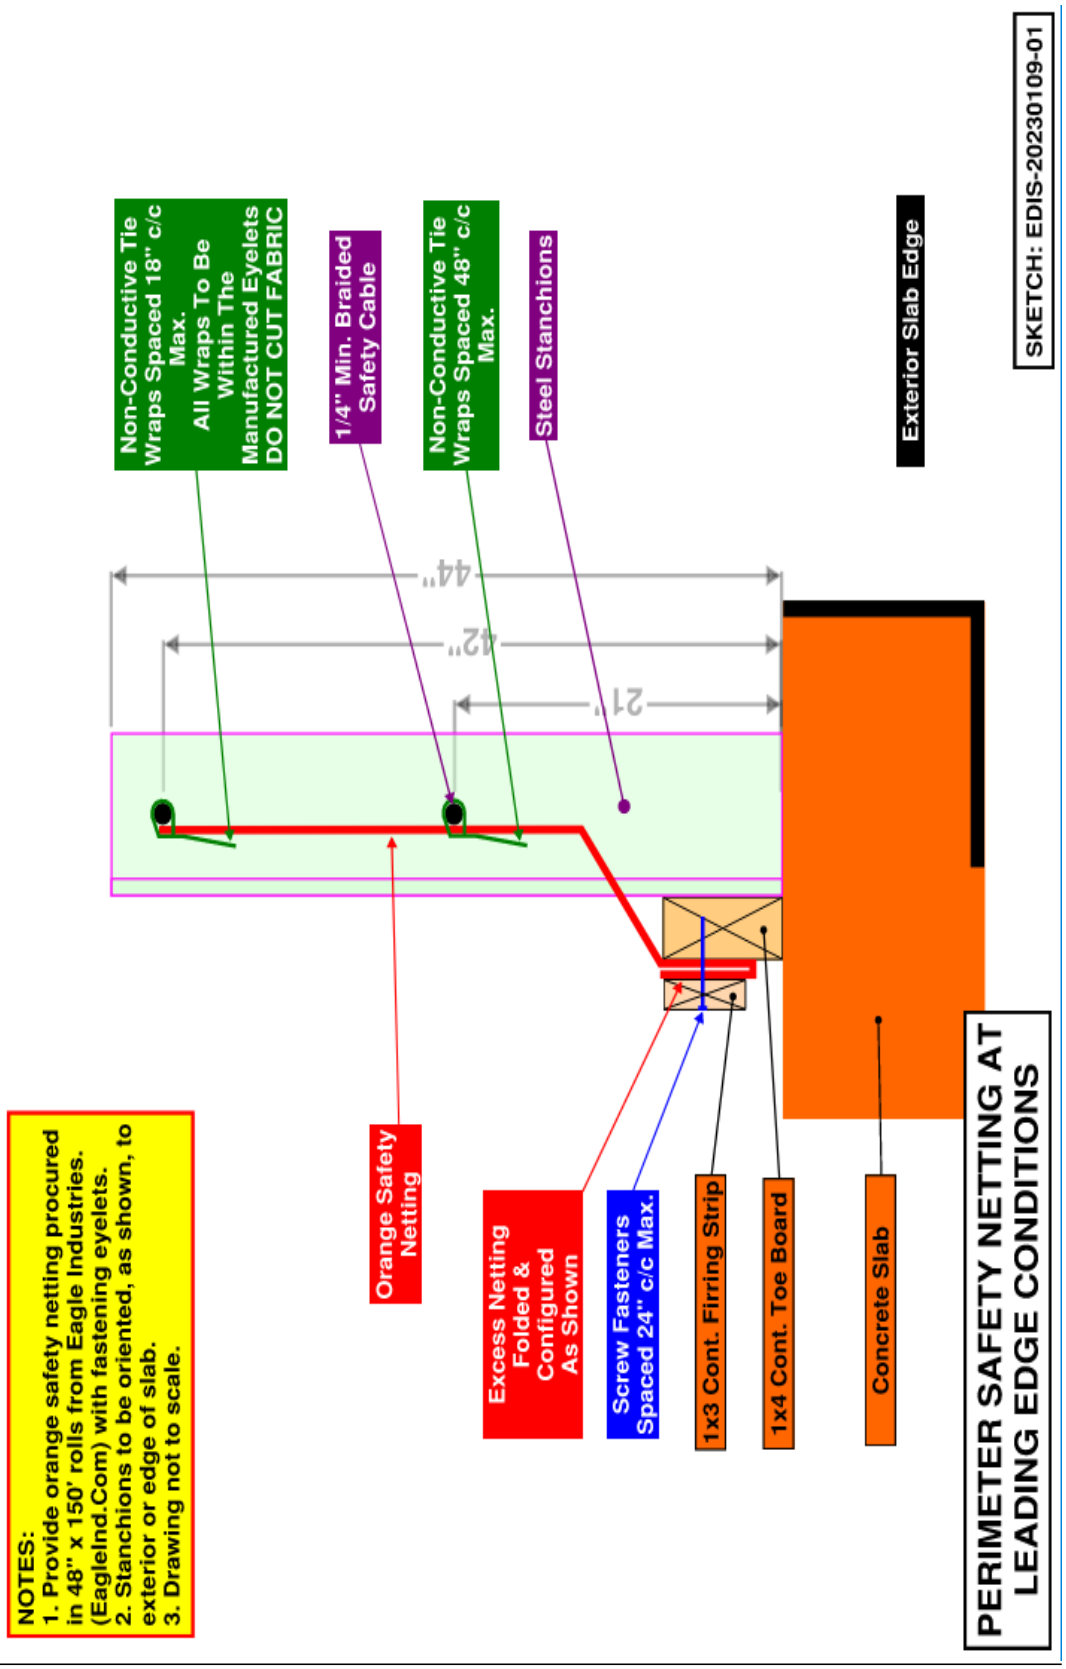
SKETCH: EDIS-20230109-01
Non-Conductive Tie Wraps Spaced 18" c/c Max. All Wraps To Be Within The Manufactured Eyelets DO NOT CUT FABRIC
1/4" Min. Braided Safety Cable
Non-Conductive Tie Wraps Spaced 48" c/c Max.
Steel Stanchions
Exterior Slab Edge
44"
42"
21"
Orange Safety Netting
Excess Netting Folded & Configured As Shown
Screw Fasteners Spaced 24" c/c Max.
1x3 Cont. Firring Strip
1x4 Cont. Toe Board
Concrete Slab
NOTES:
1. Provide orange safety netting procured in 48" x 150' rolls from Eagle Industries. (EagleInd.Com) with fastening eyelets.
2. Stanchions to be oriented, as shown, to exterior or edge of slab.
3. Drawing not to scale.
PERIMETER SAFETY NETTING AT LEADING EDGE CONDITIONS

CONTRACT NO. D-05 - EXTERIOR METAL PANELS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 054000	Cold-Formed Metal Framing
Section 050500	Metal Fabrications
Section 074213.13	Metal Wall Panels
Section 074213.23	Metal Composite Material Wall Panels
Section 076200	Flashing and Sheet Metal
Section 079100	Preformed Joint Sealants
Section 079000	Joint Sealants

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide all metal panels, framing, sub girts, Z furring, insulation and all other components to provide a complete metal panel system.

2. Provide Flashing and complete "engineered and sealed" (Delegated Design) as shown in detail D1/A612. Include all flashing, closures, jamb reveal detail, self-adhered flashing tape etc. to provide a complete system at all locations. This contractor must work with and in conjunction with the spray foam system installation and sealing.

3. This contractor shall provide the MCM metal column enclosures color 2 as indicated on A-202, A-203 and A-207. Provide a complete and sealed systems.

4. The spray installation system will be provided by the Masonry contractor, however this contractor is responsible to coordination. Specifically for installation durations and the completeness of the installation of the Z furring system this contract is providing. Timely installation to not impact the spray foam installation is required by this scope of work.

5. Provide all composite metal panel return systems as identified in detail A1/A612, A7/A612 and similar details as indicated. Jamb return needs to be coordinated with the window installation.

6. Provide all fascia's, soffits, overhangs etc. as required for a complete system.

7. Flashing of panels integral with the panel system.

8. Coordinating, cutting and fitting around the work of other trades is required by this contract and should be part of your base bid work.

9. Caulking of panels as required to provide a complete system. Vertical joints where metal panels meet adjacent materials shall be caulked by the Caulking and Salant contractor.

10. Miscellaneous metal items necessary to support panels other than required structural steel.

11. Furnish anchorage items for embedding into other construction for support of panels.

12. Touch up of all welding.

13. Galvanized, epoxy or stainless steel, etc. anchors as specified.

14. Metal fascia's and copings related to the panel system.

15. This Contractor shall coordinate his shop drawings with the Window Contractor's shop drawings and the overall construction schedule.

16. Coordinate all work of this contract with the Carpentry contractor for the installation, flashing and complete installation of the louvers into the metal panel system. Close coordination of shop drawings is required by these two contracts.

17. All material handling, lifts, cranes etc. are the responsibility of this contractor.

18. Verification of field dimensions is the responsibility of this Contractor. Coordination and review window openings, door openings and others during the shop drawing process is required so materials can be ordered to accommodate schedule. Material may be required to be ordered in advance of the ability to field measure. This coordination is the responsibility of this contractor.

19. Provide all flashing as identified with the metal panel installation. Provide all hat channels and sub-girts for the panel installation. Coordinate with the work of other contractors related to the spry foam installation.

20. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

21. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

22. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

23. Include within this contracts base bid an allocation of $30,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-06 – DRYWALL AND INTERIOR METAL FRAMING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 051200	Structural Steel (related work)
Section 055000	Metal Fabrications (related work)
Section 054000	Cold-Formed Metal Framing
Section 061000	Rough Carpentry
Section 070553	Fire and Smoke Assembly
Section 072100	Thermal Insulation
Section 078400	Firestopping
Section 079200	Joint Sealers
Section 092116	Gypsum Board Assemblies
Division 15	Mechanical (coordination)
Division 16	Electrical (coordination)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide metal studs, framing, insulation, gypsum wallboard, taping, spackling and specified wall finishes. (Level 5 where identified) Include all trims and finish pieces for a complete installation.

2. This contract shall provide all insulation in the exterior walls of the building system. Coordinate all insulation work and interior drywall work with the exterior Metal Framing contractor.

3. Provide secondary support framing and fastening devices as required. If Misc. metals are required by your installation and not identified in the documents this contractor shall provide and install.

4. Provide Fireproofing at the exterior wall and the edge of slab as shown in the typical wall sections. (A1/A312 example and all related details) Sealants required to complete this system shall be provided by this contractor.

5. Provide all interior metal framing at required for back up of other materials.

6. Provide batt insulation, both thermal and acoustical and related work.

7. Include molded shapes if specified.

8. Acoustical sealants, fire safing and fire caulking as required for penetrations and top of wall conditions.

9. Removal of spray fireproofing to expose points of attachment to structural steel is to be performed in a workmanlike manner. Removal of spray fireproofing in excess of 3" greater than the attached item will require repatching which will be back charged to this Contractor.

10. This contractor shall coordinate with the other trades for all box outs, penetrations, framed openings etc. as required.

11. This contractor shall provide cleaning of the floor areas of all drywall spackle, mud, finishes etc. that are used by this contractor. Review and acceptance by the CM will be required.

12. Access panel installation (assume 100 total). Assume panels to be 30"x 30" for framing purposes.

13. Coordinate work of this contract with the Carpentry contract for wood blocking and support installation.

14. Coordination of door and interior framed openings with the Carpentry contractor who will install the door and lite frames.

15. Coordinate interior louver extensions and incorporation of louver installation with Carpentry contractor as necessary.

16. Include fire taping and sealing at perimeter edge and as shown or indicated in the contract documents.

17. Provide architectural expansion joint systems, including joint covers materials at concrete slab, drywall and masonry construction (interior only).

18. Scaffolding, lifts and material handling equipment for the course of your work.

19. Comebacks and out-of-sequence work may be required and as such should be included. Include (4) additional mobilization/return trips for touch up and repairs. Each trip shall include 16 hours of carpenter/finisher time as well as materials required for general patching.

20. Include all necessary field measurements.

21. Include three (3) passes per floor to "touch-up" mechanical penetrations to ensure ratings required. The first pass will be required prior to ceiling grid installation and the second pass will be required prior to final inspection for Certificate of Occupancy.

22. Bidders are advised to pay particular attention to top of wall conditions, fire and smoke safing of slabs and acoustical sealants. This work is include within the scope of this contract.

23. This contractor to provide caulking at the base and top of drywall partitions, furred walls and all drywall conditions.

24. This contractor shall work with other trades to install openings that are in wall assemblies being constructed.

25. Provide metal furring as required.

26. Provide all glass fiber reinforced gypsum work including materials, taping (interior only.)

27. Provide all backing board (cement board) for tile areas and as directed by the contract documents. Coordinate with the Tiling contractor for requirements of this work.

28. Engineered shop and installation drawings. (delegated design)

29. This Contractor shall include a $175,000 allocation in his contract to supply, install, inspect and maintain a complete scaffold system to accommodate the construction of the Auditorium framing, ceiling systems, clouds, MEP installation etc. This contractor shall be the responsible contractor for this scaffolding system throughout construction until all work is completed and the CM authorized the removal of the system. All contractors shall provide signed waiver forms to the controlling contractor (this contractor) before they may access the scaffold system.

30. This contractor shall include within their bid the incorporation of **1000 hours of COOP participation** by an NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5

31. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

32. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

33. Provide trash and debris removal daily. This means everything leaves the building and goes to the dumpsters. No piling of trash inside building will be permitted.

34. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

35. Include within this contracts base bid an allocation of $30,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-07 – GENERAL LABOR AND CLEAN-UP

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Procurement and Contract Requirements
Division 1	General Requirements

This contract also includes, but is not necessarily limited to, all labor, materials, and equipment for the following:

1. This contractor shall provide General labor to the project the direction of the owner and project manager.

2. Include within the Base Bid for this contract $7,500 worth of material handling tools. To include but not limited to, wheeled bins for trash removal, shovels, brooms, trash bags etc. purchased materials shall be tracked with receipts and verified. Any funds left unspent will be returned to the owner via credit change order. (all tools purchased under this allocation shall be organized and turned over to the owner at completion of the work)

3. The contract shall include a total of 6,000 manhours of general labor to be scheduled by the Construction Manager. The work will start Feb 15 2024 and the duration of the coverage could extend to 15 May 2026. This work may be scheduled anytime within the scheduled date range without penalty or additional costs to NCCVT or the CM.

4. A unit price will be provided by this contractor that will pertain to any hours that may be deducted or added to this contract.

5. Pay Applications each month will be backed up with daily tickets and a complete accounting of the monthly hours utilized. Field Superintendent or hid designated representative shall sign all daily tickets.

6. The owner and CM have the right to request replacement of any personnel provide to service this contract, without out obligation or explanation.

CONTRACT NO. D-08 - ROOFING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 072100	Thermal Insulation
Section 075300	Elastomeric Membrane Roofing
Section 076200	Sheet Metal Flashing and Trim
Section 077100	Roof Specialties
Section 077123	Manufactured Gutters and Downspouts
Section 077200	Roof Accessories
Section 079100	Preformed Joint Sealants
Section 07900	Joint Sealants
Division 23	HVAC (controls coordination)
Division 26	Electrical (power, fire alarm, lightning protection)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide single ply flexible roofing system, including rigid and tapered insulation and all related accessories.

2. This contractor shall carefully review the edge of roof details to determine if the roof can be placed before the exterior wall assembly is complete. This contractor shall include all costs associated with returning to the jobsite to complete the roof perimeter after wall assembly is complete.

3. Provide caulking and joint assemblies related to roofing, flashing and roof accessories.

4. Roof drains and associated plumbing shall be provided by the Mechanical Contractor. Flashing of the roof drains shall be by the Roofing Contractor. Openings for the roof drains in the roofing materials shall be cut by the Roofing Contractor. Openings in the metal deck shall be cut by others. This contractor shall be responsible to coordinate the roof drain locations as needed by the steel contractor and plumbing contractor so reinforcing of the decking and roof support frames may be installed in accordance with the sequence of work.

5. Metal parapet coping, receiver system and all components required for a complete coping assembly. Caulking and sealing of all copings is the responsibility of this contractor.

6. Provide boot for piping and conduits that penetrate the roofing assembly. Coordinate with other trades.

7. Coordinate the roofing installation and flashing required for line sets, piping, electric and control penetrations. Coordinate with MEP contractors.

8. Roof hatches, smoke vents, smoke hatches, access covers etc. are to be provided by this contractor.

Coordination of this work with other trades and the MEP vendors are required by this contract. Rail systems and curbs to be provided by this contract. The smoke hatches are not accessible shall be provided with remote controllers to test and re-set.

9. Walk pads and walk pad layout shop drawings are required by this contract.

10. Perform cutting, patching and maintenance of temporary patch for work performed by others on existing roofs intended to be re-roofed as part of this work.

11. Metal drip edges, complete including all caulking and sealants.

12. Gravel stops, complete including all caulking and sealants.

13. Roof curbs to be installed by this contractor, provided by the MEP trades as identified in the contract documents. Coordination with the Carpentry contractor on the roof blocking thickness is required by this contractor. Provide detail shop drawings identifying the insulation thickness so blocking can be installed accordingly.

14. This contactor shall coordinate with the carpentry contractor on location of wood blocking, curbing, etc. to facilitate the installation of the tapered insulation, crickets etc.

15. Provide expansion joints that are integral to the roof. Including but not limited to edge of wall Details E3/A590 and B1/A590.

16. Gutters, downspouts, splash pans, splash blocks. This contractor shall be responsible to coordinate with the plumbing contractor for the connection to the RW system. Provide membrane flashing, metal flashings, sealants, drip edge, gutters , drain covers etc. as related the gutter systems for this course of work.

17. Metal scuppers, over flows, drains etc. as required by the contract documents are this contractors responsibility.

18. Provide a means to lift materials to the roof for materials not stored on the roof at initial time of delivery. All costs shall be the responsibility of the roofing contractor.

19. This contractor shall manage, handle, lift and install the insulation materials supplied by the steel contractor for the areas of acoustical decking. Lifting of these materials to the roof when needed is the responsibility of the roofing contractor. At areas of Acoustical Decking below, fasteners for the first layer of roof insulation shall be installed so they “do not “penetrate the bottom surface of the decking. All layers of insulation above are to be imbedded into full bed od adhesive in accordance with roofing and insulation manufacturer’s instructions.

20. This contractor shall provide waterproof seals around lightning protection system as required by roof manufacturer requirements. If location of lightning protection conduits are not clearly shown on the roof plan, include within your base bid an additional; cost to seal one penetration for every 1000 sf of roof area.

21. This contractor shall review the schedule for the roofing scope of work and include within the base bid

considerations (costs) for cold weather roofing installations. This shall include but is not limited to providing a warming hut/enclosure to keep material warm and allow the roof installation to continue in cold temperatures. All costs related to cold weather roof installation shall be the responsibility of this contractor.

22. The owner may at any time select to have a third party roof inspector review and inspect the roofing installation and finished roof system. This contractor shall work with and allow access to this third party inspector as needed.

23. All trach shall be removed from this contractors work area daily to the dumpsters. No trash may be stored on the roof area.

24. Flashing and sheet metal systems related to the scope of this contract work.

25. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

26. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

27. This contractor shall include within the base bid proposal (2) additional roofing inspections of the entire roofing assembly to facilitate any damage or overuse repairs that may be required. These inspections will be schedule by the CM within the duration of the construction schedule. These inspections do not in any way take the place of the final warranty inspections as required by the contract documents.

21. Flashing Summary:
    a. Thru wall and cavity flashing below the roof line shall be by the Masonry Contractor.
    b. Thru wall and cavity flashing above the roof line shall be by the Roofing Contractor.

22. Include within this contracts base bid an allocation of $35,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of credit change order.

CONTRACT NO. D-09 - FIREPROOFING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 072129	Sprayed Acoustical Insulation
Section 078100	Applied Fireproofing
Section 078400	Firestopping

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide all fireproofing, both exposed and concealed as required by the contract documents.

2. Provide all intumescent and special coatings required by the code documents, identified in contract drawings, plans and details.

3. Provide Sprayed Acoustical Insulation as required by the contract documents. The Alternates apply to this area of work.

4. Clean up on a daily basis, all over spray materials. Remove all excessive water from spraying operation.

5. This contractor shall be responsible to protect all non-metallic piping within the building envelope from over spray of the Applied Fireproofing, intumescent coatings, fire caulking and fire safing as it pertains to the scope of your course of work. The contractor shall be familiar with and comply with the NFPA regulations, including but not limited to the following
   6.3.7.5 Firestopping materials intended for use on nonmetallic piping penetrations shall be investigated for compatibility with the nonmetallic pipe materials.
   6.3.7.5
   Protection plan shall be submitted and reviewed with the CM prior to implementation.

6. Inspection of the fireproofing for compliance will be provided by a third party inspector provided by the owner.

7. Protect fireproofing according to advice of fireproofing manufacturer and installer from damage resulting from construction operations or other causes so that fireproofing will be without damage or deterioration at time of Substantial Completion.

8. Coordinate installation of fireproofing with other work in order to minimize the need for other trades to cut or remove fireproofing. As other trades successively complete installation of their work, maintain protection of structure afforded by fireproofing by patching any areas which have been removed or damaged prior to concealment of fireproofing by other work.

9. This contractor to include and submit as a shop drawing for review a detailed mshop drawing of all

areas of fireproofing and the required coatings on floor plans and elevations, to clearly illustrate where the fireproofing materials and special coatings will be applied.

10. This shop drawing will be shared with the Steel contractor for review and incorporation into their steel and joist preparation plan. (no primer, coatings, primers etc.)

11. Repair or replace work which has not been successfully protected.

12. Prepare all surfaces including priming of substrate if required.

13. Provide all required steel frame fireproofing whether clearly shown or not on the drawings. Do not include concrete fire proofing.

14. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

15. Provide Alternate pricing as required by the contract documents. (k-12 Sprayed Insulation at Shop Areas)

16. Include within you base bid 80 hours of labor and $20,000 of materials required to touch up fireproofing systems as required by the governing agencies (FM) or the construction manager.

CONTRACT NO. D-10 – JOINT SEALANTS AND PREFORMED JOINT ASSEMBLIES

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 078400	Firestopping
Section 079100	Preformed Joint sealants
Section 079200	Joint Sealants

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide required caulking at control and construction joints.
2. Provide all preformed joint sealant products including but not limited to Emseal expansion joint as required.
3. Provide caulking of masonry to masonry and to dissimilar materials.
4. Provide within your Base Bid proposal (240) man hours and $7,500 in materials to be utilized for Misc. fire safing and Fire sealants that may be required due to agency walk throughs and inspections. This work shall only be authorized by NCCVT or EDiS. Any remaining funds shall be returned to the owner via credit change order.
5. Provide caulking of vertical joints on exterior metal panels to adjacent materials (Metal Panel contractor to provide sealants and caulking between panels and as required to seal their assembly, including where metal panels sit on masonry.)
6. Provide caulking related to interior glazing. Caulking of interior perimeter of new aluminum windows, storefront and curtainwall to finished surfaces to be provided by this contract. To include all rated sealants and Ballistic sealants at required areas.
7. Provide all caulking and sealants for of kitchen equipment and laboratory furniture to adjacent surfaces.
8. Provide caulking of exterior perimeter of hollow metal door frames.
9. Provide caulking of interior perimeter of hollow metal door frames to masonry. (HM frames to drywall shall be provided by the Painting contractor)
10. Provide caulking of all hollow metal frames to the floor. Coordinate caulking with flooring materials.
11. Provide caulking of all interior exposed drywall to masonry and metal wall panels.

12. Provide caulking at the tops and bottoms of all exterior and interior column covers.

13. Provide caulking of all interior exposed concrete slab control joints, expansion joints and perimeter slab to walls.

14. Provide caulking for interior perimeter of sinks, urinals, toilets, bath accessories, toilet partitions, fire extinguisher cabinets, hose reel cabinets, gas cabinets and any other accessories identified on the contract documents.

15. Provide caulking of joints in ceramic tile areas, including inside corners, floors and ceilings.

16. Provide caulking of the top and sides of all finished stair stringers to adjacent materials. Include caulking of all stair stringers and bottom riser to floor.

17. Provide caulking for penetrations through wall, floors, etc. including cutting, patching, sleeves, angle rings, and fire safing.

18. Examine areas and conditions where joint sealers are to be installed and correct any conditions detrimental to the proper and timely completion of this scope of work. Do not proceed with work until unsatisfactory conditions are corrected to permit proper installation.

19. Provide mock ups of all products and adhesion tests for exterior caulking.

20. Provide custom colors or all caulks and sealants.

21. Protection and cleaning of adjacent surfaces to be the responsibility of this contractor.

22. This contractor shall include the Pollution Insurance coverage as specified in the contract documents.

23. This is not a secure site, the contractor is responsible for the safe storage of all of their materials. NCCVT and EDiS will not be responsible for lost or stolen materials

24. All subbase preparation, priming etc. to be performed before caulking is applied.

25. Include caulking and preparation of all painted materials prior to painting

26. Include within this contracts base bid an allocation of $15,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-11 - HOLLOW METAL, WOOD DOORS, AND FINISH HARDWARE

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 081113	Hollow Metal Doors and Frames
Section 081416	Flush Wood Doors
Section 081700	Integrated Door Opening Assemblies
Section 087100	Door Hardware
Section 087106	Door Hardware Schedule
Section 088000	Glass and Glazing (coordinate with glazing contractor)
Section 084313	Aluminum Framed Storefronts (coordination of keying)
Section 089100	Louvers (as related to doors)
Division 26	Electrical (coordination)
Division 27	Communications (coordination)
Division 28	Electronic Safety and Security (Coordination)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Furnish only hollow metal doors, frames, vision panels, wood doors and finish hardware.

2. Keying for Aluminum Entrance doors to be coordinated and provided by this contract.

3. Keying. All lock sets. Provide Owner with a complete schedule of all keying and pin schedules as required.

4. Provide hex keys or flat keys for hardware not keyed to building hardware.

5. Provide cylinders and keying for elevator, light switches, panic bar dogging and door openers.

6. Construction door cylinders shall be provided by this contractor to the Carpentry contractor for use during construction. Plan and include the cost of providing (3) three separate levels of cylinders (green, red, blue) to allow areas to be secured separately as required by the CM. Provide (25) keys per color system.

7. All exterior Hollow Metal frames shall include a box and raceway built into the door frame for locations at the latch and hinge as required. Provide a box and raceway at the head of the frames for door contact access and installation.

8. This contractor shall pay close attention to the Alternate section of the specifications as they relate to the scope of this contracts scope of work. (Access Control System- Salto Alternate)

9. This contractor shall coordinate the hardware and door materials with the Carpentry contractor prior

to ordering materials. Including but not limited to all coordination meetings with the Owner, CM Carpentry contractor and Special Systems contractor as required to properly coordinate all doors, frames, hardware and connections, prior to ordering of materials.

10. This contractor shall deliver all materials as coordinated with the installer to the project site in an orderly organized manner. Deliveries will not be received unless the Carpentry contractor is notified and the delivery is coordinated. The Owner and EDiS will receive any materials. Additionally provide 48 hour notice prior to delivery. All deliveries are to be between 7:00 AM and 3:30 PM (allow time for check in of all hardware when scheduling)

11. Provide field assistance to Electrical and Carpentry Contractor as required to facilitate the installation of the materials supplied by your course of work.

12. This contractor to coordinate with the Special Systems contractor and Electrical contractor to ensure that all cut outs, plates, receiver etc. that are required to be built into your doors and frames are fully coordinated. In person attendance at review and coordination meetings for the doors, hardware, special systems, raceway and electrical connections shall be the responsibility of this contractor.

13. As changes are made to the hardware schedule, whether due to issued ASI's, RFI's, architectural changes etc., this contractor shall make updates to the hardware schedule and re-issue so the schedule is always updated and submitted to EDiS.

14. Coordinate electrical requirements with any automatic door operations.

15. Provide harness lengths to reach above accessible ceilings. Coordination of this work and the lengths required is the responsibility of this contractor. Provide any harness adapters and connectors required allow hardware to have a splice free system.

16. This contractor shall provide all magnetic hold open hardware, including extensions as required.

17. Provide a key box system to hold up to 25% over the amount of keys being supplied.

18. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

CONTRACT NO. D-12: OVERHEAD COILING DOORS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 055000	Metal Fabrications
Section 083323	Overhead Coiling Doors
Division 26	Electrical (coordination)
Division 28	Electronic Safety and Security (coordination)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide all overhead coiling doors as required by the contract documents. To include but not limited to exterior and interior coiling doors systems. Hardware, openers, buttons and controllers required for a complete system shall be provided by this contractor.

2. Provide all overhead coiling grilles.

3. Include all wall framed openings and openings including trims, flashings, and sealants as required to perform your course of work.

4. Provide additional supports for overhead coiling doors. Structural members identified on the structural drawings are not part of this contract scope. Provide ancillary steel, connectors, all thread and other misc. items as required. Coordinate all electrical and special systems requirements for work of this contract with the appropriate contractors. Provide keyed switches for both electric and low voltage to match building keying.

5. Keying coordination for all lock sets. (coordinate with same hardware system as Dor Hardware supply contract..

6. Coordinate electrical requirements with any automatic overhead door operations.

7. Provide low-voltage wiring required for overhead doors automatic door operations. Include all raceways, boxes and switches required for a complete installation.

8. Ensure that all garage doors fully open the entire height of the door opening and close with the bottom edge touching the ground. Garage doors will fit square in the openings with no gaps along the top, bottom or sides when the door is closed.

9. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

10. Provide all sensing and safety devices as specified for each assembly to provide a complete assembly.

11. Exterior overhead doors and grilles shall have the appropriate specified seals, and weatherstripping at all edges. Top, sides and bottom. Seals shall maintain water tightness when installed.

12. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

13. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-13 - CURTAIN WALL/GLAZING/STOREFRONTS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 054000	Cold Formed Metal Framing (coordination)
Section 055000	Metal Fabrication (as required for work)
Section 072500	Weather Barriers
Section 079100	Preformed Joint Sealants
Section 079200	Joint Sealers
Section 089100	Louvers
Section 084313	Aluminum Framed Storefronts
Section 084333	Folding Glass Storefronts
Section 084413	Glazed Aluminum Curtain Walls
Section 084523	Translucent Wall Assemblies
Section 008710	Door Hardware
Section 088000	Glazing
Section 088723	Safety and Security Films
Division 26	Electrical (coordination)
Division 28	Electronic Safety and Security (coordination)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide curtain wall, storefront, glass and glazing systems, Fiberglass Sandwich Panel Systems, complete.

2. Provide all Safety and Security Films required by Section 088723 and the contract documents.

3. Provide aluminum door systems and handling.

4. Provide automatic aluminum door systems, including hardware, low voltage wiring, coordination of power and all hardware. Coordinate with Division 26 and Division 28 for access of their work in to your framing system.

5. All work of this contract shall be coordinated thoroughly with Division 26 Electrical and Division 28 Electronic Safety and Security.

6. Curtain wall systems complete, including all Delegated Design requirements required to provide a complete system. Coordinate your work with the envelope systems and contractors to insure sealing of the units for a tight seal. (pressure caps and Blueskin seals)

7. Furnish hardware for aluminum doors only. (all other finish hardware by Door and Hardware contract. (coordinate the keying and keying systems, including card reader systems)

8. All glass and glazing at exterior of building.

9. Caulking related to storefront doors and curtain wall systems.

10. Mock-ups as required by the Drawings and Specifications.

11. Custom breakmetal trim and infill.

12. Hoisting/scaffolding/cranes and all other material handling or access equipment. This contractor owns all material and manpower handling.

13. Coordinate edge of slab tolerances and field verify all rough openings. Field verification of edge of slab details is required by this contractor.

14. Provide all caulking and sealants, including any Preformed Sealants, required for your systems. All exterior caulking of your system and caulking to adjacent exterior surfaces by this contractor. The caulking and Sealant contractor shall caulk interior surfaces to your Alum frames.

15. Provide interior glass and glazing systems. Coordinate with the door and frame contractor and carpentry contractor.

16. Interior door, partition, vision panel and window glass.

17. Caulking and sealants related to interior glazing.

18. Do not provide interior hollow metal or hardware. These items will be provided by the Door and Hardware contractor.

19. Any openings that are missing glass (due to this contractors issues) during construction shall have plywood installed to secure and weatherproof the building by this contractor.

20. Clea up of all trash and debris related to this contract shall performed daily and removed to the dumpsters. All material shall always be stored neatly and orderly.

21. Coordinate glass types with partition and door fire ratings. Contact Construction Manager with any discrepancies. Shop drawings, samples and product data must be submitted within 3 weeks after award of contract.

22. This contract shall coordinate and work with the Special Systems contractor to allow the installation of harnesses, whips and connections while installing frames and hardware.

23. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

24. Include within this contracts base bid an allocation of $35,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-14 – TILING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 090561	Common Work Results for Flooring Preparation
Section 093000	Tiling

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide ceramic tile, marble tile, quarry tile, base material and thresholds as required by the contract documents, complete.

2. Provide all mortar bed installations as directed by the specifications and drawings.

3. Grout, including Epoxy grout and custom colors as specified.

4. Cutting and fitting around work installed by others.

5. Provide waterproofing and crack-isolation systems as required by contract documents.

6. Precast mop receptors as per contract documents.

7. Patching and leveling of "new" concrete system to be included in this contracts base bid. Contractor to review concrete floor installations and report any deficiencies in tolerance prior to mobilizing for any tile installation. Float inconsistent defects as needed to bridge tile for wall assemblies receiving wall tile.

8. Provide protection of finished products until acceptance by Construction Manager. This contract shall include the material and labor to cover all ceramic tile areas with Ramboard panels (not roll material or corrugated plastic panels. Seams to be taped and sealed for effective protection.

9. Attic stock, delivered and unloaded into owner storage room.

10. Provide crack suppression membrane for this set tile installation.

11. This contractor to coordinate work of this contract with contractor installing cement backer boards to receive your tile.

12. Provide metal strips and Schluter strips installed as part of the tile installation.

13. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or

equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

14. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

15. Include within this contracts base bid an allocation of $15,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-15 - ACOUSTICAL CEILINGS AND SPECIALTY CEILINGS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 072100	Thermal Insulation
Section 079200	Joint Sealants
Section 095100	Acoustical Ceilings
Section 095420	Specialty Ceiling Systems
Section 098400	Acoustical Room Components

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide complete acoustical ceiling systems to include suspension system, hangers and all required components for a complete system.

2. Provide specialty ceiling systems complete, including framing, supports and necessary components.

3. Provide acoustical wall treatments and acoustical room components complete.

4. This contract includes all Sound Reflecting Tiles, Sound Diffusing tiles, Suspension grids, struts, metal panel ceiling systems and architectural metal wall panel systems. Provide cutting, fitting and coordination with MEP trades for outlets, grilles, cable access etc.

5. Acoustical lay in insulation blankets and rigid panels above ceilings and behind wall grid systems as identified in the contract documents.

6. Supplemental suspension hangers at large ducts above ceilings and at openings for lighting fixtures shall be provided and coordinated to minimize exposed clips, anchors, and wires.

7. Continuous acoustical sealant on back of vertical leg before installing moldings as indicated.

8. Furnish and install hold down clips where required by governing regulations for fire resistant ratings.

9. Provide all material handling, scaffolds, lifts, Spyder cranes, access to work etc. as required for the scope of this contracts work.

10. Expansion joints for all acoustical ceilings, specialty ceilings and acoustical systems.

11. Provide ceiling grid layout on floor for cassette and duct placement in ceiling grid system.

12. This contractor shall review all documents, shop drawings, plans, and drawing model for ceiling height issues. All issues shall be reported to the EDiS prior to installing wall angles.

13. Reflected ceiling layout plans and shop drawings for approval and installation must be provided for all ceiling systems, clouds, acoustical panels, metal wall systems, etc.

14. This Contractor shall cut openings in ceilings for sprinkler heads, lights, mechanical diffusers and grilles, etc. Coordinate work with other trades.

15. Coordinate with other trades for layout and install of their materials into the grid system provided by this contract.

16. Attic stock as per the contract documents, delivered, inventoried, and moved to a storage area within the building at the owner's direction.

17. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

18. Include within this contracts base bid an allocation of $20,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner via credit change order.

CONTRACT NO. D-16 - FLOORING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 090561	Common Work Results for Flooring Preparation
Section 096500	Resilient Flooring
Section 096813	Tile Carpeting
Section 096816	Sheet Carpeting
Section 096933	Low-Profile Fixed Height Access Flooring

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide flooring in accordance with the contract documents.

2. Prepare subfloor for finished flooring including leveling and patching. Base bid shall include all flashing patching and surface preparation required to perform the work of this Contractor.

3. Provide all Resilient flooring, LVT, Sheet vinyl, rubber tile, rubber treads, rubber base, resilient base, carpeting, carpet tile complete.

4. Provide Low-Profile fixed height access flooring system, complete.

5. Provide all moldings, transitions and edge strips as required.

6. Provide recessed flooring systems at specified areas, to include a shop drawings for approval, recessed floor system, carpet inset and required attic stock materials.

7. Resilient transition and reducer strips at edges of resilient flooring and at edges of carpeting.

8. Cleaning and protection of floors after installation shall be required by the cope of this contract.

9. Seaming diagrams are required to be submitted for approval.

10. Provide mock up's as defined by the contract documents.

11. Attic stock to be delivered to the site, inventoried and then moved to a storge are within the building at the direction of the owner.

12. This contractor shall own all material handling and means to unload, move and lift materials to second floor locations.

13. Provide entrance mat systems complete.

14. Provide finish floor material in elevator cab as specified.

15. Provide cutting and fitting around work of others.

16. This contractor shall protect the adjacent work of other trades while performing the scope of this contract.

17. Include within this contracts base bid an allocation of $15,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-17: RESILIENT ATHLETIC FLOORING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 090561	Common Work Results for Flooring Preparation
Section 096566	Resilient Athletic Flooring

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide flooring in accordance with the finish schedule and specifications.

2. Provide resilient athletic flooring, base, and associated striping, logos, sealants etc.

3. Provide moisture level testing and reporting as part of this contract scope.

4. This contract includes removal of curing and sealing coatings that may be incompatible with the flooring adhesives of your product. Shot blasting, grinding or any required floor preparation is the responsibility of this contractor.

5. Prepare subfloor for finished flooring including leveling and patching. Base bid shall include all flashing patching and surface preparation required to perform the work of this Contractor. This shall include any moisture barriers that may be required.

6. Provide required flashing and transitions to adjacent materials. This include ramping of existing concrete floor if required for the fit and completeness of the Resilient Athletic Flooring system.

7. Provide cleaning, sealing and protection. Protection will be with Ramboard Pro panels with taped seams or Masonite with taped seams. Cover floor immediately after installation.

8. Seeming diagrams, and shop drawings for approval/installation.

9. Include within this contracts base bid an allocation of $15,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner via credit change order.

CONTRACT NO. D-18 - RESINOUS MATRIX TERRAZZO FLOORING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 090561	Common Work Results for Flooring Preparation
Section 096623	Resinous Matrix Terrazzo Flooring

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide vapor retarding sealer prior to terrazzo application' include required cost in this contracts base bid.

2. Provide all thresholds, reducers etc. as required to perform the work of this contract.

3. Prepare subfloor for finished flooring including leveling and patching. Include in the base bid, leveling and patching as per the manufacturer's recommendations for the resinous terrazzo flooring. Include shot blasting, grinding, and moisture barriers as required for a complete installation.

4. Provide moisture vapor treatment on all slabs on grade.

5. Provide crack suppression membrane as required. Crack suppression, control joints and expansion joints shall be clearly identified in a shop drawing of all Terrazzo areas for design team approval.

6. Provide standard and custom samples for approval. Include three (3) in-field mock ups for final selection and approval.

7. Prep all floors for terrazzo application per manufacture and industry standard.

8. Cutting and fitting around work installed by others.

9. Provide protection of finished products until acceptance by Construction Manager. Protection shall RamBoard pro Sheets with Ram tape.

10. Attic stock, delivered, unloaded and moved to owners storage area within building.

11. Protection of surrounding surfaces and work of others.

12. Provide joint sealants required for Terrazzo installation.

13. Protect materials from damage and contamination in storage or delivery, including moisture, heat, cold, direct sunlight, etc.

14. Maintain temperature of storage area between 60 and 80 degrees F (15 and 26 degrees C).

15. Keep containers sealed until ready for use.

16. Provide sound concrete surfaces free of laitance, glaze, efflorescence, curing compounds, form-release agents, dust, dirt, grease, oil, and other contaminants incompatible with Resinous Terrazzo materials. Include all bead blasting required to perform the work of this contract.

17. Close spaces to traffic during Terrazzo application. Coordinate traffic on unpolished Terrazzo with CM and construction schedule.

18. Maintain proper ventilation of the area during application and curing time period.

19. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

20. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

21. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

22. Contractor must provide additional crews as needed to maintain the project schedule.

23. Provide pricing for all alternates as described in Section 012300-Alternates.

24. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-19 - FLUID-APPLIED FLOORING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 079200	Joint Sealants
Section 090561	Common Work Results for Flooring Preparation
Section 096700	Fluid Applied Flooring

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide fluid-applied flooring and integral base.

2. Provide mock-ups as required by plans and specifications.

3. Provide standard and custom color samples for review and approval.

4. Provide vapor retarding sealer prior to resinous application, as required by specifications or manufacturer's installation instructions.

5. Provide protection of work of others as well as cutting and fitting around work installed by others.

6. Patching and leveling of areas to receive resinous flooring to be included in the base bid of this contract.

7. Provide cleaning, finishes and protection. Protection shall be RamBoard Pro sheets with Ram tape. Provide protection of finished products until acceptance by Construction Manager.

8. Provide crack suppression membrane required for the work of this contract. The submitted shop drawing for the Resinous Flooring areas shall reflect all control joints, expansion joints and crack suppression locations for review and approval.

9. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

10. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

11. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records

of exposure.

12. Contractor must provide additional crews as needed to maintain the project schedule.

13. Provide multiple out of sequence installations. Each area shall be considered a separate mobilization and all costs shall be included in the base bid.

14. Provide pricing for all alternates as described in Section 012300-Alternates.

15. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-20 - PAINT AND VWC

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 079200	Joint Sealants
Section 099113	Exterior Painting
Section 099123	Interior Painting

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide all painting and vinyl or fabric wall covering (all walls and ceilings indicated on the finish schedule) include all preparation of surfaces, trims and finish wood locations.

2. Provide sealing of all interior joints between dissimilar materials that require sealants before painting.

3. This contractor shall provide "all" interior and exterior painting complete.

4. Paint all exposed block work and concrete work as shown on the room finish schedule and contract documents. Include painting of the elevator shaft from F.F. down to the bottom of pit (white)

5. Prime, stain or seal, all wood trim and doors as required by the contract documents.

6. Paint exposed piping (sprinkler, plumbing, gas piping, electrical) and ductwork in accordance with the contract documents. Include preparation work for all items specified. Review and coordinate any color requirements specified in the contract documents or as required by code. Pay close attention to MEP documents for specific locations of piping colors.

7. Provide supplementary ventilation as required in enclosed spaces.

8. Paint and caulk all hollow metal frames and doors as shown on the door schedule.

9. Paint metal stairs and railings.

10. Prefinished items will not be painted by this Contractor.

11. Paint all semi-exposed wood blocking as indicated on the drawing.

12. Include "preparation" of all surfaces and items required to be covered by the scope of this contract.

13. This contractor shall allow a touch up pass from drywall contractor/mason contractor between prime coat and first coat of finish.

14. Protection of adjacent surfaces required by this contractor.

15. Minor patching prior to application of finishes shall be included in the base bid.

16. This contractor shall provide sealing/hardener of concrete floors, including scraping, brushing, removal of markings, grease, foreign materials and thoroughly cleaning all the floors prior to installation of the sealer/hardener materials. Coordination with other finishes will require multiple mobilizations for the sealer/hardener preparation and installation. Include within your base bid a (6) additional mobilizations for this work.

17. Installation of rated wall identification to be provided by this contractor. Access, lifts, ladders etc. to be provided by this contractor.

18. Provide painting of all exterior bollards and gates that are not prefinished.

19. Paint gas lines at both the interior and exterior of the building.

20. All lintels shall be painted by this contractor.

21. Paint all railings and handrails that are not prefinished.

22. Provide cleanup of your work areas and storage areas on a daily basis. Removal of spent paint cans and buckets is the responsibility of this contractor.

23. This contractor shall protect all areas, materials and work of others from over-spray from the work of this contract.

24. This Contractor to allow 240 man hours and all required paint materials for these man hours to be used as directed by the Construction Manager.

25. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

26. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

27. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

28. Contractor must provide additional crews as needed to maintain the project schedule.

29. Provide pricing for all alternates as described in Section 012300-Alternates

30. Include within this contracts base bid an allocation of $20,000 for work to be determined by owner and

construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-21 - WOOD STRIP FLOORING - GYM FLOORING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 062000	Finish Carpentry (coordination of work)
Section 079200	Joint Sealants
Section 090561	Common Work Results for Flooring Preparation
Section 096429	Wood Strip Flooring

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide complete gymnasium floor system including sleepers, base, plywood, finishes, transitions, and striping (including logos). Flooring installation shall be coordinated and installed so the integrity of the concrete floor is not impacted. Include within your base bid a penetrating water/vapor sealer application prior to starting the Gym floor assembly.

2. Provide underfloor ventilation fan as required by the specification or manufacturer's requirements. Power connection provided by the electrical contractor, all interconnection wiring or low voltage work to complete work shall be provided by this contractor.

3. Provide wood strip flooring, hardboard floors in, and accessories at all areas indicated by the contract documents. This contract to provide all stage flooring and the required painting.

4. Provide wall base and trims associated with wood strip flooring.

5. Coordination with the bleacher contractor and other trades with the installation of the wood floor.

6. This contractor shall include patching and leveling of low areas identified after the slab floor analysis. The high areas will be reviewed and the concrete contractor will be responsible to adjust.

7. Sealants and caulking associated with your course of work shall be provided by this contractor.

8. Provide thresholds as required to finish your course of work. Threshold locations and types shall be submitted for Owner/Design Team approval.

9. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

10. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

11. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

12. Moisture and humidity readings are the responsibility of this contractor, monitoring and reporting results will be required. Results shall be provided each day in your daily reports, with photos of measuring device and reading. In addition provide the CM with a separate set of humidity sensors and a testing device for concrete floor moisture content.

13. All work to be coordinated with the carpentry contractor installing the gym equipment. Sequencing and timing shall be discussed and agreed to by this contractor.

14. Contractor must provide additional crews as needed to maintain the project schedule.

15. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

16. Provide pricing for all alternates as described in Section 012300-Alternates.

17. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-22 - SPECIALTIES

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 061000	Rough Carpentry
Section 062000	Finish Carpentry
Section 079200	Joint Sealers
Section 101101	Visual Display Boards and Display Cases
Section 102113.19	Plastic Toilet Compartments
Section 102123	Cubicle Curtains and Track
Section 102600	Wall Protection
Section 102800	Toilet Accessories
Section 104400	Fire Protection Specialties
Section 105100	Metal Lockers
Section 107316.13	Metal Canopies

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following: (provide ad install)

1. Provide an install all specialties listed within this contract specification sections and scope.

2. Provide White boards, Markerboards (including glass markerboards), Chalk boards, tack boards, and tack strips.

3. Provide display boards and display cases.

4. This contractor shall own providing, engineering and installation of the Metal Canopies Section 107316.13. Coordinate all work with other trades.

5. Provide Projection screens if identified on documents. Electric service is the responsibility of the Electrical Contractor. All other control wiring, raceways and special boxes as specified will be the responsibility of this Contractor.

6. Provide Lockers including lockers bases that are not identified as “concrete bases”(concrete locker bases provided by the Misc. Concrete and Grouting contract.)

7. Provide Toilet partitions. Coordinate any structural requirements with the structural steel and blocking requirements with the Carpentry contractor.

8. Provide toilet and bath accessories, complete. This contract shall include installing all owner supplied toilet accessories and specialties.

9. Provide all accessories as indicated on the contract documents.

10. Provide Fire extinguishers, cabinets and accessories. Include labeling of extinguishers and cabinets. Coordinate with other trades for opening size and placement.

11. Provide Vertically Retractable Walls coordinate any structural requirements with the structural steel and carpentry contractors. Provide all supplementary steel as needed to hang partitions from structural support steel, provided by the Structural Steel Contractor. It is assumed, no additional steel will be required below structural support steel. If so, it will be provided by this contractor.

12. Provide all signage and plaques (interior and exterior.)

13. Provide wall and corner protection. Including FRP Paneling.

14. Provide Mirrors (both framed and frameless.)

15. Verification of field dimensions is the responsibility of this Contractor.

16. Anchoring devices, fasteners, inserts and other related items associated with the installation of the above items.

17. All blocking and bracing requirements for all work of this contract shall be coordinated with the Carpentry contractor for correct installation of blocking etc. Include any blocking not specified to be provided by the carpentry contractor.

18. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

19. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

20. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

21. Provide hand dryers and installation, electrical power connection by electrical contractor.

22. Contractor must provide additional crews as needed to maintain the project schedule.

23. This contractor shall include within their bid the incorporation of **500 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5

24. Provide pricing for all alternates as described in contract documents.

25. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA

requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

26. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

27. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

28. This contractor shall be on site to coordinate when walls are being installed for penetrations and sleeve installations. If penetrations and sleeves are missed, this will be the responsibility of this contractor to cover associated costs of fixing.

29. Provide $20,000 allowance to be used as directed by the owner and CM. All funds not expended will be returned to the owner via a credit change order by means of a credit change order.

CONTRACT NO. D-23 - FOOD SERVICE EQUIPMENT

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 11400	Food Service Equipment
Division 22	Plumbing
Division 24	HVAC
Division 26	Electrical

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide food service equipment, hoods, connective ductwork and accessories All final connections shall be made by the Electrical and Mechanical Contractors.

2. Any discrepancies between the Drawings, Specifications and site conditions or ambiguities in the documents shall immediately be reported to the Construction Manager in writing. Inconsistencies shall be corrected in writing or by reissuing the drawings. If the Contract Documents disagree with the quality or quantity of work required, the better quality or greater quantity shall be supplied unless otherwise instructed in writing by the Construction Manager. Any work performed by the Contractor at locations in question after his discovery of discrepancies, inconsistencies, ambiguities, or errors, without securing resolution, shall be at the Contractor's risk.

3. This Contractor shall verify all measurements at the site and assume full responsibility for their correctness before proceeding with his work. No extra compensation will be allowed because of differences between site conditions and those indicated on the drawings.

4. Manufactured articles, materials, and equipment shall be applied, installed, connected, erected, used, cleaned and conditioned as directed by the manufacturer and shall be protected from damage until acceptance. Prefinished products which are damaged before or after installation shall be replaced with new and perfect materials. Materials finished after installation which are damaged shall be refinished or replaced as the Construction Manager may direct. No additional charge will be honored by the Construction Manager for repair or replacement of finished materials.

5. Should this Contractor feel that the Contract Documents call for work which he cannot guarantee, he shall so state, in writing, prior to bidding. Proceeding with any operation shall be construed as acceptance of all guarantee conditions.

6. Secure certificates of inspection and occupancy required by authorities having jurisdiction. Deliver copies of certificates to the Construction Manager prior to filing application for final payment.

7. Supply and install any pedestals, curbs or doghouses required for equipment on the roof in this contract. This should be a finished product so the roofer can flash to the system complete.

8. Any penetrations for work of this contract are the responsibility of this contractor whether through walls, floors or roof areas. Sealing of all penetrations (sealant, fire sealant or otherwise) and coordination with others is part of this contract.

9. This contractor shall include any blocking requirements required on a drawing that shall be coordinate with the carpentry contractor for blocking installation.

10. This contractor is responsible to make field visits to review rough in of underground utilities/piping/electric conduit, for placement in relationship to equipment locations.

11. This contractor to provide complete hood assemblies, including the hood fire protection assembly (Ansul) complete.

12. This contractor shall coordinate and provide assistance to the electrical, fire alarm and controls contractor for interconnection into your hood assemblies and attached equipment.

13. Provide technicians on site to test all systems, hoods, equipment in advance of any required inspections.

14. This contractor is to accept delivery of their equipment and supplies, CM will not receive and unload equipment. Provide any and all material handling and unloading equipment and man power.

15. It is this Contractor's responsibility to make certain statutes, building codes, and regulations including those of the appropriate health agencies having jurisdiction over this type of facility are met.

16. Any items furnished as part of this Scope of Work that require mechanical or electrical rough ins or services that are different from those shown on the Contract Drawings shall be so noted at the time of bid. Failure to do so shall make this Contractor liable for costs of any changes required by same.

17. Provide all caulking and sealants for proper installation and in accordance with public health regulations. This contractor provides caulking ad sealants for your own curse of work.

18. Start, test and demonstrate all equipment installed under this category of work. Provide proposed schedule, including names and telephone numbers of attending representatives (3) three weeks in advance of demonstration.

19. Obtain approvals and permits and coordinate inspections and testing with governing local and state agencies.

20. This contractor shall provide factory start up of all equipment and the reports to document the start up's. CM to receive reports following start up.

21. (2) preliminary inspection or walk through of the project with the Health Department is to be include within this contracts scope.

22. This contractor to provide and install all low voltage capacitors, contactors etc. and requited connections to allow the kitchen hood system to communicate and interface with the fire alarm system and exhaust systems. Electrical contractor to provide power connection to units.

23. This Contractor shall verify all measurements at the site and assume full responsibility for their correctness before proceeding with his work. No extra compensation will be allowed because of differences between site conditions and those indicated on the drawings.

24. Provide protection of all equipment during and after installation has been completed.

25. Provide coordinated shop drawings that indicate all MEP requirements and accurately reflect the actual conditions and spacing of the area.

26. All foodservice components consist of those items identified in Section 114000 and the "K" Series drawings that identify the Food Service items. All items are to be included in the base bid of this contract to completely provide all systems in their entirety. This contractor shall pay particular attention to the "Standard Details" section of typical drawings within Specification section 114000.

27. Any items furnished as part of this Scope of Work that require mechanical or electrical rough ins or services that are different from those shown on the Contract Drawings shall be so noted at the time of bid. Failure to do so shall make this Contractor liable for costs of any changes required by same.

28. Provide licensed electrician to make all interconnections within equipment furnished by this contractor. This includes, but is not limited to, power and control wiring interconnecting the kitchen hoods and make-up air units provided by the mechanical contractors.

29. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

30. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

31. Include within this contracts base bid an allocation of $15,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of credit change order.

CONTRACT NO. D-24 - WINDOW SHADES AND ROLLER SHADES

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 061000	Rough Carpentry
Section 062000	Finish Carpentry
Section 122400	Window Shades
Section 122413	Window Treatment – Roller Shades

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide window shades and rollers shades complete.

2. Do not fabricate shades until field dimensions for each opening have been taken.

3. Do not install shades until final surface finishes and painting are complete.

4. Provide manual window shades as indicated on the contract documents.

5. Do not install roller shades until construction and finish work in spaces, including painting, is complete and dry and ambient temperature and humidity conditions are maintained at the levels indicated for Project when occupied for its intended use.

6. Field Measurements: Where roller shades are indicated to fit to other construction, verify dimensions of other construction by field measurements before fabrication and indicate measurements on Shop Drawings. Allow clearances for operating hardware of operable glazed units through entire operating range. Notify Architect of installation conditions that vary from Drawings. Coordinate fabrication schedule with construction progress to avoid delaying the Work.

7. Do not install shades until construction and finish work in spaces, including painting, is complete and dry and ambient temperature and humidity conditions are maintained at the levels indicated for Project when occupied for its intended use.

8. This contractor shall include any blocking not identified or specified in the Carpentry contractors scope.

9. Provide all material handling and access equipment required for your work. Including scaffolds and lifts as necessary. CM will not receive or unload an of this contracts materials.

CONTRACT NO. D-25 - LAMINATE CLAD CASEWORK, COUNTERTOPS, AND SILLS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 062000	Finish Carpentry
Section 079200	Joint Sealants
Section 123400	Manufactured Plastic Laminate Casework
Section 123600	Countertops, Backsplashes and Window Stools

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide labor and materials to perform the work related to all casework, millwork, counter tops, back splashes and window sills. Coordinate rubber base after installation with flooring contractor.

2. This contractor shall provide all plastic laminate and millwork required in the Auditorium. This shall include panels, sills, casework etc. as detailed in the contract documents.

3. Provide all SS Tops, trims and accessories as required by the contract documents.

4. Provide all field trimming required to adjust to conditions on site.

5. Coordinate power and data requirements and locations with the electrical contractor for locations and sizes of holes needed. Grommets provided by this contractor.

6. Include all venting of cabinets and casework as indicated in the contract documents.

7. Provide solid surface window stools, wood trim, aprons, wood veneer paneling, and plastic laminate veneer paneling.

8. Provide solid surface base.

9. Provide countertops and backsplashes

10. Coordinate cutting holes in casework with other trades, and provide grommets at all openings.

11. Coordinate blocking requirements with Carpentry contract.

12. Provide joint sealants integral to casework/millwork and to dissimilar materials.

13. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

14. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

15. This contractor shall include within their bid the incorporation of **1000 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5

16. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

17. Contractor must provide additional crews as needed to maintain the project schedule.

18. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

19. Provide pricing for all alternates as described in Section 012300-Alternates.

20. Include within this contracts base bid an allocation of $15,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

21. This contractor shall coordinate the installation of the Fume hood assembly with the HVAC contractor who is providing this work.

CONTRACT NO. D-26 - STAGE RIGGING, LIGHTING, AND ACCESSORIES

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 116133	Rigging Systems and Draperies
Section 111663	Loose Performance Lighting Fixtures

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide a complete theatrical rigging system as specified in Section 116133. Provide layout drawings and coordinate with electrical contractor for requirements of stage lighting and electric. This contract is responsible for any supplemental and miscellaneous steel/support required beyond the structural steel shown in the structural drawings to provide a complete and operational rigging system.

2. Provide theatrical draperies, operating systems, control wiring, motors etc. required to provide a complete system.

3. Provide Loose Lighting Fixtures and all low voltage wiring, motors, and controls to make system operational.

4. Provide (4) sets of any keys required to operate systems installed.

5. Provide specified warranties, attic stock, and as-builts. All attic stock to be delivered, inventoried, and delivered to a storage area on site directed by the owner.

6. Provide stage lighting systems including fixtures, controls, wiring, light grids, supports and attachments. Provide any Unistrut, support rods or other required anchoring devices for lighting support in theater. Coordinate work with electrical contractor for power connections.

7. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

8. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

9. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

10. Provide BIM services as detailed in spec section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

11. Contractor must provide additional crews as needed to maintain the project schedule.

12. Provide pricing for all alternates as described in Section 012300-Alternates.

13. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-27 - FIXED AUDITORIUM SEATING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 126113	Fixed Audience Seating

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide seating layout, numbering, shop drawings, product data, samples, etc.

2. Provide Fixed, Removable, and loose audience seating as detailed in the drawings and section 126113. Coordinate finishes, coverings, colors, mounting, etc. between the fixed and loose audience seating.

3. This contractor responsible for their own layout and drilling of anchors for fixed seating. After installation, each day the area shall be cleaned of concrete dust, debris, boxes, packing materials etc. All materials must go to dumpster each day. Provide dimensioned layout drawings for lighting box layout for chairs.

4. Provide specified warranty, attic stock, and as-builts. Attic stock shall be delivered, inventoried and move to a storge location on site as directed by the owner.

5. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

6. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

7. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

8. Provide BIM services as detailed in spec section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

9. Contractor must provide additional crews as needed to maintain the project schedule.

10. Provide pricing for all alternates as described in Section 012300-Alternates.

11. Provide a final clean, vacuuming and wipe down of all seating and support brackets by this contractor. Coordinate scheduling of this work with CM.

12. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-28 - TELESCOPING BLEACHERS AND PLATFORMS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 061000	Rough Carpentry
Section 079200	Joint Sealers
Section 126613	Telescoping Bleachers
Section 126623	Telescoping Chair Platforms

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide all Telescoping Bleachers and Telescoping Chair Platforms as required by the contract documents.

2. Provide bleacher seating systems. Coordinate electrical requirements with electrical contractor. Low voltage wiring, motors and controls are to be provided and installed by this contractor. Power supply will be supplied by electrical contractor.

3. This contractor shall coordinate all work of this contract with the carpentry contractor and wood flooring installer.

4. Protection of the work of others including but not limited to protection of all finished flooring installed before your scope of work can be installed. Protection of the flooring shall be reviewed with the CM before installation.

5. Verification of field dimensions is the responsibility of this Contractor.

6. Anchoring devices, fasteners, inserts and other related items associated with the installation of the above items. Provide all material handling and access equipment required for the scope of your contract.

7. All material handling. Loading, moving, lifting of the materials of this contract shall be the responsibility of this contractor. The CM will not receive or unload your materials.

8. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

9. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

10. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

11. Provide BIM services as detailed in spec section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

12. Provide pricing for all alternates as described in Section 012300-Alternates

13. Include within this contracts base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-29 - HYDRAULIC HOLELESS PASSENGER ELEVATOR

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 142013	Hydraulic Holeless Passenger Elevator
Division 26	Electrical (power and communications)
Section 284621	Addressable Fire Alarm Systems (coordination)
Section 281100	Access Control Systems (coordinate elevator access controls)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide hydraulic elevator system complete. Including all shaft anchoring, framing and Misc. steel required to install the elevator.

2. Grouting of all elevator sill angles will be the responsibility of the Misc. Concrete contractor Contract D-43.

3. Spyders for elevator shaft installation shall be delivered to the site when required by the BP-C Masonry contractor.

4. Coordinate and work directly with the fire alarm contractor to meet all local, state, fire marshal and elevator inspector requirements.

5. Before the owner accepts the elevator for substantial completion, the elevator contractor shall train the owners maintenance personnel on operation of the elevator and review the contact operation and protocol for elevator service, warranty claims, etc. The training shall be professionally videotaped as part of the warranty package.

6. Provide control wiring and telephone signal wiring to top of elevator shaft as required.

7. Provide (2) sets of elevator protection padding, in addition to all other attic stock specified by contract documents. Provide CM one of these sets for use during construction.

8. This Contractor to furnish and install all rough wiring, low voltage wiring and devices (phones) necessary for the installation of emergency telephones.

9. Electric service and disconnect switch for the elevator are the responsibility of the Electrical Contractor. (This contractor shall work with electrical to coordinate type of disconnect with Fire Marshal and Elevator Inspector before installation) All other control wiring as required will be the responsibility of this Contractor.

10. This Contractor to submit for approval the layout and detailed dimensions of the elevator pit area, sump pump area, etc.

11. Provide BIM services as detailed in spec section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

12. Provide and include warranty extensions to include 9 months of temporary construction use. This contractor to include within the base bid 600 hours of temporary elevator operator to be utilized at the discretion of the owner and CM.

13. Include the costs associated with the inspections required for "construction" use in your base bid.

14. This contractor will work with other trades to insure access is given as needed to complete all work for a complete installation. This includes lifting contractors to the top of the shaft to complete work required. This includes but is not limited to fire sealing, sprinkler heads, lighting, smoke detectors, disconnects etc. Include within the base bid 4 separate mobilizations and 8 hours of operator time to allow contractors to access the shaft for work that requires installation.

15. This contractor shall own fire sealing of all penetrations for work of this contract.

16. This contractor to owns coordinating the final keying to the owners keyed system.

17. Provide all temporary signage required for machine room or elevator I order to facilitate inspections, until completion and final signage is installed.

18. Provide (2) complete sets of tools and keys to the owner. Provide and install key cabinet in the machine room, keyed to the building system for use by the owner to store the elevator keys.

19. Provide full and complete coordination with other trades for installations within the elevator shaft and machine room.

20. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

21. Include within this contractor's base bid an allocation of $10,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-30 - FIRE PROTECTION

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Division 22	Plumbing
Division 26	Electrical
Division 32	Site Improvements
Section 312300	Excavation and Backfill for pipelines and Structures
Section 03310	Cast in Place Concrete
Section 210500	Common Work Results for Fire protection
Section 210505	Fire Suppression System Piping, Fittings and Valves
Section 211000	Water Based Fire Suppression System- Fire Pump

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide piping, fittings, couplings, valves and sprinkler heads to provide a complete Fire Protection system.

2. The fire pump, and all related work shall be part if this contract.

3. Excavation and backfill related to fire protection work as detailed below is the responsibility of this Contractor. (Geo-Tech reports included for this contractors review)

4. Backfilling is the responsibility of this Contractor. Soil types shall be in accordance with project documents. Backfill materials shall be covered after excavation and protected. If materials become wet and unusable this contractor shall remove the material from site and provide stone dust (#10 stone dust) to backfill all piping trenches and remove unsuitable material off site.

5. Provide As-built drawings in both hard copy and BIM format.

6. Provide concrete equipment pads, curbs and thrust blocks related to the Fire Protection work (sprinkler system) and Fire Pump system.

7. Permits, testing, inspections required for the Fire Protection work are to be provided by this contractor.

8. Providing of sleeve assemblies for work of this contract that penetrates the foundation wall, interior footings or any concrete footings shall be provided to the masonry and concrete contractor for installation. This contractor shall coordinate and assist with the sleeving install. Sleeves are to be sealed per contract documents.

9. Firesafing of all penetration is a requirement of this contract.

10. Design of the system, submissions to the Fire Marshall, review with Fire Marshall and expediting the permit for the Fire Suppression system is a priority of this contract scope.

11. Flow and tamper switches to be supplied by this Contractor and wired by the Electrical Contractor. It is this Contractors responsibility to provide flow and tamper switches to meet applicable state and local codes as well coordinate with the MEP contract documents.

12. Fire pump, controller and related work. Wiring of pump and controller to be by the Electrical Contractor.

13. If a water meter is required when the review process and permitting is completed, this contractor shall purchase, pay for, install and coordinate all work with the required authorities.

14. This Contractor to coordinate the need for and compatibility of his system to the emergency generator, supplied by other.

15. Pipe identification and labelling is a requirement of this contract. Valve labels, etc. are required as per the contract documents.

16. Provide fire main from +/- 5 feet outside building including connection in the building. Final connection of your fire line and the line provided by the site contractor shall be the Fire Protection contractors responsibility. Provide a registered plumbing contractor licensed to perform the tie in as part of you base bid.

17. This contractor will flush the UG system with the assistance of the site contractor and provide written documentation to the CM.

18. All cored walls require sleeves and are required to be sealed per contract documents. Any mess from the coring operation shall be immediately cleaned up by this contractor and shall not affect any installed finishes. If this work is not performed efficiently, the work will be performed by the owner and back charged to this contractor.

19. This contractor shall be onsite while walls are being constructed for layout and installation of valve cabinets, concealed, piping, etc.

20. The work of this contract will require out of sequence installations. This should be considered and included in your base bid.

21. This contractor shall provide all access panels required for the work of this contract. They should be lockable, fire rated where required. Panels shall meet the requirements of the contract documents.

22. This contractor shall include within their bid the incorporation of **750 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5.

23. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

24. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

25. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

26. Provide the necessary coordination with trades to avoid interferences with other work and make corrections at no extra charge.

27. Include within this contracts base bid an allocation of $20,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-31 – PLUMBING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Division 21	Fire Protection (coordination)
Division 22	Plumbing
Division 23	HVAC (coordination)
Division 26	Electrical (coordination)
Division 32	Site Improvements
Section 312300	Excavation and Backfill for pipelines and Structures
Section 03310	Cast in Place Concrete

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide a complete plumbing and piping system as indicated by the contract documents. All plumbing work/systems are to be fully coordinated with all other MEP trades as well as the other trades involved with the project.

2. This contractor shall provide all pipe insulation, insulation coverings, valve insulation, labelling, and identification of plumbing lines.

3. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

4. Division 26 of the specifications should be reviewed as it relates to the power wiring to trap primers and controls within this contracts scope of work. Coordinate this work with the electrical contractor.

5. Permits, testing, inspections required for the Plumbing system work are to be provided by this contractor. This contractor shall pay all permit and inspection fees for the work of their contract.

6. This Contractor shall be responsible to designate an individual within his organization, intimately familiar with this project and assigned on site, to act as the System Start-up Coordinator. This individual must be pre-approved by the Construction Manager. This individual's responsibilities shall include, but not be limited to, coordinating the start-up of all mechanical equipment, including the coordination between the Electrical Contractor, the Controls Contractor, and all testing, adjusting and balancing work. This individual shall report on a weekly basis, in written form, to the Construction Manager. These reports shall include a summary of current conditions including manufacturers' start-ups, systems' deficiencies noted to date and the remediation of same, coordination issues between trades, system interfacing and forecasting, as necessary to project the completion of each individual system within the building.

7. Excavation and backfill for underground plumbing work as detailed below is the responsibility of this

Contractor. Soil types shall be in accordance with the contract documents Refer Section 312300 for requirements on soils. (Geo-Tech reports included for reference and use)

8. Backfilling is the responsibility of this Contractor. Soil types shall be in accordance with project documents. It is the intent to use on site material and not imported fill. The use of this on site material shall conform with the compaction requirements identified in Section 312300. Excavated materials shall be covered immediately and protected from moisture mitigation. If Materials become unusable, this contractor shall own purchasing #10 stone dust to utilize as backfill in all trench or structure locations. Excess unsuitable materials from plumbing excavations shall be removed from the site by this contractor. (includes water meter pit installation) it is not acceptable for anu UG piping to e in the stone layer installed by the concrete contractor, all UG piping must be installed in the subbase with adequate soil coverage.

9. The Concrete Contractor shall furnish, install and maintain stone fill under slab. The Sitework Contractor shall leave the building pad site at subgrade to the required tolerance in the contract documents to receive stone fill. The Plumbing, Mechanical and Electrical contractors shall complete their work under the slab on grade and shall be responsible to return the pad to the subgrade elevation left by the Sitework Contractor. The Concrete Contractor shall then adjust the select material to final subgrade, fine grade the slab and place the vapor barrier and stone fill. Note: while working on the building pad area this contractor shall utilize track drive equipment only. No rubber tire equipment will be allowed. Preservation of the building pad shall be the responsibility of this contractor. The onsite testing and inspection agency provided the owner will monitor the excavation, travel and backfilling operation.

10. The plumbing and concrete contractor and CM will me to review the building pad for turnover to the next trade. If not accepted correction will need to be made to correct concerns and sign off.

11. Equipment bases and housekeeping pads identified on the structural drawings are to be provided by the BP-C concrete contractor. Any required bads or bases for the scope of this contract not identified on the documents will be provided by this contractor.

12. Permits, testing, inspections required for the Plumbing system work is to be provided by this contractor.

13. Providing of sleeve assemblies for work of this contract that penetrates the foundation wall, interior footings or any concrete footings shall be provided to the masonry and concrete contractor for installation. This contractor shall coordinate and assist with the sleeving install. All sleeves must be provided with the appropriate seals, this contract owns sealing the sleeves related to this contracts work.

14. Pipe insulation, insulation coverings, valve insulation, labelling and identification of plumbing lines shall be provided by this contractor.

15. Valve tags, charts, and labelling shall be part of this contractor's responsibility.

16. Penetrations through wall, floors, etc. including cutting, patching and fire safing.

17. Testing and balancing shall be provide by a separate contract however the Plumbing contractor shall coordinate and communicate with the testing and balancing contractor for all testing required on the plumbing system.

18. Clean up shall be provided daily, all trash, debris, crates, boxes etc. shall be moved out of the building to the dumpsters each day. No storage of trash will be allowed inside the building or courtyards.

19. All guarantees and warranties to begin at the substantial completion of the entire project. Maintain equipment prior to substantial completion.

20. This contractor shall provide all necessary material handling equipment, cranes, scaffolds, hoisting and rigging equipment and supplies for work associated with this contracts.

21. Coordination with the ATC contractor is required by this contractor.

22. Roof drains, pans, sumps and all related anchoring, support and adjustment elements that are required per the contract documents.

23. This contractor is responsible for providing, setting, bracing, anchoring, and aligning all floor drains, floor basins etc. required by the contract documents. The plumbing contractor shall have a plumber on site 100% of the time when the concrete contractor is pouring S.O.G. floors or elevated slabs. Drains that are misaligned will be demolished, removed, and replaced by this contractor. Including but not limited to replacing and re-engineering floor reinforcement and paying the concrete contractor to re-pour the slab areas.

24. Piping work associated with the emergency generator (including fuel piping, exhaust piping, regulators etc.). Include initial fill up of fuel tanks if Diesel and provide and coordinate the gas piping system is natural gas fueled. The DNREC permit submission will be provided by the Electrical contractor however this contractor must supply any required documentation for the permitting as well as coordinate all work with electrical contractor and other trades.

25. Fuel detection/monitoring system in accordance with local codes.

26. Gas piping, meter and pressure regulator valve. (proper sizing of the regulators is the responsibility of this contractor.) Include anchoring this equipment to the concrete pad provided by the concrete contractor ad anchoring the piping and stand to the exterior wall.

27. Trap priming system, including detailed submittals of the system and then provide as-builts of the location of the rack installations. Photos marked with locations to be provided by this contractor.

28. All utilities will be brought to within +/- 5 feet of the building line by others. The Plumbing Contractor is responsible for connecting the utilities from +/- 5 feet outside the building line and completing the system within the building. This contractor shall own the underground line with the assistance of the site contractor, including any chemical treatment required by NCCo, Artesian or any other regulatory agency. Reports shall be submitted to CM.

29. This contractor will flush the underground with the assistance of site contractor and provide documentation to CM.

30. Provide complete water sterilization, testing and reporting. Include within your proposal (4) additional testing mobilization for potential Phase utilization.

31. Install Owner pre-purchased equipment, if identified within the contract documents.

32. Provide access panels to the drywall contractor for framing information and final installation.

33. This contractor shall be on site to coordinate when walls are being installed for penetrations and sleeve installations. If penetrations and sleeves are missed, this will be the responsibility of this contractor to cover associated costs of fixing.

34. Final connection of kitchen equipment and appliances is the responsibility of this contractor.

35. As-built drawings is both hard copy and BIM submission as part of the project closeout.

36. This contractor shall include within their bid the incorporation of **2500 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5

37. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

38. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

39. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

40. Provide the necessary coordination with trades to avoid interferences with other work and make corrections at no extra charge.

41. Include within this contracts base bid an allocation of $75,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

CONTRACT NO. D-32 – MECHANICAL PIPING - HVAC

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 089100	Louvers
Division 21	Fire Protection (coordination)
Division 22	Plumbing
Division 23	HVAC
Section 230900	Instrumentation and Controls of HVAC system
Division 26	Electrical (coordination)
Division 28	Electronic Safety and Security (coordination of work)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide a complete mechanical system as indicated on the Drawings and in the Specifications. Coordinate all work with associated trades, Plumbing, Fire Protection, Electrical and Electronic Safety and Security

2. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

3. This contractor shall include all piping, fittings, and connections required for the installation of the complete HVAC system.

4. Provide all insulation, wraps, covers etc. for work of this contract. Include all labelling and identification markers as directed by the contract documents.

5. Provide all condensate piping and condensate pumps and installations. Backcheck valves shall be included as part of this contract.

6. Division 16 of the specifications should be reviewed as it relates to the power wiring and other requirements for HVAC equipment including the coordination of furnishing and installing motor starters as provided in the specifications.

7. This Contractor shall be responsible to designate an individual within his organization, intimately familiar with this project and assigned on site, to act as the System Start-up Coordinator. This individual must be pre-approved by the Construction Manager. This individual's responsibilities shall include, but not be limited to, coordinating the start-up of all mechanical equipment, including the coordination between the Electrical Contractor, the Controls Contractor, and all testing, adjusting and balancing work. This individual shall report on a weekly basis, in written form, to the Construction Manager. These reports shall include a summary of current conditions including manufacturers' start-ups, systems' deficiencies noted to date and the remediation of same, coordination issues between trades,

system interfacing and forecasting, as necessary to project the completion of each individual system within the building.

8. The Concrete Contractor shall furnish, install and maintain stone fill under slab. The Sitework Contractor shall leave the building pad site at subgrade as identified per the contract documents in preparation to receive stone fill. The Plumbing, Mechanical and Electrical contractors shall complete their work under the slab on grade and shall be responsible to return the pad to the subgrade elevation left by the Sitework Contractor. The Concrete Contractor shall then adjust the select material to final subgrade, fine grade the slab and place the vapor barrier and stone fill. Note: while working on the building pad area this contractor shall utilize track drive equipment only. No rubber tire equipment will be allowed. Preservation of the building pad shall be the responsibility of this contractor. The onsite testing and inspection agency provided the owner will monitor the excavation, travel and backfilling operation.

9. The HVAC, and concrete contractor and CM will me to review the building pad for turnover to the next trade. If not accepted correction will need to be made to correct concerns and sign off.

10. Equipment bases and housekeeping pads that are not included in BP-C and identified on the structural documents will be provided by the Misc. Concrete contract. This contract shall provide detailed shop drawings and field layout of the pads/bases for installation by the concrete contractor. Failure to properly coordinate this work will result in the Mechanical contractor installing the pads at no cost to the owner or any other contractor. Any bases or pads related to the scope of this contract, not identified on the drawings will be provided by this contractor (complete installation)

11. Permits, testing, inspections required for the mechanical piping and HVAC work are to be provided by this contractor.

12. Providing of sleeve assemblies for work of this contract that penetrates the foundation wall, interior footings or any concrete footings shall be provided to the masonry and concrete contractor for installation. Provide sealing of all sleeves as required. This contractor shall coordinate and assist with the sleeving install.

13. Pipe insulation, insulation coverings, valve insulation, labelling and identification of mechanical piping, ductwork, shafts, connections to systems etc. shall be provided by this contractor. (all insulation and sealing as it relates to the work of this contract)

14. Valve tags, charts, and labelling shall be part of this contractors responsibility.

15. Penetrations through wall, floors, etc. including cutting, patching and fire safing.

16. Testing and balancing shall be provided by this contract, Coordination of work with other trades is required.

17. Clean up shall be provided daily; all trash, debris, crates, boxes etc. shall be moved out of the building to the dumpsters each day. No storage of trash will be allowed inside the building or courtyards.

18. All guarantees and warranties begin at the substantial completion of the entire project. Maintain equipment prior to substantial completion.

19. This contractor shall provide all necessary material handling equipment, cranes, scaffolds, hoisting and rigging equipment and supplies for work associated with this contracts.

20. Provide pipe and duct insulation, coverings, wraps, supports and bridging for penetrations through wall, floors, etc. including cutting, patching and fire safing and fire caulking as required.

21. This contractor is responsible to coordinate the work of this contract with the Testing and balancing contractor. Coordination and assistance when the balancing is TAB is being performed is a requirement of this contract.

22. This contract should include man hours for season testing from heating to cooling or vice versa to work with the testing and balancing contractor.

23. Ductwork, flex duct, grilles, diffusers, including detailed layout for the drywall and ceiling contractor shall be provided by this contractor.

24. This contractor shall fully coordinate and verify all louver sizes, mounting details, flashing details, colors with the Carpntry and General Trades contract which will supply and install all louvers.

25. Coordinate damper size, location and type of damper with contract documents, pay special attention to architectural drawings and finish surfaces. Fire dampers are to be included as part of this contractors scope.

26. This contractor shall be on site to coordinate when walls are being installed for penetrations and sleeve installations. If penetrations and sleeves are missed, this will be the responsibility of this contractor to cover associated costs of fixing.

27. Temporary heat and ventilation installation, maintenance and removal. Refer to Division 1, Specification Section 015123 - TEMPORARY HEAT AND VENTILATION, for specific scope. This contractor shall include within the base bid an allocation of $200,000 for the fuel to power the temporary heating equipment if no other owner supplied source is available.

28. Electric baseboard heat shall furnished and installed by this contractor. Electrical connection by EC.

29. Roof curbs, rails, etc. to be provided and loaded to the roof by this contractor. Layout and installation by this contractor, coordinate with the carpentry contractor for blocking and the roofing contractor for flashing and roofing details. Include any doghouses or raceways for service lines, including coordination of flashing.

30. Provide access panels to the drywall contractor for framing information and final installation.

31. Final connection of kitchen equipment and appliances related to the mechanical piping and HVAC system provided by this contractor. Coordination with other trades (Special Systems, Electrical, Fire Alarm etc.) for final interconnections of these systems shall be provided by this contractor.

32. This contractor shall provide all required fire dampers, connections and remote controllers for the HVAC system.

33. Provide all VFD's complete for electrical contractor to install.

34. Provide (2) sets of filters for construction use. Include changing out the filters during the construction phase. Additionally include a complete change out of all filters prior to turn over to the owner (these filters shall be separate from the attic stock filters required) Providing a complete filter listing as part of the closeout documents is required.

35. As-built drawings. As-built drawings is both hard copy and BIM submission as part of the project closeout.

36. This contractor shall include within their bid the incorporation of **2000 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5

37. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

38. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

39. This is not a secure site. All contractors are responsible for concealing, locking and /or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

40. Provide the necessary coordination with trades to avoid interferences with other work and make corrections at no extra charge.

41. Include within this contracts base bid an allocation of $75,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner by means of a credit change order.

42. This contractor shall provide the work of Section 230900 Instrumentation and Controls of HVAC system in its entirety. Coordinate with all other trades as required. Provide all instrumentation, controls, coordination of work, testing as required to provide a complete ATC system for this project. This work shall include but not be limited to instrumentation and controls for: Provide all instrumentation, controls, coordination of work, testing as required to provide a complete ATC system for this project.

43. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

44. Environmental controls.

45. Ventilation controls.

46. Kitchen Ventilation Controls

47. Carbon Monoxide System Controls

48. Air Flow Monitoring Controls

49. Cooling controls.

50. Humidification controls.

51. Refrigeration controls.

52. Motorized dampers when not specified as part of the factory packaged equipment supplied to job site for distribution and installation by others.

53. Controls air compressor complete with accessories and insulation.

54. Remote reading gauges, transmitters and recorders for automatic temperature controls.

55. Building centralization controls including centralized temperature, humidity, pressure and flow indication and recorders, centralization of air conditioning, heating, ventilation, humidification and refrigeration equipment operation.

56. Smoke hatches and relief vents that are not accessible shall have remote controllers to test and reset units.

57. This contract shall supply control valves per contract documents and drawings.

58. This contractor shall coordinate closely with the Kitchen Equipment contractor for controls to equipment.

59. Coordinate and provide controls required for the emergency generator.

60. Building life safety control and equipment safety control including: operators and controls for motorized smoke dampers, operators and controls for motorized fire dampers, firestats, freeze protection thermostats, shut down safety devices forming part of automatic temperature control.

61. Provide all permits required for the work of this contract, pay all fee's.

62. Inspections as required under this contract scope.

63. Electrical thermostats intended for automatic temperature controls complete with subbases or adapter plates to mount on standard electrical box.

64. Supply only of access doors when specifically required for access to automatic temperature control.

65. Control wiring and/or air piping required for all automatic temperature controls supplied under this contract scope.

66. Wiring for remote thermostats and remote prewired auxiliary control panels for packaged equipment.

67. Boiler feed water control wiring.

68. The magnetic starter coil and relay coils supplied under contract scope 16000 and intended for automatic temperature controls, including interlocking between starters and/or relays when controlled automatically.

69. Access panels directly associated with this work if not included by other division.

70. Exclude direct reading temperature and pressure gauges connected directly to non-potable water systems.

71. Exclude motorized dampers when specified as integral part of packaged equipment.

72. Exclude automatic temperature controls when specified as integral part of packaged equipment.

73. Exclude flow measuring and control devices.

74. Exclude direct reading temperature and pressure gauges connected directly to refrigeration systems.

75. Exclude filter gauges directly connected to duct systems.

76. Electrical wiring for thermostats and controls which directly switch the power line to the equipment (directly shall mean not through magnetic coil) is by Division 16000.

77. Power wiring is by Division 16000.

78. Control power supply outlets are by Division 16000.

79. Exclude fire alarm, fan shut-down, relays and wiring Section 16720.

80. This contractor shall provide all raceways, conduits, pull strings and boxes required for the complete ATC system.

81. Review Alternate section and provide Alternate #10 to utilize Modern Controls for the work of the scope.

82. Coordinate and work alongside the commissioning team until project is fully accepted. Include multiple trips to the site with testing equipment, ten (10.)

CONTRACT NO. D-33 - TESTING, ADJUSTING, AND BALANCING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials, and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Division 21	Fire Protection
Division 22	Plumbing
Division 23	HVAC
Section 220500	Common Work Results for Plumbing
Section 230900	Instrumentation and Controls
Section 230950	Testing & Balancing of Mechanical Systems

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide water and air testing and balancing.

2. Contractor shall prepare, at a minimum, a preliminary balance report for the New Castle County Final Inspection.

3. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

4. Provide pricing for all alternates as described in Section 012300-Alternates.

5. Submissions will be reviewed once, and any resubmittals will be reviewed once. Any other submittals will be billed to the contractor at the Engineers standard rates. Please thoroughly review all submissions prior to forwarding to avoid these costs.

6. Provide complete signed and sealed testing report prior to substantial completion and final inspection as required by New Castle County.

7. This contractor has been allotted 30 days to complete all work and provide final, sealed balancing report by the Construction Manager. This contractor will need to work closely with the Construction Manager and all MEP trades to sequence work so that the completion of the balancing is completed in a manner that does not delay acceptance from New Castle County or owner.

8. Provide a pencil copy for submission to NCCo and have final official report within 30 days of the pencil copy.

9. Provide confirmation of duct testing completed by Mechanical Contractor.

10. This contractor must provide all lifts or scaffold means to access all elements.

11. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

12. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

13. Provide circulating water system test.

14. Include balancing and testing of all plumbing and heating lines installed to the future field house.

15. This contract should include seasonal testing from heating to cooling, until system has been fully commissioned and accepted.

CONTRACT NO. D-34 - ELECTRICAL, LIGHTING, AND FIRE ALARM SYSTEMS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Division 22	Plumbing (coordination of work)
Division 21	Fire Protection (coordination of work)
Division 23	HVAC (coordination of work)
Division 26	Electrical
Section 111663	Loose Performance Lighting Fixtures (coordinate)
Division 27	Communications
Division 28	Electronic Safety and Security raceways and coordination)
Section 284621	Addressable Fire Alarm Systems (complete)

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide a complete electrical system, lighting, addressable fire alarm system and infrastructure for all Division 21, Division 27 and Division 28 as indicated on the contract documents.

2. Provide Transformer and Generator system complete. Include all infrastructure, raceways, duct banks (including all excavation, backfill, identification systems, trace wiring, etc.) This contractor shall be fully responsible for preparing, submitting, paying all fees and coordinating the DNREC required permitting for the Generator. Coordinate with NCCVT as required.

3. Lightning protection shall be provided by this contract and coordinated with the Carpentry contractor and Roofing Installer.

4. This contractor to supply power to all areas of work in other trades requiring electrical power.

5. Provide complete infrastructure system for all Division 27 and Division 28 systems. Including all interior and exterior duct banks, raceways and sleeves for special systems.

6. This contractor shall include in the base bid temporary exterior lighting installed and maintained to accommodate a minimum of 3-foot candles for the exterior of the building for the purpose of site security. The lights must be installed to meet the requirements for exterior use and illuminated during low light hours. These lights will be utilized until permanent exterior lighting has been installed and powered. Supplying the temp power for this lighting is part of this contract. Include providing temporary power and lighting as needed for the entire duration of the project. This include the necessary power outlets required for all contractor use. Power must be available within a reasonable distance at all times.

7. Division 23 of the specifications should be reviewed as it relates to the power wiring and other requirements for HVAC equipment including the coordination of furnishing and installing motor

starters and controllers as detailed in the Specifications and on the Drawings.

8. This contractor shall provide all conduits, raceways and boxes required for thermostat and sensor installation.

9. The HVAC contractor will supply all VFD's to the electrical contractor for installation and powering.

10. Provide all smoke damper, power and remote controllers as required by the contract documents.

11. Excavation and backfill for underground electrical work as required below is the responsibility of this Contractor. Soil types shall be in accordance with project specifications and the Geo-Tech report. Geo-Tech reports included for review and acceptance.

12. Backfilling is the responsibility of this Contractor. Soil types shall be in accordance with project documents. It is the intent to use on site material and not imported fill. The use of this on site material shall conform to the compaction requirements identified in Section 312300. Excavated materials shall be covered immediately and protected from moisture mitigation. If Materials become unusable, this contractor shall own purchasing acceptable off site materials.

13. Provide all excavation, layout, concrete, reinforcing for duct banks, light standards, above ground conduit encasement, equipment bases and any other concrete work specifically related to the electrical work. This shall include services from the roadways and all communication duct banks as required. Include requirements of New Castle County, State and local codes for concrete encasement.

14. All runs in exposed ceilings are to be in conduit.

15. All exterior underground raceways and infrastructure are to be installed by this contractor as required by the contract documents. (Cameras, security, electric etc.)

16. Temporary electric installation, maintenance and removal. Refer to Division 1, Specification Section 015113 - TEMPORARY ELECTRIC, for additional information.

17. This contractor shall provide temporary transformers as required to provide electrical power generation until permanent service is installed by Delmarva power. Include all permits, cabling, switch gear, breakers etc.to provide a complete temporary power system capable of supplying the electrical loads required for the project. This contractor to coordinate and arrange for temporary power from the source, Delmarva Power.

18. Provide temporary power for meter bank with transformer for contractors trailers. Coordinate all work with Delmara Power.

19. Rough in and final connection and related work for equipment provided under other contracts (i.e. kitchen, elevators, HVAC, sprinkler, motorized doors, vertical walls, etc.)

20. Provide all permits and inspections. Pay all fees associated with the permits and inspection.

21. Penetrations through walls, floors, etc. including cutting, patching and fire safing.

22. Testing of all systems, as related to the scope of work for this contract shall be provided. Reporting and verification documentation shall be supplied to NCCVT and EDiS.

23. This contractor shall provide all supplemental hangers and fasteners for lighting installation to the building structure.

24. All runs in exposed ceilings shall be installed in conduit.

25. Clean up on a daily basis shall be provided by this contractor. All work areas shall be organized and cleaned up to the dumpsters each day.

26. The Concrete Contractor shall furnish, install and maintain stone fill under slab. The Sitework Contractor shall leave the building pad site at subgrade required by the contract documents in preparation to receive stone fill. The Mechanical and Electrical Contractors shall complete their work under the slab on grade and shall be responsible to return the pad to the subgrade elevation left by the Sitework Contractor. The Concrete Contractor shall then adjust the select material to final subgrade, fine grade the slab and place the vapor barrier and stone fill. Note: while working on the building pad area this contractor shall utilize track drive equipment only. No rubber tire equipment will be allowed. Preservation of the building pad shall be the responsibility of this contractor. The onsite testing and inspection agency provided the owner will monitor the excavation, travel and backfilling operation.

27. The electrical, and concrete contractor and CM will me to review the building pad for turnover to the next trade. If not accepted correction will need to be made to correct concerns and sign off.

28. Note: all raceways are to be installed into the subgrade soils and shall have adequate cover for protection from traffic above. No raceways will be installed in the stone base provided by the concrete contractor.

29. All guarantees and warranties to begin at the substantial completion of the entire project. Maintain equipment prior to substantial completion.

30. Hoisting, rigging and scaffolding required to perform you scope of work shall be provided by this contractor.

31. Provide all primary service work, including all utility company related costs/fees for this work. Coordination with the utility company is the responsibility of this contractor.

32. Provide a complete fire alarm system. Water flow devices are supplied and installed by the Sprinkler Contractor and wired by this Contractor. Include tie-in to fire sprinkler flow and tamper switch. (fire dampers, smoke detectors, remote testing switches are all part of this contract)

33. Provide all heat tracing and insulation systems as required.

34. Coordinate closely with the work of the Special Systems contractor. This contract (electrical) provides all infrastructure, conduit and raceways required for the Special Systems work. Provide pull strings and boxes for all systems. (voice, data, communication, fire alarm, AV systems, Audio systems, and public address system, clock system etc.) Include all required sleeving, sealing and fire sealing for raceways and conduits through walls, floors, ceilings etc. for this work.

35. This contract shall provide and install wire mesh cable tray for low voltage distribution as shown on documents and specified. Cable tray shall be installed 3" above drop ceilings and have 3" clear above the top rim for access.

36. This contractor shall provide and install 4' conduits as shown for low voltage distribution.

37. This contractor shall provide and install 2' conduits into each space above the ceiling for low voltage distribution.

38. Coordinate, review and fully understand and integrate all cable tray, raceways and infrastructure interior or exterior that may be indicated on all contract documents including the T series drawings.

39. Lightning protection with master UL certification. Coordinate with the Carpentry and Roofing contractors.

40. Coordinate and provide a complete grounding system for the entire project. This includes but is not limited to the building columns, interior spaces, exterior wall assemblies, Electrical rooms, IDF and IDF rooms) and provide any testing and reports required.

41. As-built drawings in both hard copy, electronic and final BIM modelling per contract documents.

42. Provide rough-in and final connection and related work for equipment provided under other contracts (i.e. kitchen, elevators, HVAC, sprinkler, motorized doors, etc.). Provide power to automatic hardware. Low voltage wiring from the controller to hardware shall be provided by the Doors, Frames and Hardware Contractor. Include power panels and power supplies supplied by other trades.

43. Provide complete infrastructure for audio and audiovisual systems.

44. Provide rough-in and final connection of kitchen equipment and appliances. Refer to Specification Section 11400 Food Service Equipment for specifics. Coordinate power/plug requirements with rough in for equipment with the Kitchen Equipment Contractor.

45. Section 116163 Loose Performance Lighting shall be provided by the Stage Rigging contractor as follows; stage lighting systems including fixtures, controls, light grids, supports and attachments shall be provided. This contract (electrical) shall provide all power and power connections to the Loose Performance lighting. All other lighting in the Auditorium shall be supplied and installed by the electrical contractor. Coordination of work between trades is tis contractors responsibility.

46. This contractor shall include within their bid the incorporation of **2500 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19 del. C.ch.5

47. Perform certification testing for all wiring and systems supplied by this contract scope.

48. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

49. Provide access doors and frames for all access to Structured Cable components or equipment that require routine or periodic maintenance. Installation of access doors and frames provided by the Metal Stud & Drywall Contractor.

50. Include within this contracts base bid an allocation of $75,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-35 - SPECIAL SYSTEMS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Division 26	Electrical (coordination of work)
Section 078400	Firestopping
Section 079200	Joint Sealants
Section 270500	Telecommunications Pathways and Spaces
Section 271000	Structured Cabling
Section 272000	Network Equipment
Section 274000	Classroom and Conference Room AV Equipment
Section 274100	Specialized AV Systems
Section 274117	Audio Video Systems
Section 275000	Public Address and Clock
Section 280501	Security Pathways and Spaces
Section 281000	Intrusion Detection System
Section 281100	Access Control System
Section 282000	Video Surveillance System
Section 283112	Public Safety – First Responder Radio Amplification System

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide a complete Special Syatem package as to include but not limited to, structured cabling, network equipment, AV systems, public address and clock system, intrusion detection, access controls, video surveillance and radio amplification system.

2. Provide wireless clock system including all equipment, cable, and accessories.

3. Telephone and voicemail system including telephone handsets and patch cables from device to jack will be provided by owner.

4. Provide intercom/public address system. Structured Cable Contractor will provide all network cabling including wiring, devices, and terminations at the source (MDF/IDF patch panel) and at the communication port (jack).

5. Provide complete cafeteria and Auditorium sound reinforcement audio/visual system. Projectors and mounts provided by the owner and installed by the Electrical Contractor.

6. The electrical contractor shall provide and install the fire alarm system, this contractor (Special Systems) will wire fire alarm terminations, and programming of electrified hold open hardware. Low voltage power to electrified hold open hardware provided by this contract. Hold open hardware provided by Carpentry and General Work Contractor.

7. Provide complete intrusion system.

8. Provide access control and security management system complete. Provide coordination with door and frame installation for a complete system. The contractor responsible for supplying the doors, frames, and hardware shall provide all wiring and accessories from the power supply (or junction box) to the door hardware. The contractor responsible for installation of doors and hardware shall provide terminations from door hardware to door whip, from door whip to power transfer, and from frame whip to power transfer. Frame whip shall be secured and protected by the door, frame, and hardware contractor(s) for the direct access of the Special Systems Contractor. Termination of the frame whip to the power supply (or junction box) shall be provided by the Special Systems Contractor. Power supply shall be furnished by the door, frame, and hardware contractor(s) and installed by the Special Systems Contractor. The Special Systems Contractor shall provide low-voltage wire from the card reader to the access controller, from the status switch (door contact) to the access controller, from access controller to the power supply(or junction box), and from power supply (or junction box) to power supply (or junction box) as necessary. The Electrical Contractor is responsible for providing 120v circuits to all power supplies and/or transformers as indicated in the documents. The Electrical Contractor shall provide conduits, device boxes, raceways, and pull strings for low-voltage wiring at doors receiving electronic, security, or access control hardware. Electrical contractor shall provide a junction box above each door scheduled to receive a card reader and a pathway & pull string. A mock-up shall be field installed and coordinated by all related Contractors for review prior to commencing work.

9. Provide a complete CCTV - Network Digital Video Management System. Owner shall provide server.

10. Provide all patch cords from communication port (jack) to each device included in this Contractor's scope. Patch cords at source (MDF/IDF) from patch panel to network switch provided by owner.

11. Provide all patch cords for switches.

12. Supply and install any fiber lines need for a complete installation including terminations.

13. Provide all testing of all installations.

14. Provide and install the racks, switches, uninterrupted power supplies etc. for a complete installation.

15. Coordinate all WAP's as per the specifications if supplied by the owner, install if not supplied provide and install under this contract.

16. This contractor shall own all notes as per the T series drawings unless note otherwise in the scope of this contract or the electrical contract. This includes but is not limited to the following series of notes. Note 6- Audio and Videa Systems, Note 7- Classroom/Conference Room AV Systems, Note 8-Demo Camera System and Note 9- Data Drop Allowance. These systems shall be provide as complete without any qualifications.

17. Provide coordination of the work of this contract with the Electrical including final equipment locations. This contractor must coordinate with Electrical Contractor as indicated on the drawings and as specified. The Electrical Contractor shall provide all device boxes, conduit and pull strings to circuits

for special systems as indicated and also to provide 120 Volt circuits for all Special Systems. This Contractor will be responsible for providing independent support systems, as indicated in the specifications, for all cable and wiring installed by this Contractor in locations where pathways and raceways are not required by the documents. All runs of cable/low voltage in open areas shall be installed in conduit. If raceways are required for the scope of this contract and they are not identified, this contractor shall provide.

18. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

19. This contractor shall be on site to coordinate when walls are being installed for penetrations and sleeve installations. If penetrations and sleeves are missed, this will be the responsibility of this contractor to cover associated costs of fixing.

20. Interactive screens/displays and mounting brackets will be supplied by Owner and mounted by the Carpentry & General Works Contractor. The Carpentry and General Works Contractor will coordinate blocking with mounting hardware and install all necessary clips and blocking to the wall for hanging. Audio/visual interface and/or controls by Special Systems Contractor.

21. Hardware for permanent exterior gates will be provided by the other trades. Access control hardware/software and fire alarm integrations of gate hardware, including terminations, cabling, etc. will be provided by this contractor. The Electrical Contractors shall provide all pathways & electrical requirements to support installation.

22. Provide access doors and frames for all access to Special Systems components or equipment that require routine or periodic maintenance. Installation of access doors and frames provided by the Metal Stud & Drywall Contractor.

23. Provide all network cabling including wiring, devices, and terminations to communication devices identified in plans and referenced on "Communications Outlet Configuration" chart on Drawing E-501. Two (2) terminations should be provided (1) at the source (MDF/IDF patch panel) and (1) at the communication port (jack) in all instances.

24. This contract shall provide communication wiring from the (3) access control panels to the source (MDF/IDF patch panel) including terminations on both ends. Location of access control panels to be coordinated with the documents and the Construction Manager prior to installation.

25. This contractor shall provide communication wiring from the intrusion control headend to the source (MDF/IDF patch panel) including terminations on both ends. This communication wiring shall include (1) dedicated POTS line from the MDF room to the intrusion control dialer. Location of intrusion control headend to be coordinated with the documents and Construction Manager prior to installation.

26. This contractor shall provide communication wiring from the Fire Alarm Control Panel (FACP) to the source (MDF/IDF patch panel) including terminations on both ends. This communication wiring shall include (2) dedicated POTS line from the MDF room to the FACP dialer(s). Location of FACP to be coordinated with the documents and the Construction Manager prior to installation.

27. This contractor shall supply communication wiring from the intercom/public address amplifiers to the

source (MDF/IDF patch panel) including terminations on both ends. Location of amplifiers to be coordinated with the documents and the Construction Manager prior to installation. Contractor should assume (3) amplifiers, one located in each MDF/IDF.

28. This contractor shall provide communication wiring from the Building Management System headend to the source (MDF/IDF patch panel). Location of Building Management System headend to be coordinated with the documents, the Mechanical Contractor, and the Construction Manager prior to installation.

29. This contractor will install all network cable within the kitchen and kitchen hood identified on the Kitchen Equipment Drawings. Final location of network drops to be coordinated with the documents, the Kitchen Equipment Contractor, and the Construction Manager prior to installation.

30. This contractor will install communication wiring from the food management systems to the POS devices, menu display boards, and temperature monitoring systems, including terminations on both ends. Final location of the food management systems to be coordinated with the documents and the Construction Manager prior to installation.

31. Provide installation for all wireless access points furnished by owner. Patch cords from device to communication port (jack) provided by this Contractor.
32. Provide penetrations through walls, floors, etc., including cutting, patching and fire safing.

33. Provide all design and coordination necessary to provide complete systems.

34. Provide and coordinate for inspections and testing.

35. Provide fire resistive sealants for the work of this contract.

36. Provide pricing for all alternates as described in Section 012300-Alternates.

37. Provide video documentation of training on systems.

38. Provide at least a 48 hour notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

39. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

40. This contractor must provide a silica exposure plan that meets or exceeds the new 2017 silica OSHA requirements before any work can commence. At a minimum, it must be incorporated into the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

41. Contractor must provide additional crews as needed to maintain the project schedule.

42. This contractor shall include within their bid the incorporation of **1200 hours of COOP participation** by a NCCVT student. Contractor to comply with project documents and requirements set forth in 19

del. C.ch.5

43. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

44. This contractor must provide a silica exposure plan that meets or exceeds the new 2017silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

45. Include within this contracts base bid an allocation of $30,000 for work to be determined by owner and construction manager. Unused allocation funds to be returned to the owner.

CONTRACT NO. D-36 - VERTICAL RETRACTABLE WALLS

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

Technical Specification sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Section 055000	Metal Fabrications
Section 079200	Joint Sealants
Section 102239	Vertically Retractable Walls
Division 26	Electrical

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide labor and materials to perform all work associated with the Vertically Retractable Walls System to provide a complete operating wall system.

2. Provide coordinated shop drawings that reflect all structural requirements with the structural steel, metal studs, ceilings, electrical power, lighting and communication systems, etc.

3. This contract includes all Division 0 and Division 1 General Requirements. All commissioning requirements are identified in Division 1 and are a requirement of this contract.

4. Provide all trim components, hardware, hinges, and operators for electrical units, appropriate finishes, sensors, key switches and pocket doors for concealing doors when not in use.

5. Coordinate any structural requirements with the structural steel and carpentry contractors. Provide all supplementary steel as needed to hang partitions from structural support steel, provided by the Structural Steel Contractor. It is assumed, no additional steel will be required below structural support steel. If so, it will be provided by this contractor.

6. Electrical connections will be provided by Electrical Contractor. This contractor shall provide assistance to Electrical Contractor for coordination and installation of necessary connections. Low voltage wiring for devices, controls, raceways, boxes etc. to be provide by this contractor (not electrical contract)

7. Provide any required signage for safe operations.

8. Provide attic stock, warranty and demonstrations for all materials and types of panels.

9. Provide specified testing, adjusting, warranty and training demonstrations on the operation.

10. Provide (3) additional sets of keys for switch operating controls over and above the number of sets required by specifications.

11. Provide data and submittal information related to the Scope of this Contract signed and sealed by a Professional Engineer as required by the Contract Documents, including but not limited to delegated design requirements.

12. Provide all low voltage wiring, motors motor transformers and final connections to allow for a complete operating system. Electrical contractor shall supply the line voltage power connection. Include all raceways and boxes for your work.

13. Provide all BIM services as specified in Section 013700 BIM Execution Plan. As part of the coordination process all contractors are responsible for obtaining a Revizto license. The cost of this license is $1,200 and shall be included in your base bid proposal.

14. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. EDiS will not be responsible for any lost tools, materials or equipment.

CONTRACT NO. D-37 - MISCELLANEOUS CONCRETE AND GROUTING

A. Work included in this contract consists of, but is not necessarily limited to, all labor, materials and equipment for:

- Technical Specification Sections:

Division 0	Bidding and Contract Requirements
Division 1	General Requirements
Division 03	Concrete
Section 033000	Concrete
Division 07	Thermal and Moisture Protection
Section 072100	Thermal Insulation
Section 072600	Under-Slab Vapor Barrier
Section 312300	Excavation and Backfill for pipeline and structures
Section 321313	Concrete Paving

This contract also includes, but is not necessarily limited to, all labor, materials and equipment for the following:

1. Provide Misc. concrete items and grouting as described in the Scope of Work and defined on the contract documents. Include all preparations and excavation, backfill, stone subbase, forms, and reinforcing required.
    - Provide footings and concrete piers as show on drawings A560-A565, include footings for dumpster pad.
    - Provide concrete locker bases as indicated in the contract documents.
    - Provide the electrical, mechanical and plumbing concrete pads as indicated on the contract documents. (Structural foundations and pads shown on Struct. Drawings excluded)
    - Provide all concrete slab on grade at the interior courtyard areas.
    - Provide all poured foundations for block walls, poured concrete walls at all areas outside of the main building foot print.
    - Provide all concrete excavation, footings and backfill as required for the masonry walls at the child care and playground areas.

2. This Contractor will be responsible for laying out all concrete work for this contract course of work.

3. This Contractor to furnish and install reinforcing steel, admixtures, curing compound, sealers, accessories, bolsters, ties and braces as required in the Contract Documents and for the performance of the work of this contract.

4. All work of this contract shall be considered “out of sequence” as such the contractor shall price each element of work as a mobilization and if required “short load” concrete delivery.

5. This contractor is responsible to provide material handling equipment, concrete pumps, etc. for work of this contract. NCCVT and EDiS will not be responsible for any additional material handling costs above the base bid proposal.

6. Provide sealants/caulking as required at grouted freezer and cooler box floors. Caulk all edges where

grout seals to box floor panels.

7. This contractor shall provide installation of sleeves required for MEP lines, under footings, below frost walls, under thickened slabs as related to this contractors course of work. This includes all excavation and backfill required for these installations. (sleeves will be supplied by the contractor installing the services, future BP-D) Coordinate with Arch and MEP documents for extent of this work.

8. Provide grouting of floor expansion joints once they are set and adjusted by installing contractors.

9. Grouting of all elevator sill angles will be the responsibility of this contractor.

10. Provide all door stoops, pads, entrance/exit concrete complete as provided for o the Architectural and MEP drawings. (if the concrete is shown on the structural drawings it shall be part of Contract C-01 Concrete and Reinforcing) This will be out of sequence work, contractor to include (5) re-mobilization to perform work out of sequence, this shall include premium costs for short load concrete pours as well.

11. Underslab vapor barrier, insulation, reglets, waterstops, control and construction joints. (Caulking by Joint and Sealants Contractor)

12. Provide foundation wall insulation and insulation under slabs. Include backfill of all foundation walls as detailed. Stone under slab to be provided by this contractor. Include re-dressing the stone after the MEP contractors have installed their UG work. As related to the work detailed for this contract.

13. Placement of related items furnished under other Specification Sections.

14. Anchor bolt assemblies to be placed with templates only.

15. All blockouts and embedment's required by plans and specifications.

16. This Contractor is responsible for grouting all structural steel base or leveling plates and elevator sill angles. As defined by the scope of this contract.

17. Include all weather, frost protection, and water pumping as required. This Contractor is also responsible for the premiums required for hot water, heated aggregate and admixtures for cold weather concrete.

18. Provide dewatering as it relates to the work of this contract.

19. All concrete testing will be completed by the Construction Manager, however, it will be the responsibility of this Contractor to furnish all samples.

20. This contractor shall include an allowance amount of $15,000 within the base bid for work to be identified by NCCVT and the CM. All unused portions of this allocation to be returned to the owner by means of a credit change order.

21. Provide all grout infill **inside the** walk-in freezers and refrigerators after freezers and refrigerators have been set in place. **Also grout the space between the freezers and refrigerator and the surrounding concrete.** Coordinate requirements with the architectural drawings for BP-D and technical

specifications.

22. This contractor owns coordinating all slab depressions identified on the documents with the products, flooring, insulation etc. shop drawings and layout drawings for each material that will be installed in the recess. A pre-install meeting will be held to review this information before each depressed pour.

23. Provide all means of transporting concrete including, but not limited to: pump trucks, cranes, ramps, chutes, buggies.

24. Provide at least 48 hours' notice prior to any delivery. All deliveries are to be between 7:00 AM and 3:30 PM.

25. Provide and maintain a DNREC approved concrete dumpster for washout required by the scope of this contracts work.

26. This is not a secure site. All contractors are responsible for concealing, locking and/or removing any materials on a daily basis. NCCVT and EDiS will not be responsible for any lost tools, materials or equipment.

27. This contractor must provide a silica exposure plan that meets or exceeds the silica OSHA requirements before any work can commence. At a minimum, it must be implemented in to the company safety plan, include all monitoring, testing, limits exposure, provide respiratory plan and/or equipment modifications such as adding water to equipment during exposed work and keep records of exposure.

28. Provide daily fine cleanup of the work is the responsibility of each individual Contractor which includes broom cleaning of their debris as required. Daily Fine clean up, on a daily basis, shall be defined as those means/methods utilized to perform the daily cleaning tasks without producing dust, noise and stacking of stored materials. Furnish fine clean up on a daily basis. All debris must be removed from the work area at the end of each work day to the appropriate dumpster. Cleaning of roadways shall be included and performed daily while this contractor is on site performing work of this contract.

29. All materials excavated for installation of footings and foundations shall immediately be protected with appropriate moisture protection.

30. BIM coordination is "not" part of this contract scope.

END OF SECTION

SECTION 012100 - ALLOWANCES

1. RELATED DOCUMENTS

   A. The general provisions of the Contract, including the Conditions of the Contract (General, Supplementary and other Conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

   B. Refer to provisions in AIA Document A232 – 2019 EDITION, GENERAL CONDITIONS OF THE CONTRACT FOR CONSTRUCTION, CONSTRUCTION MANAGER AS ADVISOR EDITION, for requirements in addition to those specified in Division 1.

   C. Refer to Scope Information Sheets for all contracts bound in the Project Manual under Section 011100 - SUMMARY OF WORK. The Scope Information Sheets describe generally the work included in each contract, but the work is not necessarily limited to that described.

   D. For work being constructed under separate prime contracts, provisions of this Section apply to each contract being bid.

   E. Include in the Contract Sum all lump sum and unit cost allowances stated in the Contract Documents.

   F. Designate in the construction progress schedule the delivery dates for products specified under each allowance.

   G. Designate in the Schedule of Values the quantities of materials required under each unit cost allowance.

2. ALLOWANCES FOR PRODUCTS

   A. The amount of each allowance includes:

      1. The cost of the product or labor to the Contractor or Subcontractor, less any applicable trade discounts.

      2. Delivery to the site.

      3. Labor required under the allowance, only when labor in specified to be included in the allowance. If labor is not specified to be included in the allowance, it shall be included in the Contractor's bid and in the resulting Contract Sum.

      4. Applicable taxes.

      5. Profit and overhead.

   B. In addition to the amount of each allowance, include in the Contract Sum the Contractor's costs

for:

1. Handling at the site; including unloading, uncrating and storage.

2. Protection from the elements and from damage.

3. Labor for installation and finishing, except where labor is specified to be a part of the allowance.

4. Other expenses required to complete the installation.

5. Contractor's and Subcontractor's overhead and profit.

C. Refer to Scope Information Sheets under Section 011100 - SUMMARY OF WORK for the amount of each lump sum allowance and for work specified in the specification sections listed below.

1. Section 011100 Contract D-01: Unit Masonry: Provide a $40,000 allowance for work to be determined by Owner and Construction Manager.

2. Section 011100 Contract D-02: Miscellaneous Metals, Stairs, and Rails: Provide a $20,000 allowance for work to be determined by Owner and Construction Manager.

3. Section 011100 Contract D-03: Exterior Structural Stud Assembly: Provide a $40,000 allowance for work to be determined by Owner and Construction Manager.

4. Section 011100 Contract D-04: Carpentry and General Work: Provide a $40,000 allowance for work to be determined by Owner and Construction Manager.

5. Section 011100 Contract D-05: Exterior Metal Panels: Provide a $30,000 allowance for work to be determined by Owner and Construction Manager.

6. Section 011100 Contract D-06 Drywall and Interior Metal Framing:
    a. Provide a $30,000 allowance for work to be determined by Owner and Construction Manager.
    b. Provide $175,000 allowance to supply, install, and maintain a complete scaffold system for auditorium ceiling installation.

7. Section 011100 Contract D-08: Roofing: Provide a $35,000 allowance for work to be determined by Owner and Construction Manager.

8. Section 011100 Contract D-09: Fireproofing: Provide a $20,000 allowance for work to be determined by Owner and Construction Manager.

9. Section 011100 Contract D-10: Joint Sealants and Preformed Joint Assemblies: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

10. Section 011100 Contract D-12: Overhead Coiling Door and Grates: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

11. Section 011100 Contract D-13: Curtainwall/Glazing/Storefronts: Provide a $35,000 allowance for work to be determined by Owner and Construction Manager.

12. Section 011100 Contract D-14: Tiling: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

13. Section 011100 Contract D-15: Acoustical Ceilings and Specialty Ceilings: Provide a $20,000 allowance for work to be determined by Owner and Construction Manager.

14. Section 011100 Contract D-16: Flooring: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

15. Section 011100 Contract D-17: Resilient Athletic Flooring: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

16. Section 011100 Contract D-18: Resinous Matrix Terrazzo Flooring: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

17. Section 011100 Contract D-19: Fluid Applied Flooring: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

18. Section 011100 Contract D-20: Paint and VWC: Provide a $20,000 allowance for work to be determined by Owner and Construction Manager.

19. Section 011100 Contract D-21: Wood Strip Flooring-Gym Flooring: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

20. Section 011100 Contract D-22: Specialties: Provide a $20,000 allowance for work to be determined by Owner and Construction Manager.

21. Section 011100 Contract D-23: Food Service Equipment: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

22. Section 011100 Contract D-25: Laminate Clad Casework, Countertops, and Sills: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

23. Section 011100 Contract D-26: Stage Rigging, Lighting, and Accessories: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

24. Section 011100 Contract D-27: Fixed Auditorium Seating: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

25. Section 011100 Contract D-28: Wood Laboratory Furniture and Specialty Casework: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

26. Section 011100 Contract D-29: Telescoping Bleachers and Platforms: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

27. Section 011100 Contract D-30: Hydraulic Holeless Passenger Elevator: Provide a $10,000 allowance for work to be determined by Owner and Construction Manager.

28. Section 011100 Contract D-31: Fire Protection: Provide a $20,000 allowance for work to be determined by Owner and Construction Manager.

29. Section 011100 Contract D-32: Plumbing: Provide a $75,000 allowance for work to be determined by Owner and Construction Manager.

30. Section 011100 Contract D-33: Mechanical Piping - HVAC:
    a. Provide a $75,000 allowance for work to be determined by Owner and Construction Manager.
    b. Provide $200,000 allowance to provide temporary heating fuel.

31. Section 011100 Contract D-35: Electrical, Lighting and Fire Alarm Systems: Provide a $75,000 allowance for work to be determined by Owner and Construction Manager.

32. Section 011100 Contract D-36: Special Systems: Provide a $30,000 allowance for work to be determined by Owner and Construction Manager.

33. Section 011100 Contract D-38: Miscellaneous Concrete and Grouting: Provide a $15,000 allowance for work to be determined by Owner and Construction Manager.

3. ADJUSTMENT OF COSTS

A. Should the net cost be more or less than the specified amount of the allowance, the Contract Sum will be adjusted accordingly by Change Order.

    1. For products and labor specified under a unit cost allowance, the unit cost shall apply to the quantities actually used with a nominal allowance for waste, as determined by receipted invoices, or by field measurement.

B. At Contract closeout, reflect all approved changes in Contract amounts in the final statement of accounting.

END OF SECTION

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

ALLOWANCE AUTHORIZATION

Project:

Architect: **Project No.**

Contractor:

AAA No.: **Initiation Date:**

The Allowance is allocated as follows:

Total original Contract Allowance was:	$
Amount of Contract Allowance Access previously authorized:	$
Adjusted Contract Allowance prior to this authorization is:	$
The amount of available Allowance will Decrease by this Access Authorization:	$
The remaining Contract Allowance, after this Access Authorization will be:	$

Recommended by:
Architect

By (Signature): _____
Date: _____

Accepted by:
Contractor

By (Signature): _____
Date: _____

Approved by:
Owner

By (Signature): _____
Date: _____

SECTION 012200 - UNIT PRICES

1. GENERAL PROVISIONS

   A. The general provision of the Contract, including the Conditions of the Contract (General, Supplementary and other conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

   B. Refer to provisions in AIA Document A232 – 2019 EDITION, GENERAL CONDITIONS OF THE CONTRACT FOR CONSTRUCTION, CONSTRUCTION MANAGER AS ADVISOR EDITION, for requirements in addition to those specified in Division 1.

   C. For work being constructed under separate prime contract, provisions of this Section apply to each contract being bid.

2. BASE BID

   A. The Base Bid shall consist of all work shown or specified in the Contract Documents, exclusive of any Additive Unit Prices specified herein.

   B. The Base Bid shall include all work in any Subtractive Unit Prices specified herein.

3. UNIT PRICES

   A. State in the Bid Form the amount to be added to (or subtracted from) the Base Bid per unit of measurement for each Unit Price specified. State this amount to include all overhead and profit. No surcharge in addition to the Unit Price listed will be permitted.

   B. See Section 002113, INSTRUCTIONS TO BIDDERS for related information.

   C. For description of Unit Prices requested, refer to the specification. The method of stating the Unit Prices is described in the Bid Form.

   D. Where both add and deduct unit prices are requested, there shall not be more that a 10% variation between the two.

4. APPLICATION OF UNIT PRICES

   A. Unit prices stated in the Bid Form will apply from the time the Bid is submitted until Contract completion.

5. MEASUREMENT OF QUANTITIES

   A. Quantities shall be determined by field measurement by contractor personnel and as verified by the Construction Manager.

B. At the Contractor's option, and at his expense, measurements may be made by a registered surveyor.

6. LIST AND DESCRIPTION OF UNIT PRICES

Unit Price No. 1: Addition or deletion of man hours from base contract.

Contract D-07 General Labor and Clean-up

A unit cost will be provided by this contractor that will pertain to any hours that may be deducted or added to this contract.

END OF SECTION

SECTION 012600 - CHANGE ORDER PROCEDURES

1. GENERAL

A. The general provisions of the Contract, including the Conditions of the Contract (General, Supplementary and other Conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

B. Refer to provisions in AIA Document A232 – 2019 EDITION, GENERAL CONDITIONS OF THE CONTRACT FOR CONSTRUCTION, CONSTRUCTION MANAGER AS ADVISOR EDITION, for requirements in addition to those specified in Division 1.

C. The Construction Manager is responsible for processing all change orders. Each request will be assigned a change order request (COR) number. The Change Order Request & Execution Form will be initiated via the web-based project management system (Building Blok) used by the CM.

D. It is to be clearly understood that no extra work shall commence without an approved written and executed change order from the Owner.

2. INITIATING A CHANGE ORDER

A. Specific changes initiated by the Owner, Architect, Construction Manager (CM) or Contractor will be processed as follows:

1. The Owner will authorize the Architect to prepare sufficient documents to establish an accurate price. These documents to be forwarded to the Construction Manager and Owner "for pricing only, not authorized for construction." The Construction Manager will develop the estimate (within 2 weeks) showing a breakdown by trades with all trade contractor quotes. The Owner will approve or reject the change request within two (2) weeks. If the Owner elects to proceed with the change, the Construction Manager will prepare formal change orders to the various trade contractors involved in the change and reference in all formal change orders the original change order request number.

2. Field Change: Contractor shall immediately notify the Construction Manager of a change due to field conditions or site conditions. If documents cannot be prepared for pricing due to schedule constraints, the Construction Manager will make every effort in estimating the field change. If the Owner and Construction Manager agree that certain field changes should be handled on a time and material basis, the Construction Manager will closely monitor the Contractor's labor and material affecting this change. At the completion of the work a formal change order will be issued.

3. Contractor Change: If a Contractor initiates a change order for work not included in the Contract, the Construction Manager and Architect will research the validity of the request, verify quantities and pricing and submit to the Owner for approval on a change order request.

B. The additional cost, or credit to the Owner resulting from a change in the Work shall be by mutual agreement of the Owner, Contractor, Construction Manager and the Architect.

3. PROCESSING A CHANGE ORDER

A. The Contractor will fill in the Change Order Request & Execution Form (COREF) with a brief description of the change, any time extension, and cost changes.

B. The Contractor will attach to the COREF copies of the written quotations from the trade contractors, Contractors, and suppliers. The Labor Detail Sheet and the Change Order Detail forms must be added as an attachment to the COREF. The Contractor and each sub-tier contractor (as applicable) must fill out the Labor Detail Sheet and Change Order Detail Sheet. Samples of these forms are attached.

C. In all cases, this cost or credit shall be based on the "DPE" wages required and the "invoice price" of the materials/equipment needed.

D. "DPE" shall be defined to mean "direct personnel expense". Direct payroll expense includes direct salary plus customary fringe benefits (prevailing wage rates) and documented statutory costs such as workman's compensation insurance, FICA, and unemployment insurance.

1. "Fringe Benefit" is any medical, life or disability insurance, paid time off, etc.

2. "Worker's Compensation" is the insurance required for injuries including medical leave, etc.

3. "FICA" is the costs association with Social Security and Medicare insurance.

4. "Unemployment insurance" is the cost associated with the governmental assessment for employee's unemployment benefits.

E. "Invoice price" of materials/equipment shall be defined to mean the actual cost of materials and/or equipment that is paid by the Contractor (or Subcontractor) to a material distributor, direct factory vendor, store, material provider, or equipment leasing entity.

F. In addition to the above, the Contractor is allowed markup for overhead and profit on additional work performed as outlined in Specification Section 012613, Contractor Compensation.

G. Building Blok Procedures: The Contractor will submit all change order requests and supporting documentation via the Building Blok web-based project management system. Each Contractor will be issued a unique login and password. Each contractor must submit the information as follows:

1. Create a new change order, from your "To-Do List" by clicking on the "Create Issue" tab in the upper right corner and select "Change Order Request".

2. The Contractor will enter a brief description of the change in the "Summary" block. A detailed description of the change will be entered in the "Description of Change" block, to include any

changes to documents or time extension. The cost of the change will be entered in the "Total Cost Change" block.

3. The Labor Detail Sheet and the Change Order Detail forms must be added as an attachment to the request. The Contractor and each sub-tier contractor (as applicable) must fill out the Labor Detail Sheet and Change Order Detail Sheet. Samples of these forms are included behind this section. In addition to these forms, the Contractor also must attach any material and equipment rental quotations. All of these documents should be scanned and saved as a PDF file. Click on the "Browse" box to upload the file. Be sure to wait until Building Blok tells you the file was "Uploaded Successfully".

4. Once the information is entered on the form and the proper attachments are uploaded, the contractor will click "Save". The Contractor will be prompted to enter their password to approve an electronic signature. Once you save the request you will have an opportunity to check it before submitting it to the CM. After you verify the COREF is correct click "Recommend Approval" to submit the change request to the CM. The Contractor will then be prompted to re-enter the password to approve an electronic signature and complete the submission request. Click on "Home" in the upper left corner to make sure the change order does not appear on your To-Do List.

5. The Change Order Request will then be reviewed by the CM Project Manager and Recommended for Approval, Rejected, or returned to the Contractor for additional information. Once the Construction Manager, Owner, and Architect have approved the request all parties will receive an email from Building Blok notifying them that a fully executed Change Order and Contract Recalculation Form can be downloaded from Building Blok. Hard copies of the executed change order and recalculation form will not be provided by the CM.

It is to be clearly stated that no extra work shall commence without an approval from the Owner or Construction Manager or Owner's representative.

END OF SECTION

CHANGE ORDER DETAIL FORM

(Provided by contractor, subcontractor or sub tier contractor)

DATE SUBMITTED:

CONTRACT:

CONTRACTOR:

PROJECT NAME:

CHANGE ORDER REQUEST #:

LABOR SECTION

TRADESMAN(s):	LABOR HOURS	RATE (per schedule)	SUBTOTAL
Subtotal			

MATERIAL SECTION

MATERIAL:	QUANTITY	UNIT COST	SUBTOTAL
Subtotal			

EQUIPMENT SECTION

EQUIPMENT:	QUANTITY	UNIT COST	SUBTOTAL
Subtotal			

SUBTOTAL	
SUBCONTRACTOR/ SUB TIER*	
OH & PROFIT (10% on sub/sub tier only))	
BOND COST	
OH & PROFIT (15% on own work)	
GRAND TOTAL	

LABOR DETAIL FORM

(Provided by contractor, subcontractor, or sub-tier contractor)

DATE:

CONTRACT:

CONTRACTOR:

PROJECT NAME:

CHANGE ORDER REQUEST #:

CLASSIFICATION:			
Base Wage Rate:			
Health Insurance			
Holidays			
Sick Days			
Life Insurance			
Disability Insurance			
Dental Insurance			
Company Vehicle			
401K			
Education			
Other (*specify below*)			
Subtotal			
Posted Prevailing Rate			
FICA (Social Security & Medicare)			
SUTA (State Unemployment)			
FUTA (Federal Unemployment)			
General Liability Insurance			
Worker's Compensation			
Total Wage Rate			

SECTION 012613 - CONTRACTOR COMPENSATION

1. GENERAL

A. The Contractor agrees to perform any additional Work, for the net cost of materials and labor (including wages paid, payroll taxes, and all insurance) plus the following percentage for all of his overhead and profit, which includes Field Supervision:

The percentages to be added or allowed for any Work change involving both added Work and omitted Work shall be applied only to the net difference in cost.

1. 15% mark-up (10% overhead and 5% profit) by the Contractor on Work performed by his own forces.

2. For work done by a Subcontractor, 10% for subcontractor overhead and 5% for subcontractor profit to which the Contractor may add 7.5% for his overhead and profit combined.

3. Contractor mark-up shall include supervision, home and field overhead, all self-owned small tools and equipment.

B. When the Contractor is directed to perform overtime work at the CM (Owner) expense to accelerate contractual work, the cost for same shall only be the actual premium costs incurred by the Contractor.

END OF SECTION

SECTION 012900 - PAYMENT PROCEDURES

1. GENERAL PROVISIONS

   A. The general provisions of the Contract, including the Conditions of the Contract (General, Supplementary and other conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

   B. Refer to provisions in AIA Document A232 - 2019 Edition, GENERAL CONDITIONS OF THE CONTRACT FOR CONSTRUCTION, CONSTRUCTION MANAGER AS ADVISOR EDITION, for requirements in addition to those specified in Division 1.

   C. For work being constructed under separate prime contracts, provisions of this Section apply to each contract being bid.

2. REQUIREMENTS INCLUDED

   A. Submit Applications for Payment to Construction Manager in accordance with the schedule and procedures established in the Contract Documents.

3. RELATED REQUIREMENTS

   A. Owner-Contractor Agreement.

   B. Conditions of the Contract: Article 9 PAYMENTS AND COMPLETION.

   C. Section 01 31 13: Project Coordination Meetings

   D. Section 01 33 00: Submittal Procedures

   E. Section 01 77 00: Closeout Procedures

4. FORMAT AND DATA REQUIRED

   A. Submit itemized applications typed on AIA Document G702/CMa, Application and Certificate for Payment, and Continuation Sheet G703, examples of which will be furnished to the Contractor at the Pre-Construction meeting.

   B. Provide itemized data on Continuation Sheet

      1. Format, schedules, line items and values: Duplicates of those of the schedule of values previously accepted by the Construction Manager.

5. PREPARATION OF APPLICATIONS FOR PROGRESS PAYMENTS

   A. Form: AIA Document G702/CMa

1. Fill in required information, including that for Change Orders executed prior to date of submittal of application.

2. Fill in summary of dollar values to agree with respective totals indicated on Continuation Sheets.

B. Continuation Sheets

1. Line items of components of Work will be subject to Owner's review and approval under the Provisions of Section 013300 - SUBMITTALS, and the General Conditions. Continuation Sheets shall follow Schedule of Values submitted at the start of the job.

2. Fill in total list of all scheduled components of Work, with item number and scheduled dollar value for each item. Fill in values of work completed in the period.

3. Fill in dollar value in each column for each scheduled line item when work has been performed or products stored; round off values to nearest dollar.

4. List each Change Order executed prior to date of submission, at the end of the Continuation Sheets; list by Change Order Number, and description, as for an original component item of work.

5. Contractor is to include a line item for "Closeout Documents" equaling 3.5% of their contract value.

6. PREPARATION OF APPLICATION FOR FINAL PAYMENT

A. Fill in Application form as specified in progress payments.

7. SUBMITTAL PROCEDURES

A. Complete Invoice:

1. Submit completed Application to the Construction Manager by the date stipulated in the Project Manual.

B. Number: Submit 3 copies of each invoice.

END OF SECTION

SECTION 013113 - PROJECT COORDINATION MEETING

1. PROJECT COORDINATION MEETING

   A. An on-site project coordination meeting will be held on a biweekly basis throughout the project construction period.

2. ATTENDANCE

   A. Attendance at the project coordination meeting is mandatory of each Contractor or major supplier on the project.

   B. The representative of the Contractor shall be the Project Manager and field superintendent unless a substitute representative has been approved by the Construction Manager.

   C. Contractor will begin attending the Project Coordination Meetings at least 4 weeks prior to mobilization on site and will continue until the Contractor has fulfilled the obligations of his Contract.

3. AGENDA

   A. The Construction Manager will set the agenda for the biweekly Project Coordination Meeting.

   B. At a minimum, the Contractor shall be prepared to discuss the following:

      1. Actual vs. as planned progress for the prior two-week period.

      2. Planned construction activities for the next four weeks.

      3. Contract document clarifications.

      4. Coordination items with other contractors.

      5. Quality Control.

      6. Recently issued change orders.

      7. Potential change orders.

      8. Submittals and shop drawings.

      9. Other items requiring Construction Manager's attention.

END OF SECTION

SECTION 013119 – PRE-INSTALLATION MEETINGS

1. PRE-INSTALLATION MEETINGS

   A. An on-site pre-installation meeting will be held at least two weeks prior to commencement of installation of work.

2. ATTENDANCE

   A. Attendance at the pre-installation meeting is mandatory of each Contractor and/or major supplier as required for each specific meeting listed below.

   B. The following individuals shall attend these meetings:
      - Contractors' Project Manager
      - Contractors' Field Superintendent
      - Contractors' Safety Representative (as needed)
      - Key Subcontractors, Suppliers, and Vendors
      - EDiS Project Manager
      - EDiS Field Manager
      - EDiS Safety Director (as needed)
      - EDiS MEP Specialist (as needed)
      - Owner's Representative (as needed)
      - Architect/Engineer (as needed)
      - Governmental Agency Representatives (as needed)
      - Testing/Inspection Agency Representatives (as needed)
      - Utility Company Representatives (as needed)

3. SUBMITTALS

   A. Each contractor is responsible to have all submittals and mock-ups, as related to the pre-installation meeting scope of work, submitted and approved prior to commencement of the pre-installation meeting.

4. LIST OF REQUIRED MEETINGS

   - Selective Demolition
   - Doors/Frames/Hardware
   - Interior Glass and Glazing
   - Finish Carpentry & Millwork
   - Acoustical Ceilings/Acoustical Wall Panels
   - Paint and VWC
   - Flooring (VCT, Carpet)
   - Operable Partitions
   - Partition Walls
     - Metal Studs
     - Drywall

  - Insulation
  - Doors/Frames/Hardware
- Fire Protection
  - Fire Sprinkler Systems
  - Fire Alarm Systems
- MEP Coordination
  - Mechanical Piping Roughin
  - Plumbing Roughin
  - Insulation
  - Electrical Roughin
  - Electrical – Bonding, grounding, lightning protection
  - Automatic Temperature Controls
  - Commissioning
- Voice/Data Low Voltage Wiring
- Security System
- Audio-Visual Equipment
- Owner Furnished Equipment
- Final Cleaning

5. AGENDA

   A. At a minimum, the Contractor shall be prepared to discuss the items as listed on the agenda template shown on the following page:

PROJECT: NCC HODGSON VOTECH HIGH SCHOOL

PRE-INSTALLATION MEETING: _____
(Insert Phase of Work)

A. ATTENDEES:

NAME	COMPANY	WORK ITEM	CONTRACT

B. TESTING & INSPECTION REQUIREMENTS
(THESE REQUIREMENTS COME FROM THE PROJECT MANUAL)

C. REVIEW CONTRACT DRAWINGS AND SPECIFICATIONS

Drawing / Spec No.	Comments / Conflicts

D. REVIEW SCOPES OF WORK ***(SEE SECTION 011100 IN THE PROJECT MANUAL)***

E. REVIEW RELEVANT RFI'S

F. REVIEW SUBMITTALS *(SEE THE SUBMITTAL REGISTER)*

G. REVIEW MATERIALS AND DELIVERIES

H. REVIEW SCHEDULE AND SEQUENCE OF WORK

I. JOB SITE SAFETY *(SEE THE CONTRACTOR'S SAFETY PROGRAM OR OSHA)*

- Safety Plans must be submitted before the start of work
- Certificates of Insurance need to be submitted before the start of work
- Minimum PPE – Hardhats, steel toe boots, safety glasses
- Lock-out, Tag, Test and Try ALL utilities is critical before the start of demolition
- Signage & HAZCOM Requirements
- Potential Hazards
    - Excavations >4 ft
    - Slips/trips/falls
    - Existing utilities to remain and protected
    - Overhead debris
    - Power tools
    - Heavy equipment

J. COORDINATION WITH OTHER TRADES

K. ACTION ITEMS AND RESPONSIBILITY

END OF SECTION

SECTION 013125– WEB-BASED PROJECT MANAGEMENT SYSTEM

1. GENERAL PROVISIONS

   A. The general provisions of the Contract, including the Conditions of the Contract (General, Supplementary and other Conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

   B. Refer to provisions in AIA Document A232 – 2019 EDITION, GENERAL CONDITIONS OF THE CONTRACT FOR CONSTRUCTION, for requirements in addition to those specified in Division 1.

   C. Refer to Scope Information Sheets for all contracts bound in the Project Manual under Section 011100 - SUMMARY OF WORK. The Scope Information Sheets describe generally the work included in each contract, but the work is not necessarily limited to that described.

   D. All Contractors shall use Internet/Web-based project management software to transmit documents, track, and otherwise manage this project.

   E. Use of this project management software will not change any contractual responsibilities of the construction team members.

2. DEFINITIONS

   A. System: A real time web-based software that shares data, translates data, organizes data, facilitates communication, archives actions, and offers scheduling prompts to identified Users.

   B. Users: Authorized participants of this project furnished with a unique password and authorized to access the system to view/input/export data. Owner, Construction Manager, Architect, and the Contractors are all Users. Other Users may be added as necessary.

   C. Contacts: Entities identified to automatically receive specific transmissions or entities selected to receive specific information sent by the system through to an e-mail address.

   D. Signees: Those individuals identified, by the Contractors, authorized to sign change orders and payment applications via electronic signature. This electronic signature is as contractually binding as an original signature on paper.

3. USE OF SYSTEM

   A. The use of the system is mandatory for the documentation of the transmittal of all non-oral information, even if the actual transmission of the information is by another means.

   B. The use of the system will be mandatory by the Contractors to send, retrieve, and respond to data.

   C. In addition to this web-based project management system, the Contractors will be required to use electronic mail (email) for day-to-day communication and correspondence. Email will be the

primary means of transmitting written communication (i.e. meeting minutes, draft pay applications, etc.).

4. QUALITY ASSURANCE

   A. A three-hour training session in the use of the software for this project will be offered by the Construction Manager at a location convenient to the project site. Attendance by one member of each Contractor's organization is mandatory. Additional attendees may enroll based on availability of training space. All attendees must have a working knowledge of computers. Training can not begin until three working days after the receipt of the submittals indicated below.

   B. Technical assistance will be provided by on-line help, email, or telephone for all Users through-out the life of the project.

5. SUBMITTALS

   A. Submit to the Construction Manager, within 5 days following the receipt of the letter of intent to award, in an electronic template, the following:

      1. Electronic logo of organization (as needed)
      2. Names, mailing address and electronic address of its Users and Contacts.
      3. Designation the role/responsibility for each User

6. SOFTWARE AND HARDWARE REQUIREMENTS

   A. Each User shall provide and maintain a computer with high-speed internet access and an email address. The computer shall have a high-speed internet browser (Internet Explorer 8.0 or higher, Firefox version 3.6.12 or higher, Google Chrome or Safari version 5.0 or higher) and a high speed cable Internet access, high speed DSL or T1 line.

   B. License(s) to Use System - Each Contractor will be provided unlimited licenses to use the system for this project. Each license will allow secure unlimited usage from the notice to proceed until the original contract completion date.

7. SYSTEM DESCRIPTION

   A. The web-based project management system is a "secure, real-time, interactive, centralized database" specifically established and maintained for the management of this construction project. The product is designed to facilitate communication and improve the time management of its users by facilitating the sharing of information. Information will be available 24/7, from any computer meeting the specifications listed above. The information is fully protected. The electronic platform allows information to be transmitted across the internet reducing printing and postage costs and the time associated with such activities.

   B. The system contains a directory of the project participants.

C. The system includes templates, with the CM's letterhead, for each document created inside the system. The template allows the use of "pull down" menus to complete significant portions of each document.

D. The system allows the templates (and attached documents created outside the system) to be distributed to Users and Contacts.

E. The System contains "translation software" to permit the viewing (and marking) of documents created outside the system. The system can view documents created by different software programs and can deliver images of its translation to any computer meeting the criteria listed above.

F. The system can be personalized by the Construction Manager to automatically send e-mail notices upon issuance of certain documents if such a practice facilitates the User's business needs.

G. The system is the product of ***Building Blok, LLC*** (www.buildingblok.com) and will be continuously updated.

H. The Construction Manager will administer the Building Blok User accounts for this project.

8. DOCUMENTS CREATED INSIDE THE SYSTEM

A. The following documents shall be created on templates inside the system.

1. Transmittals for submittals processed in the system. The transmittals are automatically created by the system when the submittal is uploaded.
2. Submittal Register showing all of the submittals required of the contract, assigned to each Contractor.
3. Submittal Log: The CM will maintain submittal log after it is initialized.
4. RFI (Requests for Information)
5. Change Orders
6. RFP (Requests for Proposal)
7. ASI (Architect's Supplemental Instructions)
8. Tasks & Memos as determined by the CM
9. Payment Applications
10. Closeout Tracking Log

B. The following documents may, at each Users option, be created on the system.

1. Morning & Afternoon Activity Reports generated by the system
2. E-mails: Contacts that do not have access to the system may be sent information from the system, by the system.
3. Reports of information on the system
4. Project Notices: "Broadcast" messages can be sent to other Users system entry screen.

9. DOCUMENTS CREATED OUTSIDE THE SYSTEM AND DISTRIBUTED BY THE SYSTEM

   A. The following documents are expected to be created outside the system and distributed through the system. The actual documents may be scanned or electronically attached to the transmittal.

      1. Technical Submittals: Shop drawings, product data, testing reports, certifications, installation instructions, operation & maintenance manuals, will be submitted and distributed through the system. The Architect will return all submissions through the system electronically. The Construction Manager will distribute submittals (after Architect's action) electronically. Contractors may download and distribute submittals to their subcontractors and suppliers or elect to print paper copies for distribution, or both.
      2. Photographs: Digital photographs and scanned images can be loaded onto the system and shared.
      3. Schedule of Values/ Payment Applications: (The "pencil" review of these documents can occur inside the system).
      4. Change Orders: (The "pencil" review of these documents can occur inside the system.)
      5. Schedules: The schedule document(s) will be available for review on the system.
      6. Data created in other software may be uploaded to the system electronically.

10. DOCUMENTS CREATED OUTSIDE THE SYSTEM AND DISTRIBUTED OUTSIDE THE SYSTEM

   A. The following documents are expected to be created outside the system and distributed outside the system. The actual documents may be scanned or electronically attached to the transmittal.

      1. Schedules: The Construction Manager will develop the Master Schedule through Microsoft Project 2003. The schedule will be distributed either through hard copies at meetings or through email.
      2. Product samples, color samples, physical samples are still required to be provided per the technical specifications, however, the transmittal documenting the distribution shall be done inside the system and submitted electronically and printed to accompany the actual submission.
      3. Meeting minutes will be created using Microsoft Word 2003 and distributed through hard copies at meetings or through email.
      4. AIA closeout documents, which require an "original" signature, will created and distributed outside the system.

END OF SECTION

SECTION 013216 - CONSTRUCTION SCHEDULE

1. PRE-BID CONSTRUCTION SCHEDULE

   A. Time is a critical element of this Project. By entering a bid, the Contractor agrees to adhere to the intermediate Milestone Dates and Dates of Substantial and Final Completion established herein. The Contractor also understands that all work must be performed in an orderly and closely coordinated sequence in order to achieve the specified Milestones and Completion Dates, and the Contractor hereby agrees to perform his work in conformance with the Pre-Bid Construction Schedule established herein, or with the then current and approved Project Construction Schedule as amended from time to time by the Construction Manager.

   B. The Pre-Bid Construction Schedule is a milestone schedule with durations that identify portions of the project that must be completed. This schedule includes allowances for time lost due to adverse and abnormal weather conditions, other than floods, hurricanes, tornadoes, lightening and other like acts of God. The Contractor understands and agrees that it shall not be entitled to any extensions of the Contract Time or adjustment to the Contract Sum, except as allowed in the General Conditions of the Contract for Construction. The Contractor further acknowledges that the Work may be required to be performed during the winter season, that conditions during this season may be adverse and abnormal, but that such conditions will not be the basis for an extension of the Contract Time or adjustment to the Contract Sum. By submitting a bid, each Contractor is certifying that they can complete their work within the durations, or less time, outlined in the milestone schedule and its bid includes any and all costs associated with the schedule. This includes one Contractor completing their work in conjunction with another Contractor's work (i.e. electrical conduits installed in CMU walls). Each Contractor agrees to provide sufficient labor, crew size, equipment and/or work overtime, weekends, or shiftwork as necessary to meet the activity durations on this schedule and subsequently the latest coordinated Project Construction Schedule.

2. SCHEDULING OF THE WORK AFTER AWARD OF CONTRACT

   A. After award of Contract, or issuance of a Notice to Proceed, the Contractor will meet with the Construction Manager to review the Pre-Bid Construction Schedule, and the overall project plan for construction. Following the above review, the Contractor will meet with each subcontractor and supplier to view the detailed plans for performing his Work. Following these meetings and within fourteen (14) days after award of the Contract or issuance of a Notice to Proceed, the Contractor shall prepare and submit for the Construction Manager's approval a Work Schedule providing for the expeditious, timely and practical execution of the Work. The Contractor's Work Schedule shall include activity descriptions and durations for shop drawings, fabrication, delivery, and installation. The Contractor's Work Schedule shall be organized by Area, Building, Phase, and/or Floor as required by the Construction Manager. If the Construction Manager so requests, the Contractor shall provide adequate explanation regarding crew sizes, production rates and similar data used to arrive at the durations and sequences. If the Contractor fails to provide a work schedule for their activities then they will be held to the Project Construction Schedule developed and updated by the Construction Manager.

   B. The Construction Manager shall review the Contractor's Work Schedule, coordinate it with the separate work by other contractors, the Owner, and the Construction Manager, and after coordination, shall incorporate it into the approved Project Construction Schedule.

C. After all Contractors submit their Work Schedules and the schedules have been incorporated into the overall Project Construction Schedule a Schedule Charrette will be held by the Construction Manager. Each Contractor is required to participate in the Schedule Charrette in order to produce a coordinated Project Construction Schedule. The Construction Manager will have the final authority concerning the sequence of work, priorities or work, and activity durations. The approved coordinated Project Construction Schedule shall be issued to the Contractors and each Contractor shall perform their Work in conformity therewith.

C. The Contractor shall submit proposed schedule revisions and obtain the written approval of the Construction Manager therefore before deviating from the Project Construction Schedule.

D. The Construction Manager will incorporate approved schedule revisions into the Project Construction Schedule and shall otherwise update and revise the Project Construction Schedule as the Construction Manager, at his sole discretion, deems necessary. Each Contractor acknowledges that Construction Manager may modify, change, or alter the sequence, duration, start dates, completion dates to maintain the progress of the work. Contractor agrees to perform the work in accordance with the revised schedules and that modification of the schedule or sequence of the work by the Construction Manager shall not be the basis of any claim by the Contractor for damages or costs.

E. Weather Delays: The project substantial completion date, shall only be adjusted due to extreme weather conditions that are above and beyond the following "Adverse Weather Days" already accounted for in the Pre-Bid Construction Schedule. These adverse weather days are based on a seven day week and come from the DelDOT Standards:

a. January (12), February (10), March (5), April (5), May (4), June (2), July (4), August (3), September (4), October (3), November (2), and December (6).
b. Time extension due to weather must be related to critical path activities.
c. Delays due to weather must be reported by the Contractor on the day they occur on the Contractor's daily report.
d. Any time lost during the work week must be made up the same week by overtime and/or working weekends. The Owner will not be responsible for additional costs for overtime.

3. ADHERENCE TO THE SCHEDULE

A. The Contractor shall start each part of its Work on the date designated for start in the approved Project Construction Schedule unless advised by the Construction Manager. The Contractor shall carry the Work forward expeditiously with adequate forces, equipment, and materials, and shall complete each part of his work on or before the date designated in the approved Project Construction Schedule.

B. If the Construction Manager determines that the Contractor is behind schedule, the Construction Manager shall have the right to require that the Contractor take steps, at the Contractor's expense, to accelerate its Work. Such steps shall include increases in manpower, equipment, and materials and/or overtime as the Construction Manager may deem necessary. If any work is not started or completed within five (5) calendar days of the schedule date in the latest Project Construction Schedule, the Construction Manager shall have the right to direct the Contractor to expedite their work by whatever means the Construction Manager

deems necessary to regain the schedule, without additional compensation to the Contractor. If any work falls behind schedule more than ten (10) days, the Construction Manager shall have the right to perform the work or have the work performed by whatever means the Construction Manager deems necessary. The costs incurred by the Construction Manager in order to "maintain the Project Construction Schedule" shall be reimbursed by the Contractor or Contractors causing the delay. If the Contractor fails to comply with the Construction Manager's instructions relating to improved rate of progress, the Contractor may be held in default under the appropriate provisions of the General Conditions of the Contract.

C. Each Contractor shall, if directed by the Construction Manager, provide the Construction Manager a two-week look ahead of anticipated manpower showing the number of men, classification, and anticipated work.

D. Each Contractor must schedule their manpower to work on all available work at a given time. Contractors must not assume that they have an entire work area available at one time or exclusive to their work. Working simultaneously in and around other trades is required. Therefore, if an area of the building is ready for the Contractor's work to begin or continue the Contractor must have manpower onsite working. While working on site, each Contractor is to have their foreman attend weekly pull planning coordination meetings in the EDiS site trailer to review and update the 2-week lookahead schedule.


E. If a Contractor misses any portion of a workday due to weather, manpower, lack of materials, failure to plan, or scheduling conflicts, they must make-up this lost time on overtime or Saturday. If two or more days are lost in the same work week, the Contractor must work overtime, the immediate Saturday and the Saturdays following the week to make up the lost days. Failure to provide sufficient manpower during the normal week days may result in charges for supervision by EDiS Company, at the discretion of EDiS Company.

F. All punchlist work and project closeout documentation shall be completed within twenty-one (21) calendar days of the Substantial Completion date. Any open punchlist items after this date will be completed by EDiS Company and back charged to the responsible Contractor.

END OF SECTION

NEW CASTLE COUNTY VO-TECH SCHOOL DISTRICT
NEW HODGSON VO-TECH HIGH SCHOOL
BP-D BID SCHEDULE

ID	Task Name	Duration	Start	Finish
1	**NEW CASTLE COUNTY VO-TECH SCHOOL DISTRICT (NCCVT) - NEW HODGSON VO-TECH HIGH SCHOOL**	**1477 days**	**Wed 1/19/22**	**Thu 9/16/27**
12	**NEW CASTLE COUNTY (NCCo), REGULATORY & AGENCY REVIEWS**	**498 days**	**Fri 3/11/22**	**Tue 2/6/24**
79	NCCo Records Project and Issues Recorded Plans	10 days	Mon 12/4/23	Mon 12/18/23
80				
81	**BUILDING PERMIT PROCESS**	**36 days**	**Tue 12/19/23**	**Tue 2/6/24**
178	**NEW HODGSON VO-TECH HIGH SCHOOL - CONSTRUCTION DOCUMENT PHASE 100% (BID PACKAGE 'E' Demolition and Fields)**	**152 days**	**Mon 1/6/25**	**Tue 8/5/25**
242	**BID PACK 'D' - BUILDING ENVELOPE AND FITOUT (PHASE 4)**	**510 days**	**Thu 12/7/23**	**Wed 11/19/25**
277	**NEW HODGSON VO-TECH HIGH SCHOOL - CONSTRUCTION ACTIVITIES**	**1134 days**	**Mon 5/15/23**	**Thu 9/16/27**
288	**PHASE 1 - ESTABLISH SWM CONTROLS**	**31 days**	**Mon 10/23/23**	**Mon 12/4/23**
289	**PRELIMINARY SITEWORK**	**31 days**	**Mon 10/23/23**	**Mon 12/4/23**
292	Install Construction Entrance	4 days	Wed 11/1/23	Mon 11/6/23
296	**PHASE 3 - CONSTRUCT ROADS/PARKING LOTS/BUILDING PAD**	**80 days**	**Wed 11/29/23**	**Tue 3/19/24**
297	Install Site Utilities	30 days	Wed 11/29/23	Tue 1/23/24
298	Prepare Building Pad	20 days	Wed 1/24/24	Tue 2/20/24
299	Construct Access Roads, Parking Lots, and Laydown Areas	20 days	Wed 2/21/24	Tue 3/19/24
300	**PHASE 4 - CONSTRUCT BUILDING**	**602 days**	**Wed 3/6/24**	**Thu 6/25/26**
301	**BUILDING FOUNDATIONS & SLABS**	**71 days**	**Wed 3/6/24**	**Wed 6/12/24**
302	**Area A: Building Foundations and Slabs**	**47 days**	**Wed 3/6/24**	**Thu 5/9/24**
303	Install Footers & Piers	10 days	Wed 3/6/24	Tue 3/19/24
304	Install CMU Foundations	8 days	Mon 3/11/24	Wed 3/20/24
305	Install Waterproofing	8 days	Thu 3/14/24	Mon 3/25/24
306	Install Backfill	2 days	Tue 3/26/24	Wed 3/27/24
307	Construct Elevator Shaft	12 days	Thu 3/28/24	Fri 4/12/24
308	Construct Stair 3	12 days	Thu 3/28/24	Fri 4/12/24
309	Install Underslab Utilities	10 days	Thu 3/28/24	Wed 4/10/24
310	Install Stone & Slab-on-Grade	9 days	Thu 4/11/24	Tue 4/23/24
311	Construct Stair 4	12 days	Wed 4/24/24	Thu 5/9/24
312	**Area B: Building Foundations and Slabs**	**32 days**	**Wed 3/20/24**	**Thu 5/2/24**
313	Install Footers & Piers	7 days	Wed 3/20/24	Thu 3/28/24
314	Install CMU Foundations	7 days	Mon 3/25/24	Tue 4/2/24
315	Install Waterproofing	8 days	Thu 3/28/24	Mon 4/8/24
316	Install Backfill	2 days	Tue 4/9/24	Wed 4/10/24
317	Install Underslab Utilities	8 days	Thu 4/11/24	Mon 4/22/24
318	Install Stone & Slab-on-Grade	8 days	Tue 4/23/24	Thu 5/2/24
319	**Area C: Building Foundations and Slabs**	**40 days**	**Fri 3/29/24**	**Thu 5/23/24**
320	Install Footers & Piers	5 days	Fri 3/29/24	Thu 4/4/24
321	Install CMU Foundations	12 days	Wed 4/3/24	Thu 4/18/24
322	Install Waterproofing	8 days	Mon 4/8/24	Wed 4/17/24
323	Install Backfill	2 days	Thu 4/18/24	Fri 4/19/24
324	Install Underslab Utilities	10 days	Mon 4/22/24	Fri 5/3/24
325	Install Stone & Slab-on-Grade	14 days	Mon 5/6/24	Thu 5/23/24
326	**Area D: Building Foundations and Slabs**	**37 days**	**Mon 3/11/24**	**Tue 4/30/24**

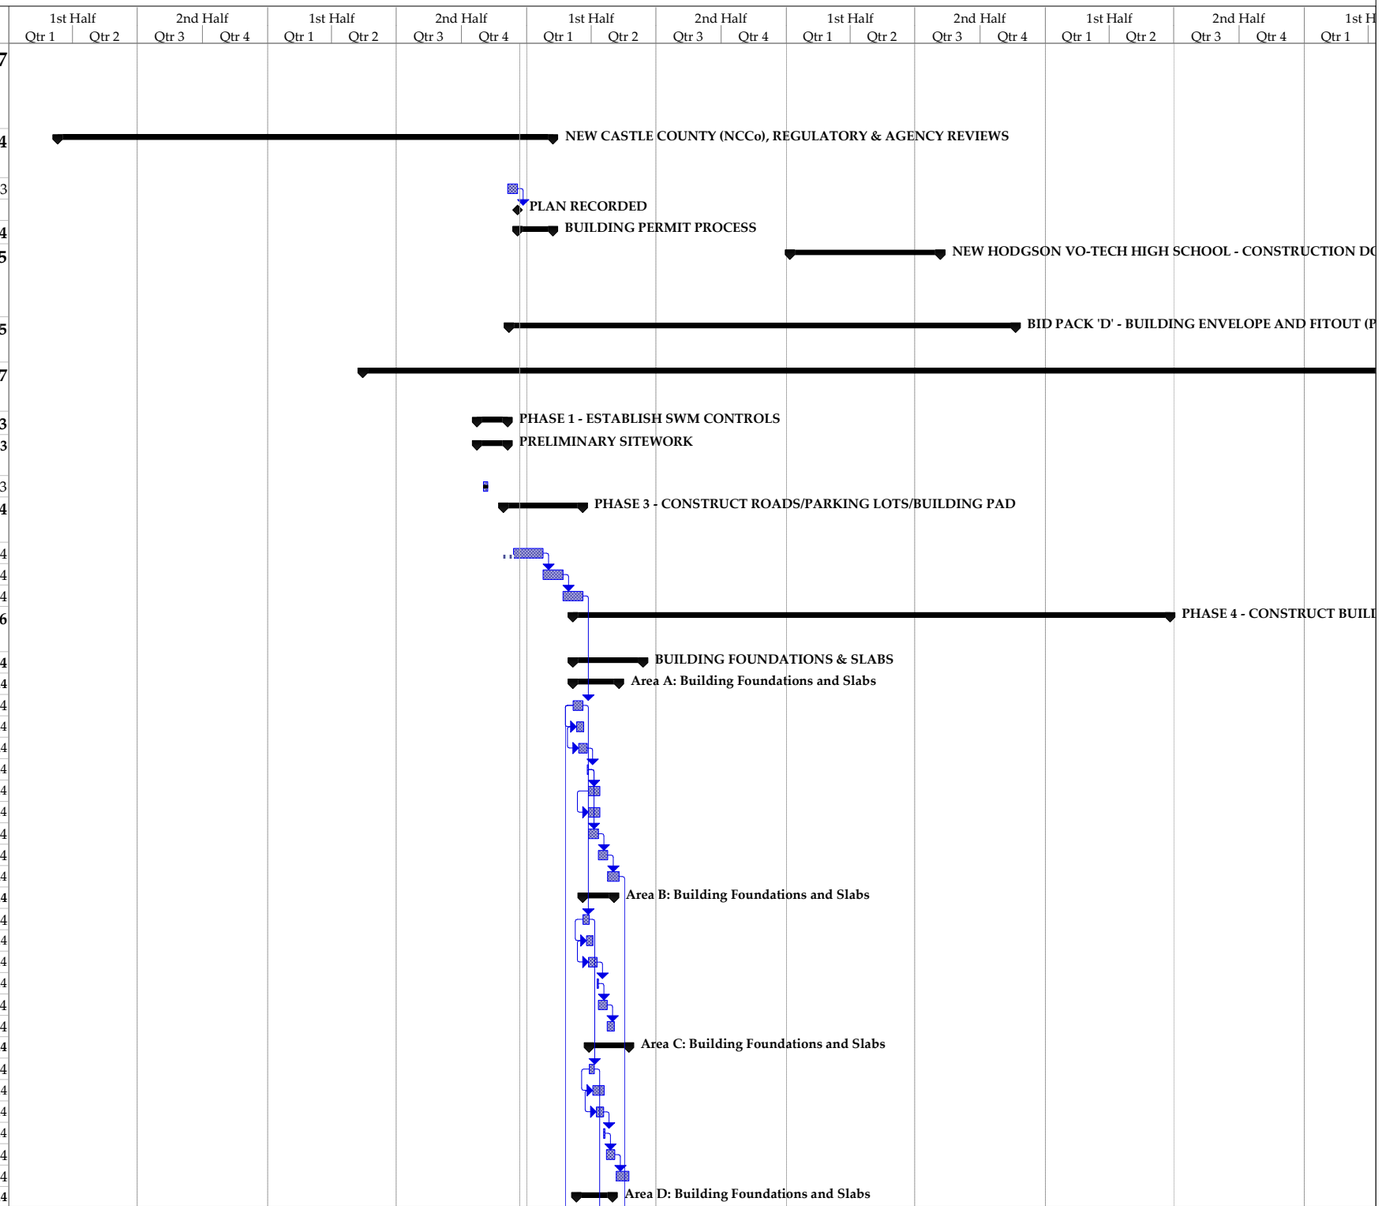


New Hodgson High School
Bid Schedule BP-D Addendum #1
Date: Updated 28Dec 2023

Task | Split | Milestone | Summary | Project Summary | Manual Summary | Start-only | Finish-only | Progress | Deadline

NEW CASTLE COUNTY VO-TECH SCHOOL DISTRICT
NEW HODGSON VO-TECH HIGH SCHOOL
BP-D BID SCHEDULE

ID	Task Name	Duration	Start	Finish
327	Install Footers & Piers	5 days	Fri 4/5/24	Thu 4/11/24
328	Install CMU Foundations	11 days	Mon 3/11/24	Mon 3/25/24
329	Install Waterproofing	8 days	Thu 3/14/24	Mon 3/25/24
330	Install Backfill	2 days	Tue 3/26/24	Wed 3/27/24
331	Install Underslab Utilities	10 days	Thu 3/28/24	Wed 4/10/24
332	Install Stone & Slab-on-Grade	14 days	Thu 4/11/24	Tue 4/30/24
333	**Area E: Building Foundations and Slabs**	**38 days**	**Fri 4/12/24**	**Tue 6/4/24**
334	Install Footers & Piers	10 days	Fri 4/12/24	Thu 4/25/24
335	Install CMU Foundations	13 days	Wed 4/17/24	Fri 5/3/24
336	Install Waterproofing	8 days	Mon 4/22/24	Wed 5/1/24
337	Install Backfill	2 days	Thu 5/2/24	Fri 5/3/24
338	Install Underslab Utilities	10 days	Mon 5/6/24	Fri 5/17/24
339	Install Stone & Slab-on-Grade	12 days	Mon 5/20/24	Tue 6/4/24
340	**Area F: Building Foundations and Slabs**	**34 days**	**Fri 4/26/24**	**Wed 6/12/24**
341	Install Footers & Piers	5 days	Fri 4/26/24	Thu 5/2/24
342	Install CMU Foundations	11 days	Wed 5/1/24	Wed 5/15/24
343	Install Waterproofing	8 days	Mon 5/6/24	Wed 5/15/24
344	Install Backfill	2 days	Thu 5/16/24	Fri 5/17/24
345	Install Underslab Utilities	7 days	Mon 5/20/24	Tue 5/28/24
346	Install Stone & Slab-on-Grade	11 days	Wed 5/29/24	Wed 6/12/24
347	BUILDING STRUCTURE & ENVELOPE	300 days	Fri 5/10/24	Thu 7/3/25
348	Erect Structural Steel	140 days	Fri 5/10/24	Thu 11/21/24
349	Pour Slab on Deck	50 days	Fri 6/21/24	Thu 8/29/24
350	Exterior Framing, Sheathing	120 days	Fri 7/5/24	Thu 12/19/24
351	Exterior Masonry Veneer	120 days	Fri 8/2/24	Thu 1/16/25
352	Exterior Metal Panels	120 days	Fri 8/30/24	Thu 2/13/25
353	Install Roofing	80 days	Fri 11/22/24	Thu 3/13/25
354	Install Windows, Storefront & Curtainwall	120 days	Fri 1/17/25	Thu 7/3/25
355	INTERIOR FRAMING AND MEP ROUGHINS	240 days	Fri 1/31/25	Thu 1/1/26
356	Install Interior CMU	120 days	Fri 1/31/25	Thu 7/17/25
357	Install Metal Stud Framing	100 days	Fri 3/14/25	Thu 7/31/25
358	Above Ceiling MEP Roughins	120 days	Fri 4/11/25	Thu 9/25/25
359	In-wall MEP Roughins	100 days	Fri 4/11/25	Thu 8/28/25
360	Hang & Finish Drywall	100 days	Fri 8/15/25	Thu 1/1/26
361	INTERIOR FINISHES	125 days	Fri 9/12/25	Thu 3/5/26
362	FINISH SITEWORK & LANDSCAPING	80 days	Fri 7/4/25	Thu 10/23/25
363	COMMISSIONING & PUNCHLIST	40 days	Fri 3/6/26	Thu 4/30/26
364	OWNER MOVE-IN AND SETUP OF FF&E	40 days	Fri 5/1/26	Thu 6/25/26
365	NEW HODGSON VO-TECH RIBBON CUTTING	0 days	Thu 6/25/26	Thu 6/25/26
366	**PHASE 5 - EXISTING BUILDING ABATEMENT & DEMOLITION**	**122 days**	**Wed 6/10/26**	**Thu 11/26/26**
371	**PHASE 6 - CONSTRUCT ATHLETIC FIELDS**	**260 days**	**Fri 9/18/26**	**Thu 9/16/27**
372	Construct Field House	60 days	Fri 9/18/26	Thu 12/10/26
373	Construct Stadium Field & Track	50 days	Fri 11/13/26	Thu 1/21/27
374	Construct Practice Fields	80 days	Fri 9/18/26	Thu 1/7/27
375	Allow Fields to be Fully Established	180 days	Fri 1/8/27	Thu 9/16/27

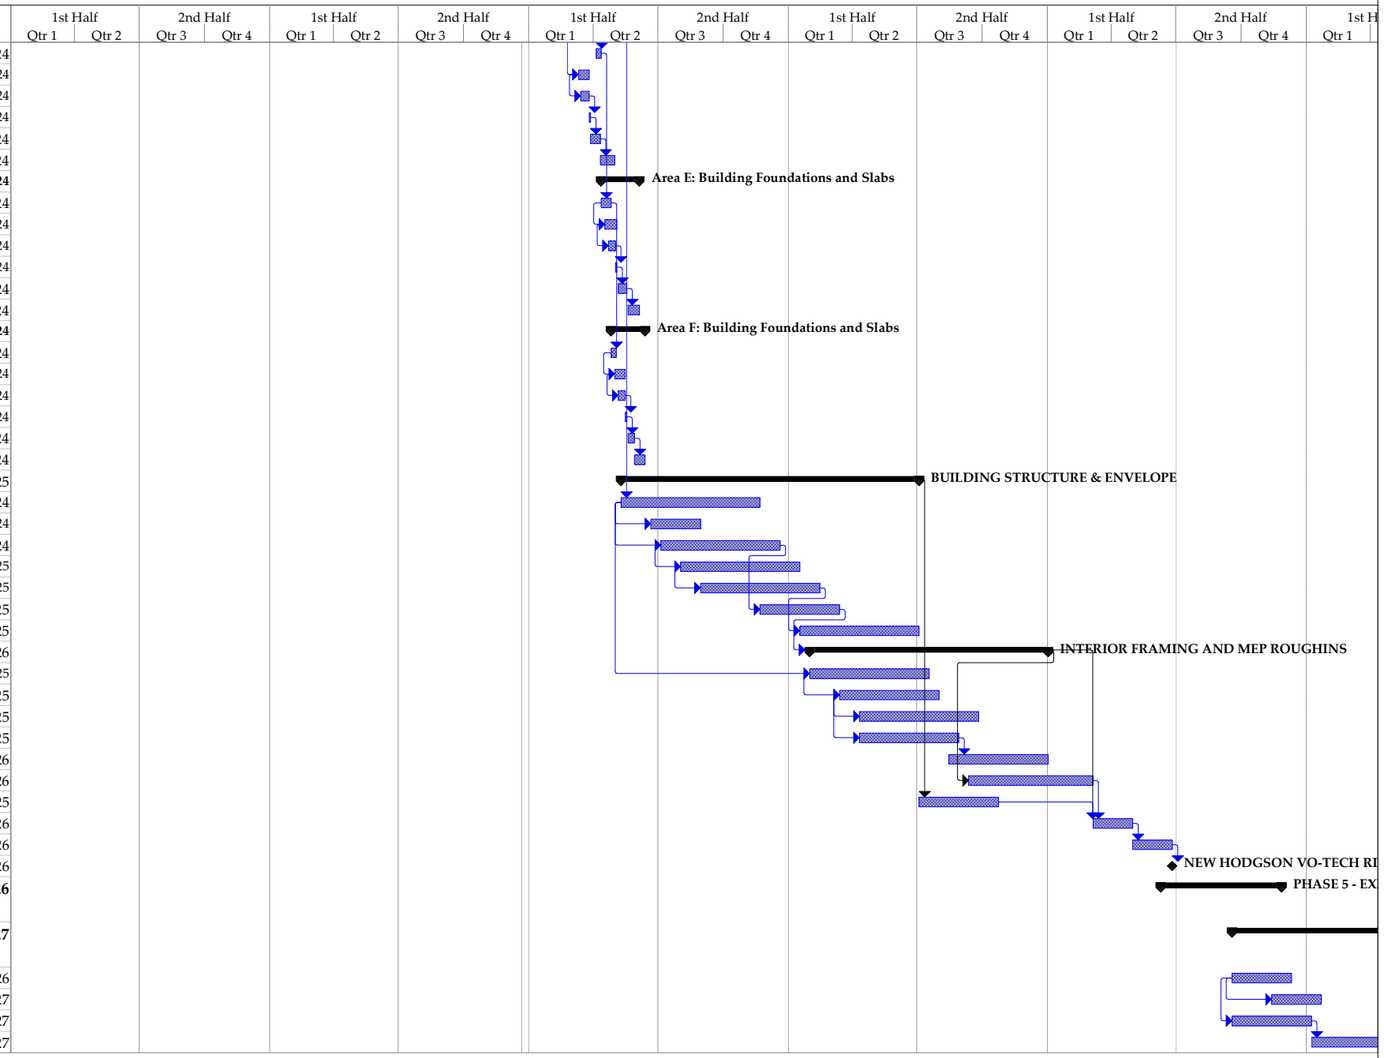

New Hodgson High School
Bid Schedule BP-D Addendum #1
Date: Updated 28Dec 2023

Task | Split | Milestone | Summary | Project Summary | Manual Summary | Start-only | Finish-only | Progress | Deadline

SECTION 013219 - SUBMITTAL REGISTER

1. SUBMITTALS/SUBMITTAL REGISTER

   A. The Contractor shall submit all items listed or specified within the sections of the Specifications included in its Work. Submittals shall include such items as: contractor's, manufacturer's or fabricator's drawings; descriptive literature including, but not limited to, catalog cuts, diagrams, operation charts or curves; test reports; samples, operations and maintenance manuals, including parts lists; certifications; warranties and other required submittals. Submittals pertinent to materials and equipment which are subject to advance approval shall be scheduled and made prior to the acquisition or the delivery thereof.

   B. The Contractor shall carefully control procurement operations to assure that each individual submittal is made on or before the dates required for timely performance of its Work.

   C. Within seven (7) days after award of Contract or issuance of Notice to Proceed, the Contractor shall execute and submit to the Construction Manager, seven (7) copies of the Submittal Register, on a form to be provided by the Construction Manager, on which shall be listed each item of equipment and material of each type for which fabricator's drawings and/or related descriptive data, test reports, samples, spare parts, operation and maintenance manuals, or other types of submittals required by the Specifications. The Submittal Register form shall be reproduced by the Contractor. The order of listing of items on the Register shall conform to the sequence of the items as they occur within the divisions. Drawings of component items forming a system or that are interrelated shall be scheduled to be correlated and submitted concurrently. Certifications to be submitted with the pertinent drawings shall be so scheduled. Adequate time shall be allowed for review and approval and possible resubmittal of any item subject to approval, because no delay damages or time extensions will be allowed for time lost in late submittals or resubmittals. The Construction Manager and Architect/Engineer will review the Submittal Register for approval action. The approved Register will become a part of the Contract and Contractor will be subject to requirements thereof. The Contractor shall revise and/or update the Register monthly to take into account all changes in the Contract. Each such revised edition and/or revision to the Register shall be resubmitted to the Construction Manager. This Register shall be coordinated with related submittals of other Contractors.

2. SAMPLES

   A. Submit tagged or labeled samples in triplicate, unless another quantity is otherwise specified by the Construction Manager.

   B. Tags or labels shall be securely affixed and contain as a minimum the following information: Project Name, Contractor's Name, Contract Title and Number, Date, Transmittal Number, Product Manufacturer's or Fabricator's Name and Product Identifier.

END OF SECTION

SECTION 013226 - CONTRACTOR DAILY REPORTS

1. CONTRACTOR DAILY REPORTS

   A. The Subcontractor shall submit a Daily Report to the Construction Manager on the forms provided covering the following subjects:

      1. Work in Progress, including areas where work is being performed, nature of the operations in progress, and the manpower assigned.

      2. Extra Work (Time and Material) in progress.

      3. Materials Received.

      4. Trade labor breakdown including identification of all workers on site and the number of hours (or portions thereof) worked by each.

      5. Inspection Checklist (performed daily).

   B. The Subcontractor shall submit the Daily Report to the Construction Manager by 9:00 AM on the next workday following the workday covered in the Daily Report.

2. DAILY EXTRA WORK REPORT

   A. The Subcontractor shall submit on the form provided a Daily Extra Work Report on each day he performs authorized Extra Work on a time and material basis.

   B. A separate Daily Extra Work Report shall be submitted for each separate authorized Extra Work item done on a time and material basis.

   C. The Subcontractor shall submit his Daily Extra Work Report as an attachment to his Daily Report by 9:00 AM on the next workday following the workday covered in the Daily Extra Work Report.

3. SAMPLE DAILY REPORT

   A. A sample daily report follows this section for your reference.

END OF SECTION

EDiS COMPANY

CONTRACTOR'S DAILY REPORT

Project Name: Hodgson Vocational Technical High School

Date:

Contractor:

Contract No. & Description:

Weather:

Foreman's Name (Print)

TRADE	*CLASS	MANPOWER COUNT	TOTAL MAN HOURS	TODAY'S DESCRIPTION / LOCATION OF WORK
	TOTAL			

* *INDICATE: F = FOREMAN; J = JOURNEYMAN; A = APPRENTICE*

Work Status/Work Planned:

Construction Equipment:

Qualified Operator(s)

Deliveries or Materials:

Machinery, tools, material, and equipment to be used:

Inspection of work area, machinery, tools, material, or equipment

The use of any machinery, tool, material, or equipment which is not in compliance with any applicable requirement Is prohibited. Such machine, tool, material or equipment shall either be identified as unsafe by tagging or locking The controls to render them inoperable or shall be physically removed from its place of operation.

Please See Other Side

Below is a general checklist of requirements on this project. Contractors will check off items that pertain to their contract and project tasks. Notify EDiS Field Manager of any issues. This checklist is not meant to be all inclusive. Please refer to additional OSHA regulations for compliance.

House Keeping

- ☐ Material Storage Area's Orderly
- ☐ Trash Containers Available and Emptied daily
- ☐ Fire Hazards
- ☐ Lighting and ventilation
- ☐ Exits and Stair clear passage
- ☐ Walkways, corridors clear passage
- ☐ Daily debris /trash removal
- ☐ _____

Personal Protective Equipment

- ☐ Hard Hats being worn
- ☐ Safety Glasses with side shields being worn
- ☐ Secondary Eye/Face protection
- ☐ Respirators as required
- ☐ Hand protection when needed
- ☐ Ear protection when needed
- ☐ Inspected & Maintained
- ☐ _____

Fire Prevention

- ☐ Fire extinguishers inspected
- ☐ Flammable / Combustibles properly store
- ☐ Approved Fuel cans used and labeled
- ☐ Oxygen / Acetylenes stored properly
- ☐ _____

Electrical

- ☐ GFI in use
- ☐ Three prong insulated extension cords used
- ☐ Extension cords in good condition
- ☐ Lockout / Tag-out program in use
- ☐ _____

Excavations

- ☐ Miss Utility been contacted
- ☐ Properly Barricaded
- ☐ Ladders in use at depths over 4'-0"
- ☐ Ladders every 25'-0" distance
- ☐ Shored, sloped, benched as required
- ☐ Dewatering as needed
- ☐ _____

Ladders

- ☐ Good condition
- ☐ Correct pitch
- ☐ Extends 3'-0" above landing
- ☐ Open and secured / tied off
- ☐ _____

Scaffolds

- ☐ Certified Scaffold Installer
- ☐ Guardrails, toe boards, and planking secured
- ☐ Appropriate signage
- ☐ Adequate cross bracing
- ☐ Secured to building over 25'-0" in height
- ☐ _____

Cranes

- ☐ Rated Load Capacity available in cab
- ☐ Swing Radius barricaded
- ☐ Appropriate certificates / decals / hand signals
- ☐ Daily safety inspection log completed
- ☐ _____

Fall Protection

- ☐ Fall protection plan on file
- ☐ Full harness / shock absorbing lanyard used
- ☐ Anchoring points secured
- ☐ Perimeter barricades
- ☐ Open sided floor protection
- ☐ 6'-0" Tie-off utilized
- ☐ _____

Paperwork

- ☐ MSDS Information
- ☐ Contractors Safety Program
- ☐ Hazardous Communications Training
- ☐ Hazardous Communications Program
- ☐ Contractor Qualified Representation
- ☐ _____

Other

- ☐ _____
- ☐ _____

Foreman / Competent Person:

Print Name_____

SECTION 013300 – SUBMITTAL PROCEDURES

1. GENERAL PROVISIONS

   A. The general provisions of the Contract, including the Conditions of the Contract (General, Supplementary and other Conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

2. ITEMS TO BE SUBMITTED AT START OF WORK

   A. Performance/Labor and Material Payment Bond(s): One (1) copy of each bond simultaneously with the signed Agreement. See General Conditions Article 11.4 and Supplementary Conditions.

   B. Policies or Certificates of Insurance: Two (2) copies simultaneously with the signed Agreement. See General Conditions Article 11 and Supplementary Conditions.

   C. Contractor's License: Submit a copy of all business licenses required by local and state agencies.

   D. Contractor's Schedule of Values: Two (2) copies for approval within 21 days after the Agreement is signed. See General Conditions Article 9.2 and provisions in this Section.

   E. Contractor's Progress Schedule: Two (2) copies for review and reference within 21 days after the Agreement is signed. See General Conditions Article 3.10 and provisions in this Section.

   F. Submittal Schedule: Two (2) copies for review and reference within 21 days after the Agreement is signed. See provisions in this Section.

   G. Products List: Two (2) copies for approval within 30 days after the Agreement is signed. See provisions in Section 016200 - MATERIAL AND EQUIPMENT.

3. NON-RESIDENT CONTRACTOR & SUBCONTRACTORS BONDS

   A. Refer to requirements in Section 011100 - INSTRUCTIONS TO BIDDERS for filing of Surety Bonds with the Division of Revenue.

   B. If such bonds are required on this project, it will be the responsibility of the Contractor to produce evidence to the Construction Manager that they have been filed, or if not required, to supply a notarized statement that they are not required. This must be done within seven (7) days after award of Contract and in any event before construction starts.

4. RELATED REQUIREMENTS

   A. See Section 017700 - CONTRACT CLOSE OUT: for submittal requirements for Contract Close out.

5. SUBMITTALS

   A. All submittals shall be directed to the Construction Manager in the manner directed by the

Construction Manager, and paragraph 9 of this section. Contractor shall use the Contractor Submittal Form appended to this section.

B. Prepare a Submittal's Schedule for Shop Drawings, Product Data and Samples. Show:

1. The dates for Contractor's submittals.

2. The dates submittals will be required for Owner-furnished products.

3. The date approved submittals will be required from the Architect.

C. Should the Architect or Construction Manager elect to omit any items from the list of items to be reviewed, it shall not relieve the Contractor from compliance with the Contract Documents with regard to that item. In such instance, the Contractor may still elect to have submittals prepared for his own use without review by the Architect or Construction Manager.

6. SHOP DRAWINGS

A. Conform to provisions in General Conditions applying to Shop Drawings.

B. Present in a clear and thorough manner.

1. Identify details by reference to sheet and details, schedule or room numbers shown on Contract Drawings.

2. Maximum sheet size: 30″ x 42″.

7. PRODUCT DATA

A. Conform to provisions in General Conditions applying to Product Data.

B. Preparation:

1. Clearly mark each copy to specifically identify products or models pertinent to project.

2. Show performance characteristics and capacities.

3. Show dimensions and clearances required.

4. Show wiring or piping diagrams and controls.

C. Manufacturer's standard schematic drawings and diagrams:

1. Modify drawings and diagrams to delete information which is not applicable to the Work.

2. Supplement standard information to provide information specifically applicable to the Work.

8. SAMPLES

A. Conform to provisions in General Conditions applying to Samples.

B. Provide samples of sufficient size and quantity to clearly illustrate:

1 .Functional characteristics of the project, with integrally related parts and attachment devices.

2. Full range of color, texture and pattern.

C. Field samples and mock-ups; See requirements, if any, in other specification Sections.

9. SUBMITTAL REQUIREMENTS

A. Make submittals promptly through the Construction Manager in accordance with published schedule, and in such sequence as to cause no delay in the Work or in the Work of any other contractor.

B. Number of submittals required.

1. Shop drawings: Submit eight (8) copies for each submittal. Copies will be marked up with corrections and comments, stamped and returned. Any additional copies required by the Contractor shall be made by him.

2. Product Data: Submit eight (8) copies. Four (4) will be retained by the Architect, the Construction Manager and the Consultants. Four (4) will be reviewed, marked and stamped by the Architect and returned to the Contractor by the Construction Manager. Any additional copies required by the Contractor shall be made by him from the stamped copy.

3. Samples: Submit four (4) each. When approved it will be returned to the Construction Manager to be retained at the site for reference use.

C. Submittals shall contain:

1. The date of submission and the dates of any previous submissions.

2. The Project title and number.

3. Contract identification.

4. The names of the Contractor, Supplier and Manufacturer.

5. Identification of the product, with the specification section number.

6. Field dimensions, clearly identified as such.

7. Relation to adjacent or critical features of the Work or materials.

8. Applicable standards, such as ASTM or Federal Specification numbers.

9. Identification of deviations from Contract Documents.

10. Identification of revisions on resubmittals.

11. An 8 inch x 3 inch blank space for Contractor and Architect's stamps.

12. Contractor's stamp, initialed or signed, certifying review of submittal, verification of products, field measurements and field construction criteria, and coordination of the information within the submittal with requirements of the Work and of Contract Documents. Submittals which have not been stamped with this stamp or its approved equivalent will be returned without being reviewed.

D. Shop Drawing coordination and interface with work of other Contracts and adjacent work is the responsibility of each individual Contractor.

E. All submittals shall be accompanied by the contractor's submittal form, a copy of which is part of this section. The contractor's submittal form must be completed in its entirety by the contractor.

10. RESUBMISSION REQUIREMENTS

A. Make any corrections or changes in the submittals required by the Architect and resubmit until approved.

B. Shop drawings and Product Data:

1. Revise initial drawings or data, and resubmit as specified for the initial submittal.

2. Indicate any changes which have been made other than those requested by the Architect.

C. Samples: Submit new samples as required for initial submittal.

11. FINAL DISTRIBUTION OF APPROVED SUBMITTALS

A. The Construction Manager will receive and log submittals and forward to Architect after processing.

B. The Construction Manager will distribute copies of Shop Drawings and Product Data which carry the Architect's stamp to:

1. Contractor that made submittal.

2. Jobsite File.

3. Record Document File.

4. Other Contractors, as required for coordination.

C. The Construction Manager will distribute samples as required.

D. The Contractor will distribute copies of Shop Drawings and Product Data which carry the Architect's stamp to:

1. Subcontractors.

2. Suppliers.

3. Fabricators.

12. SCHEDULE OF VALUES

A. Use AIA Document G703, Continuation Sheet to G702.

13. PROGRESS SCHEDULE

A. Prepare schedules in the form of a horizontal bar chart.

1. Provide separate horizontal bar chart for each trade or operation.

2. Horizontal time scale: Identify the first work day of each week.

3. Scale and spacing: To allow space for notations and future revisions.

4. Minimum sheet size 11 inches by 17 inches.

B. Format of listings: The chronological order of the start of each item of work.

C. Show the complete sequence of construction by activity.

D. Show the dates for the beginning, and completion of, each major element of construction such as:

1. Site clearing.

2. Site utilities.

3. Foundation work.

4. Structural framing.

5. Subcontractor work.

6. Equipment installation.

E. Show projected percentage of completion for each item as of the first day of each month.

F. Update Progress Schedule monthly and submit with Application for Payment and Schedule of values.

G. Indicate progress of each activity to date of submission.

H. Show changes occurring since previous submission of schedule:

1. Major changes in scope.

2. Activities modified since previous submission.

3. Revised projections of progress and completion.

4. Other identifiable changes.

I. Provide a narrative report as needed to define:

1. Problem areas, anticipated delays and the impact of the schedule.

2. Corrective action recommended, and its effect.

3. The effect of changes on schedules of other prime contractors.

J. Submit one reproducible transparency.

K. After review, distribute copies of the schedule to:

1. Jobsite File.

2. Subcontractors.

3. Architect.

4. Owner.

L. Instruct recipients to report promptly to the Contractor, in writing, any problems anticipated by the projections shown in the schedules.

END OF SECTION

SECTION 013500 – CONTRACTOR EMPLOYEE BACKGROUND CHECK

1. It is the Contractor's responsibility to perform background checks and screen all employees working onsite. The background check must include checking for a previous history of Child Abuse Convictions, Child Molestation Convictions, Felony Convictions, and Drug Convictions within the last 5 years. Any employee with any of these convictions may not enter the job site or school campus. This background check must be completed and screened by the contractor prior to an employee entering the job site. The background check cannot be any older than 1 year prior to the date of the contract between the Contractor and the Owner. The Construction Manager, the Owner's representative and the Owner have the right to request that the screening data be submitted on a case-by-case basis.

2. The contractor is required to provide the Construction Manager written notice verifying background checks were completed and screened by the contractor prior to an employee entering the job site. This notice will contain the individual's name and the last four digits of their social security numbers. Notices must be received no later than two (2) working days before access is required. Notices will be forwarded electronically to the Construction Manager. A sample notice follows this section for your reference.

END OF SECTION

Date

Project Manager
EDiS Company
110 South Poplar Street
Wilmington, DE 19805

RE: INSERT PROJECT NAME - Certification of Background Checks

Dear _____:

This letter is to certify that background checks have been completed in accordance with Section 013500 Contractor Employee Background Check. The following individuals are certified as having met the requirements of the specification:

Name	Last 4 SSN
Mr. John Smith	1234

If you require any additional information you may contact INSERT POINT OF CONTACT, PHONE NUMBER AND EMAIL ADDRESS.

Sincerely,

Company

NAME
TITLE

SECTION 013523 - SAFETY PROGRAM

1. GENERAL

A. The Contractor shall be responsible for initiating, maintaining, and supervising all safety activities and programs in connection with their Work.

B. Contractor shall be responsible for the safety of their personnel as well as their subcontractors.

C. Hard hats and safety glasses must be worn by all personnel on the jobsite, except in contractor's administrative office/trailer. All equipment must comply with OSHA standards. All job site personnel shall wear long pants, shirts (no tank tops), high visibility garments worn on the outer layer of clothing, and work boots.

2. SAFETY PROGRAM

A. Prior to commencing the work, the Contractor shall submit to the Construction Manager (1) electronic copy and (1) bound copy of its safety program and one (1) copy of SDS information in a 2" ringed notebook. One paper copy of the safety program and SDS will be retained by the Construction Manager in the field office.

B. The safety program shall outline those hazards peculiar to the Contractor's Work, and the steps to be taken to eliminate or reduce the risk of injury or loss due to those hazards. The program shall be project and site specific. Every Contractor shall implement and enforce its safety program, in accordance with all OSHA, Federal, State, and local laws.

C. Crystalline Silica Exposure Control Plan - Affected Contractors must provide a Written Exposure Control Plan for Respirable Crystalline Silica, meeting Subpart Z of the OSHA Construction Industry Regulations, that ensures each employee covered by this section of the Regulations can demonstrate knowledge and understanding meeting the requirements of the regulation, identify the competent person designated by the employer in accordance with the section, and otherwise comply with the requirements of this section of the Regulations.

D. Every Contractor shall designate a qualified Safety Supervisor and Alternate to implement the safety program. If during the progress of the work the Safety Supervisor is not performing their duties in a manner satisfactory to the Construction Manager the Contractor will designate a new qualified Safety Supervisor.

E. Every Contractor shall furnish the names and qualifications of the Primary and Alternate competent persons and qualified persons who may be required for their scope of work by the Contractor's safety procedures, and by federal, state and/or local regulations. Examples include competent persons and/or qualified persons for steel erection, excavation, scaffold erection, confined space entry, crane and rigging operations, annual crane inspections, fall protection including horizontal lifeline systems, etc.

F. The employer shall verify compliance by preparing a written certification record. The written certification record shall contain the name or other identity of the employee trained, the date(s) of the training and the signature of the person who conducted the training or the signature of the employer. If the employer relies on training conducted by another employer or completed prior to the effective date of this section, the certification record shall include the date the employer determined the prior training was adequate rather than the date of actual training.

G. Copies of any and all documents, including information stored electronically, such as safety and health program handbooks and training certification records shall be provided when necessary.

1. The employer shall instruct each employee in the recognition and avoidance of unsafe conditions and the regulations applicable to his work environment to control or eliminate any hazards or other exposure to illness or injury. Please forward certification (document) of training for each employee on an EDiS project. The latest training certificate shall be maintained.

H. Contractor Daily Reports with Safety Inspection Checklist will be submitted daily to the Superintendent, verifying inspection of work area, machinery, equipment, and tools.

I. Prior to starting work on-site, the Contractor shall arrange with the on-site Superintendent to have their employees complete the EDiS Company Zero Accidents Safety Orientation program.

J. Every Contractor shall hold, at a minimum, weekly safety toolbox talks with all its employees every Monday at 12:30 PM. Every Contractor shall designate a responsible, qualified, and capable person to conduct these meetings. Contractor's safety supervisor or superintendent must submit to the Construction Manager weekly toolbox talks attendance sheets and the topics discussed.

3. SUBSTANCE ABUSE POLICY STATEMENT

A. The Construction Manager is committed to providing a safe work site environment for its employees and Contractors' employees. The Construction Manager does not condone or permit employees and Contractors' employees to use or be under the influence of drugs or alcohol while they are on any of the Construction Manager work sites. The Policy is as follows:

1. It is a violation of the Construction Manager's policy for employees and Contractors' employees to use, possess, sell, trade, or otherwise engage in the use of illegal drugs and alcohol.

2. It is a violation for employees and Contractors' employees to report to work while influenced by illegal drugs or alcohol.

3. It is a violation for employees and Contractors' employees to use prescription drugs illegally (i.e., to use prescription drugs that have not been legally obtained) and to use prescription drugs in a manner other than the prescribed intentions.

4. Employees and Contractors' employees who are taking medication, which is prescribed by their physician, are expected to discuss potential side effects with their prescribing physician, as it relates to the work requirements.

B. Violations of this policy will require disciplinary action. If any employees or Contractors' employees are observed or suspected of being influenced by drugs or alcohol, they will be instructed to stop work and may be required to leave the work site.

4. EXECUTION

A. Every Contractor shall comply with all applicable federal, state and local laws, regulations and orders relating to occupational safety and health, and related procedures, and shall, to the extent permitted by law, indemnify and hold Construction Manager, Owner and Architect, and their respective directors, officers, or agents and employees, harmless from any and all liability, public or private, penalties, contractual or otherwise, losses, damages, costs, attorney's fees, expenses, causes of action, claims or judgments resulting from a claim filed by anyone in connection with the aforementioned acts, or any rule, regulation or order promulgated thereunder, arising out of the Contractor's Work, this Agreement or any subcontract executed in prosecution of the Work. Every Contractor further agrees in the event of a claim of violation of any such laws, regulations, orders, or procedures arising out of or in any way connected with the performance of this agreement, Construction Manager may immediately take whatever action is deemed necessary by Owner and/or Construction Manager to remedy the claim or violation. Any and all costs or expenses paid or incurred by Owner and/or Construction Manager in taking such action shall be borne by the Contractor and may be deducted from any payments due Contractor.

B. The Contractor agrees to (1) take all necessary steps to promote safety and health on the job site; (2) cooperate with Owner and/or Construction Manager and other Contractors in preventing and eliminating safety and health hazards: (3) train, instruct and provide adequate supervision to ensure that its employees are aware of, and comply with, applicable Federal and State safety and health laws, standards, regulations and rules, safe healthful work practices and all applicable safety rules, regulations and work practices and procedures (4) not create any hazards or expose any of its employees, employees of the Owner and/or Construction Manager or employees of Contractors to any hazards; and (5) where the Contractor is aware of the existence of a hazard not within its control, notify the Construction Manager of the hazard as well as warn exposed persons to avoid the hazard.

C. The Contractor / Sub-contractor shall prepare a written Job Hazard Analysis (JHA) common to the construction industry for any work of a high risk nature. This JHA will be prepared and signed by each work crew each day prior to starting work on a specific area of work and any time a crew is re-assigned to a new work task. The JHA form is generally in table form and simply describes tasks to be performed, potential hazards and mitigating measures. The form is used to identify, analyze, understand and mitigate potential hazards associated with repetitive or potentially hazardous work operations. Each employee associated with the work to be performed shall be instructed by their companies designated Competent Person of the safety measures listed on the form and shall sign the document prior to the commencement of work.

(examples of "high risk": pre-cast concrete, scaffold activities, steel erection, work at heights, work at depths, road work, etc.) If the contractor prepares a similar assessment form it must be reviewed to meet the criteria of a Job Hazard Analysis (JHA) as described by the U.S. Department of Labor (OSHA 3071 2002 Revised).

D. The Contractor's Superintendent or Safety Supervisor shall immediately, verbally report, and promptly thereafter confirm in writing to the Construction Manager any unsafe conditions or practices that are observed, or violations of job safety which are not within the Contractor's control.

E. Contractors shall immediately, verbally report, and promptly thereafter confirm in writing, to the Construction Manager any unsafe practices or conditions that are observed which are not under the Contractor's control.

F. The Contractor's Superintendent or Safety Supervisor shall ensure that adequate first aid supplies are available, and that personnel are qualified to administer first aid/CPR, as required by State and/or Federal regulations.

G. Every Contractor shall promptly notify Construction Manager of any personal injury requiring medical treatment of any of the Contractor's employees at the Project site; or of significant damage to property arising in connection with Contractor's performance, as promptly as possible after the occurrence of such injury or damage. Within twenty-four hours of such occurrence, Contractor shall furnish to Construction Manager a complete written report of such injury or damage.

H. Contractor certifies that the forgoing terms shall be made applicable to all Contractors' subcontractors, suppliers, materialmen, or anyone furnishing labor and/or materials to the site.

I. Every Contractor shall continue to educate their job Safety Supervisor or Superintendent of their responsibilities, which shall include:

1. Instructing workers and subcontractors under its supervision in safe work practices and work methods at the time they are given work assignments.

2. Ensuring that its workers and subcontractors have and use the proper protective equipment and suitable tools for the job.

3. Continuously checking to see that no unsafe practices or conditions are allowed to exist on any part of his job.

4. Acquainting its workers and subcontractors with all applicable safety requirements and ensuring that they are enforced.

5. Setting a good example for their workers.

6. Making a complete investigation of incidents to determine facts necessary to take corrective action.

7. Promptly completing an "Incident Investigation Form" with his Supervisor's assistance and distributing as required.

8. Holding weekly "tool box" safety meetings with their employees to:

   a. Discuss observed unsafe work practices or conditions including a review of current foreman meeting and progress meeting reports.

   b. Review each incident with their employees and discuss correction of incident root causes.

   c. Encourage safety suggestions from his men.

9. Seeing that prompt medical treatment is administered to an injured employee.

10. Correcting or reporting immediately to project superintendent any observed unsafe conditions, practices or violations of job safety or security.

11. Making all reports required by these Contract Documents to the Construction Manager in a full and timely fashion.

5. SAFETY MEETINGS

A. The Contractor's Project Manager or Superintendent shall attend weekly or biweekly supervisory job meetings. The first topic of these meetings will be job site safety. The weekly safety reports will be reviewed, and violations must be corrected immediately. Contractors will be encouraged to participate in the on-going jobsite safety.

6. TOOL BOX SAFETY MEETINGS

A. The Contractor shall schedule weekly "tool box" safety sessions to be held by their project safety supervisor or competent person / superintendent for all their employees.

B. A member of the Contractor's management staff shall periodically attend "tool box" safety sessions to evaluate their effectiveness and offer any appropriate suggestions for improvement.

7. REPORTS

A. Contractors shall report all accidents or injuries on a timely basis in accordance with all applicable regulations.

B. Contractors shall promptly complete an incident investigation report of all incidents.

C. A record of all "tool box" safety sessions shall be made and submitted to the Construction Manager.

8. SAFETY REPRESENTATIVE

A. The Construction Manager (CM) may employ the services of a Safety Representative on the project.

B. The CM Safety Representative will visit the job site on a weekly basis, or as necessary, to determine if the work is being performed in a safe manner and in accordance with OSHA, State and Local safety regulations. The CM Safety Representative is not responsible for observing and documenting all possible safety violations. The Contractors' Safety Representatives, Safety Supervisors, or Superintendents shall attend job site safety inspections with the CM Safety Representative.

C. The CM Safety Representative will prepare a written report at the end of each inspection listing the safety violations observed during the inspection. This report will be distributed to all Contractors. Contractors will immediately correct all safety violations and provide written documentation to the CM verifying that all hazards have been corrected.

9. RIGHT TO STOP THE WORK DUE TO SAFETY VIOLATIONS

A. The Construction Manager, in its sole discretion, may order the Contractor to stop the work due to safety violations under the following circumstances:

1. If the Construction Manager observes the Contractor is violating safety regulations and the Contractor takes no immediate action to correct the violation.

2. If the Contractor has been notified by the Construction Manager in writing that he is in violation of safety regulations and fails to take action to correct the violation within 24 hours of the notice.

B. If the Construction Manager directs the Contractor to stop the work due to safety violation, it will be done in accordance with the General Conditions of the Contract. Contractor shall not be permitted an adjustment of the Contract Time or Sum for the days lost to any suspension of work.

C. If the Construction Manager or Safety Representative observes Contractor's employee violating this safety program or OSHA Standards in a habitual manner, or creating a serious life safety violation, the Construction Manager or Safety Representative may instruct the Contractor's superintendent or foreman to remove the violator from the work site for failure to comply with the safety program and the contract.

10. EMERGENCY PROCEDURES

A. The Construction Manager shall establish a central meeting location for the assembly of all Contractors' employees in the event of a job site emergency.

B. Contractors shall assemble all their personnel and account for all employees. Contractors must immediately report to the Project Superintendent with the status of their employees.

11. FALL PROTECTION PROCEDURES

A. Contractors are responsible, in accordance with federal, state, local laws and regulations including OSHA. to provide and enforce their own site specific fall protection program and equipment. The following fall protection procedures shall be enforced by all Contractors as a minimum standard.

1. All workers on walking/working surfaces with unprotected sides or edges six feet (6') or higher above the next lower level must be protected from falls by the use of guardrail systems, net systems, fall arrest systems or control access zone programs. It is intended that when fall protection is required, it is required 100% of the time. All contractors are reminded that relevant industry regulations require that contractors comply with the following standards.

a. Workers constructing or working near leading edges must be protected.

b. Workers on the face of formwork or reinforcing steel must be protected at a height of 6 feet (6') or greater.

c. Employees working from scaffolds shall be guarded / protected from falling 6 feet (6') above next lower level. The erection and use of the "Baker" / "Narrow Tower scaffold. Each contractor is obligated to train their employees and follow the OSHA and Manufacture guidelines. The employer shall erect and use scaffolds according to the manufacture and OSHA guidelines (the most stringent will take precedence) using manufactured approved scaffold components. Base plates must be used during assembly and guardrails must be used at all heights when in use. Manufacture booklet must be on site and stickers on each unit must be legible.

d. Brick layers performing overhand bricklaying and related work six feet (6') or higher above lower levels must be protected from falls.

e. Roofers must comply with OSHA regulations for roof work.

f. The Contractor's controlled access zone plan shall be included in their site-specific safety program and shall be submitted prior to the start of work. Contractors are responsible for assuring programs are OSHA compliant.

g. Guidelines for Residential Construction or any interpretations will not be accepted in lieu of 1926 Standards.

h. Contractors must provide certification per OSHA CFR29 § 1926.503(b) of employee training and retraining on fall protection upon request.

B. Contractor shall provide their own fall protection. Fall protection may be provided by guardrail

systems, net systems, or personal fall arrest systems. All fall protection systems must comply with OSHA regulations.

C. Stepladders, exposed to shafts or edges of the building, greater than six feet (6′) above the next lower level, must be tied off or otherwise secured. Employee must wear fall protection, i.e., harness/lanyard.

D. The Safety Cable System shall not be altered or removed without a written request submitted to the Project Manager with a copy to the Superintendent. It shall be the responsibility of each Contractor that is removing or altering the Safety Cable System to maintain the fall protection safety provided by the safety cable and not leave the area unprotected. Each Contractor shall be responsible to re-install the Safety Cable System immediately after work is completed. Each Contractor shall be responsible to re-install the Safety Cable System in accordance with OSHA regulations.

E. Fall protection will be enforced for Structural Steel Erectors.

1. Contractors engaged in structural steel erection are specifically advised that structural steel erectors shall comply with all protection requirements for all work at a height of six feet (6′) or greater above the next lower level, 100 percent of the time, by any of the following means.

a. Standard guardrail system.

b. Personal Fall Arrest System (PFAS) – full body harness with shock absorbing lanyard. PFAS must meet the requirements of CFR 1926 subpart M.

c. Access to work area shall be provided by ladders or other safe methods. There shall be sufficient number of ladders, or other safe methods, available to reduce the amount of "beam walking." When it is absolutely necessary to traverse a beam, 100% fall protection must be utilized.

d. Steel erection Contractors must, at all times, be able to certify in writing that each of their employees have been properly trained in both OSHA fall protection standards and the Contractor's site specific project fall protection procedures.

e. Prior to the erection of the steel, the Contractor shall meet with the Project Manager and Safety Representatives to review and document site specific procedures.

12. AIRBORNE CONTAMINENTS PROCEDURES

A. Contractors must provide and use equipment furnished with Exhaust Purifiers / Scrubbers when any equipment produces airborne containments and will be used in an enclosed building.

B. The Contractor shall verify air quality by the use of air monitoring equipment and document such verified air quality on the daily report. The monitoring equipment shall, at a minimum, be

designed with an auditory alarm and shall provide continuous monitoring of these four gases: Oxygen, Hydrogen Sulfide, Carbon Monoxide and Combustible gases.

C. The Contractor must provide administrative or engineering controls to protect its workers from exposure to occupational health, environmental or other hazards to be implemented whenever feasible. When such controls are not feasible to achieve full compliance, protective equipment or other protective measures shall be used to keep the exposure of employees to air contaminants within the limits prescribed by local, state, and federal regulations. Any equipment and technical measures used for this purpose must first be approved for each particular use by a competent industrial hygienist or other technically qualified person. Whenever respirators are used, their use shall comply with 1926.103.

13. CELL PHONE AND RADIO USE POLICY

A. Use of cell phones on EDiS Company projects should be limited to non-construction type activity areas and away from active construction areas (i.e., project office). This includes both cell phone use and the review of data, information, texts, and the internet. Except in an emergency circumstance, phones should only be used in the designated areas. Anyone observed using a cell phone outside of these designated areas without regard to maintaining a safe focus on their surroundings can be subject to discipline, up to and including removal from the project. Use of ear buds, ear phones, and portable radios are absolutely prohibited on EDiS Company project sites. Anyone using ear buds, ear phones, or any other device that would prevent the wearer from receiving auditory cues about the surrounding environment will be subject to discipline, up to and including removal from the project.

14. EXCAVATION PROCEDURES

A. Before ANY excavation work is to commence, the Contractor/Excavator shall contact the utility companies or utility owners and advise them of the proposed work and ask them to mark the location of the underground utility installations. This notification shall be done within established or customary local response times. If the work is on private property and the utility company will not mark out the utilities, the Contractor/Excavator will hire a private locating service to mark the utilities. Once the utilities are located and marked, the Contractor/Excavator will excavate by hand or use a vacuum truck to expose the utilities and record the exact location and elevation of the utilities.

B. The Contractor/Excavator must submit the Excavation Permit to EDiS Company verifying their assurance of communication with the utility companies or utility owners. The Contractor/Excavator must follow State, Local, and Federal Guidelines prior to proceeding with excavations. The Contractor/Excavator will have these marks restored as long as there is work to perform.

C. Once the Contractor has installed new utilities, they will provide to EDiS Company an as-built drawing, within 7 days, showing the exact location and elevation of the utilities. The installing Contractor will be responsible for locating and marking these utilities for other contractors that

may have work in the same area.

D. Definition: "Excavator" shall mean any person, including those acting either as an employer or employee, intending to perform or performing excavation or demolition work.

E. Definition: "Excavate" or "Excavation" shall mean any operation in which earth, rock or other material in the ground is moved, removed, or otherwise displaced or disturbed by means of any tools, equipment or explosives and includes, without limitation, grading, trenching, digging, dredging, ditching, drilling, auguring, tunneling, boring, backfilling, post pounding, driving objects into the ground, installation of form pins, hammering, scraping, cable or pipe plowing or driving.

15. TRAFFIC CONTROL PROCEDURES: Manual on Uniform Traffic Control Devices (MUTCD)

(Project Manager's Note: When the traffic control plan is shown in the contract drawings this work should be assigned to a Contractor. The following paragraphs are intended as requirements for ALL Contractors when their work requires them to work in the public right-of-way.)

A. Traffic control plan(s) for the work may be required by the Authorities Having Jurisdiction (AHJ). Traffic control plans, if required, shall be prepared per AHJ standards, at the Contractor's expense, for review and approval by the AHJ. (Note: anything on a public right of way controlled by the state will require an engineer's stamp.) The implementation of the traffic control plan and any associated maintenance shall be performed at the Contractor's expense in accordance with the requirements of the AHJ. All warning signs and safety devices used by the Contractor to perform the work shall conform to the requirements contained in the State where the work is being performed, and the Department of Transportation's current edition of "Manual on Uniform Traffic Control Devices". The Contractor shall also be responsible for all traffic control required by the AHJ over the Project on the intersecting streets.

B. Contractors must submit a traffic control plan to the AHJ over the project for approval within fourteen (14) calendar days of Contract award. The approved traffic plan must be submitted prior to the commencement of work in a public street. The Contractor's representative on the site responsible for traffic control shall produce evidence that he/she has completed training acceptable to the Department of Transportation for safety through construction zones. All of the streets in which the work will occur shall remain open to traffic and one lane of traffic maintained at all times unless otherwise directed by the AHJ. Businesses and residences adjacent to the work shall be notified forty- eight (48) hours in advance of closing of streets, roadways, driveways, etc. The Contractor shall make every effort to minimize the amount of public parking temporarily eliminated due to construction in areas fronting businesses. No stockpiles of pipe or other material will be allowed in traveled right-of- ways unless otherwise approved. These requirements shall not authorize any extension of time for performance of this Contract.

16. SCAFFOLDING PROCEDURES

A. A written project specific scaffold inspection checklist must be completed by the Contractor's competent person responsible for inspecting the scaffolding before each work shift, and after any occurrence which could affect a scaffold's structural integrity. A copy of the documented scaffold inspection checklist must be maintained by each company performing work on a scaffold and a second copy provided for record to the EDiS project office.

B. Contractors are required to ensure that all employees working on or around scaffolding are properly trained. Contractors shall provide documented verification of scaffold training upon request.

C. Scaffold erectors and dismantlers are required to wear fall protection during the erecting, modifying and dismantling scaffolds. In cases where fall protection is infeasible or creates a greater hazard, the competent person shall document their decision at each specific location of scaffold assembly. At minimum, the scaffold erectors and dismantlers shall wear a fall protection harness during the erection, modification and dismantling of scaffolds.

D. Contractors shall utilize a scaffold tag system. The scaffold tag system shall be color coded and visible. The competent person shall sign and date the scaffold tag.

1. Green tags are reserved for complete systems.
2. Red tags are reserved for erection/dismantling activities and for scaffolds with deficiencies in the system.

3. Yellow tags are reserved for systems that require the use of both PFAS and guardrail systems for incomplete scaffold systems or platforms.

END OF SECTION

CONTRACTOR

COMPETENT / QUALIFIED PERSON DESIGNATION LOG

Project: **Field Manager:**

Contract: Contrctor:	Applicable to Subcontractor (yes / no)		Foreman	Competent Person (if not foreman)
Subpart C-General Provisions				
1926-20 General Safety				
Subpart D - Health and Environmental Controls				
1926-53 Ionizing Radiation				
1926-55 Gases, Vapors, Fumes, Dusts, Mists				
1926-57 Ventilation				
1926.59 Hazard Communication				
1926.62 Lead				
Subpart E - Personal Protective Equipment				
1926.101 Hearing				
1926.103 Respirator Protection				
Subpart H - Materials Handling, Storage				
1926.251 Rigging Equipment for Material Handling				
Subpart J - Welding and Cutting				
1926.354 Welding, Cutting and Heating				
Subpart K - Electrical				
1926.404 Wiring Design and Protection				
Subpart L - Scaffolding				
1926.451 Scaffolding				
Subpart M - Fall Protection				
1926.502 Fall Protection Criteria and Practices				
1926.503 Training				
Subpart N - Cranes, Derrick -Redesignated 1926.1501				
Subpart O - Motor Vehicles and Equipment				
1926.601 Motor Vehicles				
Subpart P - Excavations				
1926.651 Specific Excavation Requirements				
1926.652 Requirements to Protective Systems				
Subpart S - Tunnels, Shafts, Caissons				
1926.800 Tunnels, Shafts, Caissons				
1926.803 Compressed Air				
Subpart T - Demolition				
1926.850 Preparatory Operations				
1926.852 Chutes				
1926.859 Mechanical Demolition				
Subpart V - Power Transmission and Distribution				
1926.955 Overhead Lines				

Contract: Contrctor:	Applicable to Subcontractor (yes / no)		Foreman	Competent Person (if not foreman)
Subpart X - Stairways and Ladders				
1926.1053 Ladders				
1926.1060 Training Requirements				
Subpart Z - Toxic and Hazardous Substances				
1926.1101 Asbestos				
1926.1101 thru 1926.1148 Toxic and Hazardous Substances				

I certify that the listed employees are competent persons, as defined and required by specific OSHA standards. They are capable of identifying existing and predictable hazards in the surroundings or working conditions which are unsanitary, hazardous or dangerous to employees, and who has authorization to take prompt corrective measures to eliminate them.

Name (print)

Contractor Signature

Date

PU19, Revised 07/2021

Certification of Training Documents to be Submitted with Safety Policy/Program

Provide a certification of training for employees on your safety program.

Certification of training must include: Employee's name, date of training, person conducting the training, topics covered, and a statement that the student has successfully completed the course.

In addition, Contractor shall provide certification of training on the following programs, as they pertain to your contract and project tasks. This list is not meant to be all inclusive: please refer to OSHA regulations for applicable safety requirements.

a. ☐ Scaffold: 1926.454

b. ☐ Fall Protection 1926.503

c. ☐ Crane Operator: 1926.1427

d. ☐ Signal person (this is for any persons connecting material or equipment for lifting): 1926.1428

e. ☐ Crane maintenance: 1926.1429

f. ☐ Steel erection fall protection: 1926.761

g. ☐ Respiratory protection (medical clearance and training records complying with 1910.134

h. ☐ Powder-actuated tools: 1926.302

i. ☐ Motor Vehicles (are those vehicles that operate within an off-highway jobsite, not open to public traffic): 1926.21

Work Area:		**JOB HAZARD/RISK ANALYSIS**
Site:		
Company:		

Describe Activity:		**Date:**	
Completed By:			

Work Process and Tasks *Describe the tasks / steps involved*	**Hazards Identified for each Task / Step**	**Risk Level** *High – Medium*	**Control / Safe Work Procedures for each Task** *Controls to be implemented (consider the hierarchy of hazard controls)*

Checklist for Guidance		
• Does Task effect other trades?	• Any overhead and / or underground utilities?	• What type of PPE will be used?
• Any Fall Conditions greater than 6 feet?	• What are the potential “hazards”?	• How can the “hazard” be eliminated?
• Have employees been trained in the assignment? (e.g. fall protection, scaffold, excavation, etc..)	• What “hazards” are present?	• Excavation Safety System to be used?

Competent Person / Supervisors Comments	**Date:**	
Employee Name:	**Competent Person Signature:**	

BIM PROJECT EXECUTION PLAN

FOR

NCC VOTECH SCHOOL DISTRICT
PAUL M. HODGSON
VOCATIONAL TECHNICAL HIGH SCHOOL
2575 GLASGOW AVENUE
NEWARK, DE 19702

DEVELOPED BY AMP CONSULTING

OCTOBER 9, 2023



Please direct any questions about this Plan to AMP Consulting: Chris Donahue (cdonahue@ampconsulting.build)

BIM PROJECT EXECUTION PLAN
FOR
HODGSON HIGH SCHOOL
DEVELOPED BY AMP CONSULTING
OCTOBER 9, 2023

TABLE OF CONTENTS

1.0 BIM Project Execution Plan Overview 3
2.0 Project Information 4
3.0 Key Project Contacts 5
4.0 Organizational Roles and Staffing 7
5.0 Project BIM Objectives and Project BIM Uses 9
6.0 Designing the BIM Execution Process 13
7.0 Facility Attribute Data Requirements 15
8.0 Collaboration Procedures 15
9.0 Technological Infrastructure 18
10.0 Model and Database Structure 19
11.0 Quality Control Procedures 23
12.0 Project Deliverables 25
13.0 Attachments 25
14.0 Exhibit "I" 30

1.0 BIM PROJECT EXECUTION PLAN OVERVIEW

A BIM Project Execution Plan outlines the overall vision along with implementation details for the team to follow throughout the project. To effectively integrate BIM into a project, it is important for the project team to develop a detailed execution plan for BIM implementation. The overarching goal for a BIM Project Execution Plan is to stimulate and direct additional communication and coordination by the team members during all phases of a building project.

The BIM Project Execution Plan for this project will be developed using the BIM Project Execution Plan Template provided in the early design phase of the project and then submitted to the for approval. The BIM Project Execution Plan will work in conjunction with the BIM Addendum; any revisions to the BIM Addendum should be reflected within the project specific BIM Project Execution Plan (BIM Plan).

Purpose:

- To successfully implement Building Information Modeling (BIM) on the project.
- To define uses for BIM on the project (e.g. building systems analysis, cost estimating, and design coordination).
- To describe the process for executing BIM throughout the project lifecycle.
- To ensure Hodgson High School receives the end product they expect and are able to put it to use in the future.

Goals for BIM Process:

- Sharing of the Revit model between all parties of the design and construction team for review every two weeks after the middle of the Design Development Phase.
- Use of the ICon lab in the middle to end of the Design Development phase and in the beginning of the Construction Documents phase for the purpose of immersing the Hodgson High School user group in to proposed modelled spaces for review of space and materials.
- Ownership and Use of BIM Model and Database
- The BIM model is the property of ABHA|BSA+A and will be shared with the Design-Build team.

This BIM Model is an instrument of service and is considered to be a component of Design and Construction Documents without exception. In addition, each Model Element Author (MEA) contributing to the BIM model(s) and database agrees to provide all project stakeholders and Hodgson High School (Owner) a non-revocable, exclusive license to utilize any and all intellectual property provided by each MEA contained within this BIM for the sole purpose of completing the design, construction and other uses as stipulated and/or implied by the executed Owner/ Professional Agreement and Owner/Contractor Agreement for this project.

1.1 RECORD MODEL & AS-BUILT MODEL DEVELOPMENT PROCESS

The following process is defined for the Record Model and the As-Built Model. Specific details to be confirmed by the project team:

- ABHA|BSA+A is responsible for the initial Design Intent Model. AMP Consulting is responsible for the initial Means & Methods Model.

- ABHA|BSA+A is to provide the coordinated Design Intent Model to AMP Consulting to be used for the creation of the Means & Methods Model.
- AMP Consulting will update the Means & Methods Model with all as-built conditions to form the As-Built Model deliverable in Revit.
- ABHA|BSA+A will revise the Design Intent Model with all design revisions (architectural, structural, and MEP) to form the Record Model deliverable in Revit.
- AMP Consulting will transition the Revit Model to Revizto 5.
- All 2D Record and As-Built Documents will be produced from their respective models.

2.0 PROJECT INFORMATION

2.1 PROJECT OVERVIEW INFORMATION

Facility Owner	New Castle County Votech School District
Project Name	Hodgson High School
Project Location	2575 Glasgow Avenue Newark, DE 19702
Contract Type/Delivery Method	

2.2 PROJECT NUMBERS

PROJECT INFORMATION	PROJECT NUMBER
Hodgson High School Building Number	
ABHA|BSA+A Job No.	
AMP Consulting Job No.	

2.3 PROJECT DESCRIPTION

EDiS Company retained AMP Consulting to provide BIM/VDC services on Hodgson High School project. AMP Consulting will manage the BIM/VDC work during design and construction. AMP Consulting will provide a full-time in-house BIM manager and BIM Coordination on the project team.

2.4 ADDITIONAL PROJECT INFORMATION


- Operations and Maintenance are under the auspice of Hodgson High School

2.5 PROJECT MILESTONES

PROJECT MILESTONE	ESTIMATED START	ESTIMATED COMPLETION	REVISE BIM PLAN	INVOLVED PROJECT STAKEHOLDERS
Construction	9/27/2023	5/26/26	N/A	EDiS
Project Closeout	9/27/2023	5/26/26	N/A	EDiS

3.0 KEY PROJECT CONTACTS

3.1 ORGANIZATION CHART

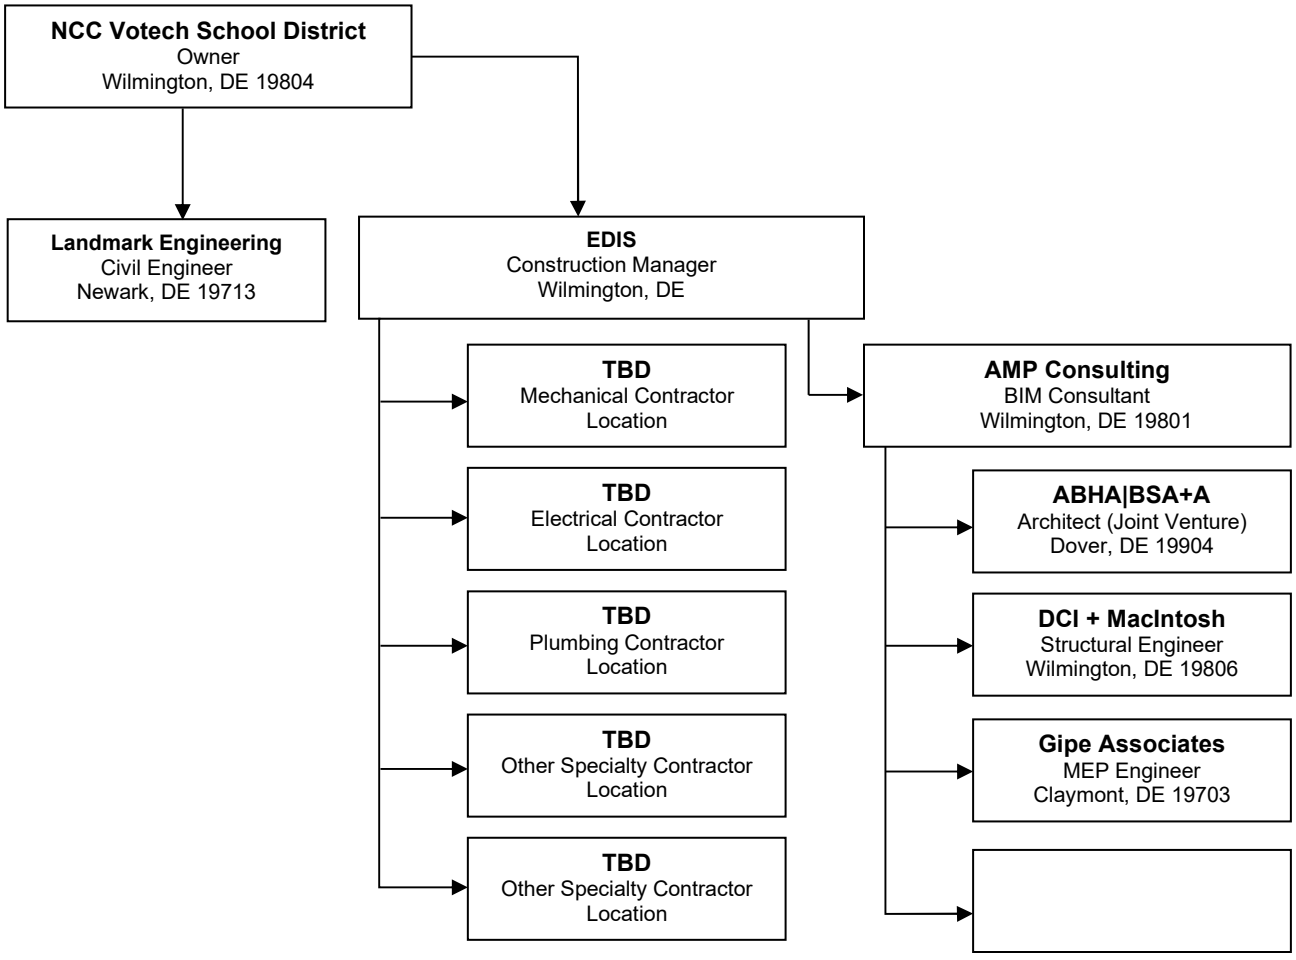

3.2 HODGSON HIGH SCHOOL PROJECT STAKEHOLDERS

The following client team staff members are providing leadership for BIM execution on behalf of NCC Votech School District:

ORGANIZATION	ROLE	NAME	EMAIL	PHONE
EDiS Company	Project Manager	Kevin Lucas	klucas@ediscompany.com	302-420-3083
AMP Consulting	BIM Director/ Manager	Christopher Donahue	cdonahue@ampconsulting.build	302-893-0492

3.3 DESIGN TEAM PROJECT STAKEHOLDERS

The following consultants are providing professional services for this project. For each firm, key leadership personnel listed includes Principals, Managers, Architect/Engineers, and Designers. BIM Managers/Coordinators are also listed below. This list will be updated as needed as additional team members are assigned to the project. Members of the Design Team include:

ORGANIZATION	ROLE	NAME	EMAIL	PHONE
Hodgson High School	Representative	Al Schrum, Jr	a.schrum@nccvt.k12.de.us	302-299-9106
EDiS Company	Construction Manager	Kevin Lucas	klucas@ediscompany.com	302-420-3083
AMP Consulting	BIM Consultant	Christopher Donahue	cdonahue@ampconsulting.build	302-893-0492
ABHA|BSA+A	Architect	Kathy Knotts	knotts@simpers.com	302-658-9300
DCI+MacIntosh Engineers	Structural Engineer	Chelsea Collins	ccollins@dci-engineers.com	303-252-9200
Gipe Associates	MEP Engineer	Adam Kegan	akegan@gipe.net	410-832-2420
Landmark Engineering	Civil Engineer	Ted Williams	tedw@landmark-se.com	302-323-7933

3.4 CONSTRUCTION TEAM PROJECT STAKEHOLDERS

The following construction specialists are providing professional services for this project during both the design and construction phases. This list will be updated as needed as additional team members are assigned to the project. Members of the Construction Team include:

ORGANIZATION	ROLE	NAME	EMAIL	PHONE
EDiS Company	Construction Manager	Kevin Lucas	klucas@ediscompany.com	302-420-3083
AMP Consulting	BIM Consultant	Christopher Donahue	cdonahue@ampconsulting.build	302-893-0492

3.5 OWNER CONTRACTED CONSULTANTS

The following construction specialists are providing professional services for this project during the design phase and construction on behalf of EDiS Company as a sole source provider.

ORGANIZATION	ROLE	NAME	EMAIL	PHONE
AMP Consulting	BIM Manager	Christopher Donahue	cdonahue@ampconsulting.build	302-893-0492
AMP Consulting	Senior BIM Tech	Rodger Breeding	rbreeding@ampconsulting.build	302-421-2942

4.0 ORGANIZATIONAL ROLES AND STAFFING

4.1 BIM MODEL MANAGER

The BIM Model Manager shall have sufficient BIM experience for the size and complexity of the project and shall have relevant proficiency in the proposed BIM authoring and coordination software. The BIM Model Manager shall serve as the main point of contact with EDiS Company/AMP Consulting and the project team for BIM related issues.

During each phase of a Hodgson High School project, the model manager is required, but not limited to:

- Ensure completeness and accuracy for BIM Plan
- Ensure completeness and accuracy for overall project model
- Coordinate all updates for individual models, specialized models, and databases

4.1.1 RESPONSIBILITES DURING PLANNING AND DESIGN

- Act as lead contact for BIM related issues with all relevant project stakeholders and manage collaboration between all parties
- Lead the process of BIM Plan development as per requirements of the BIM Addendum
  - Ensure project stakeholder compliance with the EDiS Company/AMP Consulting approved BIM Plan
  - Develop, coordinate, publish, and verify all necessary configurations required for seamless integration of BIM Model(s) and facility data
- Facilitate the transfer of information on the file sharing exchange protocol
  - Assure that the design deliverables specified in the contract are provided in accordance with the required formats
  - Determine the project BIM geo-reference point(s) and assures all technical discipline models are properly referenced
  - Maintain BIM Model(s) and facility data standards and requirements
  - Assure proper BIM derived 2D documents conforms with the Design and Construction Standard

- Coordinate with project team to assure creation of required final BIM deliverables at project turnover
- Coordinate with the for facility management data and file exchange as needed
- Lead meetings with lead BIM technicians and project BIM Team
- Assemble composite design model for coordination meetings
- Facilitate use of composite design models in design coordination/clash detections meetings and generate detection reports by the identification and resolution of all hard and soft collisions within the BIM Model(s)
- Perform design reviews to test design in compliance with functionality and constructability requirements

4.1.2 RESPONSIBILITIES DURING PRECONSTRUCTION AND CONSTRUCTION

- Act as lead contact for BIM related issues with all relevant project stakeholders and manage collaboration between all parties
- Perform model checks and deliver full report on the model/document properly.
- Maintain and revise BIM Plan with additional construction information on an as needed basis
  - Ensure project stakeholder compliance with the EDiS Company/AMP Consulting approved BIM Plan
  - Develop, coordinate, publish, and verify all necessary configurations required for seamless integration of BIM Model(s) and facility data during construction
- Coordinate and maintain the transfer of information on the file sharing exchange protocol
  - Coordinate the exchange of BIM model(s)and facility data between the Design Team and construction trades
  - Coordinate any field revisions that have been documented and updated to the Design Model with the Design Team in a timely manner
  - Coordinate with Lead BIM Technicians to integrate 3D fabrication models with the updated design model to ensure compliance with project deliverables
  - Maintain accurate As-Built/Record Model
  - Coordinate with contractor, design team, and commissioning agent to verify facility data before project turnover
  - Coordinate with the facility management data and file exchange as needed
- Lead meetings with lead BIM technicians and project BIM Team
  - Assemble composite construction model for coordination meetings
  - Facilitate use of composite trade models in construction coordination/clash detections meetings and generate detection reports by the identification and resolution of all hard and soft collisions within the BIM Model(s)
  - Coordinate construction sequencing and scheduling activities and assure they are integrated with the relevant BIM Model(s) and facility data
  - Perform constructability reviews

4.1.3 RESPONSIBILITES DURING POST CONSTRUCTION

- Meet with facilities management group for review of turnover documents
- Finalize BIM As-Built/Record Model and facility data
- Verify model accuracy and completeness in accordance to Owner Requirements
- Facilitate the transfer of information on the file sharing exchange protocol
- Hand over
- BIM As-Built/Record Model(s) and facility data to for use in operations

4.2 DISCIPLINE LEAD BIM TECHNICIANS

Each major design discipline and subcontractor shall assign an individual to the role of lead BIM Technician for the duration of the project. These individuals shall have the relevant BIM experience required by the complexity of the project. As a minimum, the Lead BIM Technician would have the following responsibilities for their discipline:

- Act as Lead BIM contact for the duration of the project
- Maintain and manage integrity of model, including:
  - Coordinate BIM development, standards, data requirements, etc. as required
  - Lead the technical BIM team in its documentation and analysis efforts
  - Exchange files between other disciplines
  - Upload and maintain models to file exchange server
  - Prepare model for review, as required
- Ensure development and documentation of clash resolution
  - Maintain a continuous interface with the BIM Model Manager
  - Participate in coordination and BIM technology meetings
- Coordinate trade items into the Record Model and/or As-built Model, in accordance with project BIM Plan

5.0 PROJECT BIM OBJECTIVES AND PROJECT BIM USES

5.1 PROJECT BIM GOALS/OBJECTIVES

The following goals have been established for BIM execution associated with this project:

PRIORITY (HIGH/MED/LOW)	GOAL DESCRIPTION
Required	Prepare BIM model to be transferred between project stakeholders to minimize duplication of effort
Required	Conduct conflict resolution analysis during design to eliminate design clashes, resulting in a well-coordinated model prior to construction

Required	Utilize model for 3D Design Reviews to assist with equipment clearances and owner design decisions
Required	Conduct coordination review of key systems with construction manager and specialty trade contractors during construction
Required	Develop an accurate Record Model and As-Built Model to be used for integration into EDiS Company/AMP Consultant's facility management system(s) within the traditional standard of care provisions that govern the design and construction of the project. Record Documents should also include all approved submittals, shop drawings, O&M Manuals, building control drawings, construction photos, inspection reports, and commissioning data
Required	Integrate project data into for use in Asset Management after turnover and specific to campus asset management plan
Required	Prepare accurate design documents and construction documents derived from the model to establish basis of design within the traditional standard of care provisions that govern the design of the project
Required	Implement a process in which BIM software utilizes the model and energy attributes to determine the most effective engineering methods based on design specifications
High	Enhance Design Consolidation/ Coordination
Medium	Prepare accurate design model for piping, ductwork, etc. to Facilitate Prefabrication Efforts
Low	Field BIM to provide more immediately available accurate information on changes during construction
Low	Provide Interactive Operations and Maintenance Reference (Asset Management)

5.2 PROJECT BIM USES

BIM Use is defined as a task or procedure on a project which can benefit from the application and integration of BIM technologies and add value to the overall project.

BIM USE CLASSIFICATION	DEFINITION
Mandatory	Required on all Hodgson High School construction projects using the BIM Project Execution Plan
Significant Effort	Project team should make serious attempt to pursue BIM Use. Any reasons for noncompliance must be submitted to Hodgson High School for approval

The following BIM Uses marked **Mandatory** are the minimum requirement for BIM use during all phases of the project, as well as recommended effort for other BIM Uses. Additional uses specific to the project may be added using the table below:

5.2.1 BIM USES DURING PLANNING THROUGH 8.2.4

BIM USE	OBJECTIVE	RESPONSIBLE PARTY	EFFORT
Energy Analysis	Conduct energy assessments for building design, inspect building energy standard compatibility, and optimize proposed design to reduce facility lifecycle costs	ABHA|BSA+A	**Mandatory**
Existing Conditions Modeling	Develop a 3D model of the existing conditions for a site, facilities on a site, or a specific area within an existing facility		**Not Pursued**
Site Analysis	Evaluate site to determine if site meets the required criteria according to project requirements, technical factors and/or financial factors	ABHA|BSA+A	**Significant Effort**
Programming	Analyze spatial program and requirements and accurately assess design performance in regard to space standards and regulations	ABHA|BSA+A	Minimal Effort
Massing	Analyze exterior massing of the building as it relates to the site and surroundings.	ABHA|BSA+A	**Significant Effort**

5.2.2 BIM USES DURING DESIGN

BIM USE	OBJECTIVE	RESPONSIBLE PARTY	EFFORT
Design Intent Model Development	Develop model based on criteria that is important to the translation of the building's design	EDiS Company	**Mandatory**
Design Reviews	Review design development / progress and require feedback based on design	EDiS Company	**Mandatory**
3D Design Coordination	Determine and resolve major system design conflicts prior to construction	EDiS Company	**Mandatory**
Energy Analysis	Analyze model based on energy design specifications (Trane Trace 700)	EDiS Company	**Mandatory**
Model Auditing	Organize and assess asset attribute data into model	EDiS Company	**Mandatory**
Preconstruction Coordination	Coordinate constructability issues with Contractor	AMP Consulting	**Significant Effort**
Structural Analysis	Analyze model based on structural specifications	AMP Consulting	**Significant Effort**
Mechanical Analysis	Analyze mechanical systems based on design specifications	AMP Consulting	**Significant Effort**

Lighting Analysis	Analyze lighting systems based on design specifications	AMP Consulting	**Significant Effort**
LEED Evaluation	Organize information for USGBC	AMP Consulting	Minimal Effort
Cost Estimation & Quantity Takeoff	Supplement model with progress drawings to track quantities and counts	AMP Consulting	Minimal Effort
Code Evaluation	Streamline code review		Not Pursued

5.2.3 BIM USES DURING CONSTRUCTION

BIM USE	OBJECTIVE	RESPONSIBLE PARTY	EFFORT
Means & Methods Model Development	Develop model based on criteria that is important to the translation of the building's construction	AMP Consulting	**Mandatory**
Constructability Reviews	Evaluate construction feasibility	AMP Consulting	**Mandatory**
3D Construction Coordination	Determine and eliminate system conflicts prior to installation	AMP Consulting	**Mandatory**
Model Auditing	Verify asset attribute data into model	AMP Consulting	**Mandatory**
Site Utilization Planning	Visually depict site conditions	AMP Consulting	**Significant Effort**
Cost Estimation	Trend quantities	AMP Consulting	Minimal Effort
Digital Fabrication	Prefabricate objects (CNC, Preassembly, modularization)	AMP Consulting	Minimal Effort
3D Control and Planning	Use model to layout and install equipment, track production		Not Pursued
Construction System Design	Plan and design temporary components and safety systems		Not Pursued

5.2.4 BIM USES PRIOR TO PROJECT TURNOVER

BIM USE	OBJECTIVE	RESPONSIBLE PARTY	EFFORT
Record Model	Compare design intent to installed conditions	AMP Consulting	**Mandatory**
As-Built Model	Capture installed conditions during construction	AMP Consulting	**Mandatory**
Continuous Commissioning	Commission facility based off of end-user requirements	AMP Consulting	**Significant Effort**

Asset Management	Track manufacturer, commissioning, and maintenance records	AMP Consulting	**Significant Effort**
Space Management and Tracking	Identify space use and track use throughout management of facility and movable assets		Not Pursued
BAS System Integration	Integrate model with existing Building Automation System		Not Pursued

6.0 DESIGNING THE BIM EXECUTION PROCESS

6.1 MAPPING THE BIM EXECUTION PROCESS

A process diagram for the overall use of BIM on the project has been developed for the project. The attached diagram summarizes the workflow BIM uses and their associated information exchanges for the project. The BIM Execution Process Diagram for this project can be found in **Attachment 1** of this document.

6.2 DEVELOPING INFORMATION EXCHANGES

The project team should document the information exchanges created as part of the planning process when creating the BIM Plan. The level of development (LOD) for each model element is based on the model content criteria established by the AIA Document E202, Building Information Modeling protocol Exhibit. The LOD will assist in determining the level of involvement for each project stakeholder from project conception through project turnover. The LOD Matrix for the project is located in **AIA Document G204-2022 Model Element Table**.

6.3 BIM INFORMATION EXCHANGE METHODOLOGY

The following section lists the typical procedures for information exchanges, model sharing, and coordination throughout the project. Please validate accordingly for the project.

6.3.1 COORDINATION AND CONFLICT RESOLUTION

This Section shall be utilized in conjunction with the BIM Coordination Protocol. If conflicts exist between the two documents, this document shall govern.

When conflicts are discovered in the model, regardless of project phase or LOD, the discovering party shall promptly notify the Model Element Author. Upon notification, the Model Element Author shall act promptly to mitigate the conflict. All project stakeholders and responsible parties must post their models to the designated shared server on a weekly basis as specified. Before the model(s) are shared and/or transferred, the model should be audited to conform to the following standards:

- Begin coordination process as early as possible

- Designate the Project Model Manager
- Designate BIM contact for each project stakeholder
- Specify LOD for all Model Attributes
- Create file storage and transfer process (workspace, model naming convention, model protocol)
- Verify file type, compatibility, and needs

- Create schedule of expectations for model delivery
  - Deadlines for each project stakeholder based on level, area, phase
  - Set file upload dates (weekly) with time for interdisciplinary coordination
- Validate Model
  - Apply construction means and methods to architectural and structural model
  - Ensure model integrity and accuracy
- Establish conceptual placement of components within the architectural space
- Determine coordination hierarchy, for example:
  - Architectural
  - Structural
  - Equipment
  - HVAC Duct
  - Wet Mechanical
  - Gravity Plumbing
  - MEPF Risers
  - HVAC Distribution
  - Plumbing Distribution
  - Electrical Distribution
  - Fire Protection Distribution
- Clash Detection process
  - Project stakeholders access each other's models to work on specific level, area, and phase
  - Clash resolution to be worked out among project stakeholders
  - BIM Model Manager will check models for interference and conflicts
  - BIM Model Manager will distribute composite model in .nwd format showing unresolved clashes and clash report document for project stakeholder review and resolution before next coordination meeting
  - Weekly coordination meetings will take place to address unresolved issues with the composite model
  - BIM Model Manager will distribute meeting minutes and resolution decisions after each meeting to project team
  - Process begins again to address the next level, area, and phase
  - Clash-free model is then distributed to all parties and signed off as per project phase
  - All clash detection is in Revizto

6.3.2 ADDITIONAL BIM METHODOLOGY

- Design Model Reviews Bi-monthly: models will be sent via Dropbox to AMP Consulting for review.

7.0 FACILITY ATTRIBUTE DATA REQUIREMENTS – NOT APPLICABLE

7.1 ASSET ATTRIBUTE INFORMATION
7.2 ASSET DATABASE REQUIREMENTS

8.0 COLLABORATION PROCEDURES

8.1 COLLABORATION STRATEGY OVERVIEW

Our team will collaborate through the use of BIM from the Design Development stage through opening day. We will share the model between the Designers, Construction Managers, and Subcontractors, to work out both pre-construction and field items. The model will be shared with AMP Consulting – EDiS during design at two week intervals to ensure they have the most current information. All meetings for the project will be held on campus at Hodgson High School and our BIM meetings will be organized as follows:

A BIM requirements kickoff meeting will be held during the early planning stages in order to help the Owner (, Housing, other interested campus parties), Construction Manager, Design Assist Subcontractors, and Designers understand the other parties' needs, processes, and the abilities of their hardware and software so the final deliverable will be suitable for Hodgson High School 's needs.

Design Coordination Sessions and Construction over-the-Shoulder Progress reviews will be held throughout all phases of Design and Construction. Participants may include: Owner (individuals as determined by Hodgson High School), Construction Manager, Design Assist Subcontractors, and Designers.

Design Build Team Construction Coordination reviews and Field Change Design Discussions and on site will be held frequently during construction through the use of Revit, Navisworks, and Blue Beam.

8.2 MEETING PROCEDURES

MEETING TYPE	PROJECT STAGE	FREQUENCY	PARTICIPANTS	LOCATION
BIM Requirements Kick-off	Planning	Once	Senior Management, BIM Management Staff	Virtual
BIM Plan Review	ALL	Monthly	Senior Management, BIM Management Staff, Hodgson High School , BIM Coordinator	Virtual
3D Design Coordination	Design Documents Construction Documents	Bi-weekly	Design Team	Virtual

Mechanical Space Review	Design Documents Construction Documents	TBD	Hodgson High School , Work Control Center, Design Team, Construction Team,	Virtual
Model Commissioning Checks	Construction Documents, 75% Submittal Approval	TBD	BIM Management Staff	Virtual
3D Construction Coordination	Construction	Weekly	Construction Team	Virtual

8.3 MODEL DELIVERY/ EXCHANGE SCHEDULE FOR SUBMISSION AND APPROVAL

INFORMATION EXCHANGE	FILE SENDER	FILE RECEIVER	FREQUENCY	START DATE	MODEL FILE	MODEL SOFTWARE	Native File Type	File EXCHANGE TYPE
Design Authoring – 3D Design Coordination	ABHA|BSA+A	ABHA|BSA+A	Sharing			Revit 2023	rvt	Dropbox
	ABHA|BSA+A	ABHA|BSA+A	Sharing			Revit 2023	rvt	Dropbox
	ABHA|BSA+A	AMP Consulting	2 weeks			Revit 2023	rvt	Dropbox
Design	ABHA|BSA+A	AMP Consulting	As needed			Revit 2023	rvt	Dropbox
Prime Contractors – 3D Construction Coordination	AMP Consulting	ABHA|BSA+A	1x/ month			Revit 2023	rvt	Dropbox
	AMP Consulting	ABHA|BSA+A	1x/ month			Revit 2023	rvt	Dropbox
Additional Software								

8.4 FILE TRANSFER PROTOCOL

An electronic workspace of File Transfer Protocol (FTP) will be established for the purpose of efficient and timely transfer of model and database files. This workspace will provide a collaborative location where the current contract CAD/Revit files, coordination files, and fully coordinated submittal files will reside. Each BIM coordination team member stores and obtains data from this location. Project team members are to upload updated copies of their files, provide notification, and to make collaboration comments and annotations as often as necessary to maintain project schedule.

8.5 ELECTRONIC COMMUNICATION PROCEDURES

“hyperlink to model folder”

Contact info for access:

Chris Donahue
AMP Consulting, BIM Manager
302-421-2963
cdonahue@ampconsulting.build

The BIM Model Manager will manage and maintain all user accounts and model access rights that include the creation, deletion, and modification of elements. All project participants will be given view and download rights to the federated model files. The BIM Model Manager will apply access controls to users so that only authorized users of the model can add the files for their respective component model(s). The following table consists of the model and data access rights for the project:

MODEL ACCESS RIGHTS

FTP FILE BREAKDOWN STRUCTURE	Project Stakeholders								
	O	A/E	S	M	P	E	FP	C	SC
Virtual Construction									
BIM Requirements	D	M	D	D	D	D	D	M	D
BIM Execution Plan	M	M	D	D	D	D	D	M	D
Coordination									
Coordination Key Plans									
Subfolders per Design Aspect	D	D	D	D	D	D	D	M	D
Architect CAD Files	D	M	D	D	D	D	D	M	D
Coordination Background Data Sets	D	V	D	D	D	D	D	M	D
Revizto/Origin	D	M	D	D	D	D	D	M	D
Object Enablers	D	M	M	M	M	M	M	M	M
Component Models									
Subfolders per Design Aspect	D	D/M	D/M	D/M	D/M	D/M	D/M	D/M	D/M
Federated Models/Interference Reports									
Subfolders per Level/Area/Zone	D	D	D	D	D	D	D	M	D
Signed-off Coordination Component Models									
Subfolders per Level/Area/Zone	D	D	V	V	V	V	V	M	V
Asset Database	M	M	V	M	M	M	V	M	M
Construction Submittals	D	D	D	D	D	D	D	M	M
Project Stakeholders: O = Owner, A/E = Architect/Engineer, C = Contractor, SC = Specialty Contractor									

Permissions: V = View, M = Modify, D = Download	

8.6 RIGHT OF RELIANCE

The BIM Model produced by the project stakeholders associated with the Design Team will serve as the basis of design and is considered a **Design Intent Model** only. The model prepared by the Design Team will be used by AMP Consulting/ EDiS to prepare a **Means and Methods Model**. This Right of Reliance pertains to all models and applications associated with the model and associated applications.

The Construction Team may rely on the accuracy of the model(s) prepared by the Design Team in accordance with traditional Standard of Care provisions that apply and govern the design and construction of comparable buildings in two (2) - dimensional design formats and methods.

Conversely, the Design Team may rely on the accuracy of the model(s) prepared by the Construction Team in accordance with traditional Standard of Care provisions that apply and govern the preparation of shop drawings, fabrication drawings, sequencing and other instruments used to convey the means and methods under the control of AMP Consulting, its subcontractors, consultants, and other agents working on this project.

As mutually agreed by all parties including ABHA|BSA+A, AMP Consulting/ EDiS and Owner, nothing shall be construed by the content and/or preparation of the associated model(s) as a warranty or guarantee of accuracy and/or completeness by the Design Team. Standard and traditional procedures for design, documentation, means and methods, shop drawing submittals, verification by the contractor, requests for information in question, etc**. shall apply** to the design, construction and construction administration of the project.

The construction manager, contractors and subcontractors shall be solely responsible for means and methods and the execution of the Design Intent Model through the execution, preparation and management of delegated design, the Means and Methods Model(s), fabrication, installation and construction.

9.0 TECHNOLOGICAL INFRASTRUCTURE

9.1 COMPUTERS / HARDWARE

Recommended Hardware: Quad Core Processor / 8-12 GB RAM / Windows 10

9.2 SOFTWARE

9.2.1 APPLICABLE SOFTWARE APPLICATIONS FOR DESIGN

The following software applications will be utilized by the Team for this project during design:

SOFTWARE	VERSION	PROJECT STAKE HOLDER	TASK TYPE
Revizto	5	AMP Consulting	Design Model/ Record Model
AutoCad	2023	ABHA|BSA+A	Design/ Drafting
Bluebeam	2020	ABHA|BSA+A	Design/ Presentations
RAM Structural System	14.06.01.00	ABHA|BSA+A	Design Calc

9.2.2 APPLICABLE SOFTWARE APPLICATIONS FOR CONSTRUCTION

The following software applications will be utilized by the team for this project during construction:

SOFTWARE	VERSION	PROJECT STAKE HOLDER	TASK TYPE
Revit	2023	AMP Consulting and Subcontractors	As-Built Model
Revit	2023	ABHA|BSA+A	Design Model/ Record Model/ Construction Bulletins
Sketchup	8	ABHA|BSA+A	Design
Adobe Creative Cloud		ABHA|BSA+A	Design/ Presentations
Navisworks Manage	2023	ABHA|BSA+A/Amp Consulting/ Subcontractors	Coordination Review
Revizto	5	Supplied by AMP Consulting	

A variety of software systems will be used by subcontractors, fabricators, and third parties to prepare delegated design elements. In the event these design elements are more accurate than the Construction Documents, the geometric information should be converted into Revit format.

****Revizto license** Subcontractors to allow $1,200 for Revizto license.**

10.0 MODEL AND DATABASE STRUCTURE

10.1 PROJECT NAMING CONVENTIONS

10.1.1 FILE NAMING CONVENTIONS

Files should be named according to the following conventions: **TBD**

10.1.2 ROOM NUMBERING CONVENTIONS

Please refer to Design and Construction Standards for the room numbering convention used for all locations, on both new construction and renovation projects. This system provides a consistent method for identifying and managing building space and shall be adhered to unless approval for deviation is received from the Signage Administrator. The room numbering convention is as follows:

- **(x)(x)(x)** = x numeric identify floor and room number
- **(x)(x)(x)(A)** = alpha suffix identifies room subdivisions
- **(J)(x)(x)(x)** = alpha prefix identifies a unique room space (J – Janitorial Room)

Room Number Coordination and Validation drawing(s) and report deliverables are noted in Section 12.1: Design Deliverable Requirements and will be reviewed by Hodgson High School at project milestones.

10.2 MODEL STRUCTURE

The success of a BIM enabled project delivery process is highly dependent upon the level at which the entire project team can communicate and work collaboratively for the duration of the project.

- For buildings with a large footprint or multiple floors, the project team may split the model into several zones (or floors) with the corresponding trades
- All trades will be modeled at the correct elevation
- All elements of the building must be represented in only one file and should be modeled by their specific trade. (For example, the architectural model provided for 3D Coordination should not include any of the structural elements contained in the structural model. Lights should be modeled by the electrical engineer, not the architect)
- All 3D model files must strip extraneous 2D and/or 3D elements from the model before submission for clash detection
- The architectural ceilings should contain information for openings for lights, registers, etc. as required by design. (For example, lights are to be centered on a grid with proper spacing)
- All models should include separate 3D representations of required clearances and/or access requirements for equipment access, light clearances, overhead cable tray access, etc. These clearance/access models should be in a separate layer(s)/level(s) per each trade and labeled as such

10.2.1 MEASUREMENT AND COORDINATE SYSTEM

X-reference point will be 0, 0, 0.

10.2.2 MODEL ELEMENT REQUIREMENTS BY DESIGN TEAM DISCIPLINE

The following section lists the typical BIM model and related elements by discipline and/or exclusions. Please refer to the LOD Matrix for responsible party, project phase, and level of detail information.

Every discipline is required to provide all relevant schedules, reports, and intelligent attribute data defined by the project scope and BIM Plan.

SITE/CIVIL MODEL

Model(s) shall contain all site-related features of the project which are not integral with the building envelope:

- Utilities
- Topography
- Water Quality Ponds
- Storm water Detention and Filtration Structures
- Planting Materials
- Paving
- Site stairs, ramps, and railings
- Retaining walls
- Site furnishings
- Erosion Control (Temporary and Permanent)

ARCHITECTURAL MODEL

Model(s) shall contain all architectural features for a building and site-related features extending 5′-0″ beyond the facility footprint:

- Exterior wall systems
- Interior wall systems
- Fire rated walls
- Architectural floor slabs
- Roofing system
- Fire extinguishers and fixed equipment
- Reflected ceiling plans
- Core and vertical systems (including elevators, stairs, escalators, and railings)
- Doors (including frames)
- Glazing (including windows, interior glazing, curtain walls, and storefronts)
- Millwork and Casework
- Furniture
- Finishes
- Toilet Partitions

STRUCTURAL MODEL

Model(s) shall contain all structural features for a building:

- Footings, concrete piers, foundation walls (including areaways), and pits
- Structural slab-on-grade (as solid mass)
- Elevated floor slabs, CMU bearing walls, CMU shear walls
- All structural steel members in their true shape and dimensions
- Exclusions: nuts and bolts

- Column Gridlines
- Primary floor openings (stairs, elevators, mechanical shafts)
- Primary bearing wall openings
- Elevator hoist

MECHANICAL, ELECTRICAL, PLUMBING, FIRE PROTECTION MODEL(S)

Model(s) shall contain all MEP features for a building:

Mechanical Model:

- Major mechanical equipment (including energy recovery units, pumps, boilers, chillers, heat exchangers, and control panels)
- Major mechanical equipment requiring service clearance will be model with required clearance indicated.
- Mechanical ductwork and associated components (including flex duct, supply diffusers, and return grilles)
- Ductwork will be modeled using their inside dimensions and will include insulation if applicable and as required for coordination
- Mechanical piping and associated components (including flow meters and isolation valves, check valves and control valves for mains and branch mains)
- Piping will be modeled using their outside dimensions and will include insulation if applicable and as required for coordination

Electrical Model:

- Electrical conduit 1 1/4" and larger (or two or more regardless of size)
- Telecommunication racks and under floor tray(s)
- Safety and security systems
- Electrical equipment including specialty systems and pads
- Power feeds to equipment, transformers, panels, gear, junction boxes, cable trays, distribution boxes, etc
- Hangers and structural supports, unless they do not influence the coordination process of other trades
- Electrical light fixtures and ceiling devices
- Electrical panels and panel schedules
- Clearance requirements for equipment access, service space requirements, gauge reading, valve clearances, panel access, and other operation clearances

Plumbing Model:

- Domestic water piping
- Sanitary waste and vent piping
- Storm drainage piping

- Valves and meters
- Drains, cleanouts, and interceptors
- Plumbing equipment
- Plumbing fixtures
- Vents, valves, meters, cleanouts
- Plumbing equipment and fixtures

Fire Protection Model:

- Fire protection mains/standpipes
- Clearance requirements for equipment access, service space requirements, gauge reading, valve clearances, panel access, and other operation clearances

11.0 QUALITY CONTROL PROCEDURES

11.1 OVERALL STRATEGY FOR QUALITY CONTROL

The purpose of this process is to ensure project teams are using best practices in the development and file exchange of models and facility data. This is an ongoing process, which is to be conducted by the project team and validated by the Project manager at both project milestones and at random intervals to ensure that each model is being constructed in accordance with the BIM Standards and is suitably modeled for its intended use. The goal is to ensure that there are no unresolved issues during construction or any significant loss of data upon transfer of as-built models and record documents at facility turnover.

Each BIM Manager will be responsible for running quality control checks on their model(s) on a consistent and frequent basis. For issues involving other disciplines, the issue shall be made known to the corresponding BIM Manager.

We will perform Navisworks checks periodically to ensure fewer clashes in the model where two building components are overlapping. As we work, our technicians will ensure that the BIM Standard have been followed and that there are no unintended model components present. Our team will validate that the Project Facility Data set is as requested by the Owner is followed. One member of the project team will oversee all of the asset data and export it to a spreadsheet for verification that it has no undefined, incorrectly defined or duplicated elements.

11.2 QUALITY CONTROL CHECKS

CHECKS	DEFINITION	RESPONSIBLE PARTY	RECOMMENDED PROJECT MILESTONES
Standards	Ensure the BIM Standards and Guidelines have been followed	AMP Consulting	Construction Documents Project Closeout
Visual	Ensure there are no unintended model components and the design intent has been followed	AMP Consulting/ ABHA|BSA+A	Design Development Construction Documents 50% Construction Project Closeout
Model Integrity	Ensure that the Facility Data set has no undefined, incorrectly defined, or duplicated elements; ensure a reporting process and corrective action plans have been developed for noncompliant elements	AMP Consulting/ ABHA|BSA+A	Construction Documents 50% Construction Project Closeout
Model Commissioning	Provide report verifying model and database compliance with defined quality control procedures for component LOD and stakeholder information	AMP Consulting	Construction Documents 50% Construction Project Closeout

11.3 QUALITY CONTROL PROCEDURES

BIM Managers to define an appropriate quality control procedure for the project. The following is an example of a quality control procedure and must be validated for the project:

- Review random 10% of documented information
- If percent error is less than 3%, document reasons for error and revise throughout remaining model
- If percent error is between 3-5%, review additional 15% of randomly selected documented information.
- If percent error is greater than 3% after 25% review, project team to revise and resubmit information, as to not delay downstream user progress
- If percent error is less than 3% after 25% review, document reasons for error and revise throughout remaining model
- If percent error is greater than 5%, project team is to revise and resubmit information, as to not delay downstream user progress

11.4 MODEL ACCURACY AND TOLERANCES

Model(s) should be developed as accurate as possible. Dimension tolerances should be set at 1/16" to facilitate the accuracy of the model.

12.0 PROJECT DELIVERABLES

The BIM deliverables indicated below are required to be submitted with the standard phase deliverables for each project phase. The BIM Plan should establish the responsible parties and corresponding tasks for each deliverable. The level of development for each BIM deliverable should be, at a minimum, sufficient to fulfill the 2D document submission requirement.

12.1 DESIGN DELIVERABLE REQUIREMENTS

BIM DELIVERABLE	RESPONSIBLE PARTY	DUE DATE	FORMAT	NOTES
BIM Project Execution Plan	EDiS/AMP Consulting		.pdf	
Design Intent Model(s)	ABHA|BSA+A	Design Development	.rvt .nwd native	See information Exchange Worksheet to ensure that the proper information is contained in the model
Design Drawings: Design Development	ABHA|BSA+A	Design Development	.pdf	Documents to be printed directly from model. Documents to be stamped and signed in traditional practice to comply with local permitting requests
Room Number Coordination & Validation (Design Development)	ABHA|BSA+A	Design Development	.pdf	Document and schedule to be printed directly from model for review.
Design Drawings: Construction Documents	ABHA|BSA+A	Construction Documents	.pdf	Documents to be printed directly from model. Documents to be stamped and signed in traditional practice to comply with local permitting requests
Room Number Coordination & Validation (Construction Documents)	ABHA|BSA+A	Construction Documents	.pdf	Document and schedule to be printed directly from model for review.
Interference Check Reports	EDiS/AMP Consulting	Construction Documents	.xls	
Model Attribute Report	AMP Consulting	Post Construction Documents	.xls	
Hodgson High School Facility Attribute Data Compliance Report	AMP Consulting	Post Construction Documents	.pdf .xls	

12.2 CONSTRUCTION DELIVERABLE REQUIREMENTS

BIM DELIVERABLE	RESPONSIBLE PARTY	DUE DATE	FORMAT	NOTES
BIM Project Execution Plan	AMP Consulting	TBD	.pdf	
Interim Means and Methods Model(s) per Discipline	AMP Consulting		.rvt .nwd native	See information Exchange Worksheet to ensure that the proper information is contained in the model
Interference Check Reports	AMP Consulting/ ABHA|BSA+A		.xls	
Construction Submittals	AMP Consulting		.pdf	
Model Attribute Report	AMP Consulting		.pdf	
AMP Consulting Facility Attribute Data Compliance Report	AMP Consulting		.pdf .xls	

12.3 PROJECT CLOSEOUT DELIEVERABLE REQUIREMENTS

BIM DELIVERABLE	RESPONSIBLE PARTY	DUE DATE	FORMAT	NOTES
Record Model	ABHA|BSA+A	30-60 After Completion	.rvt .nwd native	See information Exchange Worksheet to ensure that the proper information is contained in the model
As-Built Model	AMP Consulting	30-60 After Completion	.rvt .nwd native	See information Exchange Worksheet to ensure that the proper information is contained in the model
Record Drawings	ABHA|BSA+A	30-60 After Completion	.pdf	Documents to be printed directly from model. Documents to be stamped and signed in traditional practice to comply with local permitting requests
Hodgson High School Facility Attribute Database	AMP Consulting	30-60 After Completion	.pdf .xls	

13.0 ATTACHMENTS

1. BIM Model LOD Matrix
2. AIA Document G203-2022 BIM Execution Plan
3. AIA Document G204-2022 Model Element Table
4. Exhibit "I" – BIM Coordination

ATTACHMENT 1: BIM MODEL LOD MATRIX

The project team should document the information exchanges created as part of the planning process when creating the BIM Plan. The following table describes the Model Element Author (MEA) referenced by the BIM

Model LOD Matrix:

MODEL ELEMENT AUTHOR		
ACRONYM	**ORGANIZATION**	**ROLE**
City	New Castle County Vocational Technical School District	Owner
HPL	Hodgson High School	Tenant
BMG	ABHA|BSA+A	Design Team
AMP	AMP Consulting	BIM
DCI	DCI + MacIntosh	Structural Engineer
Gipe	Gipe Associates	MEP Engineer
LSE	Landmark Engineering	Civil Engineer

The level of development (LOD) for each model element is based on the model content criteria established by the AIA Document E202, Building Information Modeling protocol Exhibit. The LOD will assist in determining the level of involvement for each project stakeholder from project conception through project turnover. The content for the LOD is described as follows:

Level of Development	Description
LOD 100 Schematic Design	The LOD 100 model consists of overall building massing designed to perform whole building type analysis including building orientation, square foot costs. LOD 100 also pertains to 2D representation of elements as required by the 2D Construction Documents which may include drawings, narratives, and hand-built models.

LOD 200 Design Development	The LOD 200 model consists of generalized systems including approximate quantities, sizes, shapes, location, and orientation. The LOD 200 mode(s) are used for analysis of defined systems and general performance objectives. LOD 200 model(s) include attributes and parameters defined by the owner in the Owner Requirements document and BIM Plan.
LOD 300/350 Construction Documentation	Model will include elements equivalent to traditional construction documents and shop drawings. LOD 300/350 models are well suited for estimating as well construction coordination for clash detection, scheduling, and visualization purposes. LOD 300/350 model(s) include attributes and parameters defined by the owner in the Owner Requirements document and BIM Plan.
LOD 400 Construction Administration/ Shop Drawings	Model elements are modeled as specific assemblies which are accurate in terms of quantity, size, shape, location, and orientation. LOD 400 model(s) are virtual representations of the proposed elements and considered to be suitable for construction, fabrication, and assembly. This LOD is most likely used by specialty trade contractors and fabricators to build and fabricate project components including MEP systems.
LOD 500 Project Completion/ Record Drawings/ As-Built Conditions	Model elements represent the project as it has been constructed, including as-built conditions. The model is configured to be the central data storage for integration into the building maintenance and operations system(s). LOD 500 Model(s) will include completed parameters and attributes specified in the Owner Requirements document and BIM Plan. At the completion of construction, the BIM model(s) will be finalized, linked, and cross referenced.
LOD 510, 520, 530, 540	Model elements represent the project as it has been constructed, including as-built conditions. LOD 510, LOD 520, LOD 530, and LOD 540 models will contain LOD 100, LOD 200, LOD 300, LOD 400 facility and geometry data respectively and will be configured to contain the Operations and Maintenance manuals, warranty information, submittal information, and/or any other documents as applicable or required.
LOD 550 Owner Reserved	Owner reserved, LOD 550 model elements will not be generated during planning, design, or construction.
Exhibit 'I'	Contractors LOD Requirement

The BIM LOD Matrix worksheet shall be completed by the project team during BIM Plan development.

EXHIBIT 'I'

BIM COORDINATION

1.0 CONTRACTOR 3-D MODEL RESPONSIBILITY

The purpose of a three-dimensional model is to aid in project review development. Contractor and its sub-contractors, as part of the Hodgson High School project, shall hold all responsibility to adhere to AIA G203-2022 BIM Executive Plan and AIA G204-2022 Model Element Table while creating their BIM model respectively. This BIM model shall reflect the two-dimensional contract drawings provided in bidding package, RFI, and ASI. The Contractor's referenced and shared three-dimensional model is only utilized as a visual aid to begin per matrix LOD required by Contractor.

1.01 Architect and their consultants will Furnish Contractor one set of Revit 2023 Building Information Modeling files (BIM) of Drawing for use in preparing coordination digital data files.

- Architect makes no representations as to the accuracy or completeness of digital data files as they relate to drawings.
- Digital data software program: Drawings are available in Revit 2023 digital data software working on the Windows operating system. Sheet views will be deleted to protect the architect and consultants. Full model will be available for coordination.
- Contractor shall execute a data licensing agreement in the form of the agreement included in the project manual.
- The Contractor and its prime contractors are responsible to execute all licensing for requested software to coordinate the project.

1.02 BIM File Incorporation: Develop and incorporate coordination drawing information into Building Information Model established for Project.

- Each of the Prime Contractors shall model their respective systems in the BIM model that are part of their contract and provide updated files to the HVAC contractor.
- The HVAC contractor (Prime Coordinator) shall perform three-dimensional component conflict analysis as part of the preparation of coordination drawings. Resolve component conflicts with each Prime prior to submittal. Indicate where conflict resolution requires modification of design requirements by Architect and obtain approval of Architect.
- HVAC contractor shall revise the BIM model as necessary to reflect the coordination changes. HVAC contractor shall pay for the cost of revisions to the BIM model. HVAC contractor shall include all cost due to the revisions of project changes such as but not limited to RFI, ASI's and owner changes. All modifications, enhancements, additions, and changes to structural, mechanical, electrical, plumbing, fire protection, or HVAC components shall be made by the respective Prime Contractors responsible for that system as part of their contract.

2.0 DEFINITIONS

2.01 **Base Structural Model** – the structural steel mill order drawing file showing all structural elements. This model is not necessarily fully detailed with all connections.

2.02 **Base Architectural Model** – a combination of the Base Structural Model and key architectural elements. This model is to be used by all coordination participants as the background file in which to develop their work. No information within this model will be changed through the coordination process. It is for reference only.

2.03 **Base Composite Model** – this model includes all trade drawing files within the Base Architectural Model as a representation of the completed systems. This model is used to run the intermediate clash reports and is considered a work in progress.

2.04 **Final Coordination Model** – this model shows all trades' systems fully coordinated within the Base Architectural Model. All clashes have been resolved. No further coordination is required. The work shown within this model represents the upcoming installations of each system.

2.05 **Completed Coordination Model** – this model is the close-out submittal to the Owner and includes the information within the Final Coordination Model as well as any project updates that have taken place during installations such as RFI responses, as-built conditions, etc.

2.06 **Building Information Model -** A Building Information Model(s) is a digital representation of the physical and functional characteristics of the Project and is referred to in this document as the "Model(s)," which term may be used herein to describe a Model Element, a single Model or multiple Models used in the aggregate. "Building Information Modeling" means the process and technology used to create the Model.

2.07 **Level of Development** - The Level(s) of Development (LOD) describes the level of completeness to which a Model Element is developed.

2.08 **Model Element** - A Model Element is a portion of the Building Information Model representing a component, system or assembly within a building or building site. Model Elements are represented by the Construction Specifications Institute (CSI) UniFormat™ classification system in the Model Element Table in Exhibit 1 - Article 3.

2.09 **Model Element Author** - The Model Element Author is the party responsible for developing the content of a specific Model Element to the LOD required for a particular phase of the Project. Model Element Authors are identified in the Model Element Table in Exhibit 1 - Article 3.

2.10 **Model User** - The Model User refers to any individual or entity authorized to use the Model on the Project for analysis, estimating, or scheduling.

2.11 **TCD** – Trade contract drawings developed by MEP contractor.

3.0 COORDINATION DRAWING PROCESS–GENERAL REQUIREMENTS.

3.1 The coordination model shall be derived from the design base composite model which shall be in a (Program File Format – Ex: Revit 2023) format and utilized by all coordination participants. The A/E is to provide this base composite model as needed at each plan deliverable for coordination efforts. This model will be utilized to establish field installation sequence, resolve trade coordination issues prior to installation, and to make the most efficient use of installation space without sacrificing system performance for mechanical, electrical, structural, and architectural systems. (Program File Format – Ex: NAVISWORKS or IFC) design review software will be used to document, identify and resolve interferences between all trades.

3.2 Communication is a critical element to the success of this coordination process. All project team members must be in constant communication to keep the process moving forward according to the sign-off schedule (5.1). Constant collaboration is expected of all team participants and each participant should be proactive in identifying and resolving design, engineering, and model interferences. Contractors avoiding the coordination process shall receive liquidated damages for missing meetings and negatively impacting project completion.

3.3 All trade contractors own their respective modeling for their contract work. EDiS Company will facilitate and lead the 3-D coordination modeling process. It is the responsibility of all coordination participants to resolve discrepancies pertaining to their own model. All trades shall be responsible for collisions/clashes/coordination issues involving their respective trade(s) and proposed work. Coordinated work takes precedence over field routed systems. Each Contractor to provide LOD 350 total coordination models for sign off.

3.4 Coordination meetings will occur weekly starting TBD. Selected coordination team members are required to generate a clash-free model inclusive of all systems. The following participants are required to attend the weekly coordination meetings:

3.5 A mandatory coordination kick-off meeting for all participants will review; team collaboration, the execution process, the coordination schedule, establishing zones per system, use of the coordinated elements during construction, project specific information and requirements, and model/document standards.

3.6 Coordination meetings will be held at Virtual Goto Meeting to review the model's progress per the schedule and process indicated.

3.7 Utility corridors and above ceiling space for each trade, will be established by the group at the beginning of the process. These zones will be adjusted through the coordination process to meet installation requirements and feasibility.

3.8 All participants are required to identify the submittals required for accurate detailing of the coordination model (such as equipment, light fixtures, etc.) and to obtain final approval so the information can be incorporated into the modeling process.

3.9 The 3-D coordination modeling process replaces the standard submittal process as a submittal. Exceptions: The submittals issued to reflect the 3-D model content issued to A/E.

3.10 Meeting Procedures:

Meeting Type	Project Stage	Frequency	Participants	Location
EDIS BIM COMPASS	PRE-CON	Once	EDiS Team & Contracts #	EDIS Office
BIM Requirement Kick-off	Construction	Once	EDiS Team & Contracts #	Virtual
BIM Coordination	Construction	Weekly	EDiS Team & Contracts #	Virtual
BIM Clash Detection	Construction	Weekly	EDiS Team Issue to Contracts	Virtual
Field Installation Process Coordination Meetings	Construction	Weekly	EDiS Team & Contracts #	Virtual
TCD Drawings	Construction	Weekly	Contracts Mechanical	Virtual
Sign off on TCD Drawings	Construction	At completion	All Parties w/Contract	Virtual

NOTE: All contracted parties involved with coordination are required to sign off on all coordinated models via sign off TCD drawings. All clash reports issued to subcontractors require completion by next BIM meeting.

3.11 The coordination meeting:

3.11.1 The purpose is to review and resolve items on the current clash report in conjunction with the project coordination schedule. The meetings will focus on clashes that cannot be resolved by internal collaboration. EDiS Company will facilitate the meeting and will make final decisions on clash resolution that are the least impact to the project as a whole. COORDINATION MEETINGS WILL NOT BE USED TO RESOLVE INDIVIDUAL MODELER'S/ENGINEER'S/ARCHITECTURE'S/CONTRACTOR'S WORK. If a Contractor does not post a clash-free system of its own work or that only contains a very limited number of clashes internally (Example: Fire Sprinkler Clashing with Fire Sprinkler), that Contractor will be considered unprepared for the meeting and will be responsible for any delays to the project schedule and any associated costs due to that delay which shall be determined by EDiS Company.

3.11.2 Each team participant will review the clash report prior to the subsequent coordination meeting in order to clean up any clashes that can be made without review by all participants.

3.11.3 All project participants are expected to be prepared for the meeting with new drawing work of the next area to be coordinated per the coordination schedule and any drawing changes based on the published clash report. Each participant will have available any shop model, submittals or other materials required to solve identified or potential conflicts.

3.11.4 The coordination schedule will be maintained, and all identified conflicts addressed and resolved per the construction schedule. The coordination schedule may change as a result of design and/or model changes requested and made by the Owner, Architect or Engineer. In addition, the coordination schedule assumes selection of equipment is made within the time

frame of the construction schedule as needed so it is incorporated into the coordination efforts without delay.

3.11.5 All agreed upon corrections to identified clashes determined by the team at the Coordination Meeting are to be updated and resolved prior to the next meeting.

3.12 When an area of the model is fully coordinated and clash-free, each participant agrees:

3.12.1 That each trades work is fully coordinated and will be installed per the signed off area as reflected in the coordination model. Sign off drawings from each trade are turned over in PDF form with projects title block. EDiS Company will include legend and title block for trade PDF file.

3.12.2 All trades to provide Total Coordination drawings at the time of sign off. TCD's are drawings which include all trades sign off models. Models are submitted for turn over to EDiS Company. The purpose for TCD's is to provide coordinated building models for jobsite coordination. Models from Contractors to include all but not limited to: item elevations, product type and all equipment tags.

3.12.3 During the installation of each trade's work, EDiS Company will refer to the signed off report and the 3-D model to resolve any conflicts. Each installation firm agrees to install all work per the signed off drawings/model, without deviation. If a deviation, during installation, takes place without prior approval from all detailing parties, it will be the responsibility of the installing contractor to tear out the work and install it as shown on the signed off drawings/coordination model. The cost of this work will be evaluated when the issues arise; however, the party responsible for the conflict will be responsible for the cost of the fix, including the additional detailing time of all parties involved.

3.12.4 The model is not considered to be the final coordination model until the BIM Coordinator, EDiS Company's Project Manager, A/E, and Owner has approved all clash free systems and routings and documents are signed off by all parties (contractors).

3.13 Should a conflict arise during installation that was missed during the coordination process, and not a result of deviating from the signed off area, the coordination team will work together to find a solution that is optimal for all trades and the project.

3.14 The final coordination model shall be kept up to date by all participants during construction to include as-built information and any other pertinent data that is essential to the project. The data will be submitted electronically in Revit, AutoCAD, NWC, PDF format. Items to be included are:

3.14.1 RFI responses.

3.14.2 Design change orders or designs that are in addition to the original contract documents.

3.14.3 Equipment will be tagged with all (Owner required) identification information within the model (ex. Equipment schedule information and O&M Manuals). This identification information will be the same and correspond to all other close-out documentation. This close-out documentation including O&M manuals, maintenance information, etc. will be included in PDF form.

3.14.4 EDiS will provide a location for the Contractor to submit the required documentation at a later time. EDiS will generate the completed coordination model based on these documents for turn-over to the owner.

3.14.5 Tekla or Navisworks will be utilized to link PDF closeout documents, select RFI's, select Images, etc., to the closeout model. Contractors need to provide closeout documents in the format requested by EDiS for the closeout model as well as adding smart data to other model type files as determined necessary by EDiS within the time frame A/E dictates. For example, if



Revit files are needed to produce the closeout model, EDiS may direct Contractor to set up certain Revit views for the exporting of files which make up the as-built models. A/E may also request that the Contractor create viewpoints for their equipment in as-built model.

3.15 Data for coordination will be available on Dropbox, to be referenced by the other participants. Models and drawing files will never be tampered with by non-owners of the file. If a mistake occurs and a drawing is inadvertently modified, the responsible party is required to alert the project team.

3.16 The Owner's commissioning agent can attend the coordination meeting to review the detailing effort for commissioning related items.

3.17 All trades will provide Level of Development (LOD) (350) models for weekly coordination meeting.

4.0 REQUIREMENTS OF THE LEAD COORDINATOR

4.01 The Lead Coordinator will be EDiS Company.

4.02 Identification of a common insertion point for all drawing files. (Utilize Revit Models origin)

4.03 A/E to provide Lead Coordinator model exports to 2-D/3-D CAD of each trade component as needed to coordination. Origins to be maintained in exports.

4.04 All coordination files and process is via Revizto 5 file uploads and backgrounds are in Revizto.

4.05 Using the A/E's files, the Lead Coordinator will utilize & maintain the base architectural model.

- The base architectural model is a combination of the base structural model and other architectural elements. These architectural elements will include all elevated 3-D architectural elements including, but not limited to, all walls that extend to the deck, fire and smoke walls, soffits and associated framing, ceiling planes, and finish floor planes.
- This model will consist of cleaned-up floor plans void of any excessive notations, leaders, bubbles, marks, grid lines, etc. that are not required for detailing development and that may potentially cause a conflict in the base composite model.
- In the event of changes to the A/E's contract documents, the A/E must revise the base architectural model/MEP/structural models and distributed to all coordination participants. This will require Contractor participation as needed by A/E to complete the revised models for directive. Revision work will be directed by Owner through an executed change order.
- The base architectural models will be distributed and maintained by EDiS Company.

4.06 Collation of all trades' detailing models as posted to the project's web-based posting site into a Base Composite Model through the use of Navisworks 2023.

- Establish a standard two inch (2") soft tolerance within the clash detection software. This tolerance will result in a reported clash for any elements drawn closer than two inches (2") to one another.
- Assess and include most current clash files including the generation of a clash reports and distribution to all project participants per the coordination schedule.
- Collect final as-built files from all trades and generate a Final Coordination Model to submit to CM as part of the close-out requirements.
- Coordination meeting minutes shall be kept by EDiS Company Lead Coordinator or EDiS' Project Manager showing issues and resolution dates.

4.07 Each Trade Subcontractor is required to sign off on all coordinated models and drawings ensuring they are 100% coordinated and clash free fabrication level models and shop drawings.

4.08 All contractors and trades are responsible for using/acquiring a ****REVIZTO license software. The cost is $1,200 per license, per contractor.** **

5.0 REQUIREMENTS OF THE STRUCTURAL STEEL CONTRACTOR

5.01 Obtain from the A/E Structural Revit files to be used in the generation of the base structural model.

5.02 The structural Contractor will develop and provide the base structural model within the time frame dictated by EDiS and provide structural model updates to ensure the coordination team is coordinating the MEP/FP to the most up-to-date structural model.

5.03 All structural framing members in the final sizes and locations (typically referred to as a "mill order" or "procurement" model) will be shown in the model as 3-D objects with surfaces. At the discretion of the lead coordinator, this model may be void of all hardware and secondary structural steel but should include the major components: primary steel, metal decking, slab on metal decking, and gusset plates.

5.04 The structural insertion/datum point must match the architectural insertion/datum location. No detailing work shall take place until the insertion points of the architectural and structural models match.

5.05 The steel Contractor is responsible for resolving their own modeling issues (i.e.: steel not to scale, missing key structural components, missing surface data, and model showing as wire frame data, model exported to proper file format, etc.). The steel Contractor is responsible to provide a steel design model in a usable format for all coordination participants to reference as the base structural model.

5.06 A FINAL 3-D steel model and 2-D shop drawings shall be submitted to the structural engineer of record and used for field erection. It must be completed and submitted in accordance with the BIM schedule. This model shall consist of:

- All primary and secondary steel including metal deck, slab on metal deck, actual gusset plate sizes, connection details, edge of slab details (pour stop), brick relief angles, embeds, anchor bolts, and other miscellaneous metals. Curtain Wall embeds modeled by others.
- Submit final approved files to Lead Coordinator for insertion into the coordinated model, and to the design team in the form of shop drawings and/or Navisworks compatible model.

6.0 DETAILING REQUIREMENTS OF ALL PARTICIPANTS

6.01 File sharing information:

Site Contractor (SIT-1)

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Attend BIM trade coordination meetings.
- Deliver three-dimensional model to coordination team
- Required to deliver items identified in G204 matrix such as
- Develop appropriate tie-in locations of utilities with trades. Site contractor required to deliver main connections in model format
- Site underground items outside direct tie in locations not required in three dimensional models.
- Sanitary piping tie-in
- Storm water tie-in
- Domestic water tie-in

6.02 The in-progress (Coordination Software – Ex: IFC/NWC/Cad) naming convention will be: project-trade-level. Examples:

- Project Designation -MechPipe-1
- Project Designation -HVAC-1
- Project Designation –Fire Protection-1
- Project Designation -Elec-1
- Project Designation -Plumbing-1
- Project Designation -TeleCom-1 or AV-1
- Project Designation –Pneumatic Tube-1, etc.

Additional designations may be added based on project specific scope and deliverable requirements and/or deemed as a critical component to the coordination process.

6.03 Each model posted by the contractor shall contain model elements for the purpose of system identification and isolation during the clash detection process. Example:

HVAC-1 shall contain model elements for:

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Supply
- Return
- Exhaust
- Fire Smoke-Dampers
- VAV clearance
- AC Door Access
- Fan Coil Units
- FCU Access
- Equipment
- Equipment Pads
- Equipment Clearances
- Hangers (designated per system)
- Duct insulation
- Duct model to the outside face of dimensional duct
- Access zones, all equipment

MechPipe-1 shall contain model elements for:

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Hydronic Pipe Supply
- Hydronic Pipe Return
- Chilled Pipe Supply
- Chilled Pipe Return
- Shutoff Access
- Equipment
- Equipment Pads
- Equipment Clearances
- Hangers
- Pipe insulation

Plumbing-1 shall contain model elements for:

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.

- Domestic Water Supply
- Domestic Water Return (with additional layer designations for hot and cold)
- Gas
- Med-Gas
- Shutoff Access (designated per system)
- Sanitary
- Vent
- Roof Drain
- Rain Conductors
- Equipment
- Equipment Pads
- Equipment Clearances
- Hangers (designated per system)

Elec-1 shall contain model elements for:

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Lights
- Light Clearance
- Conduit (with additional layer designation for power and data)
- Cable Tray
- Cable Tray Access Clearance
- Pull Boxes
- Pull Box Access Clearance
- J-Boxes
- Elec. Panels
- Elec. Panel Access Clearance
- Elec. Troughs
- Elec. Trough Access Clearance
- Equipment
- Equipment Clearances
- Equipment Pads
- Hangers

Fire Protection1 shall contain model elements for:

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Mains
- Branches
- Shutoff Access
- Hangers

Pneumatic Tube-1 shall contain model elements for:

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Equipment
- Equipment Access
- Hangers

Concrete PreCast Plank

- All items which appear in a schedule and has a schedule name will correspond with a 3-D model element including model element data.
- Plank w/ camber
- Plank w/ cores and openings
- Plank w/ all conduit or piping as required
- Plank embeds
- Plank rebar
- Plank setting plates or items
- Plank vertical chase requirements must be modeled and coordinated

Additional sub layers may be added based on project specific scope and deliverable requirements and/or deemed as a critical component to the coordination process.

6.04 Clash detection files will be posted to **Revizto** before **12:00 PM**, on **Wednesday and Friday** by each of the trades. The lead coordinator will also post updated coordination models as needed. The lead coordinator will maintain the master coordination files. The weekly coordination model will be name abbreviated Project Name-Floor-Coordination Model-Month-Day-Year.

All coordination participants will maintain a current control copy of their own drawing files outside of the project's web-based posting site. Control drawings are to include all previously posted files.

6.05 Trade Colors in the Coordination environment:

- Duct Supply – Dark Green
- Duct Return- Light Blue
- Duct Exhaust –Light Green
- Mech Pipe- Orange
- Pressure lines/Gas – Tan
- Sanitary/Vent – Brown
- Rain Conductors/Roof Drains – Maroon
- Domestic Water- Blue
- Fire – Red
- Pneumatic – Purple
- Electrical – Yellow
- All Base Architectural Elements (walls, soffits, ceiling & floor planes, etc.) will assume Arch model color scheme saved in the export or Lead Coordinator will modify select color scheme in the coordination model.
- Steel – Dark Grey
- Any hangers and equipment (that is fed per the designated system) will assume the same color of that system it is associated with. Additional color schemes may be added based on project specific scope and deliverable requirements and/or deemed as a critical component to the coordination process.

6.06 When posting drawing files for coordination:

- Posted Contractor coordination files of each trades system should be clash-free with in their respective data. To clarify; trades should refrain from posting data that shows their systems clashing with itself.
- When coordination of an area is completed there should not be any unresolved clashes remaining.
- These files should be void of any text, dimensions or any other notations.

6.07 Each coordination participant is required to submit three (3) complete sets of installation drawings as well as electronic PDF's prior to any work being installed in the field. If A/E spec requires more or less than that will govern over this document. These complete drawings are to be fully dimensioned and notated. Items to be noted in the final, fully coordinated drawing paper and electronic files of each system include:

- Bottom and top elevations of duct, pipe, conduit racks, cable trays etc. must be indicated (where applicable).
- Dimensions shall be shown from the gridlines to the centerline of each element drawn (round duct, pipe, cable tray, etc.) and from finished floor.
- Height to top of light housing assembly must be indicated.
- Labeling of all equipment.

6.08 During the coordination drawing effort, priority will be given to those systems that have the least flexibility. The following list is a descending order of the system priority and shall be used as a general guideline. Throughout the coordination drawing effort, adjustments and deviations to this list can be made with the approval of EDiS Company. (0'- 6") clear above the ceiling shall be maintained for access and construction of the ceiling, whenever possible. Required maintenance and/or code access spaces and set-backs take precedence over all systems.

- Gravity Pipe
- Plumbing Vent
- Ductwork and appurtenances
- Cable tray
- Recessed light fixtures
- Fire protection piping and fixtures
- Electrical conduit over (3/4") in diameter
- Pneumatic tube and other record or material conveying systems
- HVAC piping
- Plumbing, supply and medical gas piping
- Electrical conduit smaller than 3/4" in diameter
- Above ceiling miscellaneous metal supports
- Provide all copper tube routes (racks) for mechanical systems, including valves, clearance zones and hangers.

6.09 Items to be included in the detailed drawing progress include:
[For the following trades HVAC, HVAC piping, electrical, fire protection, building management, carpentry, general works trades and structural]

- All systems must be fully detailed and shown as individual elements including ductwork, all piping 3/4" and larger, pneumatic tubing, exterior wall connections, any piping that is smaller than ½" that is racked or banked, etc.
- Ductwork is to include size, layout and routing of all metal and flex ductwork, re-heat coils, terminal units, filters registers, grilles, diffusers, and similar features; provide notation for diffuser boot sizes and heights and any other special features
- All valves, dampers and VAV's or heat pumps will note any items requiring access for service and maintenance as well as access doors in inaccessible ceilings.
- All piping valves, boxes, supports, etc. are to be fully detailed
- Sprinkler head locations shall be shown on ceiling plans.

- All electrical conduits one and a quarter inches (1 1/4") or more in diameter are to be modeled and shown in addition to smaller diameter conduit that is racked or banked.
- Electrical items such as hangers, supports, electrical fixtures, lights, speakers, detectors, sensors, cable trays, raceways, sleeves, pull boxes, and access space claims, etc. must be shown.
- If an element is not shown, under the lead coordinators approval, it will be assumed to be field routed and to not interfere with the other elements that are shown or within code clearances. Contractors who field route their elements are responsible to ensure their installation will be feasible and void of creating a clash in the field. Coordinated items take precedence over field routing.
- All major hangers and supports (including sway bracing, equipment bracing, hangers, etc.), penetrations, openings must be shown for all systems. Sharing of supports with other systems is discouraged but can be accomplished with prior owner and/or field inspector approval.
- All insulation must be shown with appropriate thicknesses. All insulation & clearance zones will be modeled or accounted for during the clash detection process.
- Sprayed Fire Protection (all methods): If required by your building type, establish a safe thickness from all structural objects with which to run your clashes. Assume fire spray will be two inches (2") thick.
- Engineered stud framing must be modeled for king studs and doors.
- Code clearances and maintenance access clearances must be shown and maintained; these include, but are not limited to access to VAVs, air handling units, egresses around pumps and tanks, smoke FDs, electrical panels, pneumatic tube transfer units, cable tray access, pull boxes, valve access, etc.
- All trades must coordinate and detail their systems with the intent of installing each system at the optimal elevation above ceiling, taking into consideration, access to equipment for maintenance, repairs, connections, filters and removal while eliminating or minimizing the impact to surrounding components.
- All concrete plank modeled by plank installers contract. 3-D model the plank per structural design calculations. Include all but not limited to cores, hollow sections, vertical sleeve locations, rebar, setting embeds and misc. structural attachment items

6.10 Established Clash Files are to be incorporated to ensure proper coordination. List of those files to be provided by the Lead Coordinator.

6.11 Refer to Appendix B – Soft Clash Requirements for additional soft-clash requirements.

7.0 SCHEDULE OF DRAWING COMPLETION AND SIGN-OFF

7.01 The participants must plan on the coordination process taking two to three months. The coordination schedule is as follows:
This table will be populated at the BIM Coordination Kick-off Meeting. OR Schedule to be developed as part of the master construction schedule development (see Section 00230).

Zone	Floor	Coordination Meeting	Sign-Off Date

7.02 At the completion of each floor, the team will determine the specific "priority walls" that will be constructed full-height ahead of other interior partitions and MEP installations.

7.03 D MEP/FP Coordination Team

- The goal of the coordination team will be to integrate the architectural, structural, mechanical, electrical, fire protection, and project specific elements into a collaborative 3-D model to identify and resolve issues pertaining to MEP/FP systems and to ensure succinct and expedited field installations of these systems following the release of each zone/floor after clash free conditions are met. (Filled out at BIM Coordination Kick-off Meeting)

BIM Coordinator	**AMP Consulting**
Main Contact	Chris Donahue
Phone Number	302-893-0492
Email Address	cdonahue@ampconsulting.build
Project Manager	**EDiS Company**
Main Contact	Kevin Lucas
Phone Number	302-420-3083
Email Address	klucas@ediscompany.com
Project Engineer	**EDiS Company**
Main Contact	Olek Kostyszyn
Phone Number	302-559-3454
Email Address	okostyszyn@ediscompany.com
Project Superintendent	**EDiS Company**
Main Contact	Matt Artymenko
Phone Number	302-218-1752
Email Address	martymenko@ediscompany.com
Site Contractor	**TBD**
Main Contact	Kent Construction Company
Phone Number	302-653-6469
Email Address	chad@kentconstructionco.com
HVAC	**TBD**
Main Contact	
Phone Number	

Email Address	
Electrical	**TBD**
Main Contact	
Phone Number	
Email Address	
Concrete	**TBD**
Main Contact	
Phone Number	
Email Address	
Plumbing and Piping	**TBD**
Main Contact	
Phone Number	
Email Address	
Architectural	**TBD**
Main Contact	
Phone Number	
Email Address	
MEP/FP Engineers	**TBD**
Main Contact	
Phone Number	
Email Address	
Structural Steel	**TBD**
Main Contact	
Phone Number	
Email Address	
Miscellaneous Steel	**TBD**
Main Contact	
Phone Number	
Email Address	

LOD REQUIREMENT

ARTICLE 1: GENERAL PROVISIONS

1.1 This document defines protocols, expected levels of development, and authorized uses of Building Information Models on this Project. It assigns specific responsibility for the development of each Model Element to a defined Level of Development at each Project phase. Where a provision in this Exhibit conflicts with a provision in the Agreement into which this Exhibit is incorporated, the provision in this Exhibit will prevail.

1.1.1 The parties agree to incorporate this Exhibit by reference into any other agreement for services or construction for the Project.

ARTICLE 2: LEVEL OF DEVELOPMENT (LOD)

2.1 The following LOD descriptions identify the specific content requirements and associated authorized uses for each Model Element at five progressively detailed levels of completeness. Each subsequent LOD builds on the previous level and includes all the characteristics of previous levels.

2.2 **LOD 350**

2.2.1 **Model Content Requirements**. Overall building massing indicative of area, height, volume, location, and orientation may be modeled in three dimensions or represented by other data.

2.2.2 **Authorized Uses**

2.2.2.1 **Analysis**. The Model may be analyzed based on volume, area and orientation by application of generalized performance criteria assigned to the representative Model Elements.

2.2.2.2 **Cost Estimating**. The Model may be used to develop a cost estimate based on current area, volume or similar conceptual estimating techniques (e.g., square feet of floor area, condominium unit, hospital bed, etc.).

2.2.2.3 **Schedule**. The Model may be used for project phasing and overall duration.

2.3 **LOD 350**

2.3.1 **Model Content Requirements**. Model Elements are modeled as specific assemblies accurate in terms of quantity, size, shape, location, and orientation. Existing building elements are modeled as shown on building record drawings. Non-geometric information such as object description and object tags (door number, equipment number, etc) and quantities should be included with each object. Examples of the details required for systems modeled to LOD 300 include, but are not limited to:

- Show all, but not limited to, unground utilities, plumbing and mechanical, concrete modeled as contract documents.
- Site Utilities (see matrix and 6.1 front end)
- Masonry
- Steel decking
- PRECAST PLANK
- Correct slopes for gravity piping for sanitary, storm or wet fire suppression systems.

- Piping materials specifically called out on documents included with model element attributes (generic manufacturer for system components are acceptable).
- Insulation around Pipe and Ducting.
- Duct dampers included with the duct system.
- Doors/Frames (hollow metal and storefront)
- Owner Furnished Fixtures, Equipment, etc. generically modeled as space claims by the Model Element Author (MEA).
- Concrete
- Anchor bolts
- Structural steel
- Steel stairs, handrails
- Floor/roof penetration steel
- Significantly sized support hangers and sleeves for all systems
- Uni-Strut associated with system components if it is located in a tight overhead space (case by case basis)
- Architectural millwork/casework
- Metal panels and support steel
- Curtainwall system
- Steel stud framing including kickers and trusses at floor penetrations.
- Valve locations (clearance)
- Access panels (these should be modeled with the system they provide access to).
- Conduit racks or other substantially wide / bundled electrical routing. (these can be generically modeled, i.e. extruded boxes, space claims)
- Single conduit runs associated with any system (lighting, power, controls, etc) if needed to coordinate concrete coring.
- Kitchen equipment
- MEP/FP & Low Voltage Equipment
- MEP/FP & Low Voltage Systems
- Pull box locations and any extra space claims for their access.
- Telecom & Data

2.3.2 **Authorized Uses**

2.3.2.1 **Construction**. Suitable for the generation of traditional construction documents. Contractors may utilize this model for coordination purposes and creation of shop drawings.

2.3.2.2 **Analysis**. The Model may be analyzed for performance of selected systems by application of specific performance criteria assigned to the representative Model Elements.

2.3.2.3 **Schedule**. The Model may be used to show ordered, time-scaled appearance of detailed elements and systems.

ARTICLE 3: MODEL ELEMENTS

3.1 **Reliance on EDiS Company's Model Element Matrix**

3.1.1 The EDiS Company Model Element Matrix at the end of this section identifies (1) the LOD required for each Model Element at the end of each Project phase, and (2) the Model

Element Author responsible for developing the Model Element to the LOD identified. Each Model Element Author's content is intended to be shared with subsequent Model Element Authors and Model Users throughout the course of the Project.

3.1.2 It is understood that while the content of a specific Model Element may include data that exceeds the required LOD identified in the Model Element Table for a particular phase, Model Users and subsequent Model Element Authors may rely on the accuracy and completeness of a Model Element consistent only with the content required for a LOD identified in the Model Element Table.

3.1.3 Any use of, or reliance on, a Model Element inconsistent with the LOD indicated in the Model Element Table by subsequent Model Element Authors or Model Users shall be at their sole risk and without liability to the Model Element Author. To the fullest extent permitted by law, subsequent Model Element Authors and Model Users shall indemnify and defend the Model Element Author from and against all claims arising from or related to the subsequent Model Element Author's or Model User's modification to, or unauthorized use of, the Model Element Author's content.

3.2 **Table Instructions**

3.2.1 The Model Element Table at the end of this section indicates the LOD to which each Model Element Author (MEA) is required to develop the content of the Model Element at the conclusion of each phase of the Project. EDiS Company holds the rights of this table and all ownership right for edits are performed via EDiS Company.

3.3 EDiS Company's Model Element Matrix AIA Document G204-2022 (attached).

3.4 Insertion Point (attached).

AIA® Document G203™ – 2022

BIM Execution Plan

BIM EXECUTION PLAN VERSION NUMBER:
DATE: October 9, 2023

PROJECT NAME:
(Name and location or address of the Project)

Paul M. Hodgson Vocational Technical High School
2575 Glasgow Avenue
Newark, DE 19702

PROJECT OWNER:
(Name and address)

New Castle County Vocational Technical School District
2575 Glasgow Avenue
Newark, DE 19702

EXHIBIT NAME:
(Identify, by date and full title, the BIM and Digital Data Exhibit for the Project (the "Exhibit"))

Paul M. Hodgson Vocational Technical High School

INTENDED GOALS FOR MODELS ON THE PROJECT:
(Summarize the intended goals for Model documentation, process, and workflow.)

ADDITIONS AND DELETIONS:
The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be incorporated into an agreement between the Parties.

AIA Document G203 – 2022. Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1331187029)

TABLE OF ARTICLES

1 PROJECT INFORMATION

2 DESIGNATED DELIVERY MILESTONES FOR MODEL VERSIONS

3 SOFTWARE REQUIREMENTS AND FILE EXCHANGE PROTOCOL

4 DATA SECURITY MEASURES

5 MODELING PROTOCOLS

6 MODEL MANAGEMENT PROTOCOLS

7 LEVELS OF DEVELOPMENT

8 RELIANCE AUTHORIZATION PROTOCOLS FOR INTERIM DELIVERABLES

9 IDENTIFICATION OF MODELS

10 OTHER BIM OR MODELING PROVISIONS

11 EXHIBITS AND ATTACHMENTS

The terms used in this BIM Execution Plan have the same meaning as those in the Exhibit.

This BIM Execution Plan may be updated, as appropriate, in accordance with the terms of the Exhibit.

ARTICLE 1 PROJECT INFORMATION

§ 1.1 Project Participants Directory

(Identify all Project Participants developing or using Models, their discipline or trade, and contact information for their key representatives.)

Project Participant *(Firm or company name)*	Discipline or Trade	Contact Name *(Insert individual name and Project role or title)*	Contact Information *(Insert phone number, email address, and other contact information)*
EDiS Company	Construction Manager	Kevin Lucas	klucas@ediscompany.com 302-420-3083
AMP Consulting	BIM Consultant	Christopher Donahue	cdonahue@ampconsulting.build 302-893-0492
ABHA | BSA+A	Architect (Joint Venture)	Kathy Knotts	knotts@simpers.com 302-658-9300
DCI+MacIntosh Engineers	Structural Engineer		
Gipe Associates	MEP Engineer	Adam Kegan	mminner@furlowassociates.com 410-832-2420
Landmark Engineering	Civil Engineer	Ted Williams	tedw@landmark-se.com 302-323-7933

§ 1.2 Project Schedule

(Insert or attach the Project schedule, including a detailed schedule for Model development. If appropriate, include the schedule's version or date.)

TBD

AIA Document G203 – 2022. Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1331187029)

§ 1.3 Existing Data
(Describe any existing survey files, as-built files, documents, or BIM content. Include any license or usage restrictions.)

Request files from ABHA | BSA+A.

ARTICLE 2 DESIGNATED DELIVERY MILESTONES FOR MODEL VERSIONS
Designated Delivery Milestones for Model Versions
(Insert or attach the delivery schedule, identifying Designated Delivery Milestones for Model Versions. State whether a Model Element Table will be included for this purpose as set forth in Article 7.)

ARTICLE 3 SOFTWARE REQUIREMENTS AND FILE EXCHANGE PROTOCOL
§ 3.1 Modeling Software
(Indicate software and version(s) to be used for modeling and any other necessary information.)

Software	Version	Other Information
Revizto	5	
Navisworks		

§ 3.1.1 Modeling Software Updates. All Project Participants agree to coordinate software updates prior to making any Model file upgrades.

§ 3.2 Other Software Tools
(Indicate other software tools to be used to interface with Models, such as for analysis, coordination, quality management, etc. Include version and update restrictions, if any.)

§ 3.3 File Exchange Protocols
§ 3.3.1 The Project Participants agree to share their respective Model Portion updates as follows:
(*Check the appropriate box.*)

[X] **§ 3.3.1.1 Cloud-Based Collaboration.** The Project Participants agree to use a cloud-based Modeling software platform for developing and sharing Models as follows:
(Indicate software, licensing, and other requirements for hosting the Project. Identify the Project Participant responsible for hosting the Project. Indicate the frequency for Model updates, such as daily, identifying the time of day.)

[ ] **§ 3.3.1.2 Separate Model Collaboration.** The Project Participants agree to use file sharing of separately developed Models, and shall develop and share their Model Portions as follows:
(Indicate the requirements for preparation of the Model Portion before it is transmitted, including how to handle links and exclusions of links, auditing, and compacting. Indicate the means of transmission, if appropriate. Indicate the frequency of file exchange for Model updates, such as at milestones, or weekly, identifying the day of the week.)

[ ] **§ 3.3.1.3 Other:**
(Specify the type of Model collaboration, which may include a hybrid of cloud-based and separate Model development.)

AIA Document G203 – 2022. Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1331187029)

§ 3.4 Collaboration Protocols. The Project Participants' protocols for the collaborative use of Models, if any, including communication protocols, method of decision tracking, and co-location requirements are as follows:

§ 3.4.1 Training and Support Parameters. The parameters for any training or support program(s) that will be implemented with respect to any collaboration protocols or technical requirements are as follows:

Training on Revizto is provided via AMP Consulting/Revizto Representative.

§ 3.4.2 Training and Support Costs. The Project Participants are each responsible for their respective software training and support, and associated costs, unless set forth below:
(Identify required software to be used on the Project and for which the Project Participants will be compensated for training and support, and state how the Project Participants will be compensated.)

ARTICLE 4 DATA SECURITY MEASURES

Data Security Measures. In addition to those data security measures identified in the Exhibit, the Project Participants agree to implement the following data security protocols:
(Indicate data security measures, such as data storage, backup, and security measures, to be implemented by all Project Participants.)

ARTICLE 5 MODELING PROTOCOLS

§ 5.1 Project Coordinates. Project coordinates, including Project north, true north angle, and physical horizontal and vertical location in real space, are set forth below. Project coordinates will not be changed without prior agreement from all Project Participants.
(Indicate the Project coordinates, which can be described in writing, represented graphically, or both.)

0, 0, 0

§ 5.2 Model Data Subdivisions. Model Authors agree to reasonably minimize the subdivision of their Model Portion(s). Any changes to subdivided Model Portions shall be communicated to all Project Participants.

§ 5.3 Common Data Fields
(Indicate common data fields intended to be shared for sheet indices and Model coordination.)

§ 5.4 Construction Phasing. If the Project will be constructed in separate phases, then indicate the phases below. The Project Participants agree that Model phases will be consistent across all Models. If additional phases, or modifications to phases indicated below, are required, then all Project Participants agree to use any new or modified phases.
(Indicate the phases for the Project, such as when the Project includes existing buildings.)

§ 5.5 Sheets
(Indicate the standard format(s) for 2D output(s), such as sheet sizes for the Project, title block format, and requirements to name, number, and identify deliverables.)

AIA Document G203 – 2022, Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1331187029)

§ 5.6 Design Options
(Indicate any protocols for addressing or exploring design options.)

§ 5.7 File Naming Conventions
(Indicate protocols for naming each type of file.)

§ 5.8 Modeling Standards
(Indicate standards to be used by the Project Participants, or attach and identify a separate document.)

ARTICLE 6 MODEL MANAGEMENT PROTOCOLS

§ 6.1 Responsibility
(Define individual roles and responsibilities for Model management.)

§ 6.2 Meetings
(Indicate meeting types, the stage or phase within which the meeting occurs, and the meeting frequency.)

Meeting Type	Project Stages or Phases	Frequency
Virtual	Prior to begin field work	weekly

§ 6.3 Quality Control and Model Health.
§ 6.3.1 Internal Quality Control. Each Project Participant is responsible for producing quality Model Portions that can be used and opened effectively by all other Project Participants. Project Participants will perform checks on their respective Model Portions pursuant to Section 6.3.1.1.

§ 6.3.1.1 Model Checking. The following checks should be performed by each Model Author to assure Model quality:
(Describe each quality control measure to be implemented throughout the development of Model Portions.)

[ ] **§ 6.3.1.1.1 Visual Check.** Perform a visual check to confirm that there are no unintended Model components and confirm design intent has been followed:
(Indicate the frequency with which Visual Checks will be performed and modify the description if required.)

[X] **§ 6.3.1.1.2 Interference Check.** Detect problems within individual Model Portions and with the interface between Model Portions where two building components clash, including where required clearances clash:
(Indicate the frequency with which Interference Checks will be performed and modify the description if required.)

[X] **§ 6.3.1.1.3 Modeling Protocols Check.** Confirm that the protocols reflected in Article 5 of this BIM Execution Plan have been followed:
(Indicate the frequency with which Modeling Protocols Checks will be performed and modify the description if required.)

AIA Document G203 – 2022. Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1331187029)

[ ] **§ 6.3.1.1.4 Model Integrity Check.** Check for items that affect the integrity of each Model Portion, such as corrupted Models, duplicated Model Elements, software warnings, Models with overly large file sizes, etc.:
(Indicate the frequency with which Model Integrity Checks will be performed and modify the description if required.)

[ ] **§ 6.3.1.1.5 Other:**

§ 6.3.2 External Quality Control. Upon receipt of another Project Participant's Model Portion, Project Participants shall report to the Model Author any Model quality issues discovered. Model Authors shall promptly resolve reported Model quality issues and issue a new Version of the Model Portion.

ARTICLE 7 LEVELS OF DEVELOPMENT

§ 7.1 Level of Development Descriptions. The Level of Development (LOD) descriptions shall be as set forth in the Exhibit.

§ 7.2 The Project Participants intend to identify the LOD for Model Elements at Designated Delivery Milestones as follows:
(Check the appropriate box.)

[ ] AIA Document G205™–2022, Abbreviated Model Element Table

[ ] AIA Document G204™–2022, Model Element Table

[ ] Describe the LOD to be applied to Model Elements as follows:
(Describe how the LOD will be applied to Model Elements. Itemize by discipline or trade as appropriate. If the Project Participants will use a custom model element table, then identify that model element table.)

§ 7.3 Level of Accuracy. The level(s) of accuracy used for Model Elements indicated as LOD 500 shall be as follows:
(Describe a single level or multiple levels of accuracy that will be applied to LOD 500 Model Elements.)

ARTICLE 8 RELIANCE AUTHORIZATION PROTOCOLS FOR INTERIM DELIVERABLES

For Interim Deliverables, Model Authors will authorize or limit reliance on Model Versions of their respective Model Portions as follows:
(Define the means of authorization, whether described within the Model Version or in a separate document, or both. If appropriate, attach the authorization text or form as an exhibit.)

ARTICLE 9 IDENTIFICATION OF MODELS

§ 9.1 Identification of Model Versions Enumerated as a Contract Document
(Describe how the Project Participants will identify a Model Version enumerated as a Contract Document, if any, such as by file name, by Model Author, through the use of a Model Element Table, or other method.)

AIA Document G203 – 2022. Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes: (1331187029)

§ 9.2 Identification of Models or Model Portions not Enumerated as a Contract Document
(Describe how the Project Participants will identify a Model or Model Portions that are not enumerated as a Contract Document, such as by file name, by Model Author, through the use of a Model Element Table, or other method.)

ARTICLE 10 OTHER BIM OR MODELING PROVISIONS

Other provisions related to BIM or Modeling are as follows:

All contractors involved with the coordination process are responsible for paying the Revizto license cost. The license cost is $1,200.

ARTICLE 11 EXHIBITS AND ATTACHMENTS

(List here any exhibits and attachments to this BIM Execution Plan.)

AIA Document G203 – 2022. Copyright © 2022. All rights reserved. "The American Institute of Architects," "American Institute of Architects," "AIA," the AIA Logo, and "AIA Contract Documents" are trademarks of The American Institute of Architects. This document was produced at 15:03:54 ET on 12/05/2023 under Order No.4104239075 which expires on 01/17/2024, is not for resale, is licensed for one-time use only, and may only be used in accordance with the AIA Contract Documents® Terms of Service. To report copyright violations, e-mail docinfo@aiacontracts.com.
User Notes:
(1331187029)

AIA® Document G204™ – 2022

Model Element Table

MODEL ELEMENT TABLE DATE: October 9, 2023

This Model Element Table dated the day and year written above is incorporated into the BIM Execution Plan between the Parties for the following Project:

(Name and location or address of the Project)

NCC Votech School District Paul M. Hodgson Vocational Technical High School
2575 Glasgow Avenue
Newark, DE 19702

BIM EXECUTION PLAN NAME:

(Identify, by date and full title, the BIM Execution Plan into which this LOD Table is incorporated) (the "BIM Execution Plan")

Paul M. Hodgson Vocational Technical High School BIM Project Execution Plan

MOST RECENT BIM EXECUTION PLAN VERSION OR DATE:

EXHIBIT NAME:

(Identify, by date and full title, the BIM and Digital Data Exhibit into which the BIM Execution Plan is incorporated) (the "Exhibit")

Paul M. Hodgson Vocational Technical High School BIM Project Execution Plan

TABLE OF ARTICLES

ARTICLE 1 LEVELS OF DEVELOPMENT

ARTICLE 2 MODEL ELEMENT TABLE

The terms used in this Model Element Table have the same meaning as those in the Exhibit.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be incorporated into an agreement between the Parties.

AIA Document G204™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

ARTICLE 1 LEVELS OF DEVELOPMENT

§ 1.1 Level of Development Definitions. The Level of Development (LOD) descriptions shall be as set forth in the Exhibit.

§ 1.2 Any Model Element that does not have an LOD defined at a phase is not required to be Modeled at that phase. If a Model Element is modeled and no LOD is provided at that phase, the Model Element may not be relied upon.

ARTICLE 2 MODEL ELEMENT TABLE

§ 2.1 Table Instructions. The Model Element Table in Section 2.4 indicates the LOD to which each Model Element shall be developed at each identified Project milestone and the Model Element Author.

§ 2.2 Model Element Table Abbreviations. Abbreviations for each Model Element Author to be used in the Model Element Table are as set forth in the Abbreviations tab.

§ 2.3 Model Element Table Notes. Notes for each Model Element in the Model Element Table are as set forth in the Notes tab. Limitations or qualifications on Model Elements may be described in the Notes.

AIA Document G204™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.4 Model Element Table

Identify (1) whether a Model Element will be modeled, (2) the LOD required for each Model Element at each Project milestone, (3) the Model Element Author, and (4) references to any applicable notes found in Section 2.3.

Indicate whether the Model Element is included in the Project by inserting an “x” in the "Modeled' column. If a “Modeled” cell is left blank, the Element in that row will not be included in a Model Portion.

Insert abbreviations for each MEA identified in the "Abbreviations" tab.

Project Milestones headings may be modified to identify delivery milestones as defined in the Agreement.

NOTE: LODs must be adapted for the unique characteristics of each Project.

Model Elements Utilizing CSI UniFormat™				Modeled - Bid Package 'D'	Bid Package 'D' Construction Manager Construction Coordination			As-Built (TBD)		
					LOD	MEA	Notes	LOD	MEA	Notes
B	**Shell**									
	B20	**EXTERIOR VERTICAL ENCLOSURES**								
		B2010	**Exterior Walls**							
			B2010.10	Exterior Wall Veneer	x	350	D-01, D-05			
			B2010.20	Exterior Wall Construction	x	350	D-03			
			B2010.40	Fabricated Exterior Wall Assemblies	x	350	D-03			
			B2010.80	Exterior Wall Supplementary Components	x	350	D-02			
			B2010.90	Exterior Wall Opening Supplementary Components	x	350	D-13			
		B2020	**Exterior Windows**							
			B2020.10	Exterior Operating Windows	x	350	D-13			
			B2020.20	Exterior Fixed Windows	x	350	D-13			
			B2020.30	Exterior Window Wall	x	350	D-13			
			B2020.50	Exterior Special Function Windows	x	350	D-13			
		B2050	**Exterior Doors and Grilles**							
			B2050.10	Exterior Entrance Doors	x	350	D-11, D-13			
			B2050.20	Exterior Utility Doors	x	350	D-11, D-13			
			B2050.30	Exterior Oversize Doors	x	350	D-12			
	B30	**EXTERIOR HORIZONTAL ENCLOSURES**								
		B3010	**Roofing**							
			B3010.10	Steep Slope Roofing	x	350	D-08			
			B3010.50	Low-Slope Roofing	x	350	D-08			
			B3010.70	Canopy Roofing	x	350	D-08			
			B3010.90	Roofing Supplementary Components	x	350	D-08			
		B3060	**Horizontal Openings**							
			B3060.50	Vents and Hatches	x	350	D-11			
			B3060.90	Horizontal Opening Supplementary Components	x	350	D-11			
C	**Interiors**									
	C10	**INTERIOR CONSTRUCTION**								
		C1010	**Interior Partitions**							
			C1010.10	Interior Fixed Partitions	x	350	D-06			
			C1010.20	Interior Glazed Partitions	x	350	D-13			
			C1010.50	Interior Operable Partitions	x	400	D-38			
		C1020	**Interior Windows**							
			C1020.20	Interior Fixed Windows	x	350	D-13			
			C1020.50	Interior Special Function Windows	x	350	D-13			
			C1020.90	Interior Window Supplementary Components	x	350	D-13			
		C1030	**Interior Doors**							
			C1030.10	Interior Swinging Doors	x	400	D-11			
			C1030.20	Interior Entrance Doors	x	400	D-11			
			C1030.25	Interior Sliding Doors	x	400	D-11			
			C1030.30	Interior Folding Doors	x	400	D-11			
			C1030.40	Interior Coiling Doors	x	400	D-11			
			C1030.50	Interior Panel Doors	x	400	D-11			

AIA Document G205™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.4 Model Element Table

Identify (1) whether a Model Element will be modeled, (2) the LOD required for each Model Element at each Project milestone, (3) the Model Element Author, and (4) references to any applicable notes found in Section 2.3.

Indicate whether the Model Element is included in the Project by inserting an “x” in the "Modeled' column. If a “Modeled” cell is left blank, the Element in that row will not be included in a Model Portion.

Insert abbreviations for each MEA identified in the "Abbreviations" tab.

Project Milestones headings may be modified to identify delivery milestones as defined in the Agreement.

NOTE: LODs must be adapted for the unique characteristics of each Project.

Model Elements Utilizing CSI UniFormat™				Modeled - Bid Package 'D'	Bid Package 'D' Construction Manager Construction Coordination			As-Built (TBD)		
					LOD	MEA	Notes	LOD	MEA	Notes
		C1030.70	Interior Special Function Doors	x	400	D-11				
		C1030.80	Interior Access Doors and Panels	x	400	D-11				
		C1030.90	Interior Door Supplementary Components	x	400	D-11				
	C1060	**Raised Floor Construction**								
		C1060.10	Access Flooring	x	350	D-21				
		C1060.30	Platform/Stage Floors	x	350	D-21				
	C1070	**Suspended Ceiling Construction**								
		C1070.10	Acoustical Suspended Ceilings	x	350	AMP				
		C1070.20	Suspended Plaster and Gypsum Board Ceilings	x	350	AMP				
		C1070.50	Specialty Suspended Ceilings	x	350	AMP				
		C1070.70	Special Function Suspended Ceilings	x	350	AMP				
		C1070.90	Ceiling Suspension Components	x	350	AMP				
	C1090	**Interior Specialties**								
		C1090.40	Toilet, Bath, and Laundry Accessories	x	400	D-04				
C20	**INTERIOR FINISHES**									
	C2030	**Flooring**								
		C2030.80	Athletic Flooring	x	350	D-21				
D	**Services**									
D10	**CONVEYING**									
	D1030	**Horizontal Conveying**								
		D1030.10	Moving Walks	x	400	D-30				
D20	**PLUMBING**									
	D2010	**Domestic Water Distribution**								
		D2010.20	Domestic Water Equipment	x	350	D-32				
		D2010.40	Domestic Water Piping	x	350	D-32				
		D2010.60	Plumbing Fixtures	x	350	D-32				
		D2010.90	Domestic Water Distribution Supplementary Components	x	350	D-32				
	D2020	**Sanitary Drainage**								
		D2020.10	Sanitary Sewerage Equipment	x	350	D-32				
		D2020.30	Sanitary Sewerage Piping	x	350	D-32				
		D2020.90	Sanitary Drainage Supplementary Components	x	350	D-32				
	D2030	**Building Support Plumbing Systems**								
		D2030.10	Stormwater Drainage Equipment	x	350	D-32				
		D2030.20	Stormwater Drainage Piping	x	350	D-32				
		D2030.30	Facility Stormwater Drains	x	350	D-32				
		D2030.90	Building Support Plumbing System Supplementary Components	x	350	D-32				
	D2060	**Process Support Plumbing Systems**								
		D2060.10	Compressed-Air Systems	x	350	D-32				
		D2060.20	Vacuum Systems	x	350	D-32				
		D2060.30	Gas Systems	x	350	D-32				
		D2060.40	Chemical-Waste Systems	x	350	D-32				
		D2060.50	Processed Water Systems	x	350	D-32				

AIA Document G205™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.4 Model Element Table

Identify (1) whether a Model Element will be modeled, (2) the LOD required for each Model Element at each Project milestone, (3) the Model Element Author, and (4) references to any applicable notes found in Section 2.3.

Indicate whether the Model Element is included in the Project by inserting an “x” in the "Modeled' column. If a “Modeled” cell is left blank, the Element in that row will not be included in a Model Portion.

Insert abbreviations for each MEA identified in the "Abbreviations" tab.

Project Milestones headings may be modified to identify delivery milestones as defined in the Agreement.

NOTE: LODs must be adapted for the unique characteristics of each Project.

Model Elements Utilizing CSI UniFormat™				Modeled - Bid Package 'D'	Bid Package 'D' Construction Manager Construction Coordination			As-Built (TBD)		
					LOD	MEA	Notes	LOD	MEA	Notes
		D2060.90	Process Support Plumbing System Supplementary Components	x	350	D-32				
D30	**HEATING, VENTILATION, AND AIR CONDITIONING (HVAC)**									
	D3020	**Heating Systems**								
		D3020.10	Heat Generation	x	350	D-32, D-33				
		D3020.30	Thermal Heat Storage	x	350	D-32, D-33				
		D3020.70	Decentralized Heating Equipment	x	350	D-32, D-33				
		D3020.90	Heating System Supplementary Components	x	350	D-32, D-33				
	D3030	**Cooling Systems**								
		D3030.10	Central Cooling & Equipment	x	350	D-32, D-33				
		D3030.90	Cooling System Supplementary Components							
	D3050	**Facility HVAC Distribution Systems**								
		D3050.50	HVAC Air Distribution	x	350	D-32				
		D3050.90	Facility Distribution Systems Supplementary Components	x	350	D-32				
	D3060	**Ventilation**								
		D3060.10	Supply Air	x	350	D-32, D-33				
		D3060.20	Return Air	x	350	D-32, D-33				
		D3060.30	Exhaust Air	x	350	D-32, D-33				
		D3060.40	Outside Air	x	350	D-32, D-33				
		D3060.60	Air-to-Air Energy Recovery	x	350	D-32, D-33				
		D3060.70	HVAC Air Cleaning	x	350	D-32, D-33				
		D3060.90	Ventilation Supplementary Components	x	350	D-32, D-33				
D40	**FIRE PROTECTION**									
	D4010	**Fire Suppression**								
		D4010.10	Water-Based Fire-Suppression	x	350	D-31				
		D4010.50	Fire-Extinguishing	x	350	D-31				
		D4010.90	Fire Suppression Supplementary Components	x	350	D-31				
	D4030	**Fire Protection Specialties**								
		D4030.10	Fire Protection Cabinets	x	350	D-31				
		D4030.30	Fire Extinguishers	x	350	D-31				
		D4030.70	Fire Extinguisher Accessories	x	350	D-31				
D50	**ELECTRICAL**									
	D5010	**Facility Power Generation**								
		D5010.10	Packaged Generator Assemblies	x	350	D-36				
		D5010.70	Transfer Switches	x	350	D-36				
		D5010.90	Facility Power Generation Supplementary Components	x	350	D-36				
	D5020	**Electrical Service and Distribution**								
		D5020.10	Electrical Service	x	350	D-36				
		D5020.30	Power Distribution	x	350	D-36				
		D5020.70	Facility Grounding	x	350	D-36				
		D5020.90	Electrical Service and Distribution Supplementary Components	x	350	D-36				
	D5030	**General Purpose Electrical Power**								
		D5030.10	Branch Wiring System	x	350	D-36				
		D5030.50	Wiring Devices	x	350	D-36				

AIA Document G205™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.4 Model Element Table

Identify (1) whether a Model Element will be modeled, (2) the LOD required for each Model Element at each Project milestone, (3) the Model Element Author, and (4) references to any applicable notes found in Section 2.3.

Indicate whether the Model Element is included in the Project by inserting an "x" in the "Modeled' column. If a "Modeled" cell is left blank, the Element in that row will not be included in a Model Portion.

Insert abbreviations for each MEA identified in the "Abbreviations" tab.

Project Milestones headings may be modified to identify delivery milestones as defined in the Agreement.

NOTE: LODs must be adapted for the unique characteristics of each Project.

Model Elements Utilizing CSI UniFormat™				Modeled - Bid Package 'D'	Bid Package 'D' Construction Manager Construction Coordination			As-Built (TBD)		
					LOD	MEA	Notes	LOD	MEA	Notes
		D5030.90	General Purpose Electrical Power Supplementary Components	x	350	D-36				
	D5040	**Lighting**								
		D5040.10	Lighting Control	x	350	D-36				
		D5040.20	Branch Wiring for Lighting	x	350	D-36				
		D5040.50	Lighting Fixtures	x	350	D-36				
		D5040.90	Lighting Supplementary Components	x	350	D-36				
	D5080	**Miscellaneous Electrical Systems**								
		D5080.10	Lightning Protection	x	350	D-36				
		D5080.90	Miscellaneous Electrical Systems Supplementary Components	x	350	D-36				
D60	**COMMUNICATIONS**									
	D6010	**Data Communications**								
		D6010.10	Data Communications Network Equipment	x	350	D-36				
		D6010.20	Data Communications Hardware	x	350	D-36				
		D6010.30	Data Communications Peripheral Data Equipment	x	350	D-36				
		D6010.50	Data Communications Software	x	350	D-36				
		D6010.60	Data Communication Program and Integration Services	x	350	D-36				
	D6020	**Voice Communications**								
		D6020.10	Voice Communications Switching and Routing Equipment	x	350	D-36				
		D6020.20	Voice Communications Terminal Equipment	x	350	D-36				
		D6020.30	Voice Communications Messaging	x	350	D-36				
		D6020.40	Call Accounting	x	350	D-36				
		D6020.50	Call Management	x	350	D-36				
	D6030	**Audio-Video Communication**								
		D6030.10	Audio-Video Systems	x	350	D-36				
		D6030.50	Electronic Digital Systems	x	350	D-36				
	D6060	**Distributed Communications and Monitoring**								
		D6060.10	Distributed Audio-Video Communications Systems	x	350	D-36				
		D6060.50	Distributed Systems	x	350	D-36				
D80	**INTEGRATED AUTOMATION**									
	D8010	**Integrated Automation Facility Controls**								
		D8010.10	Integrated Automation Control of Equipment	x	350	D-36				
		D8010.30	Integrated Automation Control of Fire-Suppression Systems	x	350	D-36				
		D8010.40	Integrated Automation Control of Plumbing Systems	x	350	D-32				
		D8010.50	Integrated Automation Control of HVAC Systems	x	350	D-32, D-33				
		D8010.60	Integrated Automation Control of Electrical Systems	x	350	D-36				
		D8010.80	Integrated Automation Control of Electronic Safety and Security Sys	x	350	D-36				
E	**Equipment and Furnishings**									
E10	**EQUIPMENT**									
	E1030	**Commercial Equipment**								
		E1030.10	Mercantile and Service Equipment	x	350	D-23				
		E1030.30	Refrigerated Display Equipment	x	350	D-23				
		E1030.55	Unit Kitchens	x	350	D-23				
		E1030.80	Foodservice Equipment	x	350	D-23				
	E1040	**Institutional Equipment**								

AIA Document G205™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.4 Model Element Table

Identify (1) whether a Model Element will be modeled, (2) the LOD required for each Model Element at each Project milestone, (3) the Model Element Author, and (4) references to any applicable notes found in Section 2.3.

Indicate whether the Model Element is included in the Project by inserting an “x” in the "Modeled' column. If a “Modeled” cell is left blank, the Element in that row will not be included in a Model Portion.

Insert abbreviations for each MEA identified in the "Abbreviations" tab.

Project Milestones headings may be modified to identify delivery milestones as defined in the Agreement.

NOTE: LODs must be adapted for the unique characteristics of each Project.

Model Elements Utilizing CSI UniFormat™				Modeled - Bid Package 'D'	Bid Package 'D' Construction Manager Construction Coordination			As-Built (TBD)		
					LOD	MEA	Notes	LOD	MEA	Notes
		E1040.10	Educational and Scientific Equipment	x	350	D-28				
		E1040.20	Healthcare Equipment	x	350	D-28				
	E1060	**Residential Equipment**								
		E1060.10	Residential Appliances	x	350	D-33				
	E1070	**Entertainment and Recreational Equipment**								
		E1070.10	Theater and Stage Equipment	x	350	D-26				
		E1070.20	Musical Equipment	x	350	D-26				
		E1070.50	Athletic Equipment	x	350	D-26				
		E1070.60	Recreational Equipment	x	350	D-26				
E20	**FURNISHINGS**									
	E2010	**Fixed Furnishings**								
		E2010.30	Casework	x	350	D-25				
		E2010.70	Fixed Multiple Seating	x	350	D-27				
		E2010.90	Other Fixed Furnishings	x	350	D-29				
	E2050	**Movable Furnishings**								
		E2050.60	Movable Multiple Seating	x	350	D-29				
F	**Special Construction and Demolition**									
F10	**SPECIAL CONSTRUCTION**									
	F1060	**Athletic and Recreational Special Construction**								
		F1060.10	Indoor Soccer Boards	x	350	D-36				
		F1060.40	Floor Sockets	x	350	D-36				
G	**Sitework**									
G30	**LIQUID AND GAS SITE UTILITIES**									
	G3010	**Water Utilities**								
		G3010.10	Site Domestic Water Distribution	x	350	D-32				
		G3010.30	Site Fire Protection Water Distribution	x	350	D-32				
		G3010.50	Site Irrigation Water Distribution	x	350	D-32				
	G3020	**Sanitary Sewerage Utilities**								
		G3020.10	Sanitary Sewerage Utility Connection	x	350	D-32				
		G3020.20	Sanitary Sewerage Piping	x	350	D-32				
		G3020.40	Utility Septic Tanks	x	350	D-32				
		G3020.50	Sanitary Sewerage Structures	x	350	D-32				
		G3020.60	Sanitary Sewerage Lagoons	x	350	D-32				
	G3030	**Storm Drainage Utilities**								
		G3030.10	Storm Drainage Utility Connection	x	350	D-32				
		G3030.20	Storm Drainage Piping	x	350	D-32				
		G3030.30	Culverts	x	350	D-32				
		G3030.40	Site Storm Water Drains	x	350	D-32				
		G3030.50	Storm Drainage Pumps	x	350	D-32				
		G3030.60	Site Subdrainage	x	350	D-32				
		G3030.70	Storm Drainage Ponds and Reservoirs	x	350	D-32				
	G3050	**Site Energy Distribution**								
		G3050.10	Site Hydronic Heating Distribution	x	350	D-32				

AIA Document G205™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.4 Model Element Table

Identify (1) whether a Model Element will be modeled, (2) the LOD required for each Model Element at each Project milestone, (3) the Model Element Author, and (4) references to any applicable notes found in Section 2.3.

Indicate whether the Model Element is included in the Project by inserting an “x” in the "Modeled' column. If a “Modeled” cell is left blank, the Element in that row will not be included in a Model Portion.

Insert abbreviations for each MEA identified in the "Abbreviations" tab.

Project Milestones headings may be modified to identify delivery milestones as defined in the Agreement.

NOTE: LODs must be adapted for the unique characteristics of each Project.

Model Elements Utilizing CSI UniFormat™			Modeled - Bid Package 'D'	Bid Package 'D' Construction Manager Construction Coordination			As-Built (TBD)		
				LOD	MEA	Notes	LOD	MEA	Notes
	G3050.20	Site Steam Energy Distribution	x	350	D-32				
	G3050.40	Site Hydronic Cooling Distribution	x	350	D-32				
G3060	**Site Fuel Distribution**								
	G3060.10	Site Gas Distribution	x	350	D-32				
	G3060.30	Site Gasoline Distribution	x	350	D-32				
	G3060.40	Site Diesel Fuel Distribution	x	350	D-32				
G40	**ELECTRICAL SITE IMPROVEMENTS**								
G4010	**Site Electric Distribution Systems**								
	G4010.10	Electrical Utility Services	x	350	D-36				
	G4010.20	Electric Transmission and Distribution	x	350	D-36				
	G4010.30	Electrical Substations	x	350	D-36				
	G4010.40	Electrical Transformers	x	350	D-36				
	G4010.50	Electrical Switchgear and Protection Devices	x	350	D-36				
	G4010.70	Site Grounding	x	350	D-36				
	G4010.90	Electrical Distribution System Instrumentation and Controls	x	350	D-36				
G4050	**Site Lighting**								
	G4050.10	Area Lighting	x	350	D-36				
	G4050.20	Flood Lighting	x	350	D-36				
	G4050.50	Building Illumination	x	350	D-36				
	G4050.90	Exterior Lighting Supplementary Components	x	350	D-36				
G50	**SITE COMMUNICATIONS**								
G5010	**Site Communications Systems**								
	G5010.10	Site Communications Structures	x	350	D-36				
	G5010.30	Site Communications Distribution	x	350	D-36				
	G5010.50	Wireless Communications Distribution	x	350	D-36				

AIA Document G205™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.2 Abbreviations

§ 2.2 Abbreviations for each Model Element Author to be used in the Model Element Table are as follows:
(Provide abbreviations for each Model Element Author)

Abbreviation	Model Element Author (MEA)
NCCVT	New Castle County Vocational Technical School District
HHS	Hodgson High School
EDiS	EDiS Company
AMP	AMP Consulting
ABHA|BSA	ABHA|BSA+A
Gipe	Gipe Associates
LSE	Landmark Engineering
DCI	DCI+MacIntosh
D-01	Unit Masonry
D-02	Miscellaneous Metals, Stairs, and Rails
D-03	Exterior Sturcural Stud Assembly
D-04	Carpentry and General Work
D-05	Exterior Metal Panels
D-06	Drywall and Interior Metal Framing
D-08	Roofing
D-11	Hollow Metal, Wood doors, and Finish Hardware
D-12	Overhead Coiling Doors and Grates
D-13	Curtainwall/Glazing/Storefronts
D-15	Acoustical and Specialty Ceilings
D-21	Wood Strip Flooring - Gym Flooring
D-23	Food Service Equipment
D-25	Laminate Clad Casework, Countertops, and Sills
D-26	Stage Riffing, Lighting, and Accessories
D-27	Fixed Auditorium Seating
D-28	Wood Laboratory Furniture and Specialty Casework
D-29	Telescoping Bleachers and Platforms
D-30	Hydraulic Holeless Passenger Elevator
D-31	Fire Protection
D-32	Plumbing
D-33	Mechanical Piping - HVAC
D-36	Electrical, Lighting, and Fire Alarm Systems
D-38	Vertical Retracting Walls
D-01, D-05	
D-11, D-13	
D-32, D-33	

AIA Document G204™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

§ 2.3 Notes

§ 2.3 Model Element Table Notes

Notes:

(List by number shown on table.)

1	Model Element Table is an add on document to all bid package noted above and relating to all contractor's scope of work. The table identifies all bid package requirements to provide Building Information Models (BIM) during the BIM coordination process. In addition, refer to BIM protocol instruction to see LOD descriptions.
2	Contractors are required to attend coordination meetings, submit, and post to BuildingBlok and maintain the BIM schedule production process.

AIA Document G204™ -2022. Copyright © 2022 by The American Institute of Architects. All rights reserved.

SECTION 014500 - QUALITY CONTROL

1. DESCRIPTION

   A. Quality control services include inspections and tests performed by independent agencies and governing authorities, as well as by the Contractor. Inspection and testing services are intended to determine compliance of the work with requirements specified. Specific quality control requirements are specified in individual specification sections.

2. RESPONSIBILITIES

   A. Contractor Responsibilities: Except where indicated as being the Owner's responsibility, quality control services are the Contractor's responsibility, including those specified to be performed by an independent agency and not by the Contractor. The Contractor shall employ and pay an independent agency, testing laboratory or other qualified firm to perform quality control services specified.

      1. The Owner will engage and pay for services of an independent agency to perform the inspections and tests that are specified as Owner's responsibilities.

   B. Retest Responsibility: Where results of inspections or test do not indicate compliance with Contract Documents, retests are the Contractor's responsibility.

   C. Responsibility for Associated Services: The Contractor shall cooperate with independent agencies performing inspections or test. Provide auxiliary services as are reasonable. Auxiliary services include:

      1. Provide access to the Work.

      2. Assist taking samples.

      3. Deliver samples to test laboratory.

   D. Coordination: The Contractor and independent test agency shall coordinate the sequence of their activities and shall avoid removing and replacing work to accommodate inspections and test. The Contractor is responsible for scheduling time for inspections and tests.

   E. Qualifications for Service Agencies: Contractor shall engage only inspection and test service agencies which are pre-qualified as complying with "Recommended Requirements for Independent Laboratory Qualification" by the American Council of Independent Laboratories.

   F. Submittals: Contractor shall submit a certified written report of each test, Inspection or similar service, in duplicate to the Construction Manager. Contractor shall submit additional copies of each report to any governing authority, when the authority so directs.

   G. Report Data: Written inspection or test reports shall include:

      1. Name of testing agency or test laboratory.

2. Dates and locations of samples, tests or inspections.

3. Names of individual present.

4. Complete inspection of test data.

5. Test results.

6. Interpretations.

7. Recommendations.

H. Repair and Protection: Upon completion of inspection or testing, Contractor shall repair damaged work and restore substrates and finishes. Contractor shall comply with requirements for "Cutting and Patching."

I. Special Instructions:

1. Structural tests and special inspections must be conducted by an approved agency (an agency or firm regularly engaged in conducting tests or furnishing inspection services, approved by the authority having jurisdiction.) This means that contractors will no longer be allowed to cast their own test cylinders for example.

2. Continuous special inspection (the full-time observation of work by an approved special inspector who is present until completion of the work) is required for any steel welds and connections. Critical elements may include: all slip critical bolted connections, complete and partial groove welds, multi-pass fillet welds and single pass fillet welds greater than 5/16".

3. Continuous special inspection is required during the placement of all concrete and shotcrete for the proper application techniques with a few exceptions.

4. Periodic special inspection (the part-time observation by an approved special inspector) is required for any steel welds and connections. Critical elements may include: all slip critical bolted connections, complete and partial groove welds, multi-pass fillet welds and single pass fillet welds greater than 5/16".

END OF SECTION

SECTION 015113 - TEMPORARY ELECTRICITY

1. GENERAL

A. RELATED WORK SPECIFIED ELSEWHERE

1. Electrical Basic Materials and Methods, Division 26.

B. DESCRIPTION OF SYSTEM

1. Power Source

a. Suppliers: Delmarva Power

b. The Electrical Contractor shall provide 277/480 volt, three phase, 60 cycle power service to the site. (Apply for and coordinate as needed with Delmarva Power)

c. The Electrical Contractor will make all arrangements for bringing the power supply to the site and for installation of appropriate temporary transformers to provide for the power supply in 1.B.1.b, above.

2. Electrical Service

a. Contractor will be responsible to pay for all costs associated with providing electrical service from the power source to their respective site office, temporary storage facilities or temporary construction buildings as appropriate.

b. Prior to issuance of the Notice to Proceed for the electrical contract, the Construction Manager will be responsible for providing temporary electrical service as provided in 1.B.2.c, below. After issuance of the Notice to Proceed for the electrical contract, the Electrical Contractor shall become responsible for maintaining all electrical power supply and service facilities installed by the Construction Manager. The Electrical Contractor shall also, from that date forward, be responsible for providing and maintaining temporary electrical service to the site as provided in 1.B.2.c, below.

c. The Electrical Contractor, as provided in 1.B.2.b, above, shall install temporary electric service for items below, throughout the construction period, such that power can be secured at any desired point with no more than a 60 foot extension:

(1) Power Centers for miscellaneous tools and equipment used in the construction work shall be provided with a minimum of four 20-amp, 120 volt grounding type outlets. Each outlet shall be provided with ground fault detecting circuit breaker protection.

(2) Adequate lighting for safe working conditions shall be provided and maintained on a 24 hour per day basis throughout the building, tunnels, and stairways per OSHA requirements. Each lamp must be rated at least 100 watts. Voltage of each socket must be

at least 110 volts.

(3) Power for testing and checking equipment must be supplied.

3. Capacity

a. All electrical power supply and service lines installed shall be of adequate capacity for construction use by all trades during the construction period at the locations necessary.

b. The Electrical Contractor shall notify the Power Company if unusually heavy loads, such as welding units, are anticipated.

4. Power Costs

a. The Construction Manager will pay all costs of temporary electrical power used during construction.

b. The Owner will pay all costs of power used in the permanent wiring.

C. REQUIREMENTS AND REGULATORY AGENCIES

1. The Electrical Contractor will obtain permits as required by local governmental authorities.

2. The temporary electrical service shall comply with National Electrical Code, 1990 Edition and applicable local codes and utility regulations.

D. USE OF PERMANENT SYSTEM

1. The Electrical Contractor shall regulate any part of the permanent electrical system which is used for construction purposes to prevent interference with safety and orderly progress of the Work.

2. Contractors shall leave permanent electrical services in a condition as good as new and clean.

2. PRODUCTS

A. MATERIALS

1. General

a. The materials may be new or used, but must be adequate in capacity for the purposes intended and must not create unsafe conditions or violate the requirements of applicable codes.

2. Conductors

a. Use wire, cable, or busses of appropriate type, sized in accordance with the National Electrical Code for the applied loads.

b. Use only UL labeled wire and devices.

B. EQUIPMENT

1. Provide appropriate enclosure for the environment in which used in compliance with NEMA standards.
2. This contractor (electrical contractor) shall provide Temporary transformers as may be required to support the incoming temporary electric service. (coordinate with Delmarva Power)

3. EXECUTION

A. GENERAL

1. Install all work with a neat and orderly appearance.

2. Make structurally sound throughout.

3. Maintain to give continuous service and to provide safe working conditions.

4. Modify temporary power and light installation as job progress requires.

B. INSTALLATION

1. Locate so that interference with storage areas, traffic areas and work under other Contracts is avoided.

C. REMOVAL

1. Remove all temporary equipment and materials completely upon completion of construction.

2. Repair all damage caused by the installation and restore to satisfactory condition.

END OF SECTION

SECTION 015123 - TEMPORARY HEATING, COOLING AND VENTILATING

1. GENERAL

A. RELATED REQUIREMENTS SPECIFIED ELSEWHERE

1. Temporary Electric: Section 015113

2. Temporary Facilities: Section 015200

3. Heating Requirements for Cold Weather Installation and Protection of Materials: Respective specification section for each item of work.

B. DEFINITIONS

1. Temporary Enclosures: Sufficient preliminary enclosures of an area of structure, or of an entire building, to prevent entrance or infiltration of rainwater, wind, or other elements and which will prevent undue heat loss from within enclosed area.

2. Permanent Enclosure: Stage of construction at which all moisture and weather protection elements of construction have been installed in accordance with Contract Documents, either for a portion of structure, or for an entire building.

C. DESCRIPTION OF SYSTEM

1. Prior to the building or portion of building being permanently enclosed, each Contractor shall provide temporary heat and ventilation and weather protection necessary for their work, as described below. After permanent enclosure, the HVAC Contractor shall provide and maintain temporary heat and ventilation in enclosed areas, coordinated by the Construction Manager, required to:

a. Facilitate progress of Work.

b. Protect Work and products against dampness and cold.

c. Prevent moisture condensation on surfaces.

d. Provide suitable ambient temperatures and humidity levels for installation and curing of materials.
e. Provide adequate ventilation to meet health regulations for safe working environment.

2. Temperatures Required

a. Generally, 24 hours a day: Minimum of 40 degrees F.

b. 24 hours a day during placing, setting, and curing of cementitious materials: As required by specification section for each product.

c. 24 hours a day, seven days prior to, and during, placing of interior finishes: woodwork, resilient floors, painting and finishing: As required by specification section for each product.

d. 24 hours a day after application of finishes, and until Substantial Completion: Minimum of 50 degrees F.

3. Ventilation Required:

a. Contractors shall prevent hazardous accumulations of dusts, fumes, mists, vapors, or gases in areas occupied during construction. Reference OSHA regulations CFR 1926.55 (Gases, vapors, fumes, dusts, and mists). and CFR 1926.57 (Ventilation).

(1) Provide local exhaust ventilation to prevent harmful dispersal of hazardous substances into atmosphere of occupied areas.

(2) Dispose of exhaust materials in manner that will not result in harmful dispersal of hazardous substances into atmosphere of occupied areas.

(3) Continuously ventilate storage spaces containing hazardous or volatile materials.

(4) Contractor/subcontractor must provide and use equipment which is furnished with Exhaust Purifiers/Scrubbers or is electrically power driven when any such equipment produces airborne containments and will be used in an enclosed building.

(5) The Contractor/subcontractor shall verify air quality by the use of air monitoring equipment and document the verified air quality on the daily report. The monitoring equipment shall, at a minimum, be designed with an auditory alarm and shall provide continuous monitoring of those four gasses, Oxygen, Hydrogen Sulfide, Carbon Monoxide and Combustible gasses.

4. Contractors shall provide adequate ventilation for:

a. Curing installed materials.
b. Dispersal of humidity.

c. Temporary sanitary facilities.

5. Duration of Operations:

a. For Personnel:

(1) At all times personnel occupy an area subject to hazardous accumulations of harmful elements.

(2) Continue operation of ventilation and exhaust system for time after cessation of work

process to assure removal of harmful elements.

b. For curing installed materials: As required by specification section for respective materials.

c. For humidity dispersal: Continuously ventilate to provide suitable ambient conditions for work.

d. The HVAC Contractor shall maintain supervision and operation of temporary heating and ventilating equipment in order to:

(1) Enforce conformance with applicable codes and standards.

(2) Enforce safe practices.

(3) Prevent abuse of services.

D. COSTS OF INSTALLATION AND OPERATION

1. The Contractor shall be responsible for all installation and operating costs for any heat and ventilation as required in this section until the permanent HVAC system is in operation.

2. After the permanent HVAC system is operational, the Owner will pay the costs of fuel for temporary heat and ventilation. The Contractor will pay the costs for maintaining the system until final acceptance by the Owner.

3. The HVAC Contractor shall be responsible for all installation and operating costs for any heat required to supplement that which is to be supplied by the Construction Manager in paragraph 1.C.1, above.

E. REQUIREMENTS OF REGULATORY AGENCIES

1. The Construction Manager will obtain and pay for permits as required by governing authorities for those activities required by this Section.

2. Contractor shall comply with Federal, State, and local codes, and utility company regulations.

2. PRODUCTS

A. MATERIALS

1. General

a. Materials may be new or used but must be adequate for purposes intended and must not create unsafe conditions nor violate requirements of applicable codes.

B. EQUIPMENT

1. Standard products, meeting code requirements.

2. Provide required facilities, including piping, wiring and controls.

3. Portable Heaters:

   a. Indirect hot air units, located outside with duct entering into the building. Provide a sufficient number of units to meet the temperature and ventilation requirements specified above.

   b. Provide Safety Controls against explosion, overheating, and carbon monoxide build up.

   c. Provide adequate combustion air.

   d. Provide Temperature Controls installed in the building at a location(s) designated by the Construction Manager.

   e. Provide temporary barricades around the equipment to protect against damage from other construction equipment.

   f. Provide supplementary fans / distribution equipment capable of distributing heated air evenly throughout the space(s).

4. Oil-Fired heaters will not be allowed.

3. EXECUTION

A. GENERAL

1. Comply with applicable sections of Division 26 - Mechanical.

2. Install work in neat and orderly manner.

3. Make structurally, mechanically, and electrically sound throughout.

4. Maintain to give safe, continuous service at required times and to provide safe working conditions.

5. Modify and extend system as work progress requires.

B. INSTALLATION

1. Locate units to provide equitable distribution of heat and air movements.

2. Locate to avoid interference with, or hazards to:

a. Work or movement of personnel.

b. Traffic areas.

c. Materials handling.

d. Storage areas.

e. Work of other Contractors.

f. Finishes.

C. OPERATION OF PERMANENT EQUIPMENT

1. The Construction Manager will coordinate with the HVAC Contractor.

2. The Contractor will place permanent HVAC system in operation only upon written authorization by the Construction Manager.

3. Before operating the permanent HVAC equipment, the Contractor shall confirm to the Construction Manager that:

a. Inspection has been made by proper authorities.

b. Systems, equipment piping, strainers, filters and associated operating items are sufficiently complete, cleaned, and ready for operation.

c. Controls and safety devices are complete and tested, or adequate temporary controls are provided.

d. Before operating the permanent HVAC equipment, the Contractor shall install temporary filters:

(1) For air handling units.

(2) For permanent ducts.

D. REMOVAL

1. The Contractor shall completely remove temporary materials and equipment when no longer required, or on completion of construction.

2. The Contractor shall clean and repair damage caused by temporary installation and restore equipment to specified or original condition.

3. The Contractor shall remove temporary filters and install new filters, or clean permanent filters, in the permanent HVAC system prior to final acceptance by the Owner.

END OF SECTION

SECTION 015200 - CONSTRUCTION FACILITIES & TEMPORARY CONTROLS

1. GENERAL

A. DESCRIPTION

1. Construction Manager and Contractors shall provide all temporary facilities throughout the construction period unless otherwise indicated in the Contract Documents.

2. Construction Manager and Contractors shall pay all costs for providing, maintaining and removing of all temporary facilities unless otherwise indicated in the Contract Documents.

B. RELATED WORK SPECIFIED ELSEWHERE

1. Temporary Electric: Section 015113.

2. FACILITIES

A. TEMPORARY SANITATION FACILITIES

1. Construction Manager will provide and maintain sanitary facilities for all personnel on the project.

2. The number of sanitary facilities required shall be based on the total number or workers employed on the site and shall be in accordance with the provisions of the applicable code.

3. Construction Manager will maintain sanitary facilities in a sanitary and clean condition at all times.

B. TEMPORARY WATER

1. Drinking Water: Contractor shall provide potable water for drinking purposes for all his personnel on the site. He shall furnish disposable drinking cups at water stations. Each water station shall be equipped with a suitable trash container for disposal of the drinking cups.

2. Construction Water: Construction Manager will provide and maintain tap locations for construction water of sufficiently pure and potable quality to avoid deleterious effect on any materials used. Location of construction water tap locations will be determined by the Construction Manager depending on the stage of construction of the incoming water service. Contractor shall provide and maintain all hoses, piping and valves as required for obtaining construction water from taps provided by the Construction Manager.

C. TEMPORARY TELEPHONES

1. Construction Manager will not provide any telephones or fax machines for Contractor's

personnel. Each Contractor is responsible for its own phones and fax machines.

D. FIELD OFFICE

1. During the period of the Work and until final acceptance of the project, the Construction Manager will provide a weatherproof building for the Construction Manager's Field Project Manager(s) and Superintendent(s). Contractor shall make provisions for its own field office, subject to approval by the Construction Manager.

E. FIRE PROTECTION

1. Bid Package B Contractor(s) to provide temporary fire protection as required for their work.

3. Fire extinguishers shall be 10lb, Multi-Purpose (ABC) dry chemical, UL labeled, with a rating of 3a:40bc.

F. ACCESS ROADS AND PARKING AREAS

1. The Construction Manager will provide and maintain access roads on the site.

2. Neither the Construction Manager nor the Owner will provide parking for Contractor's personnel on or about the project site. All parking provisions required for Contractors will be solely the responsibility of the Contractors or their personnel.

G. STORAGE AREAS

1. The Construction Manager will assign storage areas on the site. Storage areas are extremely limited and will be assigned in a manner which will best facilitate the work.

2. Contractor shall provide all other storage space required for its work at off-site locations.

3. All combustible or flammable materials must be safely stored in a secured area in strict accordance with regulations, codes and laws enforced by local, State or Federal agencies, whichsoever is the most stringent.

H. FIRST AID STATION

1. The Contractor's Superintendent or Safety Supervisor shall insure that adequate first aid supplies are available, and that personnel are qualified to administer first aid/CPR, as required by State and/or Federal regulations.

I. SECURITY

1. The Construction Manager will provide the following security measures at the site: security

lighting will be provided. (Existing facility lighting only)

2. All other safety and security measures shall be the responsibility of each Contractor. These measures shall include but are not limited to the provision of secured storage for tools, construction equipment, and materials and equipment scheduled for installation in the building.

J. BENCH MARKS AND BASELINE

1. The Construction Manager will lay out and establish and maintain bench marks and baselines.

2. The Contractor shall lay out his own work and shall be responsible for the accuracy of same.

3. Contractor shall check grades, lines, levels and dimensions as shown on the drawings and shall promptly report errors or inconsistencies in same to the Construction Manager before Work proceeds.

4. The Contractor is responsible for damaging or altering the bench marks and baselines established by the Construction Manager and shall bear the costs of replacing same.

K. FIELD OFFICE AND STORAGE TRAILERS

1. Contractor shall provide and maintain its own field office and storage trailers as required.

2. Contractor shall provide temporary heat and power for its field office and storage trailer.

3. Contractor's field offices and storage trailers shall be located as directed by the Construction Manager.

L. PROJECT SIGN – NOT APPLICABLE

1. The Construction Manager will provide a Project Sign naming the major participants, as determined by the Owner.

M. TRASH DISPOSAL

1. Each Contractor shall be responsible for daily clean up and depositing its common trash in the dumpsters provided by the Construction Manager.

2. The Construction Manager will not provide a trash chute.

3. The Construction Manager will provide dumpsters, and will arrange for disposal of common, non-hazardous, work-related trash deposited in these dumpsters.

N. HOISTING

1. Contractor shall provide its own materials hoists and cranes. No personnel hoist will be provided.

O. SCAFFOLDING AND WORKING PLATFORMS

1. No scaffolding shall be provided by the Construction Manager. Each Contractor shall provide all scaffolding required to perform its Work.

P. SAFETY BARRICADES AND RAILINGS

1. The Structural Contractor shall provide barricades **and protective barriers** around elevator, stair, shaft and cut openings in floors and roofs, and edges of floors and roofs. The methods and materials used in barricading shall be in accordance with OSHA and local code regulations. Barricades and protective barriers will be installed immediately after the installation of the floor slab on any level or part of a level on the Building. Until a level has been fully barricaded, the Structural Contractor will be responsible for maintenance of the barricades. When a warning barricade is used to prohibit employees from entering a restricted work area. The "warning barricade" shall meet the requirements of CFR 1926.502 (f)(2). The supported rope, wire, or chain shall be flagged at not more than 6-foot (1.8 m) intervals with high-visibility material and maintain between 34 and 39 inches above the walking/working surface; Warning signs and tags shall be used in accordance with Subpart G of CFR OSHA Construction Industry Regulations.

2. After the barricades and protective barriers are no longer needed, the Structural Contractor will remove the barricades from the site. The Construction Manager will determine the location and scheduling of barriers to be removed.

3. Contractor shall provide for its own barricades at all other trenches, excavations, and locations not specifically identified in Paragraph 1 above.

4. Contractors who remove barricades shall be responsible for replacing them. If, after proper notification, in writing, from the Construction Manager the responsible Contractor does not correct his deficiencies in safety barricade placement, the Construction Manager reserves the right to undertake this work and backcharge the responsible Contractor(s).

5. During the execution of his work, Contractor will provide daily maintenance of, and upon completion of same, restore all barricades in a manner acceptable to prevailing safety standards enforced by local, State or Federal ordinance, whichsoever is most stringent. The intent is to leave no floor penetration or perimeter opening in an unsafe condition.

6. The Construction Manager shall arrange for temporary ladders required for access to each of the floor levels after the completion of floor slab work, and until the final stairs are ready for use.

Q. PUMPING AND DRAINAGE

1. Contractor shall provide its own pumping and drainage.

2. When an area is released by one Contractor to another, the Contractor releasing an area shall be responsible for leaving it in a drained condition. The incoming Contractor shall assume responsibility for drainage on the day that he is scheduled to start work in the area. If the incoming Contractor is late in starting work, he shall assume responsibility for pumping and drainage arising as a result.

R. TEMPORARY BUILDING ENCLOSURES – NOT APPLICABLE

1. The Construction Manager will equip all temporary exterior doors of the building with self-closing hardware and padlocks.

2. All other temporary enclosures and protection shall be provided by the Contractor requiring the protection.

3. Temporary enclosures required due to late delivery of materials or untimely installation of work shall be the responsibility of the Contractor responsible for the delay.

S. TEMPORARY POWER AND LIGHTING – All power to be provided by Bid Package B Contractor. Refer to Section 015113 - TEMPORARY ELECTRIC.

1. Contractor shall provide all extension cords and outlets as required for obtaining electric power from power centers provided by the Electrical Contractor. Refer to Section 015113 - TEMPORARY ELECTRIC.

2. Contractor shall provide its own additional temporary lighting of sufficient lighting levels to properly install his work.

T. TEMPORARY HEAT– NOT APPLICABLE

1. Contractor shall provide temporary heat as required for its operations. Once a building has reached the "Permanent Enclosure" stage, temporary heat will be provided as specified in Section 015123 - TEMPORARY HEAT AND VENTILATION.

2. Equipment and methods of temporary heating shall be reported to the Construction Manager.

U. PROTECTION OF ADJACENT MATERIALS

1. Contractor shall protect adjacent materials and finishes from damage as a result of its work.

V. CLEAN UP

1. Contractor shall arrange for clean up and removal of debris resulting from its operations, and shall dispose of debris in accordance with the provisions of Paragraph 2.13 above. Clean up shall be on a continual basis to ensure that building, grounds and public properties are

maintained free from accumulations of waste materials and trash.

2. The Contractor will limit use of and ensure that all materials, including waste, that are combustible or flammable will be removed from the building continually, as work progresses, **and at a minimum** at the end of each work day. All trash which is potentially edible or may attract rodents or insects will be disposed of in metal containers and removed by the end of the work day.

3. At completion of its Work, each Contractor shall remove waste materials, rubbish, tools, equipment, and clean up all exposed surfaces in preparation for final cleaning.

4. If, after notification in writing from the Construction Manager, the Contractor does not correct its deficiencies in housekeeping within twenty four (24) hours, the Construction Manager reserves the right to undertake the Work and to backcharge the Contractor.

5. Final clean up and preparation of field and associated work for turnover to the Owner to be provided by Bid Package A Contractor.

X. PROTECTION OF EXISTING CONSTRUCTION

1. Contractor shall be responsible for all damage that it may cause to materials and equipment stored or installed by other Contractors.

Y. OTHER

1. Contractor shall provide any other Temporary Facilities and services that it requires and which are not specifically identified above.

3. PERMITS – (BUILDING PERMIT FROM NCCO NOT REQUIRED FOR THIS CONTRACT)

3.1 The Construction Manager will obtain the Building Permit. **ALL OTHER PERMITS ARE TO BE OBTAINED AND PAID FOR BY THE CONTRACTOR REQUIRING THEM.**

4. EXECUTION

A. GENERAL

1. Contractor shall install all temporary facilities in accordance with applicable codes.

2. Contractor shall maintain temporary facilities for which it is responsible throughout the construction period.

3. Contractor shall remove all temporary facilities for which it is responsible when they are no longer required or when the Construction Manager directs the removal of same.

4. Contractor shall repair all damage to the Project Site caused by the installation of its temporary facilities.

END OF SECTION

SECTION 016200 - MATERIAL AND EQUIPMENT

1. GENERAL CONDITIONS

   A. The general provisions of the Contract, including the Conditions of the Contract (General, Supplementary and other Conditions, if any) and Division 1 as appropriate apply to the Work specified in this Section.

   B. Where work is to be executed under Separate Prime Contracts, the provisions of this Section apply to each Contract.

2. REQUIREMENTS INCLUDED

   A. All materials and equipment incorporated into the Work shall:

      1. be new;

      2. conform to applicable specifications and standards; and

      3 comply with size, make, type and quality specified, or as specifically approved in writing by the Architect.

   B. Manufactured and Fabricated Products shall conform to the following requirements:

      1. Designed, fabricated and assembled in accord with the best engineering and shop practices.

      2 Manufactured like parts of duplicate units to standard sizes and gauges, to be interchangeable.

      3. Two or more items of the same kind shall be identical, by the same manufacturer.

      4 Products shall be suitable for service conditions.

      5. Equipment capacities, sizes and dimensions shown or specified shall be adhered to unless variations are specifically approved in writing.

   C. Contractor shall not use materials or equipment for any purpose other than that for which it is designated or is specified.

   D. Materials removed from existing structures shall not be reused in the completed work unless specifically indicated or specified.

   E. For materials and equipment specifically indicated or specified to be reused in the Work:

      1. Contractor shall use special care on removal, handling storage and reinstallation, to assure proper function in the completed Work.

2. Arrange for transportation, storage and handling of products which require off-site storage, restoration or renovation. Pay all costs for such work.

3. MANUFACTURER'S INSTRUCTIONS

A. When Contract Documents require that installation of work shall comply with manufacturer's printed instructions, Contractor shall obtain and distribute copies of such instructions to parties involved in the installation, including two copies to Construction Manager.

1. Maintain one set of complete instructions at the job site during installation and until completion.

B. Contractor shall handle, install, connect, clean, condition and adjust products in strict accord with such instructions and in conformity with specified requirements.

1. Should job conditions or specified requirements conflict with manufacturer's instructions, Contractor shall consult with Construction Manager for further instructions.

2. Contractor shall perform work in accord with manufacturer's instructions. Contractor shall not omit any preparatory step or installation procedure unless specifically modified or exempted by Contract Documents.

4. TRANSPORTATION AND HANDLING

A. Contractor shall arrange deliveries of Products in accord with construction schedules, coordinate to avoid conflict with work and conditions at the site.

1. Deliver Products in undamaged condition, in manufacturer's original containers or packaging, with identifying labels intact and legible.

2. Contractor shall immediately on delivery, inspect shipments to assure compliance with requirements of Contract Documents and approved submittals, and that Products are properly protected and undamaged.

B. Contractor shall provide equipment and personnel to handle Products by methods to prevent soiling or damage to Products or packaging.

5. STORAGE AND PROTECTION

A. Contractor shall store Products in accord with manufacturer's instructions, with seals and labels intact and legible.

1. Contractor shall store Products subject to damage by the elements in weathertight enclosures.

2. Contractor shall maintain temperature and humidity within the ranges required by

manufacturer's instructions.

B. Exterior Storage

1. Contractor shall store fabricated Products above the ground, on blocking or skids, to prevent soiling or staining. Cover Products which are subject to deterioration with impervious sheet coverings; provide adequate ventilation to avoid condensation.

2. Contractor shall store loose granular materials in a well-drained area on soiled surfaces to prevent mixing with foreign matter.

C. Contractor shall arrange storage in a manner to provide easy access for inspection. Contractor shall make periodic inspections of stored Products to assure that Products are maintained under specified conditions, and free from damage or deterioration.

D. Contractor shall store flammable materials so as to prevent contact with flames and fire. Conform with manufacturer's recommendations and local laws. Pay particular attention to storage of:

1. Roof insulation.

2. Roofing materials, including solvents.

3. Paint materials.

4. Cleaning and other solvents.

5. Fuels.

E. Protection after Installation:

1. Contractor shall provide substantial coverings as necessary to protect installed Products from damage from traffic and subsequent construction operations. Remove when no longer needed.

6. SUBSTITUTIONS AND PRODUCT OPTIONS

A. Product List.

1. Within 30 days after Contract Date, Contractor shall submit to Construction Manager a complete list of major products proposed to be used, with the name of the manufacturer and the installing Contractor.

B. Contractor's Options.

1. For Products specified only by reference standard, Contractor shall select any Product

meeting that standard.

2. For Products specified by naming several Products or manufacturers, Contractor shall select any one of the Products or manufacturers named which complies with the specifications.

3. For Products specified by naming one or more Products or manufacturers and "or equal", Bidders must, during the bidding period, submit a request for substitutions for any Product or manufacturer not specifically named. See provisions in Paragraph 6.C, below.

4. For Products specified by naming only one Product and manufacturer, there is no option; and Contractor shall provide the precise Product specified.

C. Substitutions.

1. The materials, products and equipment described in the Bidding Documents establish a standard of quality, required function, dimension, and appearance to be met by any proposed substitution. The specification of a particular manufacturer or model number is not intended to be proprietary in any way. Substitutions of products for those named will be considered, providing that the Vendor certified that the function, quality, and performance characteristics of the material offered is equal or superior to that specified. It shall be the Bidder's responsibility to assure that the propose4d substitution will not affect the intent of the design, and to make any installation modifications required to accommodate the substitution.

2. Requests for substitutions shall be made in writing to the Architect at least ten days prior to the date of the Bid Opening. Such requests shall include a complete description of the proposed substitution, drawings, performance and test data, explanation of required installation modifications due the substitution, and any other information necessary for an evaluation. The burden of proof of the merit of the proposed substitution is upon the proposer. The Architect's decision of approval or disapproval shall be final. The Architect is to notify Owner prior to any approvals.

3. Until a date no later than seven (7) days before the date Bids are due, Architect will consider written requests from bidders for substitution of Products. **The contractor will submit any substitution requests to the Construction Manager for transmittal to the Architect. The** architect will review requests and will notify Bidders in an Addendum if the requested substitution is acceptable.

4. Should the Bidder desire a substitution, it shall submit a separate request for each Product, supported with complete data, with drawings and samples as appropriate, including:

   a. Comparison of the qualities of the proposed substitution with that specified.

   b. Changes required in other elements of the Work because of the substitution.

   c. Effect on the construction schedule.

d. Cost data comparing the proposed substitution with the Product specified.

e. Any required license fees or royalties.

f. Availability of maintenance service, and source of replacement materials.

5. Architect, in its sole discretion, shall be the judge of the acceptability of the proposed substitution.

6. A request for a substitution constitutes a representation that Bidder:

a. has investigated the proposed Product and determined that it is equal to or superior in all respects to that specified;

b. will provide the same warranties or bonds for the substitution as for the Product specified;

c. will coordinate the installation of an accepted substitution into the Work, and make such other changes as may be required to make the Work complete in all respects; and

d. waives all claims for additional costs, under his responsibility, which may subsequently become apparent.

D. Architect will review requests for substitutions with reasonable promptness, and notify Bidders, in writing, through the Construction Manager, of the decision to accept or reject the requested substitution. Any decision to accept a substitution must be confirmed in an Addendum issued during the bidding period in order to be valid. Oral approvals will not be binding.

E. The Architect shall have no obligation to consider any substitutions after the Contract award.

END OF SECTION

SECTION 017123 - FIELD ENGINEERING

1. GENERAL PROVISIONS

   A. The general provisions of the Contract, including the Conditions of the Contract, (General, Supplementary and other Conditions, if any) and Division 1 as appropriate, apply to the Work specified in this Section.

   B. The provisions of the section apply to all contracts.

2. SURVEY

   A. The Owner has had a site survey prepared by Landmark Science & Engineering This information has been included in this Bid Package.

3. CONSTRUCTION MANAGER

   A. The Construction Manager will establish a bench mark and base line from which structures and grades shall be laid out by Contractors as designated in this section. The total extent of this layout is shown on the site drawings. One bench elevation shall be provided.

END OF SECTION

SECTION 017329 - CUTTING AND PATCHING

1. GENERAL

A. Definition: "Cutting and Patching" includes cutting into existing construction to provide for the installation or performance of other work and subsequent fitting and patching required to restore surfaces to their original condition.

B. Refer to Other Sections of these specifications for specific cutting and patching requirements and limitations applicable to individual units of work.

C. Structural Work: Do not cut and patch structural work in a manner resulting in a reduction of load carrying capacity or load deflection ratio. Submit proposal and request and obtain Architect's/Engineer's approval before proceeding with cut and patch of structural work.

D. Operational/Safety Limitations: Do not cut and patch operational elements and safety components in a manner resulting in decreased performance, shortened useful life, or increased maintenance. Submit proposals and requests and obtain Architect's/Engineer's approval before proceeding with cut and patches of structural work.

E. Visual/Quality Limitations: Do not cut and patch work exposed to view (exterior and interior) in manner resulting in noticeable reduction of aesthetic qualities and similar qualities, as judged by Architect/Engineer.

1. Engage the original Installer/Fabricator, or (if not available) an acceptable equivalent entity, to cut and patch the following categories of exposed work but not limited to

2. Exterior wall materials, ie., curtain wall

3. Finish floor materials, ie., substrate, carpet, ceramic tile

4. Walls

5. Ceilings

F. Limitation on Approvals: Architect's/Engineer's approval to proceed with cutting and patching does not waive right to later acquire removal/replacement of work found to be cut and patched in an unsatisfactory manner, as judged by Architect/Engineer.

2. MATERIALS

A. General: Use materials for cutting and patching that are identical to existing materials. If identical materials are not available, or cannot be used, use materials that match existing adjacent surfaces to the fullest extent possible with regard to visual effect. Use materials for cutting and patching that will result in equal or better performance characteristics.

3. EXECUTION

A. Inspection: Before cutting, examine surfaces to be cut and patched and conditions under which the work is to be performed. If unsafe or otherwise unsatisfactory conditions are encountered, take corrective action before proceeding with the work.

B. Temporary Support: To prevent failure provide temporary support of work to be cut.

C. Protection: Protect other work during cutting and patching to prevent damage. Provide protection from adverse weather conditions for that part of the project that may be exposed during cutting and patching operations.

1. Avoid interference with use of adjoining areas or interruption of free passage to adjoining areas.

2. Take precautions not to cut existing pipe, conduit or duct serving the building but scheduled to be relocated until provisions have been made to bypass them.

D. Cutting: Cut the work using methods that are least likely to damage work to be retained or adjoining work. Where possible review proposed procedures with the original installer; comply with original installer's recommendations.

1. Where cutting is required use hand or small power tools designed for sawing or grinding, not hammering and chopping. Cut through concrete and masonry using a cutting machine such as a carborundum saw or core drill. Cut holes and slots neatly to size required with minimum disturbance of adjacent work. To avoid marring existing finished surfaces, cut and drill from the exposed or finished side into concealed surfaces. Temporarily cover openings when not in use.

E. Patching: Patch with seams which are durable and as invisible as possible. Comply with specified tolerances for the work.

1. Restore exposed finishes of patched areas and where necessary extend finish restoration into retained adjoining work in a manner which will eliminate evidence of patching and finishing.

END OF SECTION

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

SECTION 01 74 19

CONSTRUCTION WASTE MANAGEMENT

PART 1 – GENERAL

1.1 SUMMARY

A. Section includes: Administrative and procedural requirements for construction waste management activities.

1.2 DEFINITIONS

A. Construction, Demolition, and Land clearing (CDL) Waste: Includes all non-hazardous solid wastes resulting from construction, remodeling, alterations, repair, demolition and land clearing. Includes material that is recycled, reused, salvaged or disposed as garbage.

B. Salvage: Recovery of materials for on-site reuse, sale or donation to a third party.

C. Reuse: Making use of a material without altering its form. Materials can be reused on-site or reused on other projects off-site. Examples include, but are not limited to the following: Crushing or grinding of concrete for use as sub-base material. Chipping of land clearing debris for use as mulch.

D. Recycling: The process of sorting, cleaning, treating, and reconstituting materials for the purpose of using the material in the manufacture of a new product.

E. Source-Separated CDL Recycling: The process of separating recyclable materials in separate containers as they are generated on the job-site. The separated materials are hauled directly to a recycling facility or transfer station.

F. Co-mingled CDL Recycling: The process of collecting mixed recyclable materials in one container on-site. The container is taken to a material recovery facility where materials are separated for recycling.

G. Approved Recycling Facility: Any of the following:

1. A facility that can legally accept CDL waste materials for the purpose of processing the materials into an altered form for the manufacture of a new product.

2. Material Recovery Facility: A general term used to describe a waste-sorting facility. Mechanical, hand-separation, or a combination of both procedures, are used to recover recyclable materials.

H. Universal waste components (UWC) are as follows: electric motors, PCB ballasts, non PCB ballasts, capacitors, contactors, circuit breakers, elemental and liquid mercury containing articles, transformers, lead acid batteries, fluorescent light bulbs, and all HID light bulbs.

1.3 SUBMITTALS

A. Contractor shall develop a Waste Management Plan: Submit 3 copies of plan within 14 days of date established for the **Notice to Proceed**.

B. Contractor shall provide Waste Management Report: Concurrent with each Application for Payment, submit **3** copies of report.

1.4 PERFORMANCE REQUIREMENTS

A. General: Divert a minimum of **75%** CDL waste, by weight, from the landfill by one, or a combination of the following activities:

1. Salvage
2. Reuse
3. Source-Separated CDL Recycling
4. Co-mingled CDL Recycling

B. CDL waste materials that can be salvaged, reused or recycled include, but are not limited to, the following:

1. Acoustical ceiling tiles
2. Asphalt
3. Asphalt shingles
4. Cardboard packaging
5. Carpet and carpet pad
6. Concrete
7. Drywall
8. Fluorescent lights and ballasts
9. Land clearing debris (vegetation, stumpage, dirt)
10. Metals
11. Paint (through hazardous waste outlets)
12. Wood
13. Plastic film (sheeting, shrink wrap, packaging)
14. Window glass
15. Wood
16. Field office waste, including office paper, aluminum cans, glass, plastic, and office cardboard.

1.5 QUALITY ASSURANCE

A. Waste Management Coordinator Qualifications: Experienced firm, with a record of successful waste management coordination of projects with similar requirements, that employs a LEED Accredited Professional, certified by the USGBC as waste management coordinator.

B. Refrigerant Recovery Technician Qualifications: Certified by EPA-approved certification program.

C. Regulatory Requirements: Conduct construction waste management activities in accordance with hauling and disposal regulations of all authorities having jurisdiction and all other applicable laws and ordinances.

D. Preconstruction Conference: Schedule and conduct meeting at Project site prior to construction activities.

1. Attendees: Inform the following individuals, whose presence is required, of date and time of meeting.

    a. Owner
    b. Architect
    c. Contractor's superintendent
    d. Major subcontractors
    e. Waste Management Coordinator
    f. Other concerned parties.

2. Agenda Items: Review methods and procedures related to waste management including, but not limited to, the following:

    a. Review and discuss waste management plan including responsibilities of Waste Management Coordinator.
    b. Review requirements for documenting quantities of each type of waste and its disposition.
    c. Review and finalize procedures for materials separation and verify availability of containers and bins needed to avoid delays.
    d. Review procedures for periodic waste collection and transportation to recycling and disposal facilities.
    e. Review waste management requirements for each trade.

3. Minutes: Record discussion. Distribute meeting minutes to all participants.
   Note: If there is a Project Architect, they will perform this role.

1.6 WASTE MANAGEMENT PLAN – Contactor shall develop and document the following:

A. Develop a plan to meet the requirements listed in this section at a minimum. Plan shall consist of waste identification, waste reduction plan and cost/revenue analysis. Distinguish between demolition and construction waste. Indicate quantities by weight throughout the plan.

B. Indicate anticipated types and quantities of demolition, site-cleaning and construction waste generated by the project. List all assumptions made for the quantities estimates.

C. List each type of waste and whether it will be salvaged, recycled, or disposed of in an landfill. The plan should included the following information:

1. Types and estimated quantities, by weight, of CDL waste expected to be generated during demolition and construction.

2. Proposed methods for CDL waste salvage, reuse, recycling and disposal during demolition including, but not limited to, one or more of the following:

    a. Contracting with a deconstruction specialist to salvage materials generated,
    b. Selective salvage as part of demolition contractor’s work,
    c. Reuse of materials on-site or sale or donation to a third party.

3. Proposed methods for salvage, reuse, recycling and disposal during construction including, but not limited to, one or more of the following:

    a. Requiring subcontractors to take their CDL waste to a recycling facility;

b. Contracting with a recycling hauler to haul recyclable CDL waste to an approved recycling or material recovery facility;
c. Processing and reusing materials on-site;
d. Self-hauling to a recycling or material recovery facility.

4. Name of recycling or material recovery facility receiving the CDL wastes.

5. Handling and Transportation Procedures: Include method that will be used for separating recyclable waste including sizes of containers, container labeling, and designated location on project site where materials separation will be located.

D. Cost/Revenue Analysis: Indicate total cost of waste disposal as if there was no waste management plan and net additional cost or net savings resulting from implementing waste management plan. Include the following:

1. Total quantity of waste.
2. Estimated cost of disposal (cost per unit). Include hauling and tipping fees and cost of collection containers for each type of waste.
3. Total cost of disposal (with no waste management).
4. Revenue from salvaged materials.
5. Revenue from recycled materials.
6. Savings in hauling and tipping fees by donating materials.
7. Savings in hauling and tipping fees that are avoided.
8. Handling and transportation costs. Including cost of collection containers for each type of waste.
9. Net additional cost or net savings from waste management plan.

PART 2 - PRODUCTS (Not Used)

PART 3 – EXECUTION

3.1 CONSTRUCTION WASTE MANAGEMENT, GENERAL

A. Provide containers for CDL waste that is to be recycled clearly labeled as such with a list of acceptable and unacceptable materials. The list of acceptable materials must be the same as the materials recycled at the receiving material recovery facility or recycling processor.

B. The collection containers for recyclable CDL waste must contain no more than 10% non-recyclable material, by volume.

C. Provide containers for CDL waste that is disposed in a landfill clearly labeled as such.

D. Use detailed material estimates to reduce risk of unplanned and potentially wasteful cuts.

E. To the greatest extent possible, include in material purchasing agreements a waste reduction provision requesting that materials and equipment be delivered in packaging made of recyclable material, that they reduce the amount of packaging, that packaging be taken back for reuse or recycling, and to take back all unused product. Insure that subcontractors require the same provisions in their purchase agreements.

F. Conduct regular visual inspections of dumpsters and recycling bins to remove contaminants.

3.2 SOURCE SEPARATION

A. General: Contractor shall separate recyclable materials from CDL waste to the maximum extent possible.

Separate recyclable materials by type.

1. Provide containers, clearly labeled, by type of separated materials or provide other storage method for managing recyclable materials until they are removed from Project site.
2. Stockpile processed materials on-site without intermixing with other materials. Place, grade, and shape stockpiles to drain surface water and to minimize pest attraction. Cover to prevent windblown dust.
3. Stockpile materials away from demolition area. Do not store within drip line of remaining trees.
4. Store components off the ground and protect from weather.

3.3 CO-MINGLED RECYCLING

A. General: Do not put CDL waste that will be disposed in a landfill into a co-mingled CDL waste recycling container.

3.4 REMOVAL OF CONSTRUCTION WASTE MATERIALS

A. Remove CDL waste materials from project site on a regular basis. Do not allow CDL waste to accumulate on-site.

B. Transport CDL waste materials off Owner's property and legally dispose of them.

C. Burning of CDL waste is not permitted.

3.5 UNIVERSAL WASTE DIVERSION

A. Remove all universal waste from fixtures, panels, and related devices for proper diversion and reclamation.

B. Store all universal waste in containers provided by contact person within facilities operations.

C. Store all universal waste in a secured location and request periodic removal from assigned contact person.

D. Exemption: electric motors, circuit breakers, transformers and lighting contactors are exempt from this provision provided the contractor chooses to salvage or reuse the components.

E. No identified universal waste will be discarded into the waste stream.
F.

END OF SECTION

STATE OF DELAWARE DIVISION OF FACILITIES MANAGEMENT

WASTE MANAGEMENT PROGRESS REPORT

MATERIAL CATEGORY	DISPOSED IN MUNICIPAL SOLID WASTE LANDFILL	DIVERTED FROM LANDFILL BY RECYCLING, SALVAGE OR REUSE		
		Recycled	Salvaged	Reused
1. Acoustical Ceiling Tiles				
2. Asphalt				
3. Asphalt Shingles				
4. Cardboard Packaging				
5. Carpet and Carpet Pad				
6. Concrete				
7. Drywall				
8. Fluorescent Lights and Ballasts				
9. Land Clearing Debris (vegetation, stumpage, dirt)				
10. Metals				
11. Paint (through hazardous waste outlets)				
12. Wood				
13. Plastic Film (sheeting, shrink wrap, packaging)				
14. Window Glass				
15. Field Office Waste (office paper, aluminum cans, glass, plastic, and coffee cardboard)				
16. Other (insert description)				
17. Other (insert description)				
Total (In Weight)		(TOTAL OF ALL ABOVE VALUES – IN WEIGHT)		
		Percentage of Waste Diverted	(TOTAL WASTE DIVIDED BY TOTAL DIVERTED)	

SECTION 017700 – CONTRACT CLOSEOUT

1. DESCRIPTION OF REQUIREMENTS

   A. Provisions of this section apply to the procedural requirements for the actual close out of the Work, not to the administrative matters such as final payment or the change over of insurance. Close out requirements relate to both substantial and final completion of the Work; they also apply to individual portions of completed work as well as the Total work. Specific requirements contained in other sections have precedence over the general requirements contained in this section.

2. PROCEDURES AT SUBSTANTIAL COMPLETION

   A. Prerequisites: Contractor shall comply with the General Conditions and complete the following before requesting inspection of the Work, or a designated portion of the Work, for certification of substantial completion:

      1. submit executed warranties, workmanship bonds, maintenance agreements, inspection certificates, releases of liens, tax certification and similar required documentation for specific units of work, and documents needed to enable Owner's unrestricted occupancy and use;

      2. submit record documentation, maintenance manuals, tools, spare parts, keys and similar operational items;

      3. complete instructions of Owner's operating personnel, and start up of systems; and

      4. complete final cleaning and remove temporary facilities and tools.

   B. Inspection Procedures: Upon receipt of Contractor's request, Architect/Engineer will either proceed with inspection or advise Construction Manger of prerequisites not fulfilled. Following initial inspection, Architect/Engineer will either prepare certificate of substantial completion, or advise Construction Manager of work which must be performed prior to issuance of certificate. The Architect/Engineer will repeat the inspection when requested and assure that the work has been substantially completed. Results of the completed inspection will form the initial "punch list" for final acceptance.

   C. Punch List Procedures: Each Contractor shall be given a copy of the punch list with its appropriate work identified. Each Contractor shall be given 9 (nine) calendar work days to complete their punch list work. On the 10th day or as determined by the Construction Manager the Construction Manager shall employ other Contractors, as required, to complete any incomplete punch list work and retain from the appropriate Contractors retainage all costs incurred.

3. PROCEDURES AT FINAL ACCEPTANCE

   A. Reinspection Procedure: The Architect/Engineer will reinspect the Work upon receipt of the

Contractor's notice that, except for those items whose completion has been delayed due to circumstances that are acceptable to the Architect/Engineer, the Work has been completed, including punch list items from earlier inspections. Upon completion of reinspection, the Architect/Engineer will either recommend final acceptance and final payment, or will advise the Contractor of work not completed or obligations not fulfilled as required for final acceptance. If necessary, this procedure will be repeated.

4. RECORD DOCUMENTATION

A. Record Drawings: Contractor shall maintain a complete set of either blue or black line prints of the contract documents and shop drawings for record mark-up purposes throughout the Contract Time. Contractor shall mark up these drawings during the course of the Work to show both changes and the actual installation, in sufficient detail to form a complete record for Owner's purposes giving particular attention to work that will be concealed and difficult to measure and record at a later date, and Work which may require servicing or replacement during the life of the project. Require the entities marking prints to sign and date each mark up. Bind prints into manageable sets, with durable paper cover, appropriately labeled.

B. Installation, Operation and Maintenance Manual: Contractor shall provide 3-ring vinyl covered binders containing required maintenance manuals, properly identified and indexed and including operating and maintenance instructions extended to cover emergencies, spare parts, warranties, inspection procedures, diagrams, safety, security, and similar appropriate data for each system of equipment item.

C. State Tax Certification: Contractor shall provide recent Delaware State Tax Certification form as issued by State of Delaware, Department of Finance, Division of Revenue, Carvel State Office Building, 820 N. French Street, Wilmington, Delaware 19801. To obtain this certificate, the contractor will be required to provide the Division of Revenue the completed State Form 8821 DE (attached to this section) along with a processing fee of $40.

D. AIA Documents: Contractors shall provide the following AIA documents with their final payment application submission:
- AIA G732, Application for Payment for 100% Complete
- AIA G732, Final Application for Payment for Retainage
- AIA G734-CMA, Certificate of Substantial Completion – 4 originals
- AIA G706, Affidavit of Payment of Debts & Claims
- AIA G706A, Affidavit of Release of Liens
- AIA G707, Consent of Surety

E. Release of Liens: Contractors shall provide the following release of liens with their final payment application submission:
- Prime Contractor's Release of Liens
- Subcontractors' & Suppliers' Release of Liens (major subs and suppliers)

5. GENERAL CLOSE OUT REQUIREMENTS

A. Operator Instruction: Contractor shall require each Installer of systems requiring continued operation and maintenance by Owner's operating personnel, to provide on location instruction to Owner's personnel, sufficient to ensure safe, secure, efficient, non-failing utilization and operation of systems. Contractor shall provide instructions for the following categories of work:

1. Mechanical/electrical/electronic systems (not limited to work of Division 15 and 16).

2. Roofing, flashing, joint sealers.

3. Floor finishes.

4. Door hardware

6. FINAL CLEANING

A. At the time of project close out Contractor shall clean or re-clean the Work to the condition expected from a normal, commercial building cleaning and maintenance program. Complete the following cleaning operations before requesting the Architect/Engineer's inspection for certification of substantial completion:

1. Bid Package B Contractor(s) to provide all final cleaning and preparation of field and all contract work areas prior to substantial completion.

2. Remove non-permanent protections and labels.

2. Polish glass.

3. Clean exposed finishes.

4. Touch up minor finish damage.

5. Clean or replace mechanical systems filters.

6. Remove debris.

7. Broom clean unoccupied spaces.

8. Sanitize plumbing and food service facilities.

9. Clean light fixtures and replace burned out lamps.

10. Sweep and wash paved areas.

11. Police yards and grounds.

END OF SECTION

SECTION 01 79 00 - DEMONSTRATION AND TRAINING

PART 1 - GENERAL

1.1 RELATED DOCUMENTS

A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

A. Section includes administrative and procedural requirements for instructing Owner's personnel, including the following:

1. Demonstration of operation of systems, subsystems, and equipment.
2. Training in operation and maintenance of systems, subsystems, and equipment.
3. Demonstration and training video recordings.

B. Related Requirements:

1. Divisions 02 through 33 Sections for specific requirements for demonstration and training for products in those Sections.

1.3 INFORMATIONAL SUBMITTALS

A. Instruction Program: Submit outline of instructional program for demonstration and training, including a list of training modules and a schedule of proposed dates, times, length of instruction time, and instructors' names for each training module. Include learning objective and outline for each training module.

1. Indicate proposed training modules using manufacturer-produced demonstration and training video recordings for systems, equipment, and products in lieu of video recording of live instructional module.

B. Qualification Data: For instructor.

C. Attendance Record: For each training module, submit list of participants and length of instruction time.

D. Evaluations: For each participant and for each training module, submit results and documentation of performance-based test.

1.4 CLOSEOUT SUBMITTALS

A. Demonstration and Training Video Recordings: Submit two copies within seven days of end of each training module.

1. Identification: On each copy, provide an applied label with the following information:

a. Name of Project.
b. Name and address of videographer.
c. Name of Architect.
d. Name of Construction Manager.
e. Name of Contractor.
f. Date of video recording.

2. Transcript: Prepared in PDF electronic format. Include a cover sheet with same label information as the corresponding video recording and a table of contents with links to corresponding training components. Include name of Project and date of video recording on each page.
3. At completion of training, submit complete training manual(s) for Owner's use prepared and bound in format matching operation and maintenance manuals.

1.5 QUALITY ASSURANCE

A. Facilitator Qualifications: A firm or individual experienced in training or educating maintenance personnel in a training program similar in content and extent to that indicated for this Project, and whose work has resulted in training or education with a record of successful learning performance.

B. Instructor Qualifications: A factory-authorized service representative, complying with requirements in Division 01 Section "Quality Requirements," experienced in operation and maintenance procedures and training.

C. Videographer Qualifications: A professional videographer who is experienced photographing demonstration and training events similar to those required.

D. Pre-instruction Conference: Conduct conference at Project site to comply with requirements in Division 01 Section "Project Management and Coordination." Review methods and procedures related to demonstration and training including, but not limited to, the following:

1. Inspect and discuss locations and other facilities required for instruction.
2. Review and finalize instruction schedule and verify availability of educational materials, instructors' personnel, audiovisual equipment, and facilities needed to avoid delays.
3. Review required content of instruction.
4. For instruction that must occur outside, review weather and forecasted weather conditions and procedures to follow if conditions are unfavorable.

1.6 COORDINATION

A. Coordinate instruction schedule with Owner's operations. Adjust schedule as required to minimize disrupting Owner's operations and to ensure availability of Owner's personnel.

B. Coordinate instructors, including providing notification of dates, times, length of instruction time, and course content.

C. Coordinate content of training modules with content of approved emergency, operation, and maintenance manuals. Do not submit instruction program until operation and maintenance data has been reviewed and approved by Architect.

PART 2 - PRODUCTS

2.1 INSTRUCTION PROGRAM

A. Program Structure: Develop an instruction program that includes individual training modules for each system and for equipment not part of a system, as required by individual Specification Sections.

B. Training Modules: Develop a learning objective and teaching outline for each module. Include a description of specific skills and knowledge that participant is expected to master. For each module, include instruction for the following as applicable to the system, equipment, or component:

1. Basis of System Design, Operational Requirements, and Criteria: Include the following:

    a. System, subsystem, and equipment descriptions.
    b. Performance and design criteria if Contractor is delegated design responsibility.
    c. Operating standards.
    d. Regulatory requirements.
    e. Equipment function.
    f. Operating characteristics.
    g. Limiting conditions.
    h. Performance curves.

2. Documentation: Review the following items in detail:

    a. Emergency manuals.
    b. Operations manuals.
    c. Maintenance manuals.
    d. Project record documents.
    e. Identification systems.
    f. Warranties and bonds.
    g. Maintenance service agreements and similar continuing commitments.

3. Emergencies: Include the following, as applicable:

    a. Instructions on meaning of warnings, trouble indications, and error messages.
    b. Instructions on stopping.
    c. Shutdown instructions for each type of emergency.
    d. Operating instructions for conditions outside of normal operating limits.
    e. Sequences for electric or electronic systems.
    f. Special operating instructions and procedures.

4. Operations: Include the following, as applicable:

    a. Startup procedures.
    b. Equipment or system break-in procedures.
    c. Routine and normal operating instructions.
    d. Regulation and control procedures.
    e. Control sequences.
    f. Safety procedures.
    g. Instructions on stopping.
    h. Normal shutdown instructions.
    i. Operating procedures for emergencies.
    j. Operating procedures for system, subsystem, or equipment failure.
    k. Seasonal and weekend operating instructions.
    l. Required sequences for electric or electronic systems.
    m. Special operating instructions and procedures.

5. Adjustments: Include the following:

    a. Alignments.
    b. Checking adjustments.
    c. Noise and vibration adjustments.
    d. Economy and efficiency adjustments.

6. Troubleshooting: Include the following:

    a. Diagnostic instructions.
    b. Test and inspection procedures.

7. Maintenance: Include the following:

    a. Inspection procedures.
    b. Types of cleaning agents to be used and methods of cleaning.
    c. List of cleaning agents and methods of cleaning detrimental to product.
    d. Procedures for routine cleaning
    e. Procedures for preventive maintenance.
    f. Procedures for routine maintenance.
    g. Instruction on use of special tools.

8. Repairs: Include the following:

    a. Diagnosis instructions.
    b. Repair instructions.
    c. Disassembly; component removal, repair, and replacement; and reassembly instructions.
    d. Instructions for identifying parts and components.
    e. Review of spare parts needed for operation and maintenance.

PART 3 - EXECUTION

3.1 PREPARATION

A. Assemble educational materials necessary for instruction, including documentation and training module. Assemble training modules into a training manual organized in coordination with requirements in Division 01 Section "Operations and Maintenance Data."

B. Set up instructional equipment at instruction location.

3.2 INSTRUCTION

A. Facilitator: Engage a qualified facilitator to prepare instruction program and training modules, to coordinate instructors, and to coordinate between Contractor and Owner for number of participants, instruction times, and location.

B. Engage qualified instructors to instruct Owner's personnel to adjust, operate, and maintain systems, subsystems, and equipment not part of a system.

1. Architect will furnish an instructor to describe basis of system design, operational requirements, criteria, and regulatory requirements.
2. Owner will furnish an instructor to describe Owner's operational philosophy.
3. Owner will furnish Contractor with names and positions of participants.

C. Scheduling: Provide instruction at mutually agreed on times. For equipment that requires seasonal operation, provide similar instruction at start of each season.

1. Schedule training with Owner with at least seven days' advance notice.

D. Training Location and Reference Material: Conduct training on-site in the completed and fully operational facility using the actual equipment in-place. Conduct training using final operation and maintenance data submittals.

E. Evaluation: At conclusion of each training module, assess and document each participant's mastery of module by use of a demonstration performance-based test.

F. Cleanup: Collect used and leftover educational materials and give to Owner. Remove instructional equipment. Restore systems and equipment to condition existing before initial training use.

END OF DEMONSTRATION AND TRAINING

DIVISION 01 SECTION 01 91 13
GENERAL COMMISSIONING REQUIREMENTS
TABLE OF CONTENTS

PART 1. GENERAL 3
1.1. RELATED DOCUMENTS 3
1.2. SUMMARY 3
1.3. DEFINITIONS 3
1.4. COMMISSIONING TEAM 3
1.5. OWNER'S RESPONSIBILITIES 4
1.6. CONTRACTOR'S RESPONSIBILITIES 4
1.7. CxA'S RESPONSIBILITIES 6
1.8. COMMISSIONING DOCUMENTATION 7
1.9. SUBMITTALS 10
1.10. QUALITY ASSURANCE 10
1.11. COORDINATION 11
1.12. ALTERNATES 11
PART 2. PRODUCTS (NOT USED) 11
PART 3. EXECUTION 11
3.1. OPERATION AND MAINTENANCE TRAINING REQUIREMENTS 11
END OF SECTION 12

THIS PAGE LEFT INTENTIONALLY BLANK

SECTION 01 91 13
GENERAL COMMISSIONING REQUIREMENTS

PART 1. GENERAL

1.1. RELATED DOCUMENTS

A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2. SUMMARY

A. This Section includes general requirements that apply to implementation of commissioning without regard to systems, subsystems, and equipment being commissioned.

B. Related Sections include the following:

1. Division 01 Section "HVAC Commissioning Requirements" for specific requirements for commissioning HVAC systems.

2. Division 01 Section "Electrical Commissioning Requirements" for specific requirements for commissioning electrical systems.

3. Division 01 Section "Plumbing System Commissioning Requirements" for specific requirements for commissioning Plumbing systems.

4. Division 01 Section "Contract Closeout" for specific requirements for closeout at substantial and final completion.

5. Division 01 Section "Contract Closeout" for Specific Requirements for training and demonstration of systems to Owner.

6. Division 01 Section "Contract Closeout" for Specific Requirements related to the Preparation of systems operation and maintenance manuals.

1.3. DEFINITIONS

A. CxA: Commissioning Authority.

B. OPR: Owner's Project Requirements.

C. Systems, Subsystems, and Equipment: Where these terms are used together or separately, they shall mean "as-built" systems, subsystems, and equipment.

D. TAB: Testing, Adjusting, and Balancing.

1.4. COMMISSIONING TEAM

A. Members Appointed by Contractor(s): Individuals, each having authority to act on behalf of the entity he or she represents, explicitly organized to implement the commissioning process through coordinated actions. The commissioning team shall consist of, but not be

limited to, representatives of Contractor, including Project superintendent and subcontractors, installers, suppliers, and specialists deemed appropriate by the CxA.

B. Members Appointed by Owner:

1. CxA: The designated person, company, or entity that plans, schedules, and coordinates the commissioning team to implement the commissioning process. Owner will engage the CxA under a separate contract.

2. All contractor commissioning requirements and costs associated with commissioning the project shall be included in the base bid.

3. Representatives of the facility user and operation and maintenance personnel.

4. Architect and Engineering design professionals.

1.5. OWNER'S RESPONSIBILITIES

A. Assign operation and maintenance personnel and schedule them to participate in commissioning team activities including, but not limited to, the following:

1. Coordination meetings.

2. Training in operation and maintenance of systems, subsystems, and equipment.

3. Testing meetings.

4. Demonstration of operation of systems, subsystems, and equipment.

1.6. CONTRACTOR'S RESPONSIBILITIES

A. Provide utility services required for the commissioning process.

B. Contractor shall assign representatives with expertise and authority to act on behalf of the Contractor and schedule them to participate in and perform commissioning team activities including, but not limited to, the following:

1. Participate in commissioning and construction-phase coordination meetings.

2. Participate in maintenance orientation and inspection.

3. Participate in operation and maintenance training sessions.

4. Participate in final review at acceptance meeting.

5. Certify that Work is complete and systems are operational according to the Contract Documents, including calibration of instrumentation and controls.

6. Evaluate performance deficiencies identified in test reports and, in collaboration with entity responsible for system and equipment installation, recommend corrective action.

7. Review and approve final commissioning documentation.

8. Certify that all pre-test work and pre-testing of functional performance tests are complete and operational prior to scheduling performed testing by CxA. Submit completed functional performance test forms with data from pre-testing.

9. During functional performance testing, a representative from the mechanical contractor, controls contractor, and test/balance engineer must be present and participate in testing.

C. Subcontractors shall assign representatives with expertise and authority to act on behalf of subcontractors and schedule them to participate in and perform commissioning team activities including, but not limited to, the following:

1. Pre-test all systems/equipment prior to engaging CxA for Functional Performance Testing.

2. Participate in commissioning and construction-phase coordination meetings.

3. Participate in maintenance orientation and inspection.

4. Participate in procedures meeting for testing.

5. Participate in final review at acceptance meeting.

6. Provide schedule for operation and maintenance data submittals, equipment startup, and testing to CxA for incorporation into the commissioning plan. Update schedule on a weekly basis throughout the construction period.

7. Provide information to the CxA for developing construction-phase commissioning plan.

8. Participate in training sessions for Owner's operation and maintenance personnel.

9. Provide updated Project Record Documents to the CxA on a daily basis.

10. Gather and submit operation and maintenance data for systems, subsystems, and equipment to the CxA, as specified in Division 01 Section "Operation and Maintenance Data."

11. Provide technicians who are familiar with the construction and operation of installed systems and who shall develop specific test procedures and participate in testing of installed systems, subsystems, and equipment.

12. The test/balance subcontractor, mechanical contractor, and automatic temperature controls subcontractor must be on-site and provide assistance during all functional performance testing.

D. Contractors and subcontractors must pre-inspect and pre-test all equipment and systems prior to requesting functional performance testing by the CxA. All pre-start/start-up checklists and functional performance test forms must be completed and submitted to

Engineer prior to scheduling formal functional performance testing.

1.7. CXA'S RESPONSIBILITIES

A. Organize and lead the commissioning team.

B. Prepare a construction-phase commissioning plan. Collaborate with Contractor and with subcontractors to develop test and inspection procedures. Include design changes and scheduled commissioning activities coordinated with overall Project schedule. Identify commissioning team member responsibilities, by name, firm, and trade specialty, for performance of each commissioning task.

C. Convene commissioning team meetings for the purpose of coordination, communication, and conflict resolution; discuss progress of the commissioning processes. Responsibilities include arranging for facilities, preparing agenda and attendance lists, and notifying participants. The CxA shall prepare and distribute minutes to commissioning team members and attendees within five workdays of the commissioning meeting.

D. At a mutually agreed upon time, conduct an initial construction-phase coordination meeting for the purpose of reviewing the commissioning activities and establishing tentative schedules for operation and maintenance submittals; operation and maintenance training sessions; TAB Work; and Project completion.

E. Observe and inspect construction and report progress and deficiencies. In addition to compliance with the Contract Documents, inspect systems and equipment installation for adequate accessibility for maintenance and component replacement or repair.

F. Prepare Project-specific test and inspection procedures and checklists.

G. Schedule, direct, witness, and document tests, inspections, and systems startup.

H. Compile test data, inspection reports, and certificates and include them in the systems manual and commissioning report.

I. Certify date of acceptance and startup for each item of equipment for start of warranty periods.

J. Review Project Record Documents for accuracy. Request revisions from Contractor to achieve accuracy. Project Record Documents requirements are specified in Division 01 Section "Project Record Documents."

K. Review and comment on operation and maintenance documentation and systems manual outline for compliance with the Contract Documents. Operation and maintenance documentation requirements are specified in Division 01 Section "Operation and Maintenance Data."

L. Assemble the final commissioning documentation, including the commissioning report and Project Record Documents.

1.8. COMMISSIONING DOCUMENTATION

A. Commissioning Plan: A document, prepared by CxA, that outlines the schedule, allocation of resources, and documentation requirements of the commissioning process, and shall include, but is not limited to the following:

1. Plan for delivery and review of submittals, systems manuals, and other documents and reports. Identification of the relationship of these documents to other functions and a detailed description of submittals that are required to support the commissioning processes. Submittal dates shall include the latest date approved submittals must be received without adversely affecting commissioning plan.

2. Description of the organization, layout, and content of commissioning documentation (including systems manual) and a detailed description of documents to be provided along with identification of responsible parties.

3. Identification of systems and equipment to be commissioned.

4. Description of schedules for testing procedures along with identification of parties involved in performing and verifying tests.

5. Identification of items that must be completed before the next operation can proceed.

6. Description of responsibilities of commissioning team members.

7. Description of observations to be made.

8. Description of requirements for operation and maintenance training, including required training materials.

9. Description of expected performance for systems, subsystems, equipment, and controls.

10. Schedule for commissioning activities with specific dates coordinated with overall construction schedule.

11. Identification of installed systems, subsystems, and equipment, including design changes that occurred during the construction phase.

12. Process and schedule for documenting changes on a continuous basis to appear in Project Record Documents.

13. Process and schedule for completing prestart and startup checklists for systems, subsystems, and equipment to be verified and tested.

14. Step-by-step procedures for testing systems, subsystems, and equipment with descriptions for methods of verifying relevant data, recording the results obtained, and listing parties involved in performing and verifying tests.

B. Test Checklists: CxA, with assistance of Contractor and Subcontractors, shall develop test

checklists for each system, subsystem, or equipment including interfaces and interlocks, and include a separate entry, with space for comments, for each item to be tested. Prepare separate checklists for each mode of operation and provide space to indicate whether the mode under test responded as required. Provide space for testing personnel to sign off on each checklist. Specific checklist content requirements are specified in Division 01 Section "HVAC Commissioning Requirements", "Electrical Commissioning Requirements" and "Plumbing System Commissioning Requirements". Test checklists will be jointly developed as the project progresses. Each checklist, regardless of system, subsystem, or equipment being tested, shall include, but not be limited to, the following:

1. Name and identification code of tested item.

2. Test number.

3. Time and date of test.

4. Indication of whether the record is for a first test or retest following correction of a problem or issue.

5. Dated signatures of the person performing test and of the witness, if applicable.

6. Individuals present for test.

7. Deficiencies.

8. Issue number, if any, generated as the result of test.

C. Certificate of Readiness: Certificate of Readiness shall be signed by Contractor, Subcontractor(s), Installer(s), and CxA certifying that systems, subsystems, equipment, and associated controls are ready for testing. Completed test checklists signed by the responsible parties shall accompany this certificate.

D. Test and Inspection Reports: CxA shall record test data, observations, and measurements on test checklists. Photographs, forms, and other means appropriate for the application shall be included with data. CxA shall compile test and inspection reports and test and inspection certificates and include them in systems manual and commissioning report.

E. Corrective Action Documents: CxA shall document corrective action taken for systems and equipment that fail tests. Include required modifications to systems and equipment and revisions to test procedures, if any. Retest systems and equipment requiring corrective action and document retest results.

F. Issues Log: CxA shall prepare and maintain an issues log that describes design, installation, and performance issues that are at variance with the Contract Documents. Identify and track issues as they are encountered, documenting the status of unresolved and resolved issues.

1. Creating an Issues Log Entry:

a. Identify the issue with unique numeric or alphanumeric identifier by which the issue may be tracked.

b. Assign a descriptive title of the issue.
c. Identify date and time of the issue.
d. Identify test number of test being performed at the time of the observation, if applicable, for cross-reference.
e. Identify system, subsystem, and equipment to which the issue applies.
f. Identify location of system, subsystem, and equipment.
g. Include information that may be helpful in diagnosing or evaluating the issue.
h. Note recommended corrective action.
i. Identify commissioning team member responsible for corrective action.
j. Identify expected date of correction.
k. Identify person documenting the issue.

2. Documenting Issue Resolution:

a. Log date correction is completed or the issue is resolved.
b. Describe corrective action or resolution taken. Include description of diagnostic steps taken to determine root cause of the issue, if any.
c. Identify changes to the Contract Documents that may require action.
d. State that correction was completed and system, subsystem, and equipment is ready for retest, if applicable.
e. Identify person(s) who corrected or resolved the issue.
f. Identify person(s) documenting the issue resolution.

3. Issues Log Report: On a periodic basis, but not less than for each commissioning team meeting, CxA shall prepare a written narrative for review of outstanding issues and a status update of the issues log. As a minimum, CxA shall include the following information in the issues log and expand it in the narrative:

a. Issue number and title.
b. Date of the identification of the issue.
c. Name of the commissioning team member assigned responsibility for resolution.
d. Expected date of correction.

G. Commissioning Report: CxA shall document results of the commissioning process including unresolved issues and performance of systems, subsystems, and equipment. The commissioning report shall indicate whether systems, subsystems, and equipment have been completed and are performing according to the Contract Documents. The commissioning report shall include, but is not limited to, the following:

1. Lists and explanations of substitutions; compromises; variances in the Contract Documents; record of conditions; and, if appropriate, recommendations for resolution. This report shall be used to evaluate systems, subsystems, and equipment and shall serve as a future reference document during Owner occupancy and operation. It shall describe components and performance that exceed requirements of the Contract Documents and those that do not meet requirements of the Contract Documents. It may also include a recommendation for accepting or rejecting systems, subsystems, and equipment.

2. Commissioning plan.

3. Testing plans and reports.

4. Corrective modification documentation.

5. Issues log.

6. Completed test checklists.

7. Punch Lists.

8. Test/Balance Reports.

9. Listing of off-season test(s) not performed and a schedule for their completion.

10. All commissioning documents must be submitted to the building Owner within 90 days of the date of receipt of the Certificate of Occupancy.

H. Systems Manual: CxA shall gather required information and compile systems manual. Systems manual shall include, but is not limited to, the following:

1. Project Record Documents as specified in Division 01 Section "Project Record Documents."

2. Final commissioning plan.

3. Commissioning report.

4. Operation and maintenance data as specified in Division 01 Section "Operation and Maintenance Data."

1.9. SUBMITTALS

A. Test Checklists and Report Forms: CxA shall submit sample checklists and forms to Contractor quality-control manager and subcontractors for review and comment. Submit two copies of each checklist and report form.

B. Test and Inspection Reports: CxA shall submit test and inspection reports.

C. Corrective Action Documents: CxA shall submit corrective action documents.

1.10. QUALITY ASSURANCE

A. Instructor Qualifications: Factory-authorized service representatives, experienced in training, operation, and maintenance procedures for installed systems, subsystems, and equipment.

B. Test Equipment Calibration: Comply with test equipment manufacturer's calibration procedures and intervals. Recalibrate test instruments immediately whenever instruments have been repaired following damage or dropping. Affix calibration tags to test instruments. Instruments shall have been calibrated within six months prior to use.

1.11. COORDINATION

A. Coordinating Meetings: CxA shall conduct coordination meetings of the commissioning team to review progress on the commissioning plan, to discuss scheduling conflicts, and to discuss upcoming commissioning process activities.

B. Pretesting Meetings: CxA shall conduct pretest meetings of the commissioning team to review startup reports, pretest inspection results, testing procedures, testing personnel and instrumentation requirements, and manufacturers' authorized service representative services for each system, subsystem, equipment, and component to be tested.

C. Testing Coordination: CxA shall coordinate sequence of testing activities to accommodate required quality-assurance and -control services with a minimum of delay and to avoid necessity of removing and replacing construction to accommodate testing and inspecting.

1. Schedule times for tests, inspections, obtaining samples, and similar activities.

D. Manufacturers' Field Services: CxA and Contractor shall coordinate services of manufacturers' field services.

1.12. ALTERNATES

A. Refer to Division 01 Section, “Alternates” for description of work under this section affected by alternates.

PART 2. PRODUCTS (NOT USED)

PART 3. EXECUTION

3.1. OPERATION AND MAINTENANCE TRAINING REQUIREMENTS

A. Training Preparation Conference: Before operation and maintenance training, CxA shall convene a training preparation conference to include Owner's operation and maintenance personnel, Contractor, and subcontractors. In addition to requirements specified in Division 01 Section "Demonstration and Training," perform the following:

1. Review installed systems, subsystems, and equipment.

2. Review instructor qualifications.

3. Review instructional methods and procedures.

4. Review training module outlines and contents.

5. Review course materials (including operation and maintenance manuals).

6. Inspect and discuss locations and other facilities required for instruction.

7. Review and finalize training schedule and verify availability of educational materials, instructors, audiovisual equipment, and facilities needed to avoid delays.

8. For instruction that must occur outside, review weather and forecasted weather conditions and procedures to follow if conditions are unfavorable.

B. Training Modules: Develop an instruction program that includes individual training modules for each system, subsystem, and equipment as specified in Division 01 Section "Demonstration and Training."

END OF SECTION

DIVISION 01 SECTION 01 91 14
PLUMBING COMMISSIONING REQUIREMENTS
TABLE OF CONTENTS

PART 1. GENERAL 3
1.1. RELATED DOCUMENTS 3
1.2. SUMMARY 3
1.3. DEFINITIONS 4
1.4. CONTRACTOR'S RESPONSIBILITIES 4
1.5. COMMISSIONING DOCUMENTATION 6
1.6. SUBMITTALS 6
1.7. ALTERNATES 7
PART 2. PRODUCTS (NOT USED) 7
PART 3. EXECUTION 7
3.1. TESTING PREPARATION 7
3.2. TAB VERIFICATION 9
3.3. TESTING 10
END OF SECTION 12

THIS PAGE LEFT INTENTIONALLY BLANK

SECTION 01 91 14
PLUMBING COMMISSIONING REQUIREMENTS

PART 1. GENERAL

1.1. RELATED DOCUMENTS

A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2. SUMMARY

A. This Section includes requirements for commissioning the plumbing system and its subsystems and equipment. This Section supplements the general requirements specified in Division 01 Section "General Commissioning Requirements."

B. Related Sections include the following:

1. Division 01 Section "General Commissioning Requirements" for general requirements for commissioning processes that apply to this Section.

C. The following systems and/or equipment shall be commissioned:

1. Backflow preventers.
2. Compressed air solenoid/valves.
3. Compressed air systems/equipment.
4. Condensate Neutralizers.
5. Dental Compressor/Vacuum Pump.
6. Domestic booster pump system.
7. Domestic Hot Water Expansion Tanks
8. Domestic hot water heaters.
9. Domestic hot water re-circulating system.
10. Domestic water meter (including interlock to ATC system).
11. Domestic water pumps.
12. Domestic water solenoid valves.
13. Elevator sump pump and controls.
14. Emergency eyewash/shower systems, mixing valves, and equipment.

15. Gas Pressure Regulators.

16. Gas Solenoid Valves

17. High/Low mixing valves.

18. Kitchen Solenoid Gas Valve.

19. Laboratory piping systems and equipment.

20. Medical Gas Systems and Alarms

21. Plumbing Fixtures.

22. Plumbing Pumps.

23. Roof Hydrants.

24. Shower head flow rates.

25. Thermostatic mixing valves below hand sinks/lavs.

26. Trap priming stations.

1.3. DEFINITIONS

A. Architect: Includes Architect identified in the Contract for Construction between Owner and Contractor, plus consultant/design professionals responsible for design of plumbing systems, electrical, communications, controls for plumbing systems, and other related systems.

B. CxA: Commissioning Authority.

C. Systems, Subsystems, and Equipment: Where these terms are used together or separately, they shall mean "as-built" systems, subsystems, and equipment.

D. TAB: Testing, Adjusting, and Balancing.

1.4. CONTRACTOR'S RESPONSIBILITIES

A. The following responsibilities are in addition to those specified in Division 01 Section "General Commissioning Requirements."

B. Contractor:

1. Attend procedures meeting for TAB Work.

2. Certify that TAB Work is complete.

3. Assist performing functional performance tests.

C. Mechanical Contractor:

1. Attend TAB verification testing.

2. Provide measuring instruments and logging devices to record test data, and data acquisition equipment to record data for the complete range of testing for the required test period.

3. Assist performing functional performance tests.

4. Assist testing flow rates of all plumbing fixtures.

D. HVAC Instrumentation and Control Contractor: With the CxA, review control designs for compliance with the Contract Documents, controllability with respect to actual equipment to be installed, and recommend adjustments to control designs and sequence of operation descriptions.

E. TAB Subcontractor:

1. Contract Documents Review: With the CxA, review the Contract Documents before developing TAB procedures.

    a. Verify the following:
        i. Accessibility of equipment and components required for TAB Work.
        ii. Verify flush valve gallons per flush matches schedules/submittals.
        iii. Adequate number and placement of balancing valves to allow proper balancing and recording of water flow.
        iv. Adequate number and placement of test ports and test instrumentation to allow reading and compilation of system and equipment performance data needed to conduct both TAB and commissioning testing.
        v. Flow rates and aerations have been specified and compared to central equipment output capacities.
    b. Identify discontinuities and omissions in the Contract Documents.
    c. This review of the Contract Documents by the TAB Subcontractor satisfies requirements for a design review report as specified in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing."
    d. Assist performing functional performance tests.

2. Additional Responsibilities: Participate in tests specified in Division 23 Sections "Instrumentation & Controls of HVAC & Plumbing Systems."

F. Electrical Contractor:

1. With the Mechanical Contractor, coordinate installations and connections between and among electrical and plumbing systems, subsystems, and equipment.

2. Attend TAB verification testing.

1.5. COMMISSIONING DOCUMENTATION

A. The following are in addition to documentation specified in Division 01 Section "General Commissioning Requirements."

B. Test Checklists: CxA with assistance of Contractor shall develop test checklists for plumbing systems, subsystems, and equipment, including interfaces and interlocks with other systems. CxA shall prepare separate checklists for each mode of operation and provide space to indicate whether the mode under test responded as required. In addition to the requirements specified in Division 01 Section "General Commissioning Requirements," checklists shall include, but not be limited to, the following:

1. Calibration of sensors and sensor function.

2. Testing conditions under which test was conducted, including (as applicable) ambient conditions, set points, override conditions, and status and operating conditions that impact the results of test.

3. Control sequences for plumbing systems and equipment.

4. Strength of control signal for each set point at specified conditions.

5. Responses to control signals at specified conditions.

6. Sequence of response(s) to control signals at specified conditions.

7. Electrical demand or power input at specified conditions.

8. Power quality and related measurements.

9. Expected performance of systems, subsystems, and equipment at each step of test.

10. Narrative description of observed performance of systems, subsystems, and equipment. Notation to indicate whether the observed performance at each step meets the expected results.

11. Interaction of auxiliary equipment.

12. Issues log.

1.6. SUBMITTALS

A. The following submittals are in addition to those specified in Division 01 Section "General Commissioning Requirements."

B. Testing Procedures: CxA shall submit detailed testing plan, procedures, and checklists for each series of tests. Submittals shall include samples of data reporting sheets that will be part of the reports.

C. Certificate of Readiness: CxA shall compile certificates of readiness from Contractor

certifying that systems, subsystems, equipment, and associated controls are ready for testing.

D. Certificate of Completion of Installation, Prestart, and Startup: CxA shall certify that installation, prestart, and startup activities have been completed. Certification shall include completed checklists provided by TAB Subcontractor as specified in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing."

E. Certified Pipe Cleaning and Flushing Report: CxA shall certify that pipe cleaning, flushing, hydrostatic testing, and chemical treating have been completed.

F. Test and Inspection Reports: CxA shall compile and submit test and inspection reports and certificates, and shall include them in systems manual and commissioning report.

G. Corrective Action Documents: CxA shall submit corrective action documents.

H. Certified TAB Reports: CxA shall submit verified, certified TAB reports.

1.7. ALTERNATES

A. Refer to Division 01 Section, “Alternates” for description of work under this section affected by alternates.

PART 2. PRODUCTS (NOT USED)

PART 3. EXECUTION

3.1. TESTING PREPARATION

A. Prerequisites for Testing:

1. Certify that plumbing systems, subsystems, and equipment have been completed, calibrated, and started; are operating according to the Contract Documents; and that Certificates of Readiness are signed and submitted.

2. Certify that plumbing instrumentation and control systems have been completed and calibrated; are operating according to the Contract Documents; and that pretest set points have been recorded.

3. Certify that plumbing procedures have been completed, and that TAB reports have been submitted, discrepancies corrected, and corrective work approved.

4. Test systems and intersystem performance after approval of test checklists for systems, subsystems, and equipment.

5. Set systems, subsystems, and equipment into operating mode to be tested (e.g., normal shut down, normal auto position, normal manual position, unoccupied cycle, emergency power, and alarm conditions).

6. Verify each operating cycle after it has been running for a specified period and is operating in a steady-state condition.

7. Inspect and verify the position of each device and interlock identified on checklists. Sign off each item as acceptable, or failed. Repeat this test for each operating cycle that applies to system being tested.

8. Check safety cutouts, alarms, and interlocks with life-safety systems during each mode of operation.

9. Annotate checklist or data sheet when a deficiency is observed.

10. Verify equipment interface with monitoring and control system and TAB criteria; include the following:

    a. Backflow preventer cross connection tests.
    b. Compressor operation including refrigerated air dryers.
    c. Discharge temperatures of water heaters.
    d. Dental equipment operation and safeties.
    e. Domestic booster pump flow rates, head, safeties, remote pressure transmitter.
    f. Domestic water meter total volume in gallons.
    g. Elevator sump pump control and alarms.
    h. Flow rates for domestic re-circulating systems.
    i. Flow rates in gallons per minute for showerheads.
    j. High/low and thermostatic mixing valve temperatures and water flow rates.
    k. Dental and shop air compressors operation and safeties.
    l. Pressure for laboratory piping systems.
    m. Re-circ. pump pressures and flow rates.
    n. Roof hydrant operation and freeze protection.
    o. Temperature for emergency eyewash/shower systems.
    p. Trap priming station water discharge.
    q. Water heater temperatures and set points.
    r. Water meter flow rates and calibration.
    s. Dental vacuum pumps operation and safeties.

11. Verify proper responses of monitoring and control system controllers and sensors to include the following:

    a. For each controller or sensor, record the indicated monitoring and control system reading and the test instrument reading. If initial test indicates that the test reading is outside of the control range of the installed device, check calibration of the installed device and adjust as required. Retest malfunctioning devices and record results on checklist or data sheet.
    b. Report deficiencies and prepare an issues log entry.

12. Verify that plumbing equipment field quality-control testing has been completed and approved. CxA shall direct, witness, and document field quality-control tests, inspections, and startup specified in individual Division 22 Sections.

13. Verify flow rates of all aerators.

14. Verify the operation and flow rates of all plumbing fixtures.

B. Testing Instrumentation: Install measuring instruments and logging devices to record test data for the required test period. Instrumentation shall monitor and record full range of operating conditions and shall allow for calculation of total capacity of system for each mode of operation. Operational modes include the following:

1. Occupied and unoccupied.

2. Emergency power supply.

3. Life-safety and safety systems.

4. Temporary upset of system operation.

5. Partial occupancy conditions.

6. Special cycles.

7. Alarm conditions.

8. Lead/lag operation where redundant equipment is indicated.

9. All alarms.

3.2. TAB VERIFICATION

A. TAB Subcontractor shall coordinate with CxA for work required in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing." TAB Subcontractor shall copy CxA with required reports, sample forms, checklists, and certificates.

B. Contractor, Plumbing Contractor, and CxA shall witness TAB Work.

C. TAB Preparation:

1. TAB Subcontractor shall provide CxA with data required for "Pre-Field TAB Engineering Reports" specified in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing."

a. CxA shall use this data to certify that prestart and startup activities have been completed for systems, subsystems, and equipment installation.

D. Verification of Final TAB Report:

1. CxA shall select, at random, 10 percent of report for field verification.

2. CxA shall notify TAB Subcontractor 10 days in advance of the date of field verification; however, notice shall not include data points to be verified. The TAB Subcontractor shall use the same instruments (by model and serial number) that were used when original data were collected.

3. Failure of an item is defined as follows:

a. A deviation of more than 10 percent.

4. Failure of more than 10 percent of selected items shall result in rejection of final TAB report.

E. If deficiencies are identified during verification testing, CxA shall notify the HVAC Contractor and Architect and shall take action to remedy the deficiency. Engineer shall review final tabulated checklists and data sheets to determine if verification is complete and that system is operating according to the Contract Documents.

F. CxA shall certify that TAB Work has been successfully completed.

3.3. TESTING

A. Test systems and intersystem performance after test checklists for systems, subsystems, and equipment have been approved.

B. Perform tests using design conditions whenever possible.

1. Simulate conditions by imposing an artificial load when it is not practical to test under design conditions and when written approval for simulated conditions is received from CxA. Before simulating conditions, calibrate testing instruments. Set and document simulated conditions and methods of simulation. After tests, return settings to normal operating conditions.

2. Alter set points when simulating conditions is not practical and when written approval is received from CxA.

3. Alter sensor values with a signal generator when design or simulating conditions and altering set points are not practical. Do not use sensor to act as signal generator to simulate conditions or override values.

C. Scope of Plumbing Contractor Testing:

1. Testing scope shall include entire plumbing installation, from central hot water heating equipment for heat generation through distribution systems to each fixture. It shall include measuring capacities and effectiveness of operational and control functions.

2. Test all operating modes, interlocks, control responses, responses to abnormal or emergency conditions, and verify proper response of building automation system controllers and sensors.

3. Test all plumbing fixtures.

4. Test time to reach temperature and temperature of hot water at all fixtures with thermostatic mixing valves.

5. Test discharge temperature of high/low mixing valves.

6. Test discharge of water at all trap priming stations.

7. Verify that all backflow preventers have been tested. Document in writing.

8. Test operation and interlock of all sump pumps including elevator sump pumps.

9. Test operation of all water meters.

10. Test domestic hot water heater, safeties, and operating controls.

11. Test domestic water heaters.

12. Test all dental compressed air and vacuum systems including alarms.

13. Test water meters and interlock with ATC system.

14. Test operation, set points, and safeties of water heaters.

15. Test flow rate, pressures, set points, and safeties of domestic booster pump.

16. Verify that backflow preventers have been tested.

17. Test discharge of water at all trap priming stations.

18. Test the operation of all domestic water and gas solenoid valves, including interlocks to switches.

19. Test operation, set points, and safeties of shop compressed air system.

D. Detailed Testing Procedures: CxA, with Plumbing Contractor, TAB Subcontractor, and Plumbing Instrumentation and Control Contractor, shall prepare detailed testing plans, procedures, and checklists for plumbing systems, subsystems, and equipment.

E. HVAC Instrumentation and Control System Testing:

1. Field testing plans and testing requirements are specified in Division 23 Section "Instrumentation & Controls of HVAC & Plumbing Systems." The CxA, Plumbing Contractor, and the HVAC Instrumentation and Control Contractor shall collaborate to prepare testing plans.

2. CxA shall convene a meeting of appropriate entities to review test report of HVAC instrumentation and control systems.

F. Plumbing System Testing: Plumbing Contractor shall prepare a testing plan to verify performance of water heaters, emergency eyewash/shower systems, domestic re-circulating systems, laboratory piping systems, backflow preventers, plumbing fixtures, trap priming stations, high/low mixing valves, domestic pumps, elevator sump pumps and auxiliary equipment, domestic water meters, solenoid valves, compressed air systems, thermostatic mixing valves, domestic booster pumps, dental compressed air and vacuum equipment and duplex sump pumps. Plan shall include the following:

1. Sequence of testing and testing procedures for each item of equipment and section of pipe to be tested, identified by identification marker. Markers shall be

keyed to Drawings for each pipe sector showing the physical location of each item of equipment and pipe test section. Drawings shall be formatted to allow each item of equipment and section of piping to be physically located and identified when referred to in the system testing plan.

2. Tracking checklist for managing and ensuring that all pipe sections have been tested.

3. Design and actual measurements for all equipment.

G. Deferred Testing:

1. If tests cannot be completed because of a deficiency outside the scope of the plumbing system, the deficiency shall be documented and reported to Owner. Deficiencies shall be resolved and corrected by appropriate parties and test rescheduled.

2. If the testing plan indicates specific seasonal testing, appropriate initial performance tests shall be completed and documented and additional tests scheduled.

H. Testing Reports:

1. Reports shall include measured data, data sheets, and a comprehensive summary describing the operation of systems at the time of testing.

2. Include data sheets for each controller to verify proper operation of the control system, the system it serves, the service it provides, and its location. For each controller, provide space for recording its readout, the reading at the controller's sensor(s), plus comments. Provide space for testing personnel to sign off on each data sheet.

3. Prepare a preliminary test report. Deficiencies will be evaluated by Architect to determine corrective action. Deficiencies shall be corrected and test repeated.

END OF SECTION

DIVISION 01 SECTION 01 91 15
HVAC COMMISSIONING REQUIREMENTS
TABLE OF CONTENTS

PART 1. GENERAL 3
1.1. RELATED DOCUMENTS 3
1.2. SUMMARY 3
1.3. DEFINITIONS 5
1.4. CONTRACTOR'S RESPONSIBILITIES 6
1.5. COMMISSIONING DOCUMENTATION 7
1.6. SUBMITTALS 8
1.7. ALTERNATES 8
PART 2. PRODUCTS (NOT USED) 8
PART 3. EXECUTION 8
3.1. TESTING PREPARATION 8
3.2. TAB VERIFICATION 12
3.3. TESTING 12
END OF SECTION 15

THIS PAGE LEFT INTENTIONALLY BLANK

SECTION 01 91 15
HVAC COMMISSIONING REQUIREMENTS

PART 1. GENERAL

1.1. RELATED DOCUMENTS

A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and other Division 01 Specification Sections, apply to this Section.

1.2. SUMMARY

A. This Section includes requirements for commissioning the HVAC system and its subsystems and equipment. This Section supplements the general requirements specified in Division 01 Section "General Commissioning Requirements."

B. Related Sections include the following:

1. Division 01 Section "General Commissioning Requirements" for general requirements for commissioning processes that apply to this Section.

C. The following systems and/or equipment shall be commissioned:

1. Air Flow Monitoring Stations.
2. Air Separators.
3. Smoke removal assist system.
4. Automatic Glycol Feeders.
5. Automatic Temperature Control System.
6. Boilers and burners.
7. Carbon Dioxide Sensors.
8. Carbon Monoxide Makeup Air and Exhaust Systems.
9. Chemical Water Treatment.
10. Chilled, water system.
11. Condensate overflow alarms.
12. Condensate pumps.
13. Dampers
14. Dental Equipment

15. Demand Meter/ATC Interface.
16. Differential Pressure Bypass Valves.
17. Differential Static Pressure Controllers.
18. Dishwasher Exhaust Fans.
19. Dryer Duct Booster System.
20. Duct smoke detectors.
21. Ductless heat pumps and air conditioning units.
22. Dust Collector Systems.
23. Electric Heaters/Radiant Heat Panels.
24. Energy recovery ventilators (Including variable frequency drives).
25. Exhaust air systems including fume hoods and laboratory exhaust systems.
26. Expansion tanks
27. Exhaust Fans and ventilation fans.
28. Fan coil systems.
29. Flame Failure Alarms.
30. Flow measuring stations.
31. Flow Switches.
32. Freeze protection pumps.
33. Fume hoods and fume hood exhaust air fans.
34. Heat Pipes.
35. Heating and Ventilating Units
36. High and low temperature alarms.
37. Hydronic Unit Heaters.
38. Hot water systems.
39. HVAC controls and sequences of operation.

40. Industrial air cleaners.
41. Kiln Ventilation Fans.
42. Kitchen ventilation system.
43. Lighting interface to ATC system.
44. Low Water Cut-Offs.
45. Makeup water meter flow rates and alarms.
46. Minimum Flow Bypass Valves/Controls.
47. Paint Mixing Booth Ventilation.
48. Paint spray booth. (Exhaust Fans and Gas Fired Makeup Air Unit)
49. Pressure Independent Control Valves.
50. Pumps.
51. Relative Humidity Sensors.
52. Relief Air Dampers.
53. Single Zone VAV Units.
54. Static Pressure Sensors.
55. Temperature Sensors.
56. Unit Heaters.
57. Variable frequency drives.
58. Ventilation Fans.
59. Water meter/ATC interface.
60. Welding Hood Exhaust/Make-up Air Systems.

1.3. DEFINITIONS

A. Architect: Includes Architect identified in the Contract for Construction between Owner and Contractor, plus consultant/design professionals responsible for design of HVAC, electrical, communications, controls for HVAC systems, and other related systems.

B. CxA: Commissioning Authority.

C. Systems, Subsystems, and Equipment: Where these terms are used together or separately, they shall mean "as-built" systems, subsystems, and equipment.

D. TAB: Testing, Adjusting, and Balancing.

1.4. CONTRACTOR'S RESPONSIBILITIES

A. The following responsibilities are in addition to those specified in Division 01 Section "General Commissioning Requirements."

B. Contractor:

1. Attend procedures meeting for TAB Work.

2. Certify that TAB Work is complete.

3. Assist performing functional performance tests.

C. Mechanical Contractor:

1. Attend TAB verification testing.

2. Provide measuring instruments and logging devices to record test data, and data acquisition equipment to record data for the complete range of testing for the required test period.

3. Assist performing functional performance tests.

D. HVAC Instrumentation and Control Contractor: With the CxA, review control designs for compliance with the Contract Documents, controllability with respect to actual equipment to be installed, and recommend adjustments to control designs and sequence of operation descriptions. Assist with performing functional performance tests.

E. TAB Subcontractor:

1. Contract Documents Review: With the CxA, review the Contract Documents before developing TAB procedures.

a. Verify the following:
i. Accessibility of equipment and components required for TAB Work.
ii. Adequate number and placement of duct balancing dampers to allow proper balancing while minimizing sound levels in occupied spaces.
iii. Adequate number and placement of balancing valves to allow proper balancing and recording of water flow.
iv. Adequate number and placement of test ports and test instrumentation to allow reading and compilation of system and equipment performance data needed to conduct both TAB and commissioning testing.

v. Air and water flow rates have been specified and compared to central equipment output capacities.

b. Identify discontinuities and omissions in the Contract Documents.

c. This review of the Contract Documents by the TAB Subcontractor satisfies requirements for a design review report as specified in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing."

d. Assist performing functional performance tests.

2. Additional Responsibilities: Participate in tests specified in Division 23 Sections "Instrumentation & Controls of HVAC & Plumbing Systems."

F. Electrical Contractor:

1. With the Mechanical Contractor, coordinate installations and connections between and among electrical and HVAC systems, subsystems, and equipment.

2. Attend TAB verification testing.

1.5. COMMISSIONING DOCUMENTATION

A. The following are in addition to documentation specified in Division 01 Section "General Commissioning Requirements."

B. Test Checklists: CxA with assistance of Contractor shall develop test checklists for HVAC systems, subsystems, and equipment, including interfaces and interlocks with other systems. CxA shall prepare separate checklists for each mode of operation and provide space to indicate whether the mode under test responded as required. In addition to the requirements specified in Division 01 Section "General Commissioning Requirements," checklists shall include, but not be limited to, the following:

1. Calibration of sensors and sensor function.

2. Testing conditions under which test was conducted, including (as applicable) ambient conditions, set points, override conditions, and status and operating conditions that impact the results of test.

3. Control sequences for HVAC systems.

4. Strength of control signal for each set point at specified conditions.

5. Responses to control signals at specified conditions.

6. Sequence of response(s) to control signals at specified conditions.

7. Electrical demand or power input at specified conditions.

8. Power quality and related measurements.

9. Expected performance of systems, subsystems, and equipment at each step of test.

10. Narrative description of observed performance of systems, subsystems, and equipment. Notation to indicate whether the observed performance at each step meets the expected results.

11. Interaction of auxiliary equipment.

12. Issues log.

1.6. SUBMITTALS

A. The following submittals are in addition to those specified in Division 01 Section "General Commissioning Requirements."

B. Testing Procedures: CxA shall submit detailed testing plan, procedures, and checklists for each series of tests. Submittals shall include samples of data reporting sheets that will be part of the reports.

C. Certificate of Readiness: CxA shall compile certificates of readiness from Contractor certifying that systems, subsystems, equipment, and associated controls are ready for testing.

D. Certificate of Completion of Installation, Prestart, and Startup: CxA shall certify that installation, prestart, and startup activities have been completed. Certification shall include completed checklists provided by TAB Subcontractor as specified in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing."

E. Test and Inspection Reports: CxA shall compile and submit test and inspection reports and certificates, and shall include them in systems manual and commissioning report.

F. Corrective Action Documents: CxA shall submit corrective action documents.

G. Certified TAB Reports: CxA shall submit verified, certified TAB reports.

1.7. ALTERNATES

A. Refer to Division 01 Section, “Alternates” for description of work under this section affected by alternates.

PART 2. PRODUCTS (NOT USED)

PART 3. EXECUTION

3.1. TESTING PREPARATION

A. Prerequisites for Testing:

1. Certify that HVAC systems, subsystems, and equipment have been completed, calibrated, and started; are operating according to the Contract Documents; and that Certificates of Readiness are signed and submitted.

2. Certify that HVAC instrumentation and control systems have been completed and calibrated; are operating according to the Contract Documents; and that pretest set points have been recorded.

3. Certify that TAB procedures have been completed, and that TAB reports have been submitted, discrepancies corrected, and corrective work approved.

4. Test systems and intersystem performance after approval of test checklists for systems, subsystems, and equipment.

5. Set systems, subsystems, and equipment into operating mode to be tested (e.g., normal shut down, normal auto position, normal manual position, unoccupied cycle, emergency power, and alarm conditions).

6. Verify each operating cycle after it has been running for a specified period and is operating in a steady-state condition.

7. Inspect and verify the position of each device and interlock identified on checklists. Sign off each item as acceptable, or failed. Repeat this test for each operating cycle that applies to system being tested.

8. Check safety cutouts, alarms, and interlocks with duct detectors and life-safety systems during each mode of operation.

9. Annotate checklist or data sheet when a deficiency is observed.

10. Verify equipment interface with monitoring and control system and TAB criteria; include the following:

    a. Automatic Glycol Feeder operation and ATC interlocks.
    b. All pump status alarms, pump operation, flow rates, and controls.
    c. All temperature alarms.
    d. Boiler temperatures, flow rates, low water cut-off interlock, flame failure interlocks, flow switches, and amperage.
    e. Building pressurization and room differential pressures.
    f. Carbon monoxide system including makeup air unit exhaust air fans, operation, temperature and fluid/air flow rates.
    g. Chiller flow rates, temperatures, set points, and safeties.
    h. Differential bypass valves and transmitters.
    i. Duct Smoke detectors operation and interlocks with fire alarm system.
    j. Duct dryer booster air flow rates, amperage, and set point.
    k. Ductless heat pumps and air conditioning units with air flow rates, fluid flow rates, and temperatures.
    l. Dust Collector System Control.
    m. Electric heating equipment volts, amps, and temperature rise.
    n. Electric Heat Tracing.
    o. Fan coil unit air/water flow rates and temperatures.
    p. Finned tube radiation operation and control.
    q. Freeze protection pump flow rate pressure, amperage, cut-in/cut-out temperatures.

r. Fume hood, face velocities, alarms.
s. Gas furnace operation control and leaving air temperature.
t. Paint spray booth air flow rates, gas pressure, temperature rise, safeties, and fan interlocks.
u. Head pressure controls for air cooled condensing/heat pump units or chillers.
v. Heat pipe temperatures.
w. Heating and ventilation unit operation, temperatures, fluid flow rates and air flow rates.
x. Hot water coils, airflow rates, pressure drops, temperatures, and fluid flow rate.
y. Hydronic unit heater/baseboard radiation temperature and flow rates.
z. Industrial air cleaner air flow rates.
aa. Kitchen ventilation supply and exhaust air flow rates and temperatures, including optical and exhaust sensors.
bb. Plug load interface and start/stop by ATC system.
cc. Lighting interface and start/stop by ATC system.
dd. Minimum outdoor-air intake in each operational mode and at minimum and maximum airflows.
ee. Operation/Accuracy of air and fluid flow measuring stations at various flow rates.
ff. Pump flow rates, pressure and amperage at each operating mode.
gg. Sequences of operation of all HVAC equipment.
hh. Set point and operation of high temperature alarms.
ii. Smoke removal assist system operation, safeties, and interlocks to fire alarm system.
jj. Supply and return air flow rates for all HVAC equipment.
kk. Supply, outside air, exhaust and return air flow rates for ERVs in each operating mode.
ll. Test and calibrate all static pressure sensors.
mm. Test all flow switches including operation and alarms.
nn. Test boiler low water cut-off and flame failure alarms.
oo. Test freeze protection pumps.
pp. Test operation and air temperatures of hot gas re-heat coils.
qq. Test safeties and operation of air curtains.
rr. Total exhaust airflow and total outdoor-air intake.
ss. Unit heaters operation and control.
tt. Variable speed drive parameters at each operated mode.

11. Verify proper responses of monitoring and control system controllers and sensors to include the following:

a. For each controller or sensor, record the indicated monitoring and control system reading and the test instrument reading. If initial test indicates that the test reading is outside of the control range of the installed device, check calibration of the installed device and adjust as required. Retest malfunctioning devices and record results on checklist or data sheet.
b. Report deficiencies and prepare an issues log entry.

12. Verify that HVAC equipment field quality-control testing has been completed and approved. CxA shall direct, witness, and document field quality-control tests, inspections, and startup specified in individual Division 23 Sections.

B. Testing Instrumentation: Install measuring instruments and logging devices to record test data for the required test period. Instrumentation shall monitor and record full range of operating conditions and shall allow for calculation of total capacity of system for each mode of operation. For individual room cooling tests, provide temporary heaters to impose a cooling load. Operational modes include the following:

1. Heating/Cooling Mode.
2. Occupied and unoccupied.
3. Warm up and cool down.
4. Economizer cycle/relief air fan/damper operation.
5. Emergency power supply.
6. Fluid flow rates and temperatures for all hydronic equipment.
7. H&V Units in all modes of operation.
8. Life-safety and safety systems.
9. Duct detectors.
10. Fire safety.
11. Temporary upset of system operation.
12. Partial occupancy conditions.
13. Special cycles.
14. ERV/Single Zone VAV Unit supply/exhaust air flow at partial CO2 levels.
15. Lead/lag/standby modes of operation where redundant equipment is indicated.
16. All alarms.
17. Kitchen make-up air unit and exhaust air fan at full, partial, and minimum air flow rates.
18. Flow switch shut-down and alarm.
19. Condensate overflow safety switch shut-down and alarm.
20. Condensate pump operation.

21. Test operation and accuracy of air/fluid flow measuring stations.

22. Paint spray booth interlocks, safeties, gas heater operation, and exhaust fan operation.

3.2. TAB VERIFICATION

A. TAB Subcontractor shall coordinate with CxA for work required in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing." TAB Subcontractor shall copy CxA with required reports, sample forms, checklists, and certificates.

B. Contractor, HVAC Contractor, and CxA shall witness TAB Work.

C. TAB Preparation:

1. TAB Subcontractor shall provide CxA with data required for "Pre-Field TAB Engineering Reports" specified in Division 23 Section "Testing Adjusting & Balancing for HVAC & Plumbing."

a. CxA shall use this data to certify that prestart and startup activities have been completed for systems, subsystems, and equipment installation.

D. Verification of Final TAB Report:

1. CxA shall select, at random, 10 percent of report for field verification.

2. CxA shall notify TAB Subcontractor 10 days in advance of the date of field verification; however, notice shall not include data points to be verified. The TAB Subcontractor shall use the same instruments (by model and serial number) that were used when original data were collected.

3. Failure of an item is defined as follows:

a. For all readings a deviation of more than 10 percent.

4. Failure of more than 10 percent of selected items shall result in rejection of final TAB report.

E. If deficiencies are identified during verification testing, CxA shall notify the HVAC Contractor and Architect and shall take action to remedy the deficiency. Architect shall review final tabulated checklists and data sheets to determine if verification is complete and that system is operating according to the Contract Documents.

F. CxA shall certify that TAB Work has been successfully completed.

3.3. TESTING

A. Test systems and intersystem performance after test checklists for systems, subsystems, and equipment have been approved.

B. Contractors and subcontractors must pre-inspect and pre-test all equipment and systems prior to requesting functional performance testing by the CxA. All pre-start/start-up checklists and functional performance test forms must be completed and submitted to Engineer prior to scheduling formal functional performance testing.

C. Perform tests using design conditions whenever possible.

1. Simulate conditions by imposing an artificial load when it is not practical to test under design conditions and when written approval for simulated conditions is received from CxA. Before simulating conditions, calibrate testing instruments. Set and document simulated conditions and methods of simulation. After tests, return settings to normal operating conditions.

2. Alter set points when simulating conditions is not practical and when written approval is received from CxA.

3. Alter sensor values with a signal generator when design or simulating conditions and altering set points are not practical. Do not use sensor to act as signal generator to simulate conditions or override values.

D. Scope of HVAC Contractor Testing:

1. Testing scope shall include entire HVAC installation, from central equipment for heat generation and refrigeration through distribution systems to each conditioned space. It shall include measuring capacities and effectiveness of operational and control functions.

2. Test all operating modes, interlocks, control responses, responses to abnormal or emergency conditions, and verify proper response of building automation system controllers and sensors.

E. Detailed Testing Procedures: CxA, with HVAC Contractor, TAB Subcontractor, and HVAC Instrumentation and Control Contractor, shall prepare detailed testing plans, procedures, and checklists for HVAC systems, subsystems, and equipment.

F. HVAC Instrumentation and Control System Testing:

1. Field testing plans and testing requirements are specified in Division 23 Section "Instrumentation & Controls of HVAC & Plumbing Systems". The CxA, HVAC Contractor, Equipment Provider/Manufacturer and the HVAC Instrumentation and Control Contractor shall collaborate to prepare testing plans.

2. CxA shall convene a meeting of appropriate entities to review test report of HVAC instrumentation and control systems.

G. Energy Supply System Testing: HVAC Contractor shall prepare a testing plan to verify performance of gas systems and equipment. Plan shall include the following:

1. Sequence of testing and testing procedures for each equipment item and pipe section to be tested, identified by pipe zone or sector identification marker.

Markers shall be keyed to Drawings for each pipe sector showing the physical location of each designated pipe test section. Drawings keyed to pipe zones or sectors shall be formatted to allow each section of piping to be physically located and identified when referred to in system testing plan.

2. Tracking checklist for managing and ensuring that all pipe sections have been tested.

H. Heat-Generation System Testing: HVAC Contractor shall prepare a testing plan to verify performance of air handling units, heat pumps, and auxiliary equipment, energy recovery ventilators, unit heaters, single zone VAV units, radiant heat panels, paint spray booth gas furnaces, hydronic unit heaters, welding makeup air units, heating and ventilating units, fan coil units, unit ventilators, carbon monoxide makeup air units, boilers, fan coil units and baseboard radiation rooftop/air handling units. Plan shall include the following:

1. Sequence of testing and testing procedures for each item of equipment and section of pipe to be tested, identified by identification marker. Markers shall be keyed to Drawings for each pipe sector showing the physical location of each item of equipment and pipe test section. Drawings shall be formatted to allow each item of equipment and section of piping to be physically located and identified when referred to in the system testing plan.

2. Tracking checklist for managing and ensuring that all pipe sections have been tested.

I. Refrigeration/Heat Rejection System Testing: HVAC Contractor shall prepare a testing plan to verify performance of heat pumps, rooftop units, chillers, refrigerant compressors, ductless units, single zone VAV units, condensing units, ERV units, VAV rooftop/air handling units, heat pipes, fan coil units, unit heaters and other refrigeration systems. Plan shall include the following:

1. Sequence of testing and testing procedures for each item of equipment and section of pipe to be tested, identified by identification marker. Markers shall be keyed to Drawings showing the physical location of each item of equipment and pipe test section. Drawings shall be formatted to allow each item of equipment and section of piping to be physically located and identified when referred to in the system testing plan.

2. Tracking checklist for managing and ensuring that all pipe sections have been tested.

J. HVAC Distribution System Testing: HVAC Contractor shall prepare a testing plan to verify performance of air, air handling units, and hydronic distribution systems, special exhaust ERV unit supply and exhaust, kitchen ventilation systems, single zone VAV units, fume hood exhaust fans, dust collectors, shop ventilation systems, carbon monoxide ventilation systems, welding hood ventilation systems, industrial air cleaners, and other distribution systems. Include HVAC terminal equipment and unitary equipment. Plan shall include the following:

1. Sequence of testing and testing procedures for each item of equipment and section

of pipe to be tested, identified by identification marker. Markers shall be keyed to Drawings showing the physical location of each item of equipment and pipe test section. Drawings shall be formatted to allow each item of equipment and section of piping to be physically located and identified when referred to in the system testing plan.

2. Tracking checklist for managing and ensuring that all pipe sections have been tested.

3. Equipment, air flow rates, air temperatures, fluid flow rates, safeties, freeze protection pump operation, and demand controlled ventilation.

K. Deferred Testing:

1. If tests cannot be completed because of a deficiency outside the scope of the HVAC system, the deficiency shall be documented and reported to Owner. Deficiencies shall be resolved and corrected by appropriate parties and test rescheduled.

2. If the testing plan indicates specific seasonal testing, appropriate initial performance tests shall be completed and documented and additional tests scheduled.

L. Testing Reports:

1. Reports shall include measured data, data sheets, and a comprehensive summary describing the operation of systems at the time of testing.

2. Include data sheets for each controller to verify proper operation of the control system, the system it serves, the service it provides, and its location. For each controller, provide space for recording its readout, the reading at the controller's sensor(s), plus comments. Provide space for testing personnel to sign off on each data sheet.

3. Prepare a preliminary test report. Deficiencies will be evaluated by Architect, to determine corrective action. Deficiencies shall be corrected and test repeated.

END OF SECTION

THIS PAGE LEFT INTENTIONALLY BLANK

DIVISION 01 SECTION 01 91 16
ELECTRICAL SYSTEMS COMMISSIONING REQUIREMENTS
TABLE OF CONTENTS

PART 1. GENERAL 3

1.1 RELATED DOCUMENTS 3
1.2 SUMMARY 3
1.3 DEFINITIONS 3
1.4 CONTRACTOR'S RESPONSIBILITIES 4
1.5 COMMISSIONING DOCUMENTATION 4
1.6 SUBMITTALS 5

PART 2. PRODUCTS (Not Used) 5

PART 3. EXECUTION 5

3.1 TESTING PREPARATION 5
3.2 TESTING 6
END OF SECTION 7

THIS PAGE INTENTIONALLY LEFT BLANK

SECTION 01 91 16
ELECTRICAL SYSTEMS COMMISSIONING REQUIREMENTS

PART 1. GENERAL

1.1 RELATED DOCUMENTS

A. Drawings and general provisions of the Contract, including General and Supplementary Conditions and Division 01 Specification Sections, apply to this Section.

1.2 SUMMARY

A. This Section includes requirements for commissioning the electrical system and its subsystems and equipment. This Section supplements the general requirements specified in Division 01 Section "General Commissioning Requirements."

B. Related Sections include the following:

1. Division 01 Section "General Commissioning Requirements" for general requirements for commissioning processes that apply to this Section.

C. The following systems and/or equipment shall be commissioned.

1. Emergency generator systems.

2. Fire Alarm System.

3. Exterior lighting and associated controls.

4. Athletic Field lighting and associated controls.

5. Electrical distribution system.

a. Main switchboard.
b. Distribution panelboards.
c. Motor starters.
d. Lighting contactors.

1.3 DEFINITIONS

A. Architect: Includes Architect identified in the Contract for Construction between Owner and Contractor, plus consultant/design professionals responsible for design of electrical systems, electrical, communications, and other related systems.

B. CxA: Commissioning Authority.

C. Systems, Subsystems, and Equipment: Where these terms are used together or separately, they shall mean "as-built" systems, subsystems, and equipment.

1.4 CONTRACTOR'S RESPONSIBILITIES

A. The following responsibilities are in addition to those specified in Division 01 Section "General Commissioning Requirements."

B. Electrical Contractor:

1. Provide certified and calibrated measuring instruments and logging devices to record test data, and data acquisition equipment to record data for the complete range of testing for the required test period.

C. Electrical Contractor:

1. With the Mechanical Contractor, coordinate installations and connections between and among electrical and HVAC systems, subsystems, and equipment.
2. Attend TAB verification testing.

1.5 COMMISSIONING DOCUMENTATION

A. The following are in addition to documentation specified in Division 01 Section "General Commissioning Requirements."

B. Test Checklists: CxA with assistance of Contractor shall develop test checklists for electrical systems, subsystems, and equipment, including interfaces and interlocks with other systems. CxA shall prepare separate checklists for each mode of operation and provide space to indicate whether the mode under test responded as required. In addition to the requirements specified in Division 01 Section "General Commissioning Requirements," checklists shall include, but not be limited to, the following:

1. Calibration of sensors and sensor function.

2. Testing conditions under which test was conducted, including (as applicable) ambient conditions, set points, override conditions, and status and operating conditions that impact the results of test.

3. Control sequences for electrical and emergency generator systems.

4. Strength of control signal for each set point at specified conditions.

5. Responses to control signals at specified conditions.

6. Sequence of response(s) to control signals at specified conditions.

7. Electrical demand or power input at specified conditions.

8. Power quality and related measurements.

9. Expected performance of systems, subsystems, and equipment at each step of test.

10. Narrative description of observed performance of systems, subsystems, and equipment. Notation to indicate whether the observed performance at each step meets the expected results.

11. Interaction of auxiliary equipment.

12. Issues log.

1.6 SUBMITTALS

A. The following submittals are in addition to those specified in Division 01 Section "General Commissioning Requirements."

B. Testing Procedures: CxA shall submit detailed testing plan, procedures, and checklists for each series of tests. Submittals shall include samples of data reporting sheets that will be part of the reports.

C. Certificate of Readiness: CxA shall compile certificates of readiness from Contractor certifying that systems, subsystems, equipment, and associated controls are ready for testing.

D. Certificate of Completion of Installation, Prestart, and Startup: CxA shall certify that installation, prestart, and startup activities have been completed.

E. Test and Inspection Reports: CxA shall compile and submit test and inspection reports and certificates, and shall include them in systems manual and commissioning report.

F. Corrective Action Documents: CxA shall submit corrective action documents.

PART 2. PRODUCTS (Not Used)

PART 3. EXECUTION

3.1 TESTING PREPARATION

A. Prerequisites for Testing:

1. Certify that electrical systems, subsystems, and equipment have been completed, calibrated, and started; are operating according to the Contract Documents; and that Certificates of Readiness are signed and submitted.

2. Certify that electrical instrumentation and control systems have been completed and calibrated; are operating according to the Contract Documents; and that pretest set points have been recorded.

3. Test systems and intersystem performance after approval of test checklists for systems, subsystems, and equipment.

4. Set systems, subsystems, and equipment into operating mode to be tested (e.g., normal shut down, normal auto position, normal manual position, unoccupied cycle, emergency power, and alarm conditions).

5. Verify each operating cycle after it has been running for a specified period and is operating in a steady-state condition.

6. Inspect and verify the position of each device and interlock identified on checklists. Sign off each item as acceptable, or failed. Repeat this test for each operating cycle that applies to system being tested.

7. Check safety cutouts, alarms, and interlocks with **[smoke control]** and life-safety systems during each mode of operation.

8. Annotate checklist or data sheet when a deficiency is observed.

9. Verify proper responses of monitoring and control system controllers and sensors to include the following:

   a. For each controller or sensor, record the indicated monitoring and control system reading and the test instrument reading. If initial test indicates that the test reading is outside of the control range of the installed device, check calibration of the installed device and adjust as required. Retest malfunctioning devices and record results on checklist or data sheet.

   b. Report deficiencies and prepare an issues log entry.

3.2 TESTING

A. Test systems and intersystem performance after test checklists for systems, subsystems, and equipment have been approved.

B. Perform tests using design conditions whenever possible.

1. Simulate conditions by imposing an artificial load when it is not practical to test under design conditions and when written approval for simulated conditions is received from CxA. Before simulating conditions, calibrate testing instruments. Set and document simulated conditions and methods of simulation. After tests, return settings to normal operating conditions.

C. Scope of Electrical Contractor Testing:

1. Testing scope shall include entire electrical installation, from incoming service through distribution systems to each space. It shall include measuring voltages and currents and effectiveness of operational and control functions.

2. Test all operating modes, interlocks, control responses, responses to abnormal or emergency conditions, and verify proper response of building automation system controllers and sensors.

D. Detailed Testing Procedures: CxA, with Electrical Contractor shall prepare detailed testing plans, procedures, and checklists for electrical systems, subsystems, and equipment.

E. Electrical System Testing: Electrical Contractor shall prepare a testing plan to verify performance of emergency generator, electrical distribution systems, fire alarm system, exterior lighting control systems. Plan shall include the following:

1. Sequence of testing and testing procedures for each item of equipment and section of wiring to be tested, identified by identification marker. Markers shall be keyed to Drawings for each wiring sector showing the physical location of each item of equipment and electrical wiring test section. Drawings shall be formatted to allow each item of equipment and section of wiring to be physically located and identified when referred to in the system testing plan.

2. Tracking checklist for managing and ensuring that all wiring systems have been tested.

F. Deferred Testing:

1. If tests cannot be completed because of a deficiency outside the scope of the electrical system, the deficiency shall be documented and reported to Owner. Deficiencies shall be resolved and corrected by appropriate parties and test rescheduled.

2. If the testing plan indicates specific seasonal testing, appropriate initial performance tests shall be completed and documented and additional tests scheduled.

G. Testing Reports:

1. Reports shall include measured data, data sheets, and a comprehensive summary describing the operation of systems at the time of testing.

2. Include data sheets for each electrical system to verify proper operation of the electrical systems, the system it serves, the service it provides, and its location. Provide space for testing personnel to sign off on each data sheet.

3. Prepare a preliminary test report. Deficiencies will be evaluated by Architect to determine corrective action. Deficiencies shall be corrected and test repeated.

END OF SECTION

THIS PAGE LEFT INTENTIONALLY BLANK
